


Dallas District
Dallas County Construction Projects

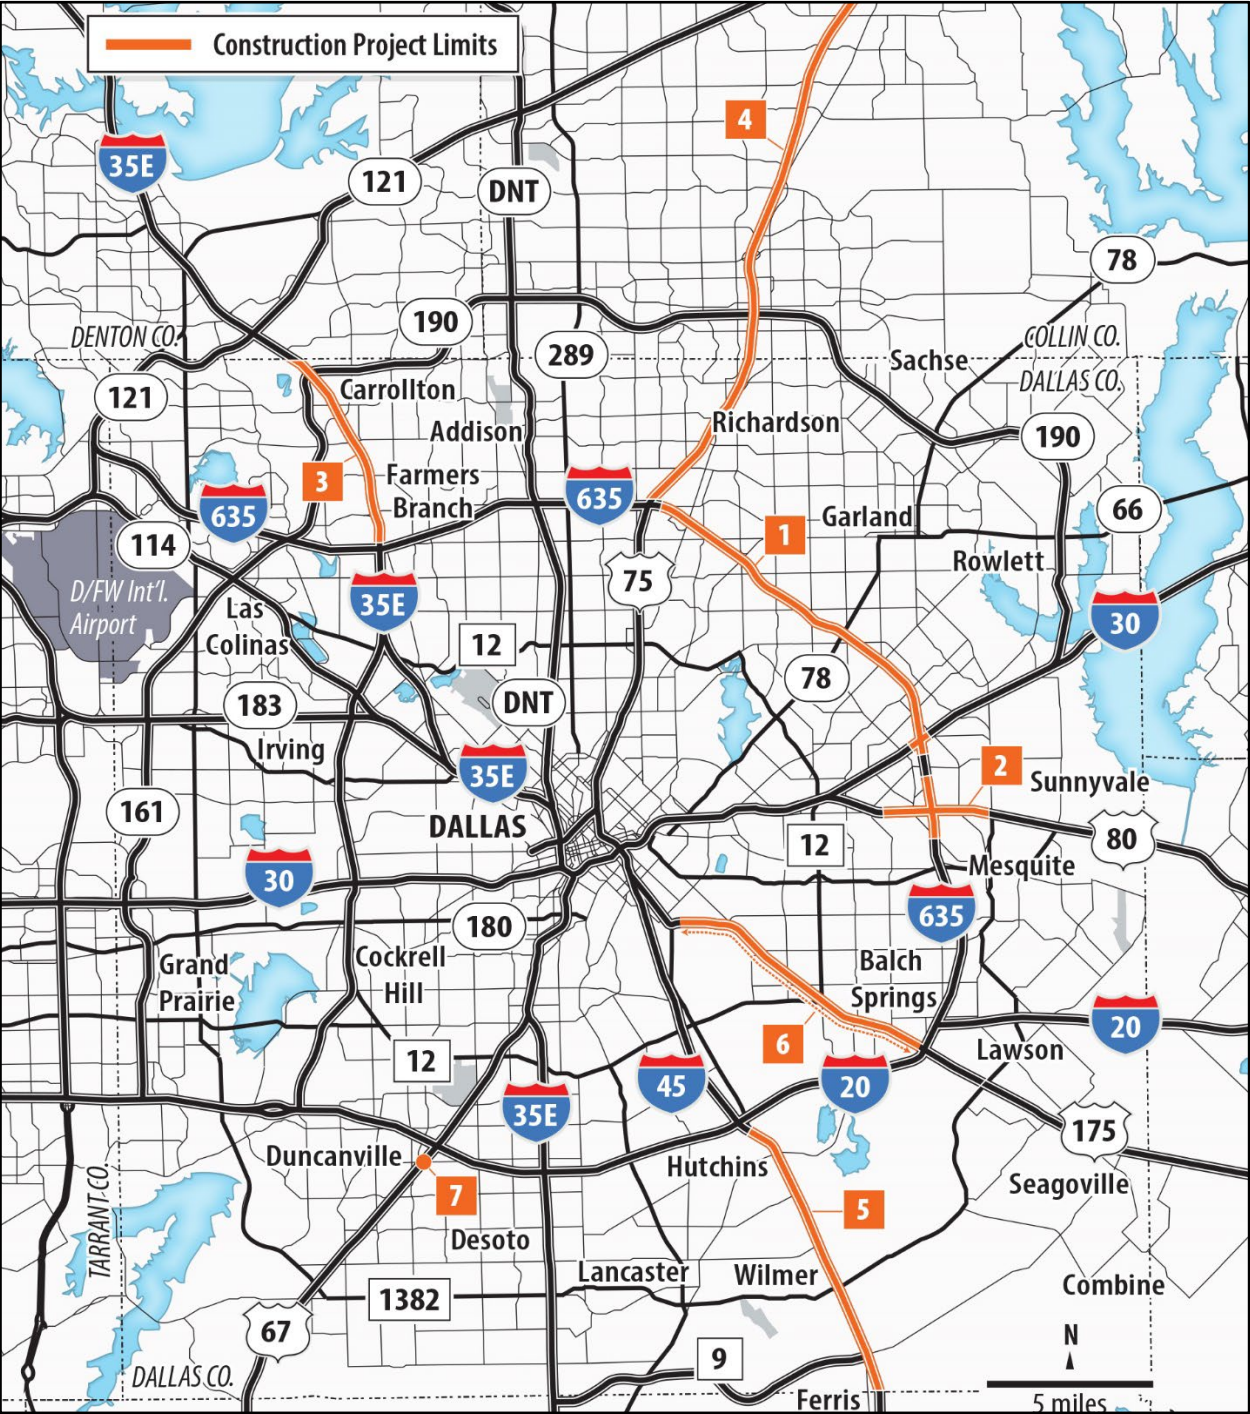

#	Control Section Job	Project Location	Description	Start /End	Contractor	Estimated Cost	Percent Complete
1	2374-01-137	I-635 (LBJ EAST) – US 75 to S of I-30; E and W on I-30 at I-635	Rebuild to 5 gen. purpose lanes and 2-3 FR lanes; intchg. improvements	Aug. 2019/ Late 2026	Pegasus Link Constructors	\$1.7 B	98%
2	2374-02-162	I-635 – At US 80 Interchange	Rebuild existing interchange	Feb. 2025/ Late 2029	Austin Bridge & Road	\$539.7 M	43%
3	0196-03-274	I-35E (Phase 2) – I-635 to Denton Co. line	Rebuild 2 reversible to 4 concurrent MLs; reconstruct 6 to 8 GPLs	Spring 2022/ Early 2027	Lone Star Constructors	\$709 M	90%
4	0047-06-158	US 75 – I-635 to SH 121 (McKinney)	Highway improvement (Collin Co. Area Office managing project)	Mar. 2024/ Dec. 2026	Webber, LLC	\$58 M	99%
5	0092-02-144	I-45 – Ellis County line to SH 310	Rehabilitate existing Roadway	Jan. 2026/ Summer 2027	Texas Materials Gp.	\$18.2 M	26%
6	0197-02-137	US 175 – Bexar St. to I-20	Rehabilitate existing roadway	Oct. 2024/ Fall 2027	Texas Materials Gp.	\$28.3 M	47%
7	0261-02-083	US 67 – At I-20 Interchange and at Wheatland Road	Bridge maintenance	Jan. 2026/ Fall 2026	Ragle Construction	\$4.9 M	90%

More Construction Projects on Next Page

Contact Information

Kenna Mitchell - Public Information Officer
Office: (430) 342-5012
Kenna.Mitchell@txdot.gov

September 2026
Source: Texas Department of Transportation
Dallas District Office:
4777 E. US 80, Mesquite, TX 75150





Estimated Total: \$4.3 Billion
