EXHIBIT 10

PRELIMINARY BASELINE SCHEDULES

TAB A: Segment 3A Facility Segment and Interchange Project Preliminary Baseline Schedule
TAB B: Segment 3C Facility Segment Preliminary Baseline Schedule

TAB A
Segment 3A Facility Segment and Interchange Project
Preliminary Baseline Schedule

[Attached]

NTE 3A / Interchange FBS-1 Approach / Narrative

Facility Baseline Schedule # 1 (FBS-1)

for the NTE 3A and Interchange Project

August 4, 2012

NTE 3A / Interchange FBS-1 Approach / Narrative

Table of Contents

1.0 Introduction .....
2.0 Schedule Organization & Structure .....
3.0 Design Approach .....
4.0 Utilities .....
5.0 Right of Way Acquisition
6.0 Activity ID's .....
7.0 Calendars .....
8.0 Segment Construction Summaries .....
  8.1 Interchange Construction (IH 35W and 820) .....
  8.2 Segment 3A Construction - IH 35W from Meacham Blvd. to IH 30 .....
9.0 Critical Path .....

NTE 3A / Interchange FBS-1 Approach / Narrative

1.0 Introduction

The NTE 3A / IC baseline project schedule attempts to mirror the intention and execution of the proposal schedule. It should be noted that at this early stage, with no construction drawings, and only the schematics available, this schedule is and will continue to be a work in progress ("Rollling Wave Planning). This baseline schedule will continue to be improved upon, as more information, details, drawings, design and traffic control plans are made available.

We believe this schedule is a sound, high-level presentation of how we can accomplish this project within the constraints identified in the contract and within the time frames allowed. As more information is made available, the schedule will be revised to present any changes in our approach and to break down the Segments into smaller more manageable portions of work.

There are two significant milestones for this project:

- Service Commencement Date = NTP2 + 60 months
- Final Acceptance Deadline = NTP2 + 63 months

It is anticipated that NTP1 and NTP2 will be received on, or about, October 1, 2012 and April 1 2013, respectively. This FBS-1 submittal is based upon these foregoing anticipated dates.

The construction schedule for the NTE 3A / IC project, is based upon the original proposal schedule as well as available design schematics. As design is developed for the various areas of the project, it becomes possible to detail more construction activities in the schedule.

The construction schedule is divided into two segments, "The IH 35W / 820 interchange" and "Segment 3A from Meacham Blvd to IH 30". Each Segment is organized by the phases and stages of construction. The Phases used in the schedule are not a timing tool, but are merely a way to break the work down into more manageable portions and therefore should not be viewed as a necessary sequence for accomplishment of a segment. That is, Phase 1 does not always need to be completed before Phase 2 can begin. This is also true with the Stages. Stage 1 does not always need to be completed before Stage 2 begins.

2.0 Schedule Organization & Structure

The Work Breakdown Structure (WBS) for the NTE 3A / IC Schedule (FBS-1) has been organized in the following order:

- Project Discipline (Design / Utilities / Right of Way / Construction etc)
- Segment 3A Construction / Interchange Construction
- Phases of Construction
- Stages of Construction
- Type of Roadworks (Frontage Road, General Purpose Lanes / Managed Lanes etc) and Location (Meacham to Dewey / Dewey to South of Trinity River, etc)
- Type of Construction work (Traffic Control, Drainage, Roadworks, Bridges, etc)

3.0 Design Approach

The Design is broken down into four major categories: 1) Preliminary Design 2) Roadway Design 3) Bridge Design and 4) Retaining Wall Design. The Design of the various elements are represented by a unique activity that lasts for approximately six months.

The preliminary design activities reflect the survey and geotech investigation works required to initiate the major design activities on the project. Currently, it is anticipated that the preliminary design work will last for approximately three months.

The roadway design is divided into different road categories (Frontage Roads (FR's), Ramps, General Purpose Lanes (GPL's) and Managed Lanes (ML's). Each design element is tied logically, within the schedule, to the start of construction work in that area.

At this point, it is anticipated that each bridge will be designed as a single package. However, some packages may end up being split into separate Foundation, Substructure and Superstructure packages, in order to expedite critical construction work, if need be. There are currently 57 bridge design packages in FBS-1. Bridges that cross the Trinity River (Bridges 224, 225, 226, 232, 242, and 243) will need reviews from TRWD and USACE and are reflected in the schedule with extended durations.

Also, the NTE 3A / IC project has 89 retaining walls (MSE & Soldier Pile Walls).

4.0 Utilities

There are numerous utilities, within the alignment, that may impact our work. We have included an activity for every utility-relocation identified to date that is in conflict with the schematics currently available. It is expected, however, that the number and extent of the conflicts will vary as design progresses. As soon as design reaches a sufficient level of completion, relationships between the utility relocations and the construction work can be made (or enhanced) with more certainty. Additionally, the durations for the relocation work are estimated. As the negotiations with Utility Owners are completed, those estimated durations will likely need to be adjusted to reflect the agreed upon periods/durations for the relocations to occur.

5.0 Right of Way Acquisition

A total of 129 Right of Way acquisition packages have been identified in the schedule, that need to be acquired as a part of the NTE 3A/IC Project. Out of the 129 packages, 38 parcels need relocation efforts. Based on the anticipated complexity of the acquisition process, several parcels have been identified as "COMPLEX" with anticipated overall duration of up to 24 months.

Out of the 26 Complex Parcels, 4 (Parcels 108, 109, 110 and 167) are on the longest path of the project as they affect the start of construction on the Northbound Frontage Road (NBFR) between South of Trinity River and IH 30.

6.0 Activity IDs

In general, the Activity IDs identify the activities' Segment, Direction of Roadway, Roadway type, location, discipline and Type of Work. Activity IDs have been modified to follow this convention.

Example: 3ANBFRMDEWRD121120

Where, 3A= Segment 3A, NB= Northbound, FR= Frontage Road, MD = Meacham to Dewey, EW = Earthwork, RD = Roadwork

This convention varies slightly with non construction activities (Design, Utilities, and Right of Way).

7.0 Calendars

- NTE 3A-IC - 7 Day Work Week
- NTE 3A-IC - Standard 5 Day Workweek
- NTE 3A-IC - Standard 5 Day Workweek w/ Basic Holidays
- NTE 3A-IC - Standard 5 Day Work Week with TxDOT Holidays
- NTE 3A-IC - Earthwork Weather Calendar. The NOAA averages for the Dallas / Fort Worth area were used to remove work days based on the average number of weather days each month.
- NTE 3A-IC - Structure Weather Calendar. This calendar is based on the Earthwork calendar but with approximately 1/3 less days and is tied to concrete work.

(Weekend or Other Special Calendars will be developed when the need arises.)

8.0 Construction Summaries

8.1 Interchange Construction (IH 35W and 820)

The Interchange construction has been divided into four phases. Each phase in the interchange construction has to be finished before the next phase is started.

Phase 1:

- Construction of Drainage and Roadworks on Northbound and Southbound Frontage Roads including Bridges 33 and 34 over Little Fossil Creek.
- Construction of Bridge 4 – 35W Managed Lanes over 820
- Construction of Northbound and Southbound General Purpose Lane Bridges (Northbound Bridge1 and Southbound Bridge 7)
- Construction of Ramps / Direct Connectors in all four direction including bridges

Phase 2:

- Construction of General Purpose and Managed Lanes Bridge 32 over Little Fossil Creek
- Construction of Eastbound and Westbound Managed Lane connections on 820.
- Construction of ramps and Direct Connectors including bridges 10, 12, 16, 17, 18 and 21

Phase 3:

- Construction of Northbound and Southbound General Purpose Lane Roadworks including Traffic Detours, Drainage, Earthwork, Asphalt Pavement Signs, Striping and Lighting.
- Construction of Direct Connector Ramps (Bridges 13, 15, 16 and 17)

Phase 4:

- Construction of Eastbound and Westbound Managed Lanes, General Purpose Lanes and Ramps including Bridges 10 and 17.
- Placing Topsoil, Seeding and Sodding Landscape Areas in all four directions.

8.2 Segment 3A Construction - IH 35W from Meacham Blvd. to IH 30

Segment 3A has been divided into four phases with each phase consisting of several stages of construction as follows:

Phase 1 Stage 1:

- Construction of Drainage, Roadwork and Retaining Wall at Yucca Ave / Northside Drive Cross Street.
- Construction of Bridge 237 (Cross Street Spur 280 over 35W)
- Construction of Temporary Detours and Retaining Walls at SH 183 / NE 28th Street
- Construction of Northbound and Southbound Frontage Roads including MSE Retaining walls S14, S16A, S20 and S32 and Soldier Pile Walls S12 and N13.
- Construction of Managed Lanes between Sta 795 and Sta 826 including Bridge 218 over the Rail Road tracks
- Construction of Southbound General Purpose Lanes including Bridges 205 and 217.
- Construction of Southbound Ramp Bridge 202 between Meacham and Dewey.

Phase 1 Stage 2:

- Construction of Cross Street Bridge 214 at SH 183 / NE 28th Street.
- Continue construction of Northbound and Southbound Frontage Roads including Retaining Walls N13, S14 and N32.
- Construction of Northbound ramp between Meacham and Dewey.

NTE 3A / Interchange FBS-1 Approach / Narrative

Phase 2 Stage 1:

- Construction of Retaining Wall 10A at Meacham Blvd.
- Construction of Southbound General Purpose Lanes including Bridges 208, 226, 230, 234 and 236
- Construction of Southbound Ramps from Meacham Blvd to IH 30.

Phase 2 Stage 2:

- Construction of Retaining Walls 21A and 21B at Cross Street SH 183
- Construction of Southbound General Purpose Lane Bridge 221, over Northside Dr.

Phase 2 Stage 3:

- Construction of temporary detours on Northbound Frontage Road from Dewey to South of Trinity River.
- Construction of Managed Lanes between Dewey and South of Trinity River (sta 775 to sta 795)
- Construction of Southbound General Purpose Lane Bridges 234 (Over 4th Street), 236 (Over RailRoad Tracks) and 240 9Over Meacham Blvd).

Phase 3 Stage 1:

- Construction of Retaining Walls 02A, 07A, 08A, 08B and 10A at Meacham Blvd.
- Construction of Northbound General Purpose Lane Bridges 207, 210 and 241.
- Construction of SH 183 entrance ramp to IH 35W Managed Lanes, including Bridge 212.

Phase 3 Stage 2:

- Construction of Northbound General Purpose Lane Bridges 219 and 224 between Dewey and South of Trinity River.
- Construction of Northbound General Purpose Lane Bridges 233 and 235 between South of Trinity River and IH 30.
- Construction of Northbound 35W exit ramp from Managed Lanes to General Purpose Lanes including bridge 203.
- Construction of Northbound entrance ramp from Spur 280 to 35W Managed Lanes including Bridge 231.
- Construction of Southbound 35W exit ramp to Spur 280 including Bridge 232.

Phase 3 Stage 3:

- Construction of Northbound Frontage Road between Dewey and South of Trinity River.
- Construction of Northbound General Purpose Lane Bridge 223, over Yucca Ave.
- Placing Topsoil, Seeding and Sodding on Northbound and Southbound Landscape areas for all of Segment 3A (Between Meacham Blvd and IH 30).

Phase 4 Stage 1

- Finish construction of cross raods at Meacham Blvd, E. 4th Street and Cypress Street.

- Finish Construction of Northbound & Southbound Managed Lanes including Bridges 225, 232, 242 and 243, over Trinity River.
- Finish Construction of Northbound and Southbound General Purpose Lanes.
- Finish construction of Southbound 35W, Managed Lane, exit ramps to SH 183 and Spur 280.

9.0 Critical Path

The project's Longest Path (Critical Path) starts off with the acquisition of several "complex" Right of Way packages/parcels, which then drives the construction of the Northbound Frontage Road between South of Trinity River and IH 30 (Seg 3A: Phase 1/ Stage 1). These Phase 1, Stage 1, Frontage Road activities then drive the Phase 2, Stage 2, Southbound General Purpose Lanes roadway in the same area.

The above work then drives the start of Segment 3A's Phase 2, Stage 3 work, which starts with Southbound General Purpose lanes, followed by the construction of General Purpose Lane Bridge 236 over the railroad tracks. The Longest Path then moves into Seg 3A's, Phase 3, Stage 1 of the Northbound General Purpose Lanes, including Bridge 207, followed by the finishing of Managed Lanes in Stage 1 of Phase 4. Thereafter, the Longest Path concludes with Substantial Completion and Service Commencement milestones, followed by Final Acceptance Preparations (Punchlist) and Final Acceptance.

Activity ID	Activity Name	Orig Dur	Start	Finish
NTE - Segment 3A & Interchange Project - FBS # 1 - Rev 8-6-12				
3ANBFRSIMSRO1081000	Parcel #108 : Initiate ROW Acquisition	0	01-Aug-12	
3ANBFRSIRO1081010	Parcel #108 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12
3ANBFRSIMSRO1091000	Parcel #109 : Initiate ROW Acquisition	0	01-Aug-12	
3ANBFRSIRO1091010	Parcel #109 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12
3ANBFRSIMSRO1101000	Parcel #110 : Initiate ROW Acquisition	0	01-Aug-12	
3ANBFRSIRO1101010	Parcel #110 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12
3ANBFRSIMSRO1581000	Parcel #158 : Initiate ROW Acquisition	0	01-Aug-12	
3ANBFRSIRO1581010	Parcel #158 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12
3ANBFRSIMSRO1591000	Parcel #159 : Initiate ROW Acquisition	0	01-Aug-12	
3ANBFRSIRO1591010	Parcel #159 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12
3ANBFRSIMSRO1671000	Parcel #167 : Initiate ROW Acquisition	0	01-Aug-12	
3ANBFRSIRO1671010	Parcel #167 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12
NTE-ROWSTART	Start Right of Way Process	0	01-Aug-12*	
3ANBFRSIRO1581030	Parcel #158 : Perform PHI ESA	30	25-Oct-12	06-Dec-12
3ANBFRSIRO1591030	Parcel #159 : Perform PHI ESA	30	25-Oct-12	06-Dec-12
3ANBFRSIRO1081020	Parcel #108 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13
3ANBFRSIRO1091020	Parcel #109 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13
3ANBFRSIRO1101020	Parcel #110 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13
3ANBFRSIRO1581050	Parcel #158 : Prepare Title Work	30	07-Dec-12	21-Jan-13
3ANBFRSIRO1591050	Parcel #159 : Prepare Title Work	30	07-Dec-12	21-Jan-13
3ANBFRSIRO1671030	Parcel #167 : Perform PHI ESA	30	07-Dec-12	21-Jan-13
3ANBFRSIRO1081050	Parcel #108 : Prepare Title Work	30	08-Jan-13	18-Feb-13
3ANBFRSIRO1091050	Parcel #109 : Prepare Title Work	30	08-Jan-13	18-Feb-13
3ANBFRSIRO1101050	Parcel #110 : Prepare Title Work	30	08-Jan-13	18-Feb-13
3ANBFRSIRO1581060	Parcel #158 : Perform Appraisals	20	22-Jan-13	18-Feb-13
3ANBFRSIRO1591060	Parcel #159 : Perform Appraisals	20	22-Jan-13	18-Feb-13
3ANBFRSIRO1671050	Parcel #167 : Prepare Title Work	30	22-Jan-13	04-Mar-13
3ANBFRSIRO1081060	Parcel #108 : Perform Appraisals	20	19-Feb-13	18-Mar-13
3ANBFRSIRO1091060	Parcel #109 : Perform Appraisals	20	19-Feb-13	18-Mar-13
3ANBFRSIRO1101060	Parcel #110 : Perform Appraisals	20	19-Feb-13	18-Mar-13
3ANBFRSIRO1581070	Parcel #158 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13
3ANBFRSIRO1591070	Parcel #159 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13
3ANBFRSIRO1671060	Parcel #167 : Perform Appraisals	20	05-Mar-13	01-Apr-13
3ANBFRSIRO1081070	Parcel #108 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13
3ANBFRSIRO1091070	Parcel #109 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13
3ANBFRSIRO1101070	Parcel #110 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13
3ANBFRSIRO1581080	Parcel #158 : TxDOT Reviews Acquisition Package	10	19-Mar-13	01-Apr-13
3ANBFRSIRO1591080	Parcel #159 : TxDOT Reviews Acquisition Package	10	19-Mar-13	01-Apr-13
NTE-ROW-BATCH5-1	Finish ROW Batch 5 Review by TxDOT	0		01-Apr-13
3ASBGPDTRO891080	Parcel #89 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBGPDTRO901080	Parcel #90 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBGPDTRO951080	Parcel #95 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBGPDTRO961080	Parcel #96 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRSIRO1601080	Parcel #160 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRSIRO1621080	Parcel #162 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRSIRO1661080	Parcel #166 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRSIRO1671070	Parcel #167 : Perform Review Appraisal	30	02-Apr-13	13-May-13
3ANBFRMDRO171080	Parcel #17 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO181080	Parcel #18 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO191080	Parcel #19 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO201080	Parcel #20 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBGPMDRO281080	Parcel #28 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO351080	Parcel #35 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO361080	Parcel #36 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO371080	Parcel #37 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO381080	Parcel #38 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO401080	Parcel #40 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO461080	Parcel #46 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO471080	Parcel #47 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO481080	Parcel #48 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ANBFRMDRO491080	Parcel #49 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO501080	Parcel #50 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO531080	Parcel #53 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRDTRO661080	Parcel #66 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO011080	Parcel #1 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO021080	Parcel #2 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO071080	Parcel #7 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO131080	Parcel #13 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO141080	Parcel #14 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
3ASBFRMDRO161080	Parcel #16 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13
NTE-ROW-BATCH6	Start ROW Batch 6 Review by TxDOT	0	02-Apr-13	
NTE-ROW-BATCH6-1	Finish ROW Batch 6 Review by TxDOT	0		15-Apr-13
3ANBFRSIRO1081080	Parcel #108 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13
3ANBFRSIRO1091080	Parcel #109 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13
3ANBFRSIRO1101080	Parcel #110 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13
NTE-ROW-BATCH7	Start ROW Batch 7 Review by TxDOT	0	16-Apr-13	
3ANBFRSIRO1081090	Parcel #108 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13
3ANBFRSIRO1091090	Parcel #109 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13
3ANBFRSIRO1101090	Parcel #110 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13

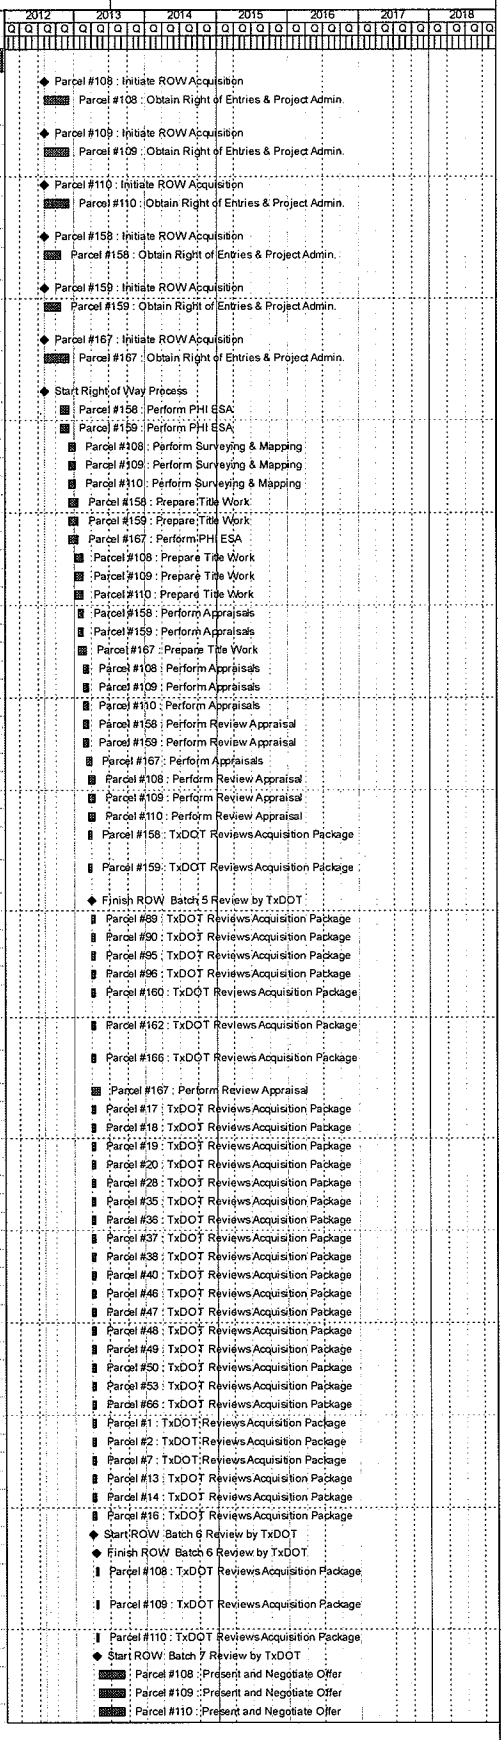

Actual Work ◆ ◆ Milestone
Remaining Work
Critical Remaining Work

NTE 3A / Interchange Project
Longest Path

Activity ID	Activity Name	Orig Dur	Start	Finish
3ANBFRSIRO1671080	Parcel #167 : TxDOT Reviews Acquisition Package	10	14-May-13	28-May-13
3ANBFRSIRO1671090	Parcel #167 : Present and Negotiate Offer	90	29-May-13	03-Oct-13
3ANBFRSIRO1081110	Parcel #108 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14
3ANBFRSIRO1091110	Parcel #109 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14
3ANBFRSIRO1101110	Parcel #110 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14
3ANBFRSIRO1671110	Parcel #167 : Condemnation Process (if required)	225	04-Oct-13	21-Aug-14
3ANBFRSIRO1081120	Parcel #108 : Prepare for Relocation	30	16-Apr-14	28-May-14
3ANBFRSIRO1091120	Parcel #109 : Prepare for Relocation	30	16-Apr-14	28-May-14
3ANBFRSIRO1101120	Parcel #110 : Prepare for Relocation	30	16-Apr-14	28-May-14
3ANBFRSIRO1081130	Parcel #108 : Execute Relocation	20	29-May-14	25-Jun-14
3ANBFRSIRO1091130	Parcel #109 : Execute Relocation	20	29-May-14	25-Jun-14
3ANBFRSIRO1101130	Parcel #110 : Execute Relocation	20	29-May-14	25-Jun-14
3ANBFRSIRO1081140	Parcel #108 : Property mgmt preparation	20	26-Jun-14	24-Jul-14
3ANBFRSIRO1091140	Parcel #109 : Property mgmt preparation	20	26-Jun-14	24-Jul-14
3ANBFRSIRO1101140	Parcel #110 : Property mgmt preparation	20	26-Jun-14	24-Jul-14
3ANBFRSIRO1081150	Parcel #108 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14
3ANBFRSIRO1091150	Parcel #109 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14
3ANBFRSIRO1101150	Parcel #110 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14
3ANBFRSIMSRO1081160	Parcel #108 : Cleared for Construction	0		21-Aug-14
3ANBFRSIMSRO1091160	Parcel #109 : Cleared for Construction	0		21-Aug-14
3ANBFRSIMSRO1101160	Parcel #110 : Cleared for Construction	0		21-Aug-14
3ANBFRSIMSRO1671120	Parcel #167 : Cleared for Construction	0		21-Aug-14
3ANBFRSITCTC111010	NBFR - Trn to I-30 Ph1Stg1 Place temp barricades, signs & striping	5	22-Aug-14	28-Aug-14
3ANBFRSITCTC111020	NBFR - Trn to I-30 Ph1Stg1 Place Temp Erosion Control	3	22-Aug-14	26-Aug-14
3ANBFRSIMSMS111000	NBFR - Trn to I-30 Ph1Stg1 Start Milestone	0	22-Aug-14	
3ANBFRSIDTTM111030	NBFR - Trn to I-30 Ph1Stg1 Construct Detours	2	27-Aug-14	28-Aug-14
3ANBFRSITCTC111040	NBFR - Trn to I-30 Ph1Stg1 Place Temp Conc Barrier	2	27-Aug-14	28-Aug-14
3ANBFRSIRMRD111090	NBFR - Trn to I-30 Ph1Stg1 Prep ROW	15	29-Aug-14	24-Sep-14
3ANBFRSIRMRD111100	NBFR - Trn to I-30 Ph1Stg1 Remove Pavement	3	22-Sep-14	24-Sep-14
3ANBFRSIEWRD111110	NBFR - Trn to I-30 Ph1Stg1 Excavate Cut Areas	13	26-Sep-14	16-Oct-14
3ANBFRSIDRDR111060	NBFR - Trn to I-30 Ph1Stg1 Install Conc Box Culvert	3	03-Oct-14	07-Oct-14
3ANBFRSIDRDR111070	NBFR - Trn to I-30 Ph1Stg1 Install RCP	60	03-Oct-14	23-Jan-15
3ANBFRSIDRDR111080	NBFR - Trn to I-30 Ph1Stg1 Drainage Misc	5	26-Jan-15	03-Feb-15
3ANBFRSISGRD111140	NBFR - Trn to I-30 Ph1Stg1 Lime Treat Subgrade	33	04-Feb-15	03-Apr-15
3ANBFRSISGRD111150	NBFR - Trn to I-30 Ph1Stg1 Place 10" Flexible Base	9	07-Apr-15	21-Apr-15
3ANBFRSISARD111160	NBFR - Trn to I-30 Ph1Stg1 Place 4" HMA Bond Breaker	2	23-Apr-15	24-Apr-15
3ANBFRSISARD111170	NBFR - Trn to I-30 Ph1Stg1 Place 7" / 10.5" HMA Base	4	27-Apr-15	05-May-15
3ANBFRSIAPRD111180	NBFR - Trn to I-30 Ph1Stg1 Place 1.5" SMA Surface	2	07-May-15	11-May-15
3ANBFRSICPRD111190	NBFR - Trn to I-30 Ph1Stg1 Place Concrete Pavement	4	13-May-15	19-May-15
3ANBFRSICGRD111200	NBFR - Trn to I-30 Ph1Stg1 Place Curb and Gutter	17	21-May-15	22-Jun-15
3ANBFRSICGRD111210	NBFR - Trn to I-30 Ph1Stg1 Place Sidewalks, Driveways & Ramps	6	23-Jun-15	01-Jul-15
3ANBFRSISFRD111220	NBFR - Trn to I-30 Ph1Stg1 Place Permanent Rail & Barriers	4	02-Jul-15	08-Jul-15
3AMSMS111000	Segment 3A - Phase 1 Stage 1 Finish	0		08-Jul-15
3ANBFRSIMSMS111050	NBFR - Trn to I-30 Ph1Stg1 Finish Milestone	0		08-Jul-15
3ASBGPSIMSMS221000	SBGP - Trn to I-30 Ph2Stg2 Start Milestone	0	09-Jul-15	
3ASBGPSITCTC221010	SBGP - Trn to I-30 Ph2Stg2 Place temp barricades, signs & striping	4	10-Jul-15	16-Jul-15
3ASBGPSIDTTM221030	SBGP - Trn to I-30 Ph2Stg2 Construct Detours	5	17-Jul-15	24-Jul-15
3ASBGPSITCTC221040	SBGP - Trn to I-30 Ph2Stg2 Place Temp Conc Barrier	3	27-Jul-15	29-Jul-15
3ASBGPSIRMRD221000	SBGP - Trn to I-30 Ph2Stg2 Prep ROW	3	30-Jul-15	03-Aug-15
3ASBGPSIRMRD221090	SBGP - Trn to I-30 Ph2Stg2 Remove Pavement	2	31-Jul-15	03-Aug-15
3ASBGPSIEWRD221100	SBGP - Trn to I-30 Ph2Stg2 Excavate Cut Areas	4	05-Aug-15	10-Aug-15
3ASBGPSIEWRD221110	SBGP - Trn to I-30 Ph2Stg2 Place Embankment	5	06-Aug-15	13-Aug-15
3ASBGPSIEWRD221120	SBGP - Trn to I-30 Ph2Stg2 Place Topsoil	5	06-Aug-15	13-Aug-15
3ASBGPSISGRD221130	SBGP - Trn to I-30 Ph2Stg2 Lime Treat Subgrade	9	14-Aug-15	27-Aug-15
3ASBGPSISGRD221140	SBGP - Trn to I-30 Ph2Stg2 Place 10" Flexible Base	3	28-Aug-15	01-Sep-15
3ASBGPSISARD221150	SBGP - Trn to I-30 Ph2Stg2 Place 4" HMA Bond Breaker	2	02-Sep-15	04-Sep-15
3ASBGPSISARD221160	SBGP - Trn to I-30 Ph2Stg2 Place 7" / 10.5" HMA Base	2	08-Sep-15	10-Sep-15
3ASBGPSIAPRD221170	SBGP - Trn to I-30 Ph2Stg2 Place 1.5" SMA Surface	2	11-Sep-15	14-Sep-15
3ASBGPSICPRD221180	SBGP - Trn to I-30 Ph2Stg2 Place Concrete Pavement	3	16-Sep-15	22-Sep-15
3ASBGPSICGRD221190	SBGP - Trn to I-30 Ph2Stg2 Place Curb and Gutter	4	23-Sep-15	28-Sep-15
3ASBGPSICGRD221200	SBGP - Trn to I-30 Ph2Stg2 Place Sidewalks, Driveways & Ramps	4	29-Sep-15	07-Oct-15
3ASBGPSISFRD221210	SBGP - Trn to I-30 Ph2Stg2 Place Permanent Rail & Barriers	2	08-Oct-15	09-Oct-15
3ASBGPSIMSMS221050	SBGP - Trn to I-30 Ph2Stg2 Finish Milestone	0		09-Oct-15
3ASBGPSIMSMS231000	SBGP - Trn to I-30 Ph2Stg3 Start Milestone	0	10-Oct-15	
3ASBGPSITCTC231010	SBGP - Trn to I-30 Ph2Stg3 Place temp barricades, signs & striping	6	12-Oct-15	20-Oct-15
3ASBGPSIDTTM231030	SBGP - Trn to I-30 Ph2Stg3 Construct Detours	4	21-Oct-15	28-Oct-15
3ASBGPSITCTC231040	SBGP - Trn to I-30 Ph2Stg3 Place Temp Conc Barrier	2	29-Oct-15	02-Nov-15
3ASBGPSIFO236231000	B236 Ph2Stg3 Bridge Removal	5	03-Nov-15	10-Nov-15
3ASBGPSIFO236231010	B236 Ph2Stg3 Excavation / Backfill	2	12-Nov-15	13-Nov-15
3ASBGPSIFO236231020	B236 Ph2Stg3 Drill Shafts for Bridge	6	16-Nov-15	24-Nov-15
3ASBGPSIFO236231030	B236 Ph2Stg3 Tie rebar for Footing	5	25-Nov-15	04-Dec-15
3ASBGPSIFO236231040	B236 Ph2Stg3 Form Footing	5	30-Nov-15	07-Dec-15
3ASBGPSIFO236231050	B236 Ph2Stg3 Pour Footing	4	01-Dec-15	07-Dec-15
3ASBGPSIFO236231090	B236 Ph2Stg3 Cure Footing	7	08-Dec-15	14-Dec-15
3ASBGPSISB236231070	B236 Ph2Stg3 Tie Rebar for Columns	7	16-Dec-15	24-Dec-15
3ASBGPSISB236231090	B236 Ph2Stg3 Form Columns	7	17-Dec-15	28-Dec-15
3ASBGPSISB236231110	B236 Ph2Stg3 Pour Columns	7	18-Dec-15	29-Dec-15
3ASBGPSISB236231120	B236 Ph2Stg3 Tie Rebar for Caps	4	30-Dec-15	05-Jan-16

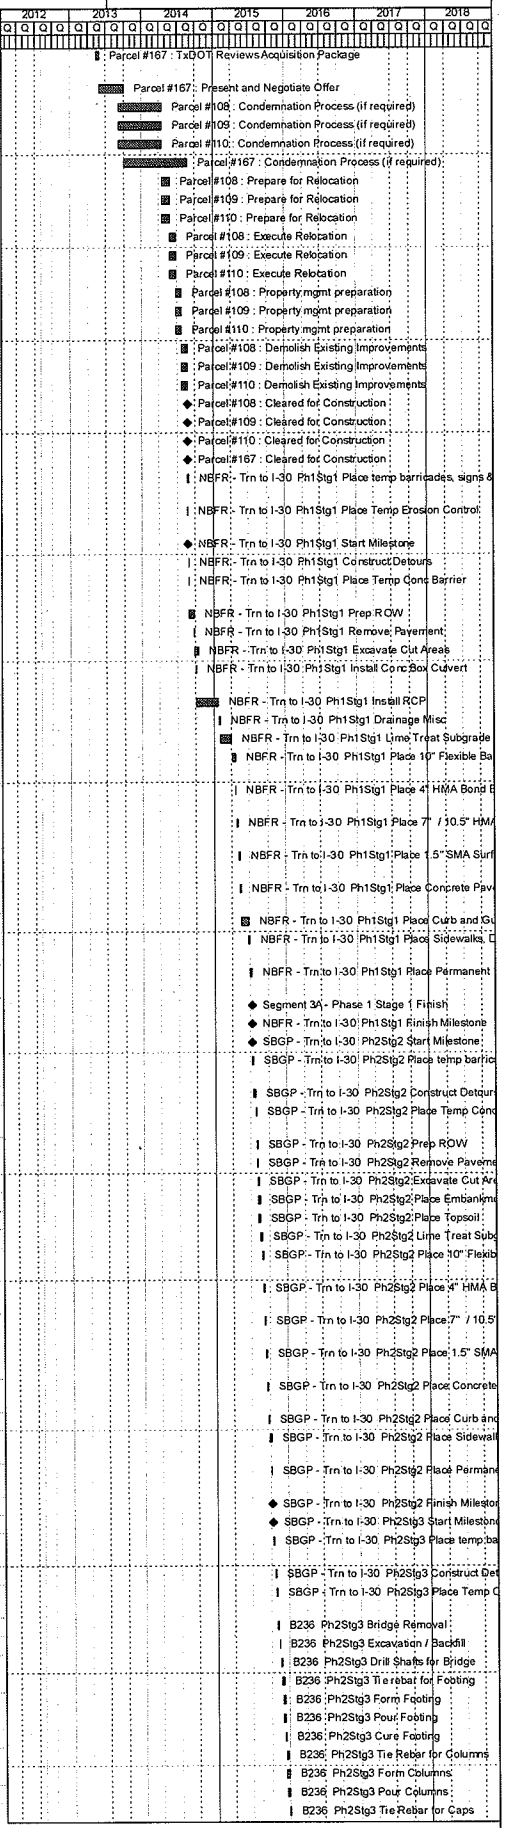

Activity ID	Activity Name	Orig Dur	Start	Finish
3ASBGPSISB236231130	B236 Ph2Stg3 Form Caps	4	31-Dec-15	06-Jan-16
3ASBGPSISB236231140	B236 Ph2Stg3 Pour Caps	4	04-Jan-16	08-Jan-16
3ASBGPSISS236231160	B236 Ph2Stg3 Install Beams	14	11-Jan-16	01-Feb-16
3ASBGPSISS236231180	B236 Ph2Stg3 Post Tensioning of Beams	14	14-Jan-16	03-Feb-16
3ASBGPSISS236231190	B236 Ph2Stg3 Deck Precast Panes	14	18-Jan-16	05-Feb-16
3ASBGPSISS236231200	B236 Ph2Stg3 Deck PMD	14	21-Jan-16	10-Feb-16
3ASBGPSISS236231210	B236 Ph2Stg3 Deck Overhangs	14	25-Jan-16	12-Feb-16
3ASBGPSISS236231220	B236 Ph2Stg3 Deck Rebar	14	27-Jan-16	16-Feb-16
3ASBGPSISS236231230	B236 Ph2Stg3 Pour Deck	14	29-Jan-16	19-Feb-16
3ASBGPSISS236231250	B236 Ph2Stg3 Deck Surface Treatment	2	22-Feb-16	23-Feb-16
3ASBGPSISS236231270	B236 Ph2Stg3 Bridge Deck Drainage	5	24-Feb-16	03-Mar-16
3ASBGPSISS236231280	B236 Ph2Stg3 Bridge Railings	2	04-Mar-16	07-Mar-16
3AMSMS21000	Segment 3A - Phase 2 Finish	0		07-Mar-16
3AMSMS231000	Segment 3A - Phase 2 Stage 3 Finish	0		07-Mar-16
3ASBGPSIMSMS231050	SBGP - Trn to I-30 Ph2Stg3 Finish Milestone	0		07-Mar-16
3ANBGPMDTCTC311010	NBGP - Mcm to Dwy Ph3Stg1 Place temp barricades, signs & striping	5	08-Mar-16	15-Mar-16
3ANBGPMDTCTC311020	NBGP - Mcm to Dwy Ph3Stg1 Place Temp Erosion Control	5	08-Mar-16	15-Mar-16
3ANBGPMDDTTM311030	NBGP - Mcm to Dwy Ph3Stg1 Construct Detours	5	08-Mar-16	15-Mar-16
3ANBGPMDTCTC311040	NBGP - Mcm to Dwy Ph3Stg1 Place Temp Conc Barrier	5	08-Mar-16	15-Mar-16
3ANBGPMDMSMS311000	NBGP - Mcm to Dwy Ph3Stg1 Start Milestone	0	08-Mar-16	
3ANBGPMDFO207311000	B207 Ph3Stg1 Bridge Removal	13	16-Mar-16	11-Apr-16
3ANBGPMDFO207311010	B207 Ph3Stg1 Excavation / Backfill	3	12-Apr-16	15-Apr-16
3ANBGPMDFO207311020	B207 Ph3Stg1 Drill Shafts for Bridge	19	18-Apr-16	19-May-16
3ANBGPMDFO207311030	B207 Ph3Stg1 Tie rebar for Footing	4	20-May-16	25-May-16
3ANBGPMDFO207311040	B207 Ph3Stg1 Form Footing	4	23-May-16	27-May-16
3ANBGPMDFO207311050	B207 Ph3Stg1 Pour Footing	5	24-May-16	01-Jun-16
3ANBGPMDFO241311080	B207 Ph3Stg1 Cure Footing	7	02-Jun-16	08-Jun-16
3ANBGPMDSB207311070	B207 Ph3Stg1 Tie Rebar for Columns	37	09-Jun-16	05-Aug-16
3ANBGPMDSB207311090	B207 Ph3Stg1 Form Columns	37	10-Jun-16	08-Aug-16
3ANBGPMDSB207311110	B207 Ph3Stg1 Pour Columns	37	13-Jun-16	09-Aug-16
3ANBGPMDSB207311120	B207 Ph3Stg1 Tie Rebar for Caps	26	18-Jul-16	25-Aug-16
3ANBGPMDSB207311130	B207 Ph3Stg1 Form Caps	26	20-Jul-16	26-Aug-16
3ANBGPMDSB207311140	B207 Ph3Stg1 Pour Caps	26	21-Jul-16	29-Aug-16
3ANBGPMDSS207311150	B207 Ph3Stg1 Install Beams	79	04-Aug-16	14-Dec-16
3ANBGPMDSS207311160	B207 Ph3Stg1 Elastomeric Bridge Bearings	79	04-Aug-16	14-Dec-16
3ANBGPMDSS207311240	B207 Ph3Stg1 Structural Steel - HS (Bent Cap / Plate Girders)	24	15-Dec-16	25-Jan-17
3ANBGPMDSS207311280	B207 Ph3Stg1 Bridge Railings	2	26-Jan-17	27-Jan-17
3AMSMS31000	Segment 3A - Phase 3 Finish	0		27-Jan-17
3AMSMS311000	Segment 3A - Phase 3 Stage 1 Finish	0		27-Jan-17
3ANBGPMDMSMS311050	NBGP - Mcm to Dwy Ph3Stg1 Finish Milestone	0		27-Jan-17
3ANSMLDTMSMS411020	NSML - Dwy to S of Trn Ph4Stg1 Start Milestone	0	28-Jan-17	
3ANSMLDTTCTC411000	NSML - Dwy to S of Trn Ph4Stg1 Place temp barricades, signs & striping	5	30-Jan-17	07-Feb-17
3ANSMLDTDTTM411030	NSML - Dwy to S of Trn Ph4Stg1 Construct Detours	3	08-Feb-17	10-Feb-17
3ANSMLDTTCTC411040	NSML - Dwy to S of Trn Ph4Stg1 Place Temp Conc Barrier	3	08-Feb-17	10-Feb-17
3ANSMLDTRMRD411090	NSML - Dwy to S of Trn Ph4Stg1 Prep ROW	3	13-Feb-17	17-Feb-17
3ANSMLDTRMRD411100	NSML - Dwy to S of Trn Ph4Stg1 Remove Pavement	7	13-Feb-17	24-Feb-17
3ANSMLDTEWRD411110	NSML - Dwy to S of Trn Ph4Stg1 Excavate Cut Areas	98	27-Feb-17	25-Aug-17
3ANSMLDTEWRD411120	NSML - Dwy to S of Trn Ph4Stg1 Place Embankment	46	09-Jun-17	25-Aug-17
3ANSMLDTEWRD411130	NSML - Dwy to S of Trn Ph4Stg1 Place Topsoil	46	09-Jun-17	25-Aug-17
3ANSMLDTSGRD411140	NSML - Dwy to S of Trn Ph4Stg1 Lime Treat Subgrade	45	29-Jun-17	12-Sep-17
3ANSMLDTITRD411330	NSML - Dwy to S of Trn Ph4Stg1 Install ITS/Toll Duct Bank	12	14-Sep-17	02-Oct-17
3ANSMLDTITRD411340	NSML - Dwy to S of Trn Ph4Stg1 Install ITS/Gantry Foundations	4	27-Sep-17	02-Oct-17
3ANSMLDTITRD411350	NSML - Dwy to S of Trn Ph4Stg1 Install Power Supply for ITS/Tolling	7	27-Sep-17	06-Oct-17
NTE-ITSFINISH	Completion of ITS (Civil) Work	0		06-Oct-17
3A-CINT-NCS1	Pulling Fiber-Optic Backbone - Segment 3A	60	09-Oct-17	29-Dec-17
3A-CINT-ITS1	Microwave Vehicle Detector (MVD) - Segment 3A	60	09-Oct-17	29-Dec-17
3A-CINT-TCS1	Gantry Structure Installation - Segment 3A	40	09-Oct-17	01-Dec-17
3A-CINT-ITS6	Weather Station - Segment 3A	5	09-Oct-17	13-Oct-17
3A-CINT-ITS7	ITS Equipment Commissioning Testing - Segment 3A	60	16-Oct-17	05-Jan-18
3A-CINT-TCS2	TCS Field Equipment installation - Segment 3A	45	04-Dec-17	02-Feb-18
3A-CINT-ITS8	ITS System Integration Testing - Segment 3A	40	08-Jan-18	02-Mar-18
3A-CINT-TCS4	TCS Equipment Commissioning Test - Segment 3A	10	05-Feb-18	16-Feb-18
3A-CINT-TCS5	TCS Site Integration Testing - Segment 3A	10	19-Feb-18	02-Mar-18
3A-CINT-ITS9	ITS Operational Test - Segment 3A	10	05-Mar-18	16-Mar-18
3A-CINT-TCS6	TCS Operational Test - Segment 3A	10	05-Mar-18	16-Mar-18
3A-CINT-ITS10	ITS/Central end-to-end testing - Segment 3A	5	19-Mar-18	23-Mar-18
3A-CINT-TCS7	TCS/Central end-to-end Testing - Segment 3A	5	19-Mar-18	23-Mar-18
NTE-SCOMP-1000	Substantial Completion Segment 3A	0		23-Mar-18
NTE-SCOMP-1010	TxDOT Issue Substantial Completion Certificate	5	26-Mar-18	30-Mar-18
NTE-SCOMP-1020	Open Traffic / Service Commencement	0		30-Mar-18*
NTE-FCOMP-1000	Completion of Punchlist Works	70	31-Mar-18	08-Jun-18
NTE-FCOMP-1010	Review and Approval of Punchlist Works by TxDOT / IE	15	09-Jun-18	23-Jun-18
NTE-FCOMP-1015	TxDOT Issue Final Completion Certificate	5	25-Jun-18	29-Jun-18
NTE-FCOMP-1020	Project Final Acceptance	0		29-Jun-18

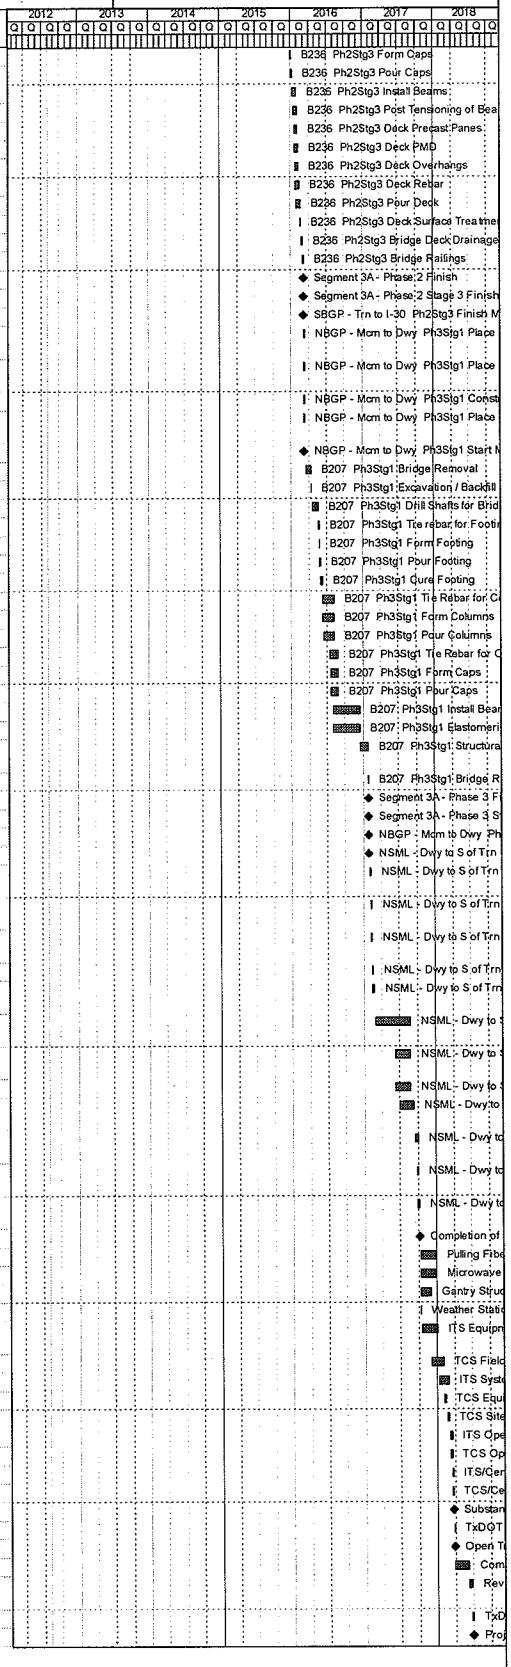

SUMMARY SCHEDULE | NTE - Segment 3A Interchange Project - FBS # 1 |

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Total		1543	01-Aug-12	29-Jun-18	0	$1,037,614,340
NTE - Segment 3A & Interchange Project - FBS # 1		1543	01-Aug-12	29-Jun-18	0	$1,037,614,340
Project Administration		1500	01-Oct-12	29-Jun-18	0	$53,014,340
Project Milestones		1500	01-Oct-12	29-Jun-18	0	$0
NTE-NTP1	Notice To Proceed # 1	0	01-Oct-12*		53	$0
NTE-NTP2	Notice to Proceed # 2	0	01-Apr-13		269	$0
NTE-PROJFINISH3B	Substantial Completion Segment 3B (By others)	0		31-Mar-16*	593	$0
NTE-ITSFINISH	Completion of ITS (Civil) Work	0		06-Oct-17	2	$0
NTE-SC-NOTICE1	Substantial Completion Notiifcation Period to TxDOT	20	26-Feb-18	23-Mar-18	20	$0
NTE-SC-NOTICE2	Notification to TxDOT / IE of Developer's Anticipated Substantial Completion	0	26-Feb-18		20	$0
NTE-SCOMP-1000	Substantial Completion Segment 3A	0		23-Mar-18	2	$0
NTE-SCOMP-1010	TxDOT Issue Substantial Completion Certificate	5	26-Mar-18	30-Mar-18	0	$0
NTE-SCOMP-1020	Open Traffic / Service Commencement	0		30-Mar-18*	1	$0
NTE-FCOMP-1000	Completion of Punchlist Works	70	31-Mar-18	08-Jun-18	1	$0
NTE-FCOMP-1010	Review and Approval of Punchlist Works by TxDOT / IE	15	09-Jun-18	23-Jun-18	1	$0
NTE-FCOMP-1005	Notification to TxDOT / IE of Develpoer's Final Completion	0	11-Jun-18		10	$0
NTE-FCOMP-1015	TxDOT Issue Final Completion Certificate	5	25-Jun-18	29-Jun-18	0	$0
NTE-FCOMP-1020	Project Final Acceptance	0		29-Jun-18	0	$0
Management Submittals		391	01-Oct-12	31-Mar-14	1038	$0
Project Schedules		391	01-Oct-12	31-Mar-14	1038	$0
Quality Management Plans		128	01-Oct-12	27-Mar-13	193	$0
Developer Deliverables for NTP # 2		120	01-Oct-12	20-Mar-13	195	$0
Developer Activities		1017	01-May-14	23-Mar-18	0	$53,014,340
Segment 3A		1017	01-May-14	23-Mar-18	0	$32,338,747
Project System Design		280	01-May-14	27-May-15	447	$6,467,749
Network Communication System (NCS)		105	09-Oct-17	02-Mar-18	10	$3,880,650
Intelligent Transportation System (ITS)		120	09-Oct-17	23-Mar-18	0	$10,186,705
Toll Collection System (TCS)		120	09-Oct-17	23-Mar-18	0	$11,803,643
Segment 3B		594	01-May-14	09-Aug-16	423	$20,675,593
Project System Design		280	01-May-14	27-May-15	447	$4,135,119
Network Communication System (NCS)		75	01-Jul-15	13-Oct-15	633	$2,481,071
Intelligent Transportation System (ITS)		290	01-Jul-15	09-Aug-16	423	$6,512,812
Toll Collection System (TCS)		150	01-Jul-15	26-Jan-16	563	$7,546,591
Right-of-Way Acquisition		548	01-Aug-12	05-Sep-14	925	$0
Acquisition by Developer		548	01-Aug-12	05-Sep-14	925	$0
NTE-ROWSTART	Start Right of Way Process	0	01-Aug-12*		1	$0
NTE-ROW-BATCH1	Finish ROW Batch 1 Review by TxDOT	0		14-Dec-12	13	$0
NTE-ROW-BATCH2	Start ROW Batch 2 Review by TxDOT	0	17-Dec-12		13	$0
NTE-ROW-BATCH2-1	Finish ROW Batch 2 Review by TxDOT	0		10-Jan-13	12	$0
NTE-ROW-BATCH3	Start ROW Batch 3 Review by TxDOT	0	11-Jan-13		12	$0
NTE-ROW-BATCH3-1	Finish ROW Batch 3 Review by TxDOT	0		01-Feb-13	12	$0
NTE-ROW-BATCH4	Start ROW Batch 4 Review by TxDOT	0	04-Feb-13		12	$0
NTE-ROW-BATCH4-1	Finish ROW Batch 4 Review by TxDOT	0		25-Feb-13	11	$0
NTE-ROW-BATCH5	Start ROW Batch 5 Review by TxDOT	0	26-Feb-13		11	$0
NTE-ROW-BATCH5-1	Finish ROW Batch 5 Review by TxDOT	0		01-Apr-13	1	$0
NTE-ROW-BATCH6	Start ROW Batch 6 Review by TxDOT	0	02-Apr-13		1	$0
NTE-ROW-BATCH6-1	Finish ROW Batch 6 Review by TxDOT	0		15-Apr-13	1	$0
NTE-ROW-BATCH7	Start ROW Batch 7 Review by TxDOT	0	16-Apr-13		1	$0
NTE-ROW-BATCH7-1	Finish ROW Batch 7 Review by TxDOT	0		29-Apr-13	11	$0
NTE-ROW-BATCH8	Start ROW Batch 8 Review by TxDOT	0	30-Apr-13		11	$0
NTE-ROW-BATCH8-1	Finish ROW Batch 8 Review by TxDOT	0		28-May-13	140	$0
NTE-ROW-BATCH9	Start ROW Batch 9 Review by TxDOT	0	29-May-13		140	$0
NTE-ROWFINISH	Complete Right of Way Process	0		05-Sep-14	1297	$0

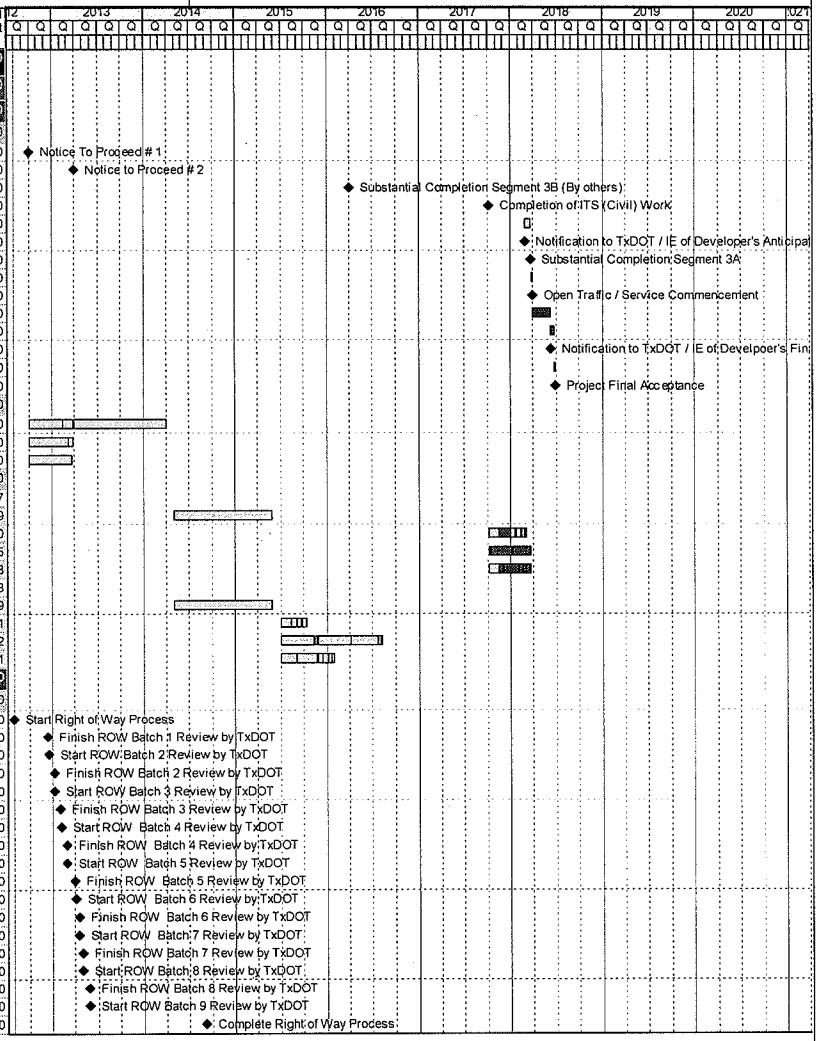

Remaining Level of Effort | Remaining Work
Actual Level of Effort | Critical Remaining Work
Actual Work | Milestone

NTE 3A / Interchange Project

SUMMAY PROGRAM SCHEDULE

SUMMARY SCHEDULE — NTE - Segment 3A Interchange Project - FBS # 1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Parcels Needing Relocation	548	01-Aug-12	05-Sep-14	382	$0
	Parcel #8 SBFR - Meacham to Dewey (STA 679+00 to STA 687+00)	400	01-Aug-12	11-Feb-14	141	$0
	Parcel #15 SBFR - Meacham to Dewey (STA 700+00 to STA 700+00)	400	01-Aug-12	11-Feb-14	141	$0
	Parcel #25 SBGP - Meacham to Dewey (STA 730+00 to STA 730+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #27 SBGP - Meacham to Dewey (STA 735+00 to STA 735+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #29 SBGP - Meacham to Dewey (STA 737+00 to STA 737+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #31 NBGP - Meacham to Dewey (STA 736+00 to STA 736+00)	476	01-Aug-12	28-May-14	440	$0
	Parcel #34 SBFR - Meacham to Dewey (STA 743+00 to STA 743+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #39 SBFR - Meacham to Dewey (STA 746+00 to STA 746+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #41 (TxDOT #821) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 747+00 to STA 747+00)	537	01-Aug-12	21-Aug-14	3	$0
	Parcel #43 SBFR - Meacham to Dewey (STA 750+00 to STA 750+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #44 (TxDOT #825) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 752+00 to STA 752+00)	537	01-Aug-12	21-Aug-14	3	$0
	Parcel #51 SBFR - Meacham to Dewey (STA 757+00 to STA 757+00)	400	01-Aug-12	11-Feb-14	140	$0
	Parcel #52 (TxDOT #830) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 757+00 to STA 762+50)	537	01-Aug-12	21-Aug-14	3	$0
	Parcel #61 (TxDOT #835) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 771+50 to STA 776+00)	537	01-Aug-12	21-Aug-14	3	$0
	Parcel #64 SBFR - Dewey to S. of trinity River (STA 777+00 to STA 777+00)	400	01-Aug-12	11-Feb-14	141	$0
	Parcel #65 (TxDOT #836) - COMPLEX - SBFR - Dewey to S. of Trinity River (STA 781+00 to STA 781+00)	537	01-Aug-12	21-Aug-14	4	$0
	Parcel #71 SBFR - Dewey to S. of trinity River (STA 788+00 to STA 788+00)	400	01-Aug-12	11-Feb-14	200	$0
	Parcel #72 (TxDOT #841) - COMPLEX - SBFR - Dewey to S. of trinity River (STA 790+00 to STA 795+00)	537	01-Aug-12	21-Aug-14	4	$0
	Parcel #73 (TxDOT #842) - COMPLEX - SBRP - Dewey to S. of Trinity River (STA 795+00 to STA 800+00)	537	01-Aug-12	21-Aug-14	4	$0
	Parcel #76 SBML - Dewey to S. of trinity River (STA 806+00 to STA 806+00)	400	01-Aug-12	11-Feb-14	200	$0
	Parcel #77 (TxDOT #846) - COMPLEX - SBGP - Dewey to S. of Trinity River (STA 805+00 to STA 810+00)	537	01-Aug-12	21-Aug-14	4	$0
	Parcel #88/80(TxDOT #847/848) COMPLEX - SBML - Dewey to S. of Trinity (STA 811+00 to STA 825+00)	537	01-Aug-12	21-Aug-14	4	$0
	Parcel #97 SBFR - Dewey to S. of trinity River (STA 862+00 to STA 862+00)	400	01-Aug-12	11-Feb-14	200	$0
	Parcel #99 SBFR - Dewey to S. of trinity River (STA 862+50 to STA)	400	01-Aug-12	11-Feb-14	200	$0
	Parcel #100 SBFR - S. of trinity River to IH 30 (STA 863+00 to STA 863+00)	400	01-Aug-12	11-Feb-14	187	$0
	Parcel #108 (TxDOT #866) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 866+00 to STA 866+00)	537	01-Aug-12	21-Aug-14	1	$0
	Parcel #109 (TxDOT #867) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 867+00 to STA 867+00)	537	01-Aug-12	21-Aug-14	1	$0
	Parcel #110 (TxDOT #874) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 867+00 to STA 867+00)	537	01-Aug-12	21-Aug-14	1	$0
	Parcel #115 (TxDOT #880) - COMPLEX - SBFR - S. of Trinity to IH 30 (STA 872+00 to STA 872+00)	537	01-Aug-12	21-Aug-14	50	$0
	Parcel #116 SBFR - S. of Trinity River to IH 30 (STA 875+00 to STA 876+00)	400	01-Aug-12	11-Feb-14	187	$0
	Parcel #117 (TxDOT #883) - COMPLEX - SBFR - S. of Trinity to IH 30 (STA 878+00 to STA 878+00)	537	01-Aug-12	21-Aug-14	50	$0
	Parcel #118 (TxDOT #885) - COMPLEX - SBFR - S. of Trinity to IH 30 (STA 881+00 to STA 884+00)	548	01-Aug-12	05-Sep-14	39	$0
	Parcel #120 SBFR - S. of Trinity River to IH 30 (STA 884+00 to STA 887+00)	400	01-Aug-12	11-Feb-14	187	$0
	Parcel #122 SBGP - S. of Trinity River to IH 30 (STA 887+00 to STA 890+00)	476	01-Aug-12	28-May-14	454	$0
	Parcel #126 (TxDOT #897) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 915+00 to STA 915+00)	548	01-Aug-12	05-Sep-14	382	$0
	Parcel #128 (TxDOT #903) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 917+00 to STA 917+00)	548	01-Aug-12	05-Sep-14	382	$0
	Parcel #161 NBFR - S. of Trinity River to IH 30 (STA 915+00 to STA 915+00)	400	01-Aug-12	11-Feb-14	138	$0
	Parcel #163 NBFR - S. of Trinity River to IH 30 (STA 914+00 to STA 914+00)	400	01-Aug-12	11-Feb-14	138	$0
	Parcels Not Needing Relocation	548	01-Aug-12	05-Sep-14	382	$0
	Parcel #1 SBFR - Meacham to Dewey (STA 666+00 to STA 671+20)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #2 SBFR - Meacham to Dewey (STA 671+20 to STA 674+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #3 NBFR - Meacham to Dewey (STA 665+00 to STA 665+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #4 NBFR - Meacham to Dewey (STA 665+00 to STA 668+50)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #5 NBFR - Meacham to Dewey (STA 669+50 to STA 671+50)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #6 NBFR - Meacham to Dewey (STA 671+50 to STA 674+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #7 SBFR - Meacham to Dewey (STA 676+00 to STA 679+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #9 NBFR - Meacham to Dewey (STA 676+00 to STA 690+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #10 NBFR - Meacham to Dewey (STA 681+00 to STA 685+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #11 NBFR - Meacham to Dewey (STA 685+00 to STA 686+50)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #13 SBFR - Meacham to Dewey (STA 689+00 to STA 694+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #14 SBFR - Meacham to Dewey (STA 695+00 to STA 701+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #16 SBFR - Meacham to Dewey (STA 701+00 to STA 725+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #17 NBFR - Meacham to Dewey (STA 690+00 to STA 695+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #18 NBFR - Meacham to Dewey (STA 695+00 to STA 669+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #19 NBFR - Meacham to Dewey (STA 669+00 to STA 703+50)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #20 NBFR - Meacham to Dewey (STA 704+00 to STA 725+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #23 NBGP - Meacham to Dewey (STA 728+00 to STA 728+00)	486	01-Aug-12	11-Jun-14	430	$0
	Parcel #24 NBGP - Meacham to Dewey (STA 728+00 to STA 728+00)	486	01-Aug-12	11-Jun-14	430	$0
	Parcel #26 NBGP - Meacham to Dewey (STA 731+00 to STA 735+00)	486	01-Aug-12	11-Jun-14	430	$0

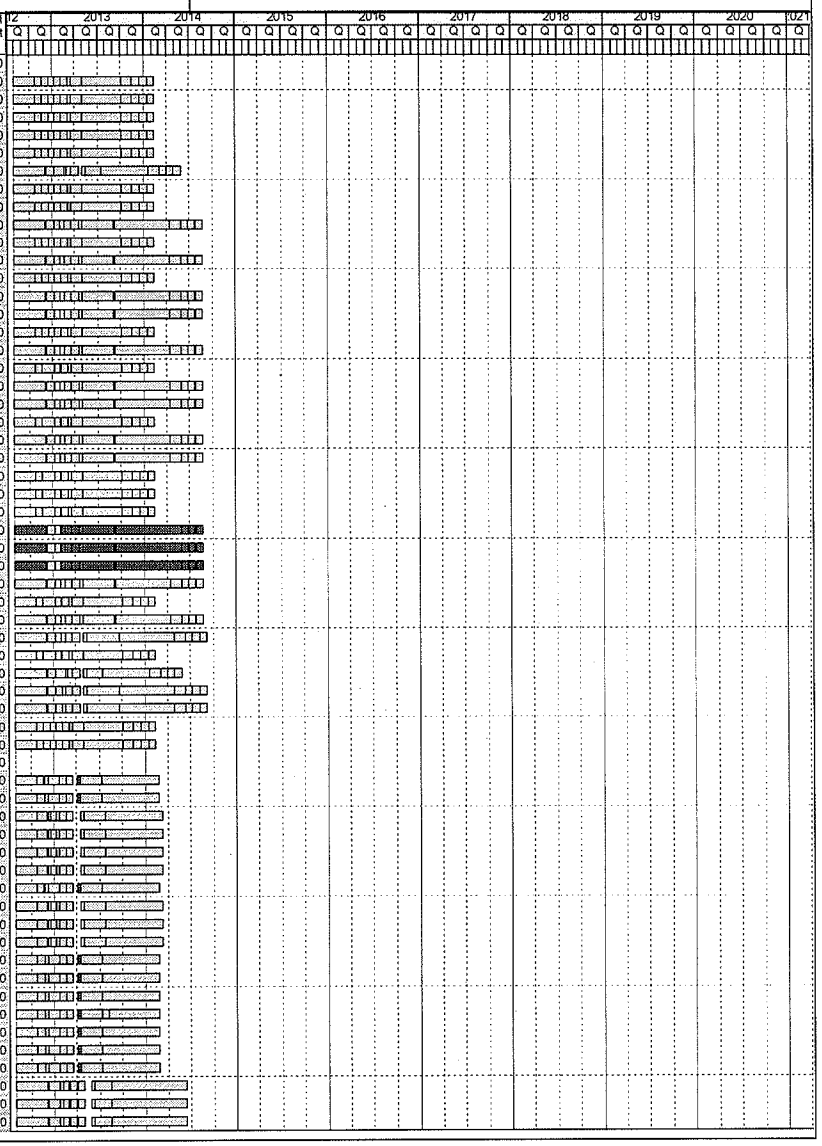

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Parcel #28 SBGP - Meacham to Dewey (STA 736+00 to STA 736+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #30 NBGP - Meacham to Dewey (STA 735+00 to STA 735+00)	486	01-Aug-12	11-Jun-14	430	$0
	Parcel #32 NBGP - Meacham to Dewey (STA 736+00 to STA 740+00)	486	01-Aug-12	11-Jun-14	430	$0
	Parcel #35 SBFR - Meacham to Dewey (STA 743+00 to STA 743+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #36 SBFR - Meacham to Dewey (STA 744+00 to STA 744+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #37 SBFR - Meacham to Dewey (STA 745+00 to STA 745+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #38 SBFR - Meacham to Dewey (STA 745+00 to STA 745+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #40 SBFR - Meacham to Dewey (STA 746+00 to STA 746+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #42 (TxDOT #821) - COMPLEX - SBFR - Meacham to Dewey (STA 750+00 to STA 750+00)	537	01-Aug-12	21-Aug-14	3	$0
	Parcel #45 NBGP - Meacham to Dewey (STA 743+00 to STA 743+00)	486	01-Aug-12	11-Jun-14	430	$0
	Parcel #46 NBFR - Meacham to Dewey (STA 743+00 to STA 745+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #47 NBFR - Meacham to Dewey (STA 746+00 to STA 750+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #48 NBFR - Meacham to Dewey (STA 750+50 to STA 751+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #49 NBFR - Meacham to Dewey (STA 751+00 to STA 756+00)	410	01-Aug-12	25-Feb-14	147	$0
	Parcel #50 SBFR - Meacham to Dewey (STA 756+00 to STA 756+00)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #53 SBFR - Meacham to Dewey (STA 762+50 to STA 766+50)	410	01-Aug-12	25-Feb-14	130	$0
	Parcel #54 NBFR - Meacham to Dewey (STA 755+00 to STA 759+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #55 NBFR - Meacham to Dewey (STA 755+00 to STA 760+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #56 NBFR - Meacham to Dewey (STA 761+00 to STA 761+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #57 NBFR - Meacham to Dewey (STA 762+00 to STA 762+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #58 NBFR - Meacham to Dewey (STA 762+00 to STA 771+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #59 NBFR - Meacham to Dewey (STA 771+00 to STA 776+00)	420	01-Aug-12	11-Mar-14	137	$0
	Parcel #60 (TxDOT #833) - COMPLEX - SBFR - Meacham to Dewey (STA 767+00 to STA 771+00)	537	01-Aug-12	21-Aug-14	3	$0
	Parcel #62 NBFR - Dewey to S. of trinity River (STA 776+00 to STA 776+00)	465	01-Aug-12	13-May-14	296	$0
	Parcel #63 NBFR - Dewey to S. of trinity River (STA 776+00 to STA 785+00)	465	01-Aug-12	13-May-14	296	$0
	Parcel #66 SBFR - Dewey to S. of trinity River (STA 782+00 to STA 782+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #67 SBFR - Dewey to S. of trinity River (STA 783+00 to STA 783+00)	465	01-Aug-12	13-May-14	135	$0
	Parcel #70 (TxDOT #839) - COMPLEX - NBGP - Dewey to S. of Trinity (STA 788+00 to STA 788+00)	548	01-Aug-12	05-Sep-14	145	$0
	Parcel #74 NBFR - Dewey to S. of trinity River (STA 788+00 to STA 804+00)	465	01-Aug-12	13-May-14	296	$0
	Parcel #75 (TxDOT #843/844) - COMPLEX - NBGP - Dewey to S. of Trinity (STA 805+00 to STA 805+00)	548	01-Aug-12	05-Sep-14	145	$0
	Parcel #78 NBGP - Dewey to S. of Trinity River (STA 810+00 to STA 811+00)	465	01-Aug-12	13-May-14	228	$0
	Parcel #87 NBGP - Dewey to S. of Trinity River (STA 815+00 to STA 829+00)	465	01-Aug-12	13-May-14	228	$0
	Parcel #89 SBGP - Dewey to S. of trinity River (STA 830+00 to STA 835+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #90 SBGP - Dewey to S. of trinity River (STA 830+00 to STA 835+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #91 NBFR - Dewey to S. of trinity River (STA 830+00 to STA 835+00)	465	01-Aug-12	13-May-14	296	$0
	Parcel #92 SBRP - Dewey to S. of trinity River (STA 839+00 to STA 842+00)	465	01-Aug-12	13-May-14	135	$0
	Parcel #95 SBGP - Dewey to S. of trinity River (STA 861+00 to STA 861+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #96 SBGP - Dewey to S. of trinity River (STA 861+00 to STA 861+00)	410	01-Aug-12	25-Feb-14	131	$0
	Parcel #98 SBFR - Dewey to S. of trinity River (STA 862+00 to STA 862+00)	465	01-Aug-12	13-May-14	135	$0
	Parcel #101 SBFR - S. of trinity River to IH 30 (STA 863+00 to STA 863+00)	420	01-Aug-12	11-Mar-14	167	$0
	Parcel #102 SBFR - S. of trinity River to IH 30 (STA 864+00 to STA 864+00)	420	01-Aug-12	11-Mar-14	167	$0
	Parcel #103 SBFR - S. of trinity River to IH 30 (STA 865+00 to STA 865+00)	420	01-Aug-12	11-Mar-14	167	$0
	Parcel #111 NBFR - S. of trinity River to IH 30 (STA 867+00 to STA 871+00)	465	01-Aug-12	13-May-14	296	$0
	Parcel #112 NBFR - S. of trinity River to IH 30 (STA 871+00 to STA 876+00)	465	01-Aug-12	13-May-14	296	$0
	Parcel #113 SBFR - S. of trinity River to IH 30 (STA 870+00 to STA 870+00)	465	01-Aug-12	13-May-14	122	$0
	Parcel #114 SBFR - S. of trinity River to IH 30 (STA 871+00 to STA 871+00)	465	01-Aug-12	13-May-14	122	$0
	Parcel #119 SBFR - S. of trinity River to IH 30 (STA 881+00 to STA 884+00)	465	01-Aug-12	13-May-14	122	$0
	Parcel #123 SBGP - S. of trinity River to IH 30 (STA 900+00 to STA 903+00)	486	01-Aug-12	11-Jun-14	444	$0
	Parcel #124 (TxDOT #---) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 903+00 to STA 910+00)	548	01-Aug-12	05-Sep-14	382	$0
	Parcel #125 (TxDOT #896) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 912+00 to STA 912+00)	548	01-Aug-12	05-Sep-14	382	$0
	Parcel #127 SBGP - S. of Trinity River to IH 30 (STA 916+00 to STA 916+00)	486	01-Aug-12	11-Jun-14	444	$0
	Parcel #129 SBGP - S. of Trinity River to IH 30 (STA 918+00 to STA 918+00)	486	01-Aug-12	11-Jun-14	444	$0
	Parcel #130 SBGP - S. of Trinity River to IH 30 (STA 918+00 to STA 923+00)	486	01-Aug-12	11-Jun-14	444	$0
	Parcel #153 NBGP - S. of Trinity River to IH 30 (STA 925+00 to STA 925+00)	465	01-Aug-12	13-May-14	432	$0
	Parcel #154 NBGP - S. of Trinity River to IH 30 (STA 924+00 to STA 924+00)	465	01-Aug-12	13-May-14	432	$0
	Parcel #155 NBGP - S. of Trinity River to IH 30 (STA 924+00 to STA 922+00)	465	01-Aug-12	13-May-14	432	$0
	Parcel #156 NBGP - S. of Trinity River to IH 30 (STA 920+00 to STA 920+00)	465	01-Aug-12	13-May-14	432	$0
	Parcel #157 NBGP - S. of Trinity River to IH 30 (STA 919+00 to STA 919+00)	486	01-Aug-12	11-Jun-14	411	$0
	Parcel #158 NBFR - S. of Trinity River to IH 30 (STA 918+00 to STA 918+00)	400	01-Aug-12	11-Feb-14	138	$0
	Parcel #159 NBFR - S. of Trinity River to IH 30 (STA 916+00 to STA 916+00)	400	01-Aug-12	11-Feb-14	138	$0

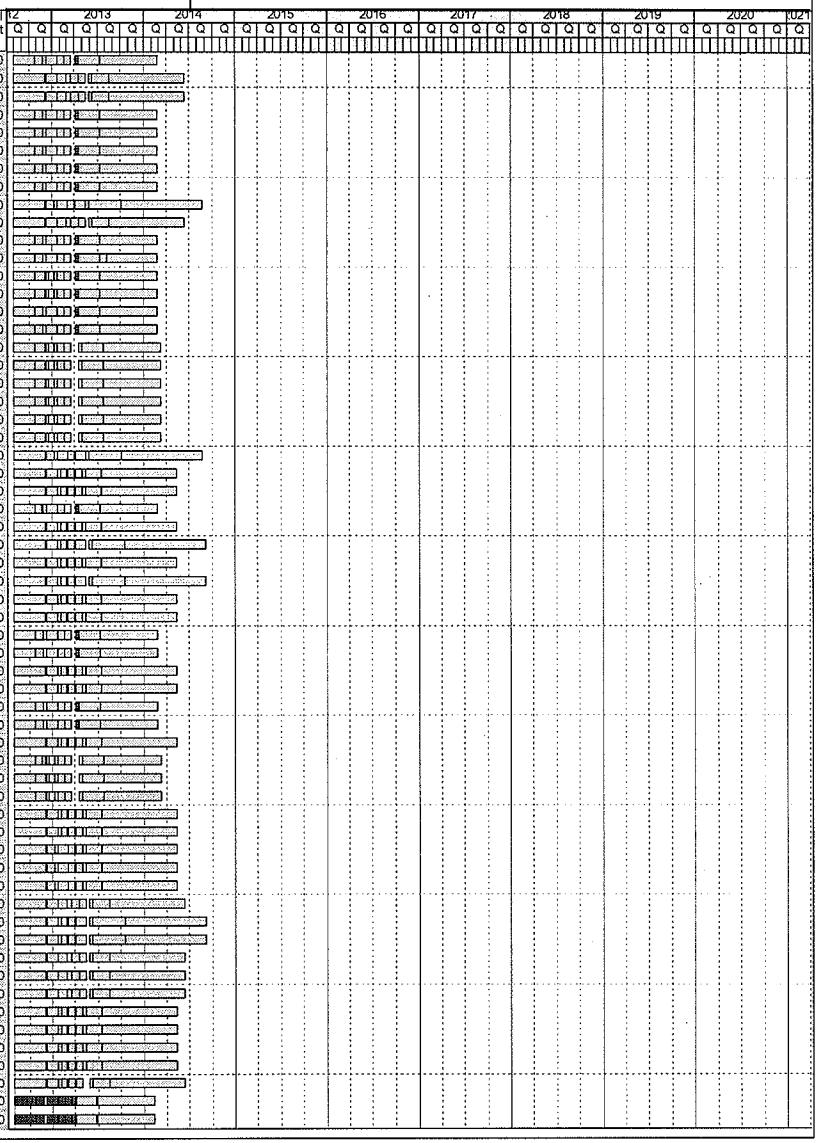

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Parcel #160 NBFR - S. of Trinity River to IH 30 (STA 915+00 to STA 915+00)		410	01-Aug-12	25-Feb-14	128	$0
Parcel #162 NBFR - S. of Trinity River to IH 30 (STA 914+00 to STA 914+00)		410	01-Aug-12	25-Feb-14	128	$0
Parcel #166 NBFR - S. of Trinity River to IH 30 (STA 910+00 to STA 908+00)		410	01-Aug-12	25-Feb-14	128	$0
Parcel #167 (TxDOT #889) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 905+00 to STA 905+00)		537	01-Aug-12	21-Aug-14	1	$0
Parcel #168 NBGP - S. of Trinity River to IH 30 (STA 903+00 to STA 903+00)		486	01-Aug-12	11-Jun-14	411	$0
Parcel #169 NBGP - S. of Trinity River to IH 30 (STA 900+00 to STA 900+00)		486	01-Aug-12	11-Jun-14	411	$0
Parcel #12 EAST (TxDOT #804) - COMPLEX - NBFR - Meacham to Dewey (STA 688+00 to STA)		537	01-Aug-12	21-Aug-14	20	$0
Parcel #12 WEST (TxDOT #805) - COMPLEX - SBFR - Meacham to Dewey (STA 688+00 to STA)		537	01-Aug-12	21-Aug-14	4	$0
Parcel #149 / 150 NBGP - S. of Trinity River to IH 30 (STA 934+00 to STA)		486	01-Aug-12	11-Jun-14	411	$0
Parcel #93A SBFR - Dewey to S. of Trinity River (STA 848+00 to STA)		465	01-Aug-12	13-May-14	135	$0
Parcel #93B SBFR - Dewey to S. of Trinity River (STA 848+00 to STA)		465	01-Aug-12	13-May-14	135	$0
Utility Adjustments		362	01-Oct-12	18-Feb-14	858	$20,463,314
Utility Coordination		215	01-Oct-12	26-Jul-13	514	$0
MSUT1000	Start of Utility Coordination Process	0	01-Oct-12		178	$0
MSUT1010	TxDOT Review of Utility Submission - Calendar Week 1	0	05-Nov-12		178	$0
MSUT1020	TxDOT Review of Utility Submission - Calendar Week 2	0	12-Nov-12		178	$0
MSUT1030	TxDOT Review of Utility Submission - Calendar Week 3	0	19-Nov-12		178	$0
MSUT1040	TxDOT Review of Utility Submission - Calendar Week 4	0	26-Nov-12		178	$0
MSUT1050	TxDOT Review of Utility Submission - Calendar Week 5	0	03-Dec-12		178	$0
MSUT1060	TxDOT Review of Utility Submission - Calendar Week 6	0	10-Dec-12		178	$0
MSUT1070	TxDOT Review of Utility Submission - Calendar Week 7	0	17-Dec-12		178	$0
MSUT1080	TxDOT Review of Utility Submission - Calendar Week 8	0	24-Dec-12		178	$0
MSUT1090	TxDOT Review of Utility Submission - Calendar Week 9	0	31-Dec-12		178	$0
MSUT1100	TxDOT Review of Utility Submission - Calendar Week 10	0	07-Jan-13		178	$0
MSUT1110	TxDOT Review of Utility Submission - Calendar Week 11	0	14-Jan-13		178	$0
MSUT1120	TxDOT Review of Utility Submission - Calendar Week 12	0	21-Jan-13		178	$0
MSUT1130	TxDOT Review of Utility Submission - Calendar Week 13	0	28-Jan-13		178	$0
MSUT1140	TxDOT Review of Utility Submission - Calendar Week 14	0	04-Feb-13		178	$0
MSUT1150	TxDOT Review of Utility Submission - Calendar Week 15	0	11-Feb-13		178	$0
MSUT1160	TxDOT Review of Utility Submission - Calendar Week 16	0	18-Feb-13		178	$0
MSUT1170	TxDOT Review of Utility Submission - Calendar Week 17	0	25-Feb-13		178	$0
MSUT1180	TxDOT Review of Utility Submission - Calendar Week 18	0	04-Mar-13		178	$0
MSUT1190	TxDOT Review of Utility Submission - Calendar Week 19	0	11-Mar-13		178	$0
MSUT1200	TxDOT Review of Utility Submission - Calendar Week 20	0	18-Mar-13		178	$0
MSUT1210	TxDOT Review of Utility Submission - Calendar Week 21	0	25-Mar-13		178	$0
MSUT1220	TxDOT Review of Utility Submission - Calendar Week 22	0	01-Apr-13		178	$0
MSUT1230	TxDOT Review of Utility Submission - Calendar Week 23	0	08-Apr-13		178	$0
MSUT1240	TxDOT Review of Utility Submission - Calendar Week 24	0	15-Apr-13		178	$0
MSUT1250	TxDOT Review of Utility Submission - Calendar Week 25	0	22-Apr-13		375	$0
MSUT1260	TxDOT Review of Utility Submission - Calendar Week 26	0	29-Apr-13		381	$0
MSUT1270	TxDOT Review of Utility Submission - Calendar Week 27	0	06-May-13		455	$0
MSUT1280	TxDOT Review of Utility Submission - Calendar Week 28	0	13-May-13		721	$0
AT&T		194	01-Oct-12	27-Jun-13	266	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	266	$0
3AAT&TMSUT1005	Start of Utility Assembly Package Relocation Process - AT&T	0	01-Oct-12		422	$0
3AAT&TMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - AT&T	0		27-Jun-13	374	$0
MUAA Process		155	01-Oct-12	03-May-13	265	$0
Utility Design		122	01-Oct-12	19-Mar-13	298	$0
Signature Process		38	06-May-13	27-Jun-13	259	$0
Procurement		28	06-May-13	12-Jun-13	277	$0
Atmos		200	01-Oct-12	05-Jul-13	269	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	269	$0
3AATMOMSUT1320	Start of Utility Assembly Package Relocation Process - ATMOS	0	01-Oct-12		436	$0
3AATMOMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - ATMOS	0		05-Jul-13	377	$0
MUAA Process		160	01-Oct-12	10-May-13	269	$0
Utility Design		122	01-Oct-12	19-Mar-13	307	$0
Signature Process		38	13-May-13	05-Jul-13	263	$0
Procurement		28	13-May-13	19-Jun-13	281	$0
3AATMODSUT1330	R.F.P. Preparation - ATMOS	5	13-May-13	17-May-13	274	$0
3AATMODSUT1340	R.F.P. Solicitation - ATMOS	15	20-May-13	10-Jun-13	274	$0

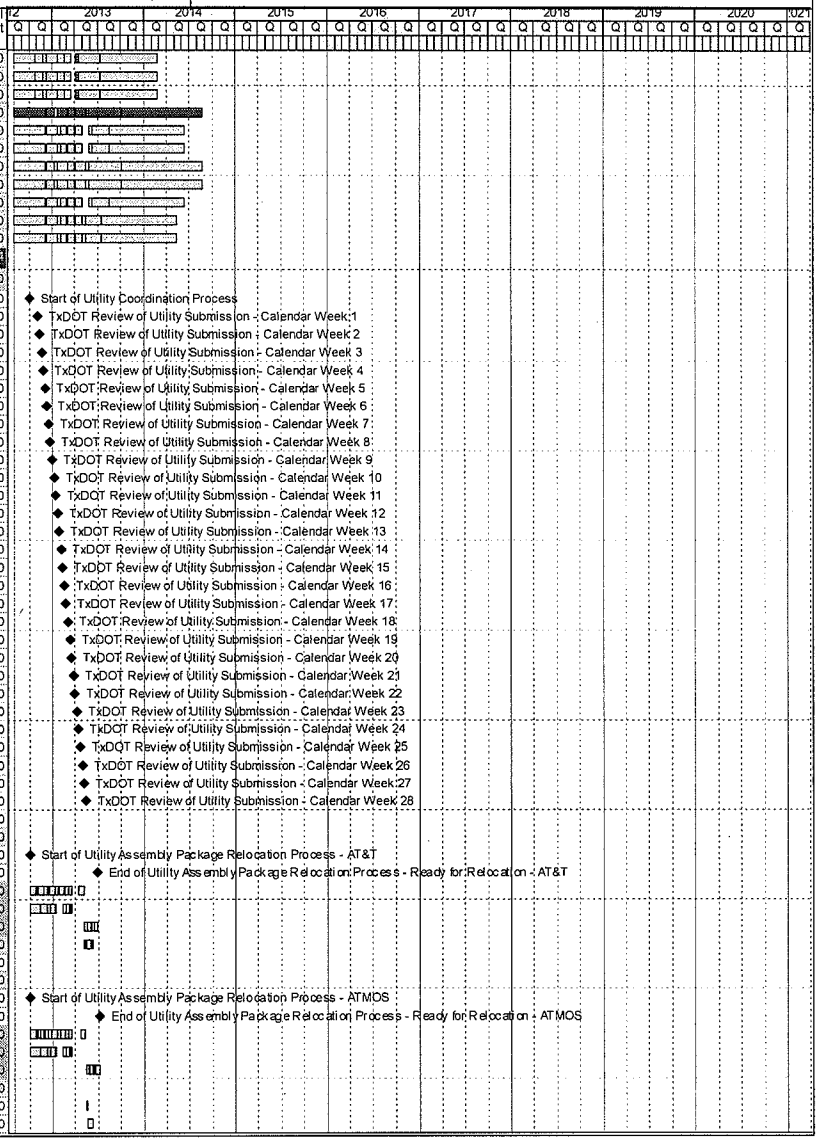

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AATMODSUT1350	Review and Selection of Contractor (s) - ATMOS	5	11-Jun-13	17-Jun-13	274	$0
3AATMODSUT1360	Executed Agreement with Contractor(s) - ATMOS	2	18-Jun-13	19-Jun-13	274	$0
3AATMOMSUT1370	Issuance of NTP to Contractor(s) - ATMOS	0		19-Jun-13	393	$0
Barnett Gathering		210	01-Oct-12	19-Jul-13	331	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	331	$0
ICBARNMSUT1000	Start of Utility Assembly Package Relocation Process - Barnett Gathering	0	01-Oct-12		539	$0
ICBARNMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Barnett Gathering	0		19-Jul-13	465	$0
MUAA Process		170	01-Oct-12	24-May-13	333	$0
Utility Design		142	01-Oct-12	16-Apr-13	361	$0
Signature Process		38	28-May-13	19-Jul-13	324	$0
Procurement		27	28-May-13	03-Jul-13	343	$0
Broadwing / Level 3		200	01-Oct-12	05-Jul-13	277	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	277	$0
3ALVL3MSUT1000	Start of Utility Assembly Package Relocation Process - Broadwing / Level 23	0	01-Oct-12		448	$0
3ALVL3MSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Broadwing / Level 3	0		05-Jul-13	389	$0
MUAA Process		160	01-Oct-12	10-May-13	278	$0
Utility Design		137	01-Oct-12	09-Apr-13	301	$0
Signature Process		38	13-May-13	05-Jul-13	271	$0
Procurement		28	13-May-13	19-Jun-13	289	$0
Charter Communication		200	01-Oct-12	05-Jul-13	270	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	270	$0
3ACHARMSUT1000	Start of Utility Assembly Package Relocation Process - Charter Communication	0	01-Oct-12		437	$0
3ACHARMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Charter Communi	0		05-Jul-13	380	$0
MUAA Process		160	01-Oct-12	10-May-13	271	$0
Utility Design		122	01-Oct-12	19-Mar-13	309	$0
Signature Process		38	13-May-13	05-Jul-13	264	$0
Procurement		28	13-May-13	19-Jun-13	282	$0
Chevron		210	01-Oct-12	19-Jul-13	361	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	361	$0
3ACHEVMSUT1001	Start of Utility Assembly Package Relocation Process - Chevron	0	01-Oct-12		578	$0
3ACHEVMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Chevron	0		19-Jul-13	507	$0
MUAA Process		170	01-Oct-12	24-May-13	362	$0
Utility Design		147	01-Oct-12	23-Apr-13	355	$0
Signature Process		38	28-May-13	19-Jul-13	353	$0
Procurement		27	28-May-13	03-Jul-13	373	$0
City of Fort Worth		194	01-Oct-12	27-Jun-13	260	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	260	$0
3ACFTWMSUT1001	Start of Utility Assembly Package Relocation Process - City of Fort Worth	0	01-Oct-12		414	$0
3ACFTWMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - City of Fort Worth	0		27-Jun-13	364	$0
MUAA Process		155	01-Oct-12	03-May-13	269	$0
Utility Design		117	01-Oct-12	12-Mar-13	298	$0
Signature Process		36	06-May-13	27-Jun-13	254	$0
Procurement		28	06-May-13	12-Jun-13	271	$0
Energy Transfer		205	01-Oct-12	12-Jul-13	279	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	279	$0
3AENTRMSUT1000	Start of Utility Assembly Package Relocation Process - Energy Transfer	0	01-Oct-12		459	$0
3AENTRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Energy Transfer	0		12-Jul-13	391	$0
MUAA Process		165	01-Oct-12	17-May-13	280	$0
Utility Design		137	01-Oct-12	09-Apr-13	308	$0
Signature Process		36	20-May-13	12-Jul-13	273	$0
Procurement		28	20-May-13	26-Jun-13	291	$0
Magellan Pipeline		200	01-Oct-12	05-Jul-13	270	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	270	$0
3AMAGEMSUT1000	Start of Utility Assembly Package Relocation Process - Magellan Pipeline	0	01-Oct-12		437	$0
3AMAGEMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Magellan Pipeline	0		05-Jul-13	380	$0
MUAA Process		160	01-Oct-12	10-May-13	271	$0
Utility Design		122	01-Oct-12	19-Mar-13	309	$0
Signature Process		38	13-May-13	05-Jul-13	264	$0
Procurement		28	13-May-13	19-Jun-13	282	$0
Oncor		194	01-Oct-12	27-Jun-13	129	$0

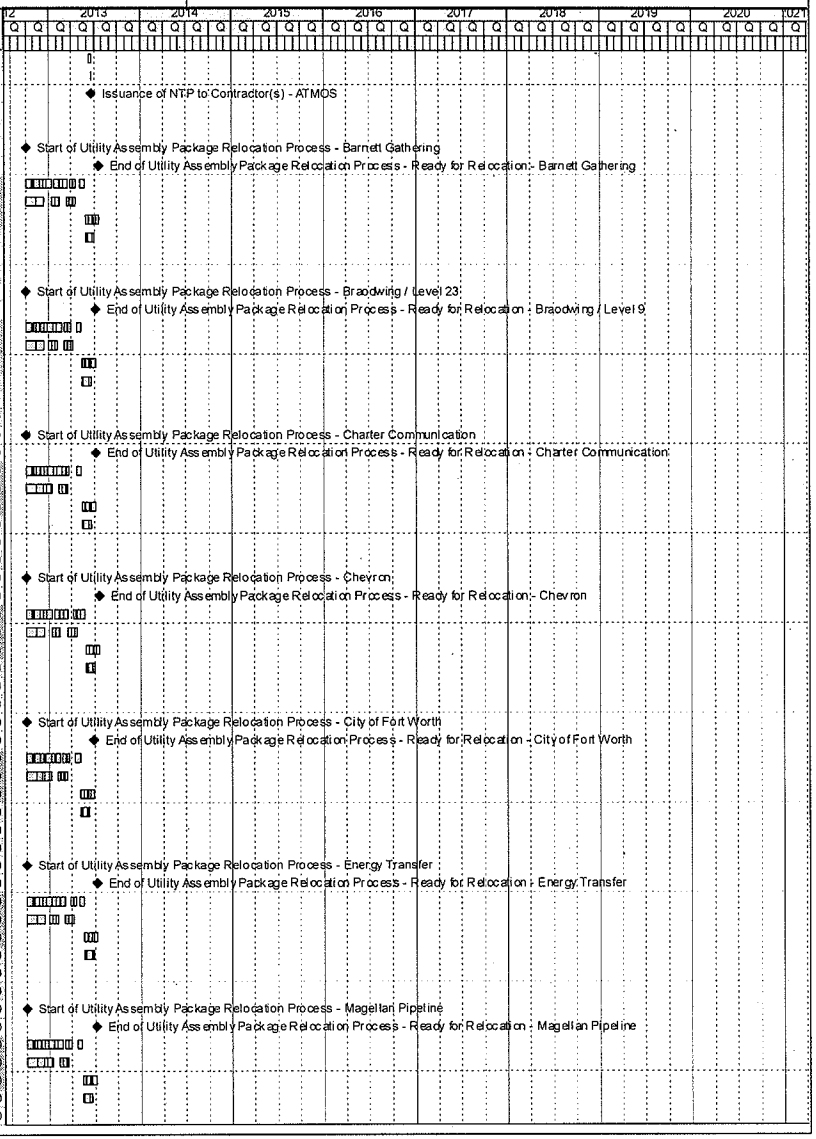

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Utility Assembly Package		194	01-Oct-12	27-Jun-13	129	$0
3AONCRMSUT1000	Start of Utility Assembly Package Relocation Process - Oncor	0	01-Oct-12		178	$0
3AONCRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Oncor	0		27-Jun-13	181	$0
MUAA Process		165	01-Oct-12	03-May-13	128	$0
Utility Design		117	01-Oct-12	12-Mar-13	166	$0
Signature Process		38	06-May-13	27-Jun-13	125	$0
Procurement		28	06-May-13	12-Jun-13	140	$0
Qwest		205	01-Oct-12	12-Jul-13	279	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	279	$0
3AQWSTMSUT1001	Start of Utility Assembly Package Relocation Process - Qwest	0	01-Oct-12		459	$0
3AQWSTMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Qwest	0		12-Jul-13	391	$0
MUAA Process		165	01-Oct-12	17-May-13	280	$0
Utility Design		132	01-Oct-12	02-Apr-13	313	$0
Signature Process		38	20-May-13	12-Jul-13	273	$0
Procurement		28	20-May-13	26-Jun-13	291	$0
Sprint		215	01-Oct-12	26-Jul-13	514	$0
Utility Assembly Package		215	01-Oct-12	26-Jul-13	514	$0
3ASPRTMSUT1000	Start of Utility Assembly Package Relocation Process - Sprint	0	01-Oct-12		801	$0
3ASPRTMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Sprint	0		26-Jul-13	720	$0
MUAA Process		176	01-Oct-12	03-Jun-13	515	$0
Utility Design		157	01-Oct-12	07-May-13	534	$0
Signature Process		38	04-Jun-13	26-Jul-13	503	$0
Procurement		28	04-Jun-13	11-Jul-13	525	$0
Texas Midstream		205	01-Oct-12	12-Jul-13	273	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	273	$0
3ATEMIMSUT1000	Start of Utility Assembly Package Relocation Process - Texas Midstream	0	01-Oct-12		449	$0
3ATEMIMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Texas Midstream	0		12-Jul-13	383	$0
MUAA Process		165	01-Oct-12	17-May-13	274	$0
Utility Design		132	01-Oct-12	02-Apr-13	307	$0
Signature Process		38	20-May-13	12-Jul-13	267	$0
Procurement		28	20-May-13	26-Jun-13	285	$0
Time Warner / Fiber Light		194	01-Oct-12	27-Jun-13	258	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	258	$0
3ATMWRMSUT1000	Start of Utility Assembly Package Relocation Process - Time Warner / Fiber Light	0	01-Oct-12		410	$0
3ATMWRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Time Warner / Fit	0		27-Jun-13	362	$0
MUAA Process		155	01-Oct-12	03-May-13	258	$0
Utility Design		117	01-Oct-12	12-Mar-13	296	$0
Signature Process		38	06-May-13	27-Jun-13	252	$0
Procurement		28	06-May-13	12-Jun-13	269	$0
Verizon		210	01-Oct-12	19-Jul-13	508	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	508	$0
3AVERZMSUT1000	Start of Utility Assembly Package Relocation Process - Verizon	0	01-Oct-12		785	$0
3AVERZMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Verizon	0		19-Jul-13	712	$0
MUAA Process		170	01-Oct-12	24-May-13	509	$0
Utility Design		157	01-Oct-12	07-May-13	522	$0
Signature Process		38	28-May-13	19-Jul-13	497	$0
Procurement		27	28-May-13	03-Jul-13	520	$0
Crosstex Energy		205	01-Oct-12	12-Jul-13	329	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	329	$0
ICCROSSMSUT1000	Start of Utility Assembly Package Relocation Process - Crosstex Energy	0	01-Oct-12		528	$0
ICCROSSMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Crosstex Energy	0		12-Jul-13	461	$0
MUAA Process		165	01-Oct-12	17-May-13	330	$0
Utility Design		142	01-Oct-12	16-Apr-13	353	$0
Signature Process		38	20-May-13	12-Jul-13	322	$0
Procurement		28	20-May-13	26-Jun-13	341	$0
Enterprisee Products		210	01-Oct-12	19-Jul-13	324	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	324	$0
ICENTRMSUT1000	Start of Utility Assembly Package Relocation Process - Enterprise Products	0	01-Oct-12		528	$0
ICENTRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Enterprise Product	0		19-Jul-13	454	$0
MUAA Process		170	01-Oct-12	24-May-13	325	$0

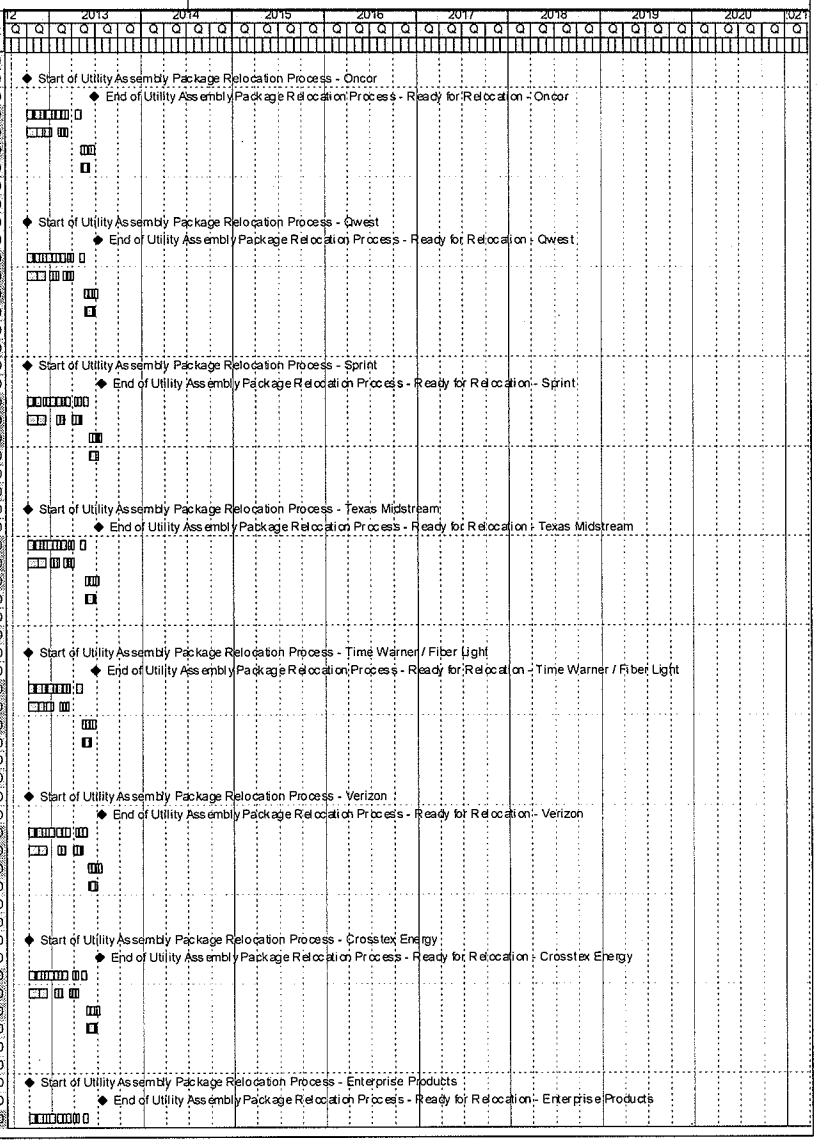

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Utility Design		147	01-Oct-12	23-Apr-13	348	$0
Signature Process		38	28-May-13	19-Jul-13	317	$0
Procurement		27	28-May-13	03-Jul-13	336	$0
Utility Relocations		168	28-Jun-13	18-Feb-14	858	$20,469,314
AT&T		58	28-Jun-13	17-Sep-13	968	$2,139,494
3AAT&TMSUT1000	Start AT&T Utility Relocation	0	28-Jun-13		374	$0
OH - 52 (Fiber Optic) 111+45 to 112+05		37	01-Jul-13	20-Aug-13	988	$67,018
OH - 14 (Fiber Optic) 870+40 to 889+00		37	01-Jul-13	20-Aug-13	347	$102,399
OH - 31 (Fiber Optic) 766+60 to 771+40		35	01-Jul-13	16-Aug-13	435	$27,527
OH - 37 (Fiber Optic) 727+50 to 729+80		39	01-Jul-13	22-Aug-13	264	$66,064
OH - 10 (Fiber Optic) 908+00 to 915+00		35	01-Jul-13	16-Aug-13	349	$22,021
OH - 14 (Fiber Optic) 884+00 to 889+00		35	01-Jul-13	16-Aug-13	349	$30,316
OH - 17 (Fiber Optic) 868+20 to 869+20		35	01-Jul-13	16-Aug-13	295	$13,800
OH - 43 (Fiber Optic) 766+40 to 766+40		35	01-Jul-13	16-Aug-13	268	$34,427
FO1 - 01 (Fiber Optic) 869+20 to 869+37		39	01-Jul-13	22-Aug-13	291	$111,574
FO1 - 03 (Fiber Optic) 869+35 to 870+45		35	01-Jul-13	16-Aug-13	349	$16,149
OH - 10 (Telephone) 908+00 to 916+00		35	01-Jul-13	16-Aug-13	349	$8,295
OH - 14 (Telephone) 884+00 to 889+00		35	01-Jul-13	16-Aug-13	349	$15,121
OH - 25 (Telephone) 793+30 to 796+05		35	01-Jul-13	16-Aug-13	387	$7,194
OH - 27 (Telephone) 788+40 to 796+00		36	01-Jul-13	19-Aug-13	386	$26,132
OH - 31 (Telephone) 766+60 to 771+40		35	01-Jul-13	16-Aug-13	284	$13,800
OH - 32 (Telephone) 761+10 to 763+25		35	01-Jul-13	16-Aug-13	550	$6,313
OH - 37 (Telephone) 727+50 to 729+80		35	01-Jul-13	16-Aug-13	293	$17,727
OH - 40 (Telephone) 724+80 to 729+00		35	01-Jul-13	16-Aug-13	293	$18,204
OH - 43 (Telephone) 766+40 to 766+40		35	01-Jul-13	16-Aug-13	307	$17,213
OH - 13 (Telephone) 916+00 to 917+80		35	01-Jul-13	16-Aug-13	349	$8,809
T1 - 02 (Telephone) 915+00 to 915+70		35	01-Jul-13	16-Aug-13	349	$0
T1 - 03 (Telephone) 862+90 to 888+00		57	01-Jul-13	17-Sep-13	327	$658,362
T1 - 04 (Telephone) 886+00 to 888+00		42	01-Jul-13	27-Aug-13	342	$146,808
T1 - 05 (Telephone) 865+80 to 886+00		51	01-Jul-13	09-Sep-13	279	$217,937
T1 - 06 (Telephone) 872+10 to 873+00		35	01-Jul-13	16-Aug-13	349	$0
T1 - 07 (Telephone) 833+35 to 838+85		48	01-Jul-13	04-Sep-13	746	$250,657
T1 - 08 (Telephone) 763+00 to 766+50		37	01-Jul-13	20-Aug-13	433	$45,878
T1 - 09 (Telephone) 755+50 to 758+30		37	01-Jul-13	20-Aug-13	433	$45,878
T1 - 11 (Telephone) 727+20 to 729+60		41	01-Jul-13	26-Aug-13	689	$143,872
Atmos		60	06-Jul-13	27-Sep-13	939	$1,398,680
3AATMOMSUT1000	Start Atmos Utility Relocation	0	06-Jul-13		377	$0
G1 - 03 (Gas) 903+50 to 908+00		35	09-Jul-13	26-Aug-13	289	$0
G1 - 02 (Gas) 911+20 to 916+00		34	09-Jul-13	23-Aug-13	344	$49,401
G1 - 09 (Gas) 875+30 to 875+80		34	09-Jul-13	23-Aug-13	344	$0
G1 - 10 (Gas) 866+30 to 867+00		34	09-Jul-13	23-Aug-13	344	$0
G1 - 11 (Gas) 861+30 to 864+30		36	09-Jul-13	27-Aug-13	342	$47,272
G1 - 17 (Gas) 744+50 to 758+40		38	09-Jul-13	29-Aug-13	426	$114,694
G1 - 04 (Gas) 903+50 to 907+50		42	09-Jul-13	04-Sep-13	956	$147,763
G1 - 06 (Gas) 869+00 to 887+20		59	09-Jul-13	27-Sep-13	319	$428,387
G1 - 07 (Gas) 876+50 to 885+10		39	09-Jul-13	30-Aug-13	285	$135,945
G1 - 08 (Gas) 876+10 to 876+50		34	09-Jul-13	23-Aug-13	290	$0
G1 - 12 (Gas) 788+60 to 794+00		35	09-Jul-13	26-Aug-13	381	$48,961
G1 - 13 (Gas) 758+40 to 783+50		45	09-Jul-13	09-Sep-13	419	$242,381
G1 - 16 (Gas) 745+80 to 761+00		39	09-Jul-13	30-Aug-13	590	$141,156
G1 - 18 (Gas) 758+40 to 758+40		35	09-Jul-13	26-Aug-13	269	$42,721
G1 - 15 (Gas) 766+80 to 766+80		34	09-Jul-13	23-Aug-13	430	$0
G1 - 14 (Gas) 776+70 to 776+70		34	09-Jul-13	23-Aug-13	382	$0
Barnett Gathering		43	20-Jul-13	18-Sep-13	537	$222,415
ICMSUT1001	Start Barnett Gathering Utility Relocation	0	20-Jul-13		465	$0
G4 - 01 (Gas) 745+90 to 745+90		35	22-Jul-13	06-Sep-13	545	$12,185
G4 - 02 (Gas) 608+05/35W to 690+90/820		43	22-Jul-13	18-Sep-13	338	$210,230
Broadwing/Level 3		43	06-Jul-13	04-Sep-13	276	$135,064
3ALVL3MSUT100	Start Broadwing / Level 3 Utility Relocation	0	06-Jul-13		389	$0
FO3 - 01 (Fiber Optic) 809+00 to 815+50		42	09-Jul-13	04-Sep-13	276	$135,064

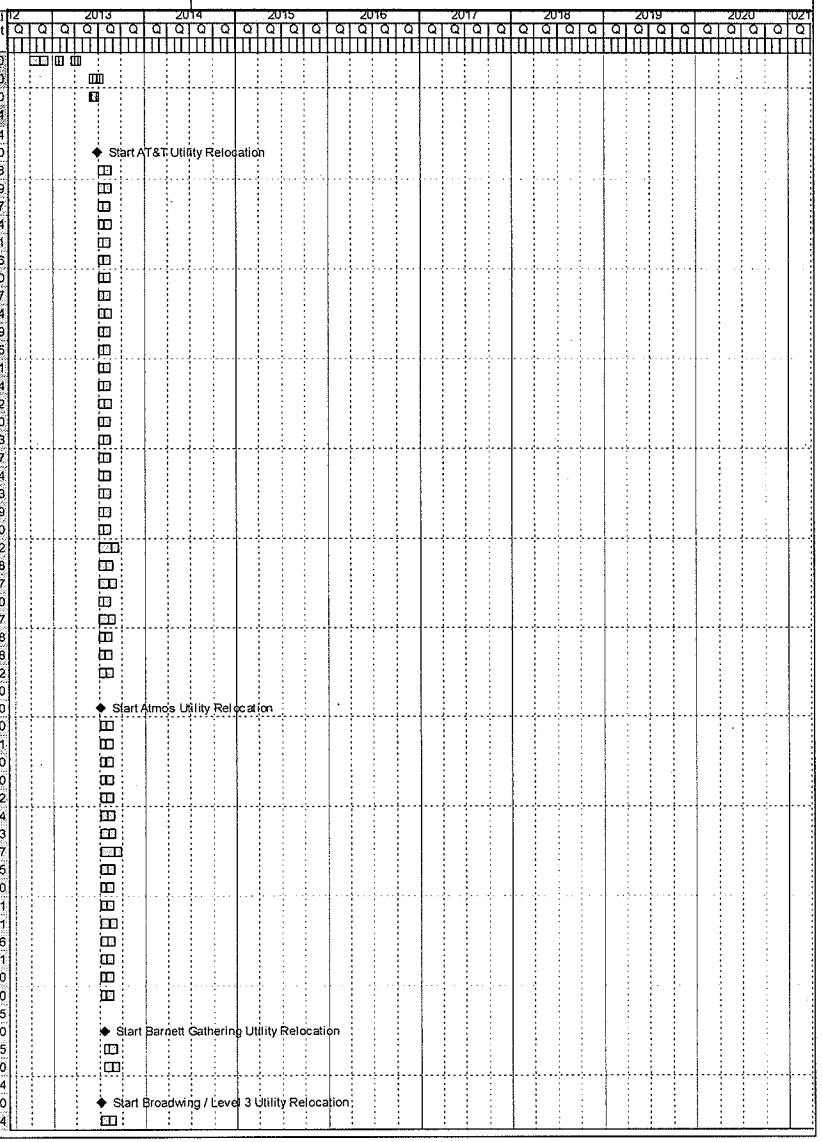

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Charter Communication		37	06-Jul-13	27-Aug-13	983	$258,420
3ACHARMSUT100	Start Charter Communication Utility Relocation	0	06-Jul-13		380	$0
OH - 13 (Cable TV) 916+00 to 917+80		34	09-Jul-13	23-Aug-13	344	$8,074
OH - 14 (Cable TV) 870+40 to 889+00		36	09-Jul-13	27-Aug-13	342	$48,153
OH - 18 (Cable TV) 860+50 to 866+00		36	09-Jul-13	27-Aug-13	342	$55,714
OH - 52 (Cable TV) 111+45 to 112+05		35	09-Jul-13	26-Aug-13	984	$44,887
OH - 31 (Fiber Optic) 766+30 to 771+00		34	09-Jul-13	23-Aug-13	430	$26,866
OH - 43 (Fiber Optic) 766+30 to 766+30		34	09-Jul-13	23-Aug-13	270	$31,637
OH - 9 (Cable TV) 902+50 to 913+00		35	09-Jul-13	26-Aug-13	289	$30,389
OH - 10 (Cable TV) 908+00 to 916+00		34	09-Jul-13	23-Aug-13	344	$12,699
Chevron		42	20-Jul-13	17-Sep-13	365	$168,830
3ACHEVMSUT1000	Start Chevron Utility Relocation	0	20-Jul-13		507	$0
PL5 - 01 (Gas) 784+00 to 810+00		42	22-Jul-13	17-Sep-13	365	$168,830
City of Fort Worth		73	28-Jun-13	08-Oct-13	953	$2,761,925
3ACFTWMSUT1000	Start City of Fort Worth Utility Relocation	0	28-Jun-13		364	$0
WI - 22 (Water) 771+10 to 771+10		35	01-Jul-13	16-Aug-13	268	$0
WI - 23 (Water) 766+80 to 766+80		35	01-Jul-13	16-Aug-13	268	$0
WI - 25 (Water) 758+40 to 758+40		35	01-Jul-13	16-Aug-13	268	$0
WI - 05 (Water) 875+00 to 887+30		48	01-Jul-13	04-Sep-13	336	$74,102
WI - 13 (Water) 866+30 to 866+90		35	01-Jul-13	16-Aug-13	349	$0
WI - 14 (Water) 863+80 to 864+30		35	01-Jul-13	16-Aug-13	349	$0
WI - 20 (Water) 741+00 to 783+50		72	01-Jul-13	08-Oct-13	398	$233,168
WI - 21 (Water) 776+30 to 776+30		35	01-Jul-13	16-Aug-13	387	$0
WI - 27 (Water) 742+00 to 743+00		35	01-Jul-13	16-Aug-13	600	$5,505
WI - 28 (Water) 730+00 to 731+80		40	01-Jul-13	23-Aug-13	288	$53,842
WI - 31 (Water) 680+50 to 681+40		35	01-Jul-13	16-Aug-13	268	$9,506
WI - 07 (Water) 883+90 to 884+30		35	01-Jul-13	16-Aug-13	349	$0
WI - 08 (Water) 881+10 to 881+50		35	01-Jul-13	16-Aug-13	349	$0
WI - 09 (Water) 876+00 to 876+80		35	01-Jul-13	16-Aug-13	349	$0
WI - 04 (Water) 885+10 to 888+00		41	01-Jul-13	26-Aug-13	259	$109,299
WI - 06 (Water) 863+50 to 885+10		52	01-Jul-13	10-Sep-13	278	$177,271
WI - 10 (Water) 860+40 to 875+00		48	01-Jul-13	04-Sep-13	336	$118,181
WI - 11 (Water) 874+40 to 874+80		35	01-Jul-13	16-Aug-13	295	$0
WI - 12 (Water) 869+50 to 868+00		36	01-Jul-13	19-Aug-13	294	$23,453
WI - 26 (Water) 755+60 to 755+60		40	01-Jul-13	23-Aug-13	270	$78,102
WI - 30 (Water) 681+40 to 686+40		39	01-Jul-13	22-Aug-13	596	$42,207
WI - 56 (Water) 107+80 to 109+95		36	01-Jul-13	19-Aug-13	989	$18,571
WI - 18 (Water) 785+70 to 796+40		42	01-Jul-13	27-Aug-13	380	$105,335
WI - 19 (Water) 785+70 to 785+70		37	01-Jul-13	20-Aug-13	385	$63,348
WI - 17 (Water) 801+40 to 801+40		37	01-Jul-13	20-Aug-13	350	$69,220
WWI - 04 (Wastewater) 925+00 to 926+10		36	01-Jul-13	19-Aug-13	534	$107,831
WWI - 28 (Wastewater) 756+30 to 759+00		36	01-Jul-13	19-Aug-13	599	$18,204
WWI - 06 (Wastewater) 911+20 to 921+00		41	01-Jul-13	26-Aug-13	343	$64,596
WWI - 08 (Wastewater) 914+80 to 914+80		41	01-Jul-13	26-Aug-13	259	$91,608
WWI - 11 (Wastewater) 862+00 to 889+70		57	01-Jul-13	17-Sep-13	327	$186,593
WWI - 12 (Wastewater) 887+90 to 888+60		35	01-Jul-13	16-Aug-13	349	$0
WWI - 13 (Wastewater) 875+50 to 875+80		35	01-Jul-13	16-Aug-13	349	$0
WWI - 14 (Wastewater) 869+60 to 869+60		35	01-Jul-13	16-Aug-13	295	$7,854
WWI - 16 (Wastewater) 867+60 to 868+10		35	01-Jul-13	16-Aug-13	349	$0
WWI - 18 (Wastewater) 865+10 to 865+50		35	01-Jul-13	16-Aug-13	349	$0
WWI - 20 (Wastewater) 805+00 to 806+20		41	01-Jul-13	26-Aug-13	283	$78,543
WWI - 25 (Wastewater) 758+60 to 777+00		52	01-Jul-13	10-Sep-13	418	$143,505
WWI - 26 (Wastewater) 776+60 to 776+60		35	01-Jul-13	16-Aug-13	387	$0
WWI - 27 (Wastewater) 771+20 to 771+20		35	01-Jul-13	16-Aug-13	435	$0
WWI - 29 (Wastewater) 744+50 to 753+50		44	01-Jul-13	29-Aug-13	541	$117,740
WWI - 32 (Wastewater) 732+50 to 736+50		37	01-Jul-13	20-Aug-13	433	$28,701
WWI - 21 (Wastewater) 794+00 to 795+10		35	01-Jul-13	16-Aug-13	387	$0
WWI - 22 (Wastewater) 794+20 to 794+20		35	01-Jul-13	16-Aug-13	387	$0
WWI - 35 (Wastewater) 674+55 to 695+00		40	01-Jul-13	23-Aug-13	568	$62,027
WWI - 61 (Wastewater) 107+80 to 109+95		36	01-Jul-13	19-Aug-13	572	$19,526

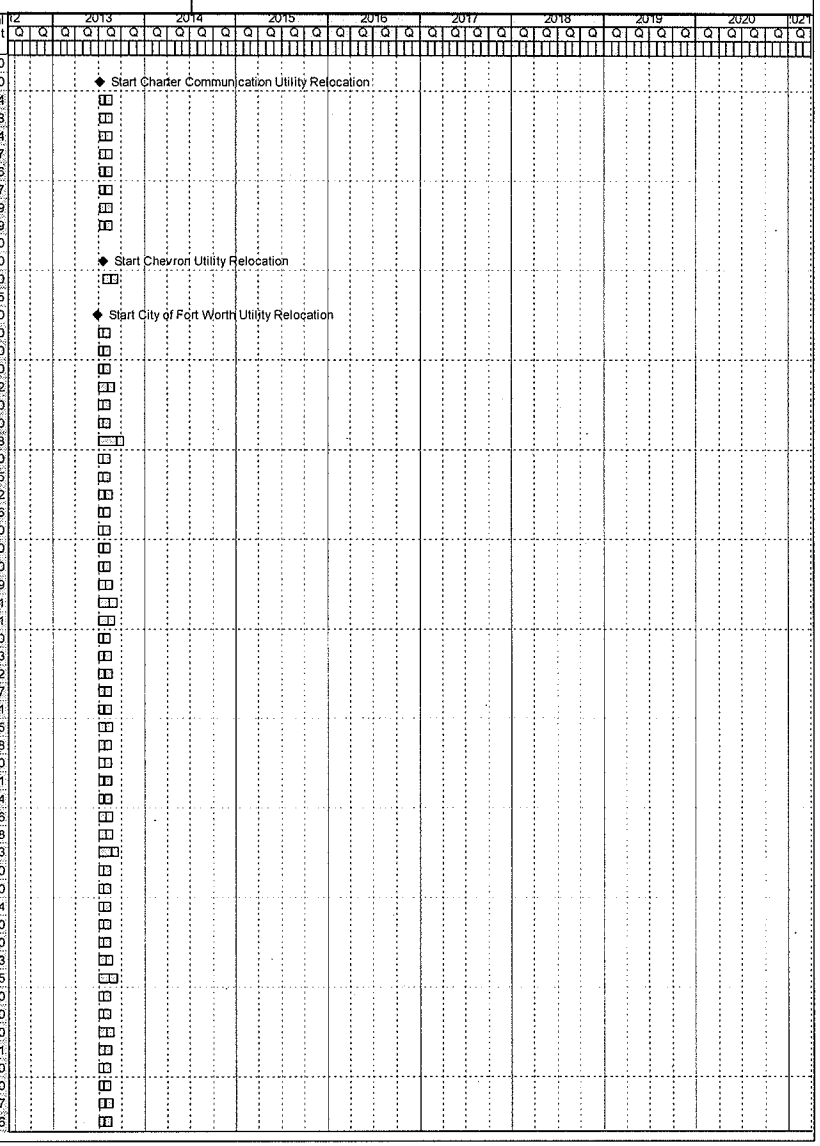

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
WW1 - 03 (Wastewater) 924+80 to 926+30		41	01-Jul-13	26-Aug-13	529	$88,672
W1 - 33 (Water) 673+80 to 673+80		39	01-Jul-13	22-Aug-13	569	$123,466
W1 - 35 (Water) 107+90 to 110+90		36	01-Jul-13	19-Aug-13	572	$37,198
WW1 - 10 (Wastewater) 903+10 to 904+00		39	01-Jul-13	22-Aug-13	291	$35,895
WW1 - 31 (Wastewater) 740+50 to 742+40		40	01-Jul-13	23-Aug-13	555	$80,433
WW1 - 30 (Wastewater) 741+00 to 751+25		42	01-Jul-13	27-Aug-13	261	$73,569
WW1 - 24 (Wastewater) 786+80 to 786+80		48	01-Jul-13	04-Sep-13	460	$125,374
WW1 - 23 (Wastewater) 794+00 to 794+00		35	01-Jul-13	16-Aug-13	387	$0
WW1 - 07 (Wastewater) 914+30 to 916+00		36	01-Jul-13	19-Aug-13	294	$24,077
WW1 - 34 (Wastewater) 730+50 to 732+60		40	01-Jul-13	23-Aug-13	288	$65,403
Energy Transfer		42	13-Jul-13	10-Sep-13	370	$389,483
3AENTRMSUT1003	Start Energy Transfer Utility Relocation	0	13-Jul-13		391	$0
PL3 - 03 (Gas) 784+00 to 810+00		42	15-Jul-13	10-Sep-13	370	$244,803
PL3 - 01 (Gas) 860+00 to 866+00		41	15-Jul-13	09-Sep-13	279	$144,680
Magellan Pipeline		35	06-Jul-13	23-Aug-13	270	$23,269
3AMAGEMSUT1004	Start Magellan Pipeline Utility Relocation	0	06-Jul-13		380	$0
PL11 - 01 (Gas) 758+45 to 768+00		34	09-Jul-13	23-Aug-13	270	$23,269
Oncor		168	28-Jun-13	18-Feb-14	858	$11,203,060
3AMSUT1003	Start Oncor Utility Relocation	0	28-Jun-13		181	$0
OH - 10 (Electric) 911+00 to 916+00		35	01-Jul-13	16-Aug-13	349	$27,894
OH - 12 (Electric) 911+00 to 914+00		41	01-Jul-13	26-Aug-13	343	$249,427
OH - 14 (Electric) 867+50 to 889+00		37	01-Jul-13	20-Aug-13	347	$93,333
OH - 17 (Electric) 868+55 to 870+70		40	01-Jul-13	23-Aug-13	290	$169,711
OH - 19 (Electric) 862+05 to 862+70		35	01-Jul-13	16-Aug-13	349	$0
OH - 20 (Electric) 857+50 to 862+00		35	01-Jul-13	16-Aug-13	349	$27,416
OH - 21 (Electric) 860+00 to 861+15		35	01-Jul-13	16-Aug-13	349	$13,470
OH - 22 (Electric) 832+50 to 839+85		36	01-Jul-13	19-Aug-13	758	$34,830
OH - 24 (Electric) 806+80 to 807+00		35	01-Jul-13	16-Aug-13	289	$0
OH - 26 (Electric) 794+50 to 794+50		35	01-Jul-13	16-Aug-13	352	$30,206
OH - 28 (Electric) 778+20 to 779+35		35	01-Jul-13	16-Aug-13	387	$10,478
OH - 29 (Electric) 776+20 to 778+20		35	01-Jul-13	16-Aug-13	352	$24,352
OH - 30 (Electric) 775+50 to 776+30		35	01-Jul-13	16-Aug-13	352	$24,352
OH - 31 (Electric) 762+90 to 776+35		36	01-Jul-13	19-Aug-13	434	$67,348
OH - 34 (Electric) 762+90 to 762+90		35	01-Jul-13	16-Aug-13	435	$0
OH - 35 (Electric) 755+60 to 758+35		35	01-Jul-13	16-Aug-13	435	$12,993
OH - 36 (Electric) 740+70 to 745+00		35	01-Jul-13	16-Aug-13	435	$20,205
OH - 37 (Electric) 727+20 to 729+65		39	01-Jul-13	22-Aug-13	289	$132,898
OH - 38 (Electric) 728+60 to 729+65		35	01-Jul-13	16-Aug-13	293	$0
OH - 7 (Electric) 913+00 to 921+00		36	01-Jul-13	19-Aug-13	294	$46,465
OH - 8 (Electric) 895+00 to 903+50		36	01-Jul-13	19-Aug-13	294	$55,916
OH - 27 (Electric) 788+25 to 794+00		35	01-Jul-13	16-Aug-13	387	$25,508
OH - 52 (Electric) 111+45 to 112+05		37	01-Jul-13	20-Aug-13	988	$104,858
OH - 103 (Electric) 784+00 to 810+00 - Complex Relocation		167	01-Jul-13	18-Feb-14	255	$1,519,467
OH - 104 (Electric) 688+30 to 688+30		35	01-Jul-13	16-Aug-13	297	$84,415
OH - 33 (Electric) 758+35 to 763+00		36	01-Jul-13	19-Aug-13	274	$823,081
OH - 100 (Electric) 755+25 to 757+00 - Complex Relocation		164	01-Jul-13	13-Feb-14	306	$1,266,223
E1 - 5 (Electric) 106+05 to 109+00		36	01-Jul-13	19-Aug-13	989	$45,768
OH - 15 (Electric) 861+80 to 884+25		39	01-Jul-13	22-Aug-13	291	$104,895
OH - 16 (Electric) 874+90 to 875+10		35	01-Jul-13	16-Aug-13	349	$0
E1 - 3 (Electric) 696+55 to 700+20		36	01-Jul-13	19-Aug-13	434	$53,622
OH - 105 (Electric) 687+60 to 687+60		35	01-Jul-13	16-Aug-13	297	$84,415
OH - 9 (Electric) 902+50 to 913+00		36	01-Jul-13	19-Aug-13	348	$53,402
OH - 11 (Electric) 913+80 to 915+30		35	01-Jul-13	16-Aug-13	295	$9,322
OH - 18 (Electric) 860+50 to 866+00		35	01-Jul-13	16-Aug-13	349	$18,571
OH - 25 (Electric) 793+30 to 796+05		35	01-Jul-13	16-Aug-13	387	$12,038
OH - 32 (Electric) 761+10 to 763+25		35	01-Jul-13	16-Aug-13	550	$9,322
OH - 42 (Electric) 678+65 to 696+55		36	01-Jul-13	19-Aug-13	434	$37,822
OH - 102 (Electric) 830+00 to 834+55 - Complex Relocation		164	01-Jul-13	13-Feb-14	630	$1,688,297
OH - 101 (Electric) 912+00 to 919+50 - Complex Relocation		164	01-Jul-13	13-Feb-14	136	$4,220,742
Qwest		40	13-Jul-13	06-Sep-13	278	$141,817

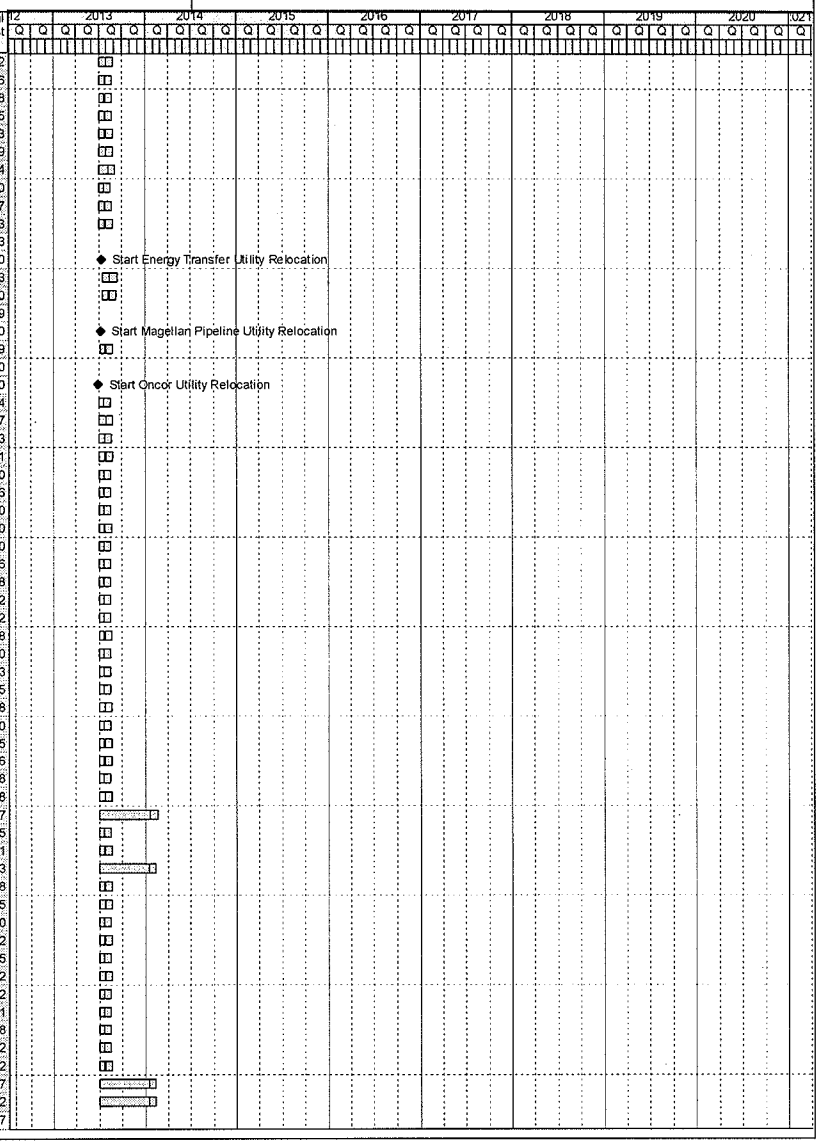

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AQWSTMSUT1000	Start Qwest Utility Relocation	0	13-Jul-13		391	$0
FO10 - 01 (Fiber Optic) 723+00 to 726+00		40	15-Jul-13	06-Sep-13	278	$141,817
Sprint		37	27-Jul-13	17-Sep-13	513	$81,038
3AMSUT1002	Start Sprint Utility Relocation	0	27-Jul-13		720	$0
FO14 - 01 (Fiber Optic) 921+00 to 921+00		37	29-Jul-13	17-Sep-13	513	$81,038
Texas Midstream		41	13-Jul-13	09-Sep-13	273	$156,351
3AMSUT1001	Start Texas Midstream Utility Relocation	0	13-Jul-13		383	$0
PL12 - 01 (Gas) 809+00 to 815+00		41	15-Jul-13	09-Sep-13	273	$156,351
Time Warner/Fiber Light		43	28-Jun-13	27-Aug-13	258	$202,596
3AMSUT1005	Start Time Warner / Fiber Light Utility Relocation	0	28-Jun-13		362	$0
FO9 - 01 (Fiber Optic) 912+30 to 916+70		42	01-Jul-13	27-Aug-13	258	$202,596
Verizon		47	20-Jul-13	24-Sep-13	508	$270,127
3AMSUT1000	Start Verizon Utility Relocation	0	20-Jul-13		712	$0
FO7 - 01 (Fiber Optic) 920+00 to 923+50		47	22-Jul-13	24-Sep-13	508	$270,127
Crosstex Energy		50	13-Jul-13	20-Sep-13	336	$376,490
ICMSUT1005	Start Crosstex Energy Utility Relocation	0	13-Jul-13		461	$0
G3 - 01 (Gas) 590+40/35W to 680+05/820		50	15-Jul-13	20-Sep-13	336	$376,490
Enterprisee Products		49	20-Jul-13	26-Sep-13	332	$540,255
ICMSUT1000	Start Enterprisee Products Utility Relocation	0	20-Jul-13		454	$0
G14 - 01 (Gas) 590+70/35W to 679+70/820		49	22-Jul-13	26-Sep-13	332	$540,255
Design		475	01-Oct-12	25-Jul-14	935	$71,355,000
NTE-3AIC-DSGN	Total Design Cost	475	01-Oct-12	25-Jul-14	935	$71,355,000
Preliminary Design		100	01-Oct-12	15-Feb-13	617	$0
Preliminary Design - Segment 3A		100	01-Oct-12	15-Feb-13	617	$0
Preliminary Design - Interchange		100	01-Oct-12	15-Feb-13	39	$0
Roadway Design		300	20-Oct-12	13-Dec-13	1078	$0
NTEIC-RDW	Start Roadway Design - Interchange	0	20-Oct-12		55	$0
NTE3A-RDW	Start Roadway Design - Segment 3A	0	20-Oct-12		410	$0
Roadway Design - Segment 3A		300	22-Oct-12	13-Dec-13	1061	$0
Roadway Design - Interchange		300	22-Oct-12	13-Dec-13	1078	$0
Bridge Design		460	20-Oct-12	25-Jul-14	887	$0
NTE3A-BRD	Start Bridge Design - Segment 3A	0	20-Oct-12		353	$0
IC1005	Start Bridge Design - Interchange	0	09-Mar-13		152	$0
Bridge Design - Segment 3A		460	22-Oct-12	25-Jul-14	887	$0
Bridge Design - Interchange		215	11-Mar-13	03-Jan-14	515	$0
Retaining Wall Design		315	20-Oct-12	03-Jan-14	1080	$0
NTE3AIC-RW1010	Start Retaining Wall Design - Segment 3A	0	20-Oct-12		554	$0
IC1000	Start Retaining Wall Design - Interchange	0	09-Mar-13		444	$0
Retaining Wall Design - Segment 3A		300	22-Oct-12	13-Dec-13	1095	$0
Retaining Wall Design - Interchange		215	11-Mar-13	03-Jan-14	712	$0
Procurement		210	22-Apr-13	07-Feb-14	276	$0
Segment 3A		210	22-Apr-13	07-Feb-14	276	$0
Shop Drawings		120	22-Apr-13	04-Oct-13	276	$0
Manufacture & Deliver		190	20-May-13	07-Feb-14	276	$0
Interchange		110	09-Sep-13	07-Feb-14	252	$0
Shop Drawings		20	09-Sep-13	04-Oct-13	252	$0
Manufacture & Deliver		90	07-Oct-13	07-Feb-14	252	$0
Permits		386	01-Oct-12	24-Mar-14	893	$0
Rail Road Permit		248	01-Oct-12	11-Sep-13	1031	$0
Rail Road Permit for Brige 205		248	01-Oct-12	11-Sep-13	256	$0
Rail Road Permit for Brige 206		248	01-Oct-12	11-Sep-13	948	$0
Rail Road Permit for Brige 207		248	01-Oct-12	11-Sep-13	654	$0
Rail Road Permit for Brige 208		248	01-Oct-12	11-Sep-13	533	$0
Rail Road Permit for Brige 209		248	01-Oct-12	11-Sep-13	1031	$0
Rail Road Permit for Brige 210		248	01-Oct-12	11-Sep-13	684	$0
Rail Road Permit for Brige 217		248	01-Oct-12	11-Sep-13	266	$0
Rail Road Permit for Brige 218		248	01-Oct-12	11-Sep-13	207	$0
Rail Road Permit for Brige 219		248	01-Oct-12	11-Sep-13	659	$0

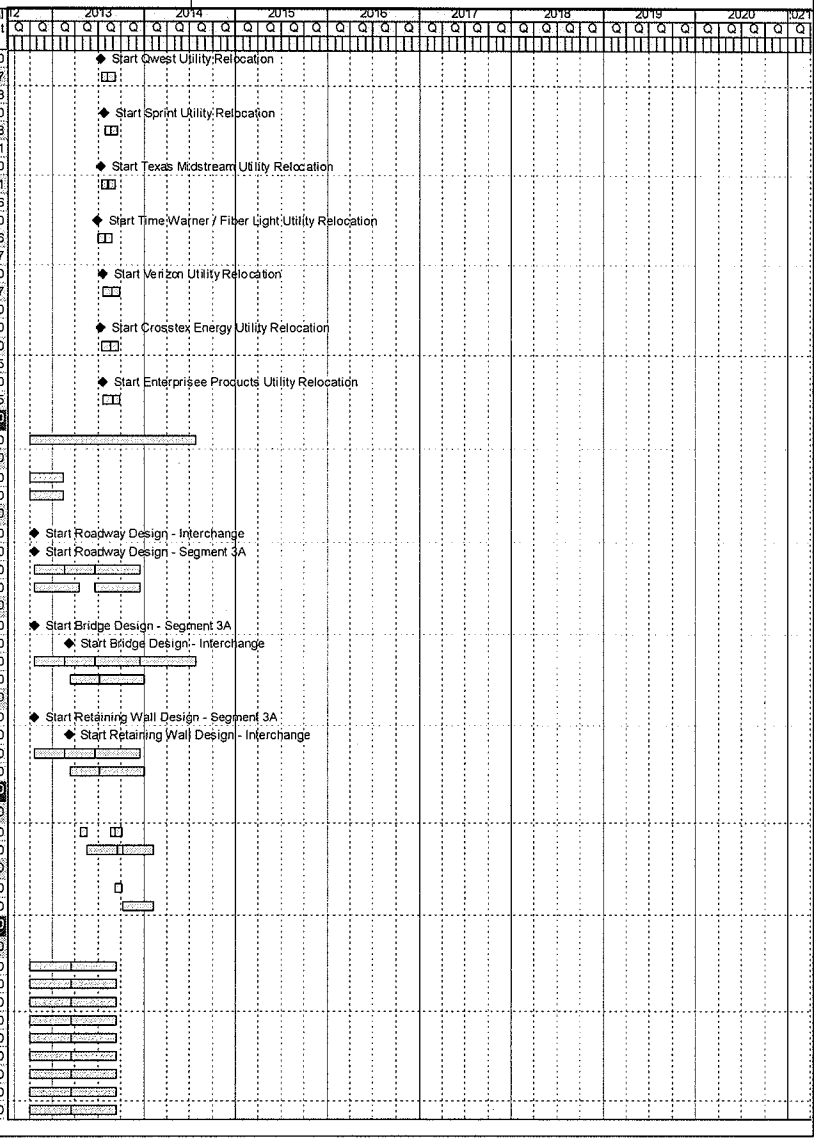

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Rail Road Permit for Brige 235		248	01-Oct-12	11-Sep-13	747	$0
Rail Road Permit for Brige 236		248	01-Oct-12	11-Sep-13	507	$0
US Army Corp Permit		540	01-Oct-12	24-Mar-14	463	$0
3ANBGPDT2241000	Preparation and application of Permit 404 and 408	180	01-Oct-12	29-Mar-13	463	$0
3ANBGPDT2241010	Review and Approval of US Army Corp Permit 404 and 408 (Bridge 224, 225 and 226)	360	30-Mar-13	24-Mar-14	463	$0
Construction		1248	20-Apr-13	31-Jan-18	37	$892,775,686
Segment 3A Construction		1248	20-Apr-13	31-Jan-18	37	$595,392,400
A132900	Base Construction Cost Over / Under	1248	22-Apr-13	31-Jan-18	37	$0
Phase 1		760	20-Apr-13	18-Mar-16	525	$170,844,858
3AMSMS11005	Segment 3A - Phase 1 Finish	0		03-Mar-16	4	$0
Stage 1		640	20-Apr-13	02-Oct-15	645	$137,910,617
3AMSMS111000	Segment 3A - Phase 1 Stage 1 Finish	0		08-Jul-15	4	$0
3AMSMS11000	Segment 3A - Phase 1 Stage 1 Misc Roadway Items Finish	0		02-Oct-15	905	$0
NBFR - Mecham to Dewey		215	22-Aug-14	18-Jun-15	721	$7,684,785
TCP & Temp Work		211	22-Aug-14	12-Jun-15	20	$172,818
Drainage		63	24-Sep-14	19-Jan-15	16	$868,095
Roadworks		142	16-Sep-14	12-Jun-15	16	$5,196,473
ITS / Signs / Stripes / Electrical / MISC.		58	31-Mar-15	18-Jun-15	721	$482,243
Noise Wall		2	26-Aug-14	27-Aug-14	227	$24,946
Retaining Wall RWN13-M1		0			0	$0
Retaining Wall RWN13-M2		0			0	$0
Retaining Wall RWN13-S		40	24-Sep-14	01-Dec-14	131	$940,909
NBFR - Dewey to S. of Trinity River		8	14-May-14	23-May-14	295	$195,286
TCP & Temp Work		8	14-May-14	23-May-14	295	$195,286
NBFR - S. of Trinity River to IH-30		236	22-Aug-14	17-Jul-15	700	$7,327,190
TCP & Temp Work		229	22-Aug-14	08-Jul-15	2	$270,747
Drainage		65	03-Oct-14	03-Feb-15	1	$979,735
Roadworks		166	29-Aug-14	09-Jul-15	1	$5,399,104
ITS / Signs / Stripes / Electrical / MISC.		62	23-Apr-15	17-Jul-15	700	$550,146
Noise Wall		2	27-Aug-14	28-Aug-14	226	$27,458
SBFR - Meacham to Dewey		291	22-Aug-14	02-Oct-15	645	$21,511,584
TCP & Temp Work		225	22-Aug-14	02-Jul-15	6	$818,349
Drainage		76	02-Oct-14	20-Feb-15	4	$2,077,698
Roadworks		163	29-Aug-14	02-Jul-15	4	$12,007,811
ITS / Signs / Stripes / Electrical / MISC.		116	24-Apr-15	02-Oct-15	645	$2,036,560
Noise Wall		3	29-Aug-14	02-Sep-14	223	$58,273
Retaining Wall RWS12		81	16-Sep-14	30-Jan-15	95	$4,158,187
Retaining Wall RWS32		20	19-Nov-14	28-Dec-14	118	$354,705
SBFR - Dewey to S. of Trinity River		185	22-Aug-14	07-May-15	761	$6,029,851
TCP & Temp Work		159	22-Aug-14	01-Apr-15	72	$498,082
Drainage		36	03-Nov-14	08-Jan-15	51	$431,611
Roadworks		101	26-Sep-14	01-Apr-15	51	$2,749,707
ITS / Signs / Stripes / Electrical / MISC.		58	17-Feb-15	07-May-15	751	$889,978
Noise Wall		2	26-Aug-14	27-Aug-14	227	$12,097
Retaining Wall RWS13B		0			0	$0
Retaining Wall RWS14		14	24-Dec-14	14-Jan-15	104	$106,409
Retaining Wall RWS16A		15	24-Dec-14	16-Jan-15	103	$218,013
Retaining Wall RWS20		47	24-Dec-14	11-Mar-15	71	$1,123,955
Retaining Wall RWS38		0			0	$0
SBFR - S. of Trinity River to IH-30		182	06-Sep-14	19-May-15	743	$4,624,007
TCP & Temp Work		176	06-Sep-14	11-May-15	44	$106,874
Drainage		49	20-Oct-14	19-Jan-15	32	$632,987
Roadworks		118	30-Sep-14	11-May-15	32	$3,479,119
ITS / Signs / Stripes / Electrical / MISC.		49	13-Mar-15	19-May-15	743	$387,282
Noise Wall		2	11-Sep-14	12-Sep-14	215	$17,745
NBGP - Dewey to S. of Trinity River		76	06-Sep-14	22-Dec-14	849	$0
TCP & Temp Work		70	06-Sep-14	12-Dec-14	150	$0
Drainage		8	29-Sep-14	08-Oct-14	109	$0
Roadworks		46	22-Sep-14	12-Dec-14	109	$0

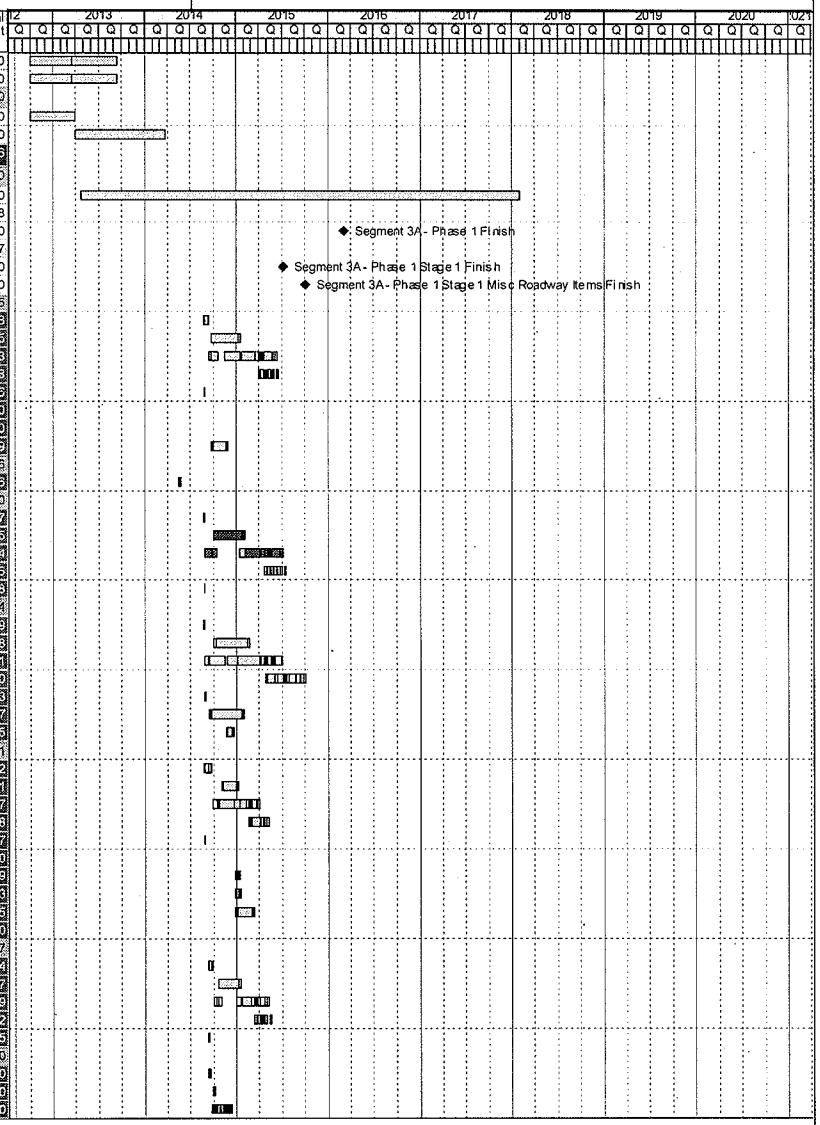

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	ITS / Signs / Stripes / Electrical / MISC.	42	24-Oct-14	22-Dec-14	849	$0
	Noise Wall	5	16-Sep-14	22-Sep-14	209	$0
	NBRP - Meacham to Dewey	23	20-Apr-13	22-May-13	557	$639,616
	TCP & Temp Work	23	20-Apr-13	22-May-13	557	$639,616
	NBRP - Dewey to S. of Trinity River	21	20-Apr-13	20-May-13	559	$597,669
	TCP & Temp Work	21	20-Apr-13	20-May-13	559	$597,669
	SBGP - Meacham to Dewey	225	22-Aug-14	02-Jul-15	711	$13,671,275
	TCP & Temp Work	225	22-Aug-14	02-Jul-15	6	$393,814
	Drainage	24	18-Sep-14	28-Oct-14	39	$529,046
	Roadworks	128	29-Aug-14	23-Apr-15	39	$5,141,971
	ITS / Signs / Stripes / Electrical / MISC.	81	02-Mar-15	22-Jun-15	719	$1,021,431
	Noise Wall	3	28-Aug-14	01-Sep-14	224	$42,539
	B205 - SB 35W GP over FWWR	220	29-Aug-14	02-Jul-15	6	$4,879,185
	Retaining Wall RWS05	0			0	$0
	Retaining Wall RWS08	58	24-Oct-14	30-Jan-15	95	$1,663,289
	SBRP - Meacham to Dewey	224	22-Aug-14	01-Jul-15	712	$17,021,965
	TCP & Temp Work	224	22-Aug-14	01-Jul-15	7	$428,955
	Drainage	24	30-Sep-14	07-Nov-14	91	$428,691
	Roadworks	65	19-Sep-14	16-Jan-15	91	$2,554,210
	ITS / Signs / Stripes / Electrical / MISC.	36	05-Dec-14	23-Jan-15	825	$243,273
	Noise Wall	2	26-Aug-14	27-Aug-14	227	$8,201
	B202 - SB 35W GP Ramp to SB 35W ML	204	19-Sep-14	01-Jul-15	7	$8,376,384
	B-XXX - FR to GPL Entrance (TBD)	203	19-Sep-14	30-Jun-15	8	$1,993,571
	Retaining Wall RWS33	0			0	$0
	Retaining Wall RWS04	21	08-Oct-14	11-Nov-14	141	$418,316
	Retaining Wall RWS05	21	08-Oct-14	11-Nov-14	141	$0
	Retaining Wall RWMB01	21	08-Oct-14	11-Nov-14	141	$0
	Retaining Wall RWMB02	21	08-Oct-14	11-Nov-14	141	$0
	Retaining Wall RWS02A	17	08-Oct-14	04-Nov-14	145	$318,678
	Retaining Wall RW02B	11	08-Oct-14	27-Oct-14	151	$42,628
	Retaining Wall RWS07	82	08-Oct-14	24-Feb-15	80	$2,209,078
	NSML - Dewey to S. of Trinity River	375	20-Apr-13	26-Sep-14	910	$21,617,973
	TCP & Temp Work	375	20-Apr-13	26-Sep-14	205	$304,591
	Drainage	30	11-Jun-13	31-Jul-13	299	$537,245
	Roadworks	146	20-May-13	10-Feb-14	275	$5,184,037
	ITS / Signs / Stripes / Electrical / MISC.	62	13-Dec-13	10-Mar-14	1054	$740,619
	Noise Wall	2	26-Apr-13	29-Apr-13	574	$33,572
	B218 - 35W ML over UPRR	271	13-Sep-13	26-Sep-14	205	$12,783,485
	Retaining Wall RWN15A-S	0			0	$0
	Retaining Wall RWS15-S	77	31-May-13	02-Oct-13	382	$2,024,424
	SBRP - Dewey to S. of Trinity River	133	22-Aug-14	24-Feb-15	803	$2,673,569
	TCP & Temp Work	130	22-Aug-14	19-Feb-15	101	$728,696
	Drainage	20	31-Oct-14	09-Dec-14	73	$223,463
	Roadworks	75	02-Oct-14	19-Feb-15	73	$1,116,785
	ITS / Signs / Stripes / Electrical / MISC.	34	08-Jan-15	24-Feb-15	803	$91,293
	Noise Wall	2	26-Aug-14	27-Aug-14	227	$8,477
	Retaining Wall RWS16	0			0	$0
	Retaining Wall RWS17A	12	24-Nov-14	15-Dec-14	123	$145,801
	Retaining Wall RW17B	0			0	$0
	Retaining Wall RWS18	19	24-Nov-14	26-Dec-14	116	$361,054
	XRDS - SH 183/NE 28th St.	47	20-Apr-13	25-Jun-13	533	$1,358,033
	TCP & Temp Work	47	20-Apr-13	25-Jun-13	533	$441,157
	Retaining Wall RW07A	24	16-May-13	25-Jun-13	444	$405,799
	Retaining Wall RW08A-S	22	16-May-13	21-Jun-13	446	$249,493
	Retaining Wall RW08B-S	22	16-May-13	21-Jun-13	446	$261,584
	XRDS - Spur 280	275	20-Apr-13	09-May-14	1010	$17,514,240
	TCP & Temp Work	275	20-Apr-13	09-May-14	305	$135,374
	Drainage	63	11-Jun-13	26-Sep-13	272	$885,615
	Roadworks	149	20-May-13	14-Feb-14	272	$2,463,096
	ITS / Signs / Stripes / Electrical / MISC.	59	03-Dec-13	21-Feb-14	1065	$471,331

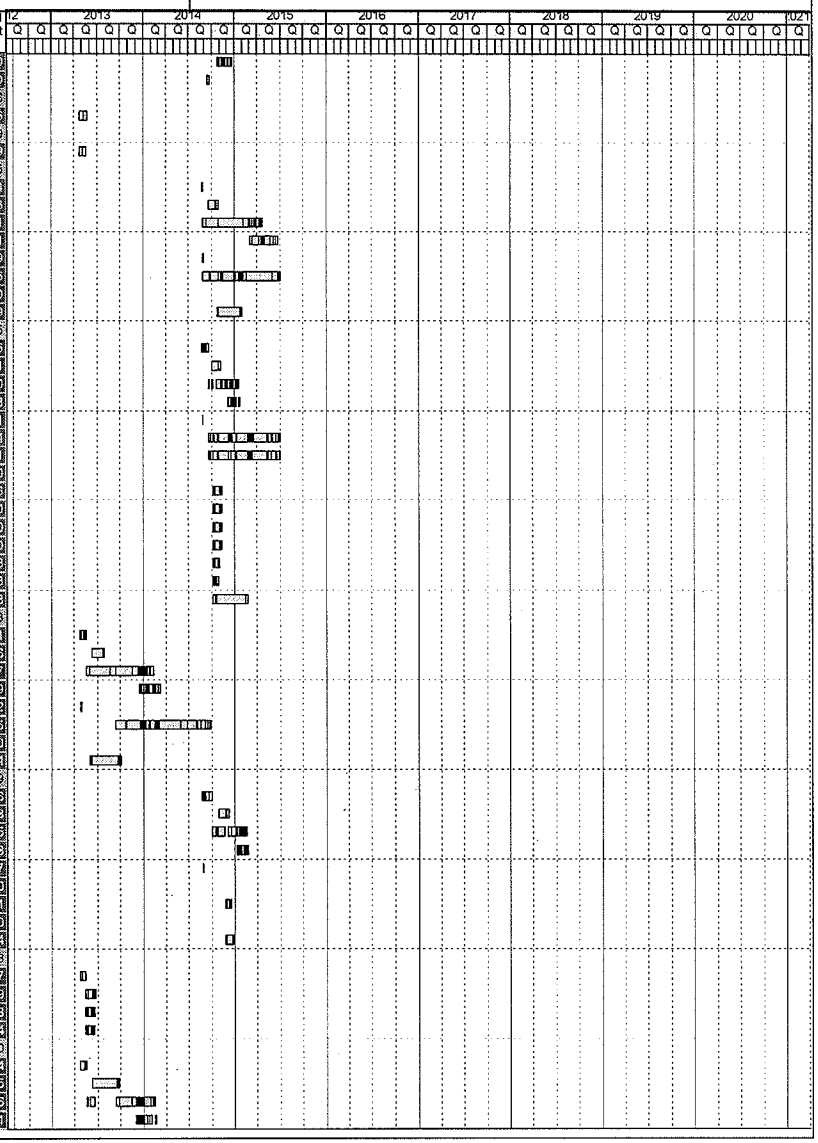

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Noise Wall	2	24-Apr-13	25-Apr-13	576	$24,255
	B237 - Spur 280 over 35W	255	20-May-13	09-May-14	305	$8,802,733
	Retaining Wall RW280S1	22	24-Jun-13	26-Jul-13	424	$446,436
	Retaining Wall RW280N1	22	24-Jun-13	26-Jul-13	424	$447,477
	Retaining Wall RW280N2-M	24	24-Jun-13	30-Jul-13	422	$464,737
	Retaining Wall RW280N2-S	62	31-May-13	09-Sep-13	397	$1,581,925
	Retaining Wall RWN27	42	31-May-13	06-Aug-13	417	$635,200
	Retaining Wall RWS28	45	31-May-13	09-Aug-13	414	$954,052
	SBGP - Dewey to S. of Trinity River	210	22-Aug-14	11-Jun-15	726	$13,399,042
	TCP & Temp Work	210	22-Aug-14	11-Jun-15	5	$220,609
	Drainage	16	30-Sep-14	24-Oct-14	61	$298,607
	Roadworks	110	12-Sep-14	02-Apr-15	37	$3,475,827
	ITS / Signs / Stripes / Electrical / MISC.	50	20-Feb-15	30-Apr-15	756	$592,687
	Noise Wall	2	26-Aug-14	27-Aug-14	211	$23,864
	Retaining Wall RWS21	0			0	$0
	B217 - SB 35W GP over UPRR	195	12-Sep-14	11-Jun-15	5	$8,789,447
	XRDS - Yucca Av./Northside Dr.	110	20-Apr-13	20-Sep-13	1175	$2,044,533
	TCP & Temp Work	105	20-Apr-13	13-Sep-13	476	$135,392
	Drainage	23	28-May-13	09-Jul-13	355	$269,007
	Roadworks	72	08-May-13	13-Sep-13	355	$1,155,908
	ITS / Signs / Stripes / Electrical / MISC.	33	07-Aug-13	20-Sep-13	1175	$97,361
	Noise Wall	4	26-Apr-13	01-May-13	572	$7,541
	Retaining Wall RW2CA	26	25-Jun-13	30-Jul-13	508	$378,325
	Stage 2	760	20-Apr-13	18-Mar-16	525	$32,934,241
3AMSMS121000	Segment 3A- Phase 1 Stage 2 Finish	0		03-Mar-16	4	$0
3AMS21000	Segment 3A- Phase 1 Stage 2 Misc Roadway Items Finish	0		18-Mar-16	737	$0
	SBGP - S. of Trinity River to IH-30	10	09-Jul-15	22-Jul-15	163	$277,725
	TCP & Temp Work	10	09-Jul-15	22-Jul-15	163	$277,725
	NBGP - S. of Trinity River to IH-30	38	09-Jul-15	31-Aug-15	135	$1,246,646
	TCP & Temp Work	38	09-Jul-15	31-Aug-15	135	$1,246,646
	NBFR - Meacham to Dewey	182	09-Jul-15	18-Mar-16	525	$7,684,785
	TCP & Temp Work	171	09-Jul-15	03-Mar-16	2	$172,818
	Drainage	45	05-Aug-15	23-Oct-15	2	$668,095
	Roadworks	123	20-Jul-15	03-Mar-16	2	$5,196,473
	ITS / Signs / Stripes / Electrical / MISC.	53	06-Jan-16	18-Mar-16	525	$482,243
	Noise Wall	2	14-Jul-15	15-Jul-15	166	$24,346
	Retaining Wall RWN13-M1	0			0	$0
	Retaining Wall RWN13-M2	0			0	$0
	Retaining Wall RWN13-S	40	28-Jul-15	29-Sep-15	92	$940,809
	SBFR - Dewey to S. of Trinity River	81	09-Jul-15	29-Oct-15	626	$911,258
	TCP & Temp Work	71	09-Jul-15	15-Oct-15	102	$22,562
	Drainage	11	06-Aug-15	24-Aug-15	75	$86,322
	Roadworks	45	28-Jul-15	16-Oct-15	75	$549,941
	ITS / Signs / Stripes / Electrical / MISC.	38	08-Sep-15	29-Oct-15	626	$143,604
	Noise Wall	5	20-Jul-15	24-Jul-15	161	$2,419
	Retaining Wall RWS14	13	18-Aug-15	04-Sep-15	105	$106,409
	NBFR - Dewey to S. of Trinity River	140	09-Jul-15	20-Jan-16	567	$5,552,590
	TCP & Temp Work	140	09-Jul-15	20-Jan-16	33	$80,166
	Drainage	16	19-Aug-15	16-Sep-15	57	$162,498
	Roadworks	62	29-Jul-15	18-Nov-15	57	$1,173,376
	ITS / Signs / Stripes / Electrical / MISC.	32	13-Oct-15	25-Nov-15	607	$54,509
	Noise Wall	2	15-Jul-15	16-Jul-15	167	$4,590
	Retaining Wall RWN32	94	11-Aug-15	20-Jan-16	29	$4,097,481
	SBFR - Meacham to Dewey	148	09-Jul-15	01-Feb-16	25	$4,158,187
	Retaining Wall RWS12	148	09-Jul-15	01-Feb-16	25	$4,158,187
	SBFR - S. of Trinity River to IH-30	85	06-Sep-14	02-Jan-15	840	$1,198,193
	TCP & Temp Work	76	03-Sep-14	22-Dec-14	148	$28,500
	Drainage	10	06-Oct-14	22-Oct-14	107	$168,797
	Roadworks	50	23-Sep-14	22-Dec-14	107	$927,765
	ITS / Signs / Stripes / Electrical / MISC.	39	11-Nov-14	02-Jan-15	840	$68,399

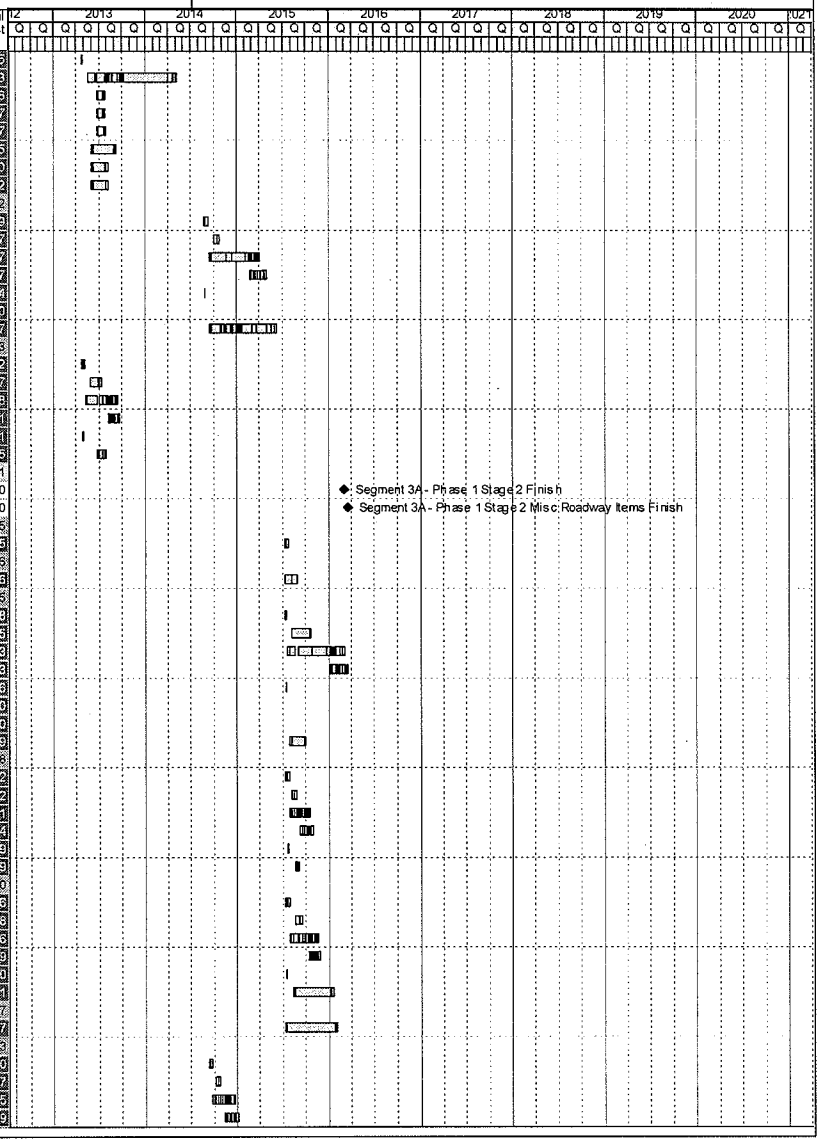

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Noise Wall	5	16-Sep-14	22-Sep-14	210	$4,732
	NBRP - Meacham to Dewey	58	09-Jul-15	28-Sep-15	649	$244,273
	TCP & Temp Work	54	09-Jul-15	22-Sep-15	119	$9,025
	Drainage	9	27-Jul-15	07-Aug-15	88	$45,909
	Roadworks	37	20-Jul-15	22-Sep-15	88	$170,578
	ITS / Signs / Stripes / Electrical / MISC.	31	17-Aug-15	28-Sep-15	649	$17,430
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$1,331
	XRDS - SH 183/NE 28th St.	295	20-Apr-13	06-Jun-14	990	$8,470,810
	TCP & Temp Work	295	20-Apr-13	06-Jun-14	456	$135,374
	Drainage	55	07-Jun-13	09-Sep-13	421	$747,965
	Roadworks	131	16-May-13	08-Jan-14	421	$3,197,426
	ITS / Signs / Stripes / Electrical / MISC.	62	04-Nov-13	14-Jan-14	1093	$404,974
	Noise Wall	2	24-Apr-13	25-Apr-13	747	$20,944
	B214 - SH 183/NE 28th Street over 35W	277	16-May-13	06-Jun-14	456	$3,984,127
	XRDS - Yucca Av./Northside Dr.	164	09-Jul-15	23-Feb-16	543	$3,189,776
	TCP & Temp Work	161	09-Jul-15	18-Feb-16	12	$93,347
	Drainage	40	17-Aug-15	28-Oct-15	10	$522,190
	Roadworks	103	07-Aug-15	18-Feb-16	10	$2,243,821
	ITS / Signs / Stripes / Electrical / MISC.	52	14-Dec-15	23-Feb-16	543	$319,780
	Noise Wall	2	20-Jul-15	21-Jul-15	164	$14,638
Phase 2		214	12-Jun-15	06-Apr-16	512	$81,182,862
3AMSMS21000	Segment 3A- Phase 2 Finish	0		07-Mar-16	0	$0
Stage 1		214	12-Jun-15	06-Apr-16	512	$40,554,527
3AMSMS211000	Segment 3A- Phase 2 Stage 1 Finish	0		29-Feb-16	7	$0
3AMS1003	Segment 3A- Phase 2 Stage 1 Misc Roadway Items Finish	0		06-Apr-16	718	$0
	SBRP - Meacham to Dewey	62	09-Jul-15	02-Oct-15	111	$1,500,285
	TCP & Temp Work	62	09-Jul-15	02-Oct-15	111	$608,730
	Retaining Wall RWS10	35	06-Aug-15	02-Oct-15	91	$891,556
	SBGP - Meacham to Dewey	188	09-Jul-15	28-Mar-16	519	$8,604,152
	TCP & Temp Work	153	09-Jul-15	08-Feb-16	20	$1,478,704
	Drainage	18	28-Aug-15	02-Oct-15	15	$363,719
	Roadworks	95	13-Aug-15	08-Feb-16	15	$3,535,105
	ITS / Signs / Stripes / Electrical / MISC.	64	30-Dec-15	28-Mar-16	519	$694,059
	Noise Wall	2	15-Jul-15	16-Jul-15	167	$29,246
	B208 - SB 35W GP over BNSF	116	13-Aug-15	21-Jan-16	32	$2,503,319
	SBGP - S. of Trinity River to IH-30	195	09-Jul-15	06-Apr-16	512	$13,147,446
	TCP & Temp Work	168	09-Jul-15	29-Feb-16	5	$519,722
	Drainage	17	03-Aug-15	28-Aug-15	4	$528,120
	Roadworks	117	27-Jul-15	29-Feb-16	4	$4,950,448
	ITS / Signs / Stripes / Electrical / MISC.	73	28-Dec-15	06-Apr-16	512	$991,015
	Noise Wall	3	17-Jul-15	21-Jul-15	164	$42,453
	B234 - SB 35W GP over 4th St.	111	27-Jul-15	28-Dec-15	50	$1,593,121
	B236 - SB 35W GP over RR (922+00)	138	27-Jul-15	03-Feb-16	23	$2,420,891
	B230 - SB 35W GP over Pharr/TX121	78	11-Sep-15	29-Dec-15	49	$669,488
	Retaining Wall RWS26-M	0			0	$0
	Retaining Wall RWS30	9	27-Aug-15	09-Sep-15	103	$76,792
	Retaining Wall RWS31	48	27-Aug-15	18-Nov-15	64	$1,255,416
	SBRP - Dewey to S. of Trinity River	80	09-Jul-15	28-Oct-15	627	$876,749
	TCP & Temp Work	74	09-Jul-15	20-Oct-15	99	$37,905
	Drainage	14	07-Aug-15	28-Aug-15	72	$130,353
	Roadworks	50	24-Jul-15	20-Oct-15	72	$651,458
	ITS / Signs / Stripes / Electrical / MISC.	33	14-Sep-15	28-Oct-15	627	$53,254
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$3,779
	NBRP - Dewey to S. of Trinity River	0			0	$0
	Retaining Wall RWN16-M	0			0	$0
	Retaining Wall RWN16-S	0			0	$0
	SBGP - Dewey to S. of Trinity River	186	12-Jun-15	26-Feb-16	540	$11,837,743
	TCP & Temp Work	186	12-Jun-15	26-Feb-16	6	$747,380
	Drainage	14	13-Jul-15	03-Aug-15	60	$242,678
	Roadworks	98	24-Jun-15	22-Dec-15	41	$2,843,859

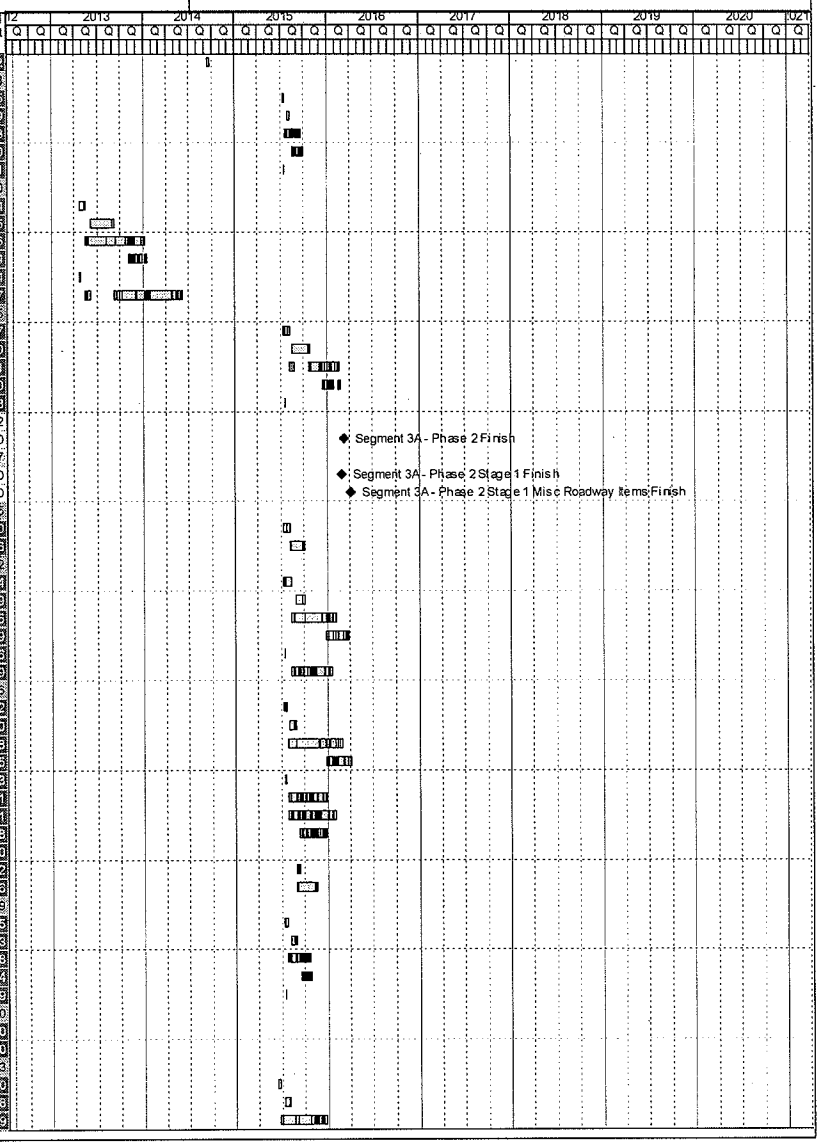

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	ITS / Signs / Stripes / Electrical / MISC.	45	04-Nov-15	05-Jan-16	578	$401,700
	Noise Wall	2	16-Jun-15	17-Jun-15	188	$19,525
	B226 - SB 35W GP over Trinity River	178	24-Jun-15	26-Feb-16	6	$7,582,601
	SBRP - S. of Trinity River to IH-30	144	09-Jul-15	26-Jan-16	563	$4,270,610
	TCP & Temp Work	137	09-Jul-15	15-Jan-16	36	$1,177,530
	Drainage	25	22-Sep-15	04-Nov-15	27	$291,347
	Roadworks	66	11-Sep-15	15-Jan-16	27	$908,082
	ITS / Signs / Stripes / Electrical / MISC.	38	04-Dec-15	26-Jan-16	563	$253,496
	Noise Wall	2	15-Jul-15	16-Jul-15	167	$8,457
	Retaining Wall RWS25	49	28-Sep-15	22-Dec-15	45	$1,180,441
	Retaining Wall RWS27	15	28-Sep-15	21-Oct-15	79	$270,296
	Retaining Wall RWS29	14	28-Sep-15	20-Oct-15	80	$180,961
	XRDS - Meacham Blvd.	17	10-Jul-15	05-Aug-15	126	$317,541
	Retaining Wall RW10A	17	10-Jul-15	05-Aug-15	126	$317,541
	Stage 2	214	12-Jun-15	06-Apr-16	512	$9,747,839
3AMSMS221000	Segment 3A- Phase 2 Stage 2 Finish	0		22-Jan-16	45	$0
3AMSRD1001	Segment 3A- Phase 2 Stage 2 Misc Roadway Items Finish	0		06-Apr-16	718	$0
	SBGP - Meacham to Dewey	63	09-Jul-15	05-Oct-15	644	$121,026
	TCP & Temp Work	57	09-Jul-15	25-Sep-15	116	$24,813
	Drainage	7	31-Jul-15	11-Aug-15	85	$33,065
	Roadworks	34	29-Jul-15	25-Sep-15	85	$321,379
	ITS / Signs / Stripes / Electrical / MISC.	31	24-Aug-15	05-Oct-15	644	$39,317
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$2,659
	SBGP - Dewey to S. of Trinity River	161	12-Jun-15	22-Jan-16	565	$5,214,423
	TCP & Temp Work	161	12-Jun-15	22-Jan-16	31	$140,389
	Drainage	12	24-Jul-15	11-Aug-15	67	$188,750
	Roadworks	81	07-Jul-15	01-Dec-15	51	$2,211,890
	ITS / Signs / Stripes / Electrical / MISC.	35	23-Oct-15	10-Dec-15	556	$341,496
	Noise Wall	2	16-Jun-15	17-Jun-15	188	$15,186
	B221 - SB 35W GP over Northside Dr/Yucca Ave	144	07-Jul-15	22-Jan-16	31	$2,316,713
	Retaining Wall RWS23	0			0	$0
	SBRP - S. of Trinity River to IH-30	93	09-Jul-15	02-Nov-15	624	$710,423
	TCP & Temp Work	78	09-Jul-15	26-Oct-15	95	$45,125
	Drainage	15	07-Aug-15	31-Aug-15	69	$145,673
	Roadworks	48	31-Jul-15	26-Oct-15	69	$494,041
	ITS / Signs / Stripes / Electrical / MISC.	32	18-Sep-15	02-Nov-15	624	$61,356
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$4,229
	SBGP - S. of Trinity River to IH-30	72	09-Jul-15	16-Oct-15	635	$1,076,947
	TCP & Temp Work	67	09-Jul-15	09-Oct-15	1	$96,999
	Drainage	4	05-Aug-15	10-Aug-15	3	$88,020
	Roadworks	40	30-Jul-15	09-Oct-15	1	$625,075
	ITS / Signs / Stripes / Electrical / MISC.	33	02-Sep-15	16-Oct-15	635	$99,777
	Noise Wall	2	14-Jul-15	15-Jul-15	83	$7,076
	SBRP - Meacham to Dewey	71	09-Jul-15	15-Oct-15	636	$1,727,092
	TCP & Temp Work	65	09-Jul-15	07-Oct-15	108	$18,602
	Drainage	10	03-Aug-15	18-Aug-15	80	$112,814
	Roadworks	40	28-Jul-15	07-Oct-15	80	$672,161
	ITS / Signs / Stripes / Electrical / MISC.	36	27-Aug-15	15-Oct-15	636	$29,602
	Noise Wall	2	14-Jul-15	15-Jul-15	169	$2,158
	Retaining Wall RWS10	35	03-Aug-15	28-Sep-15	93	$891,555
	NBRP - Dewey to S. of Trinity River	0			0	$0
	Retaining Wall RWN16-M	0			0	$0
	SBRP - Dewey to S. of Trinity River	13	10-Jul-15	28-Jul-15	159	$145,801
	Retaining Wall RWS16	0			0	$0
	Retaining Wall RWS17A	12	10-Jul-15	28-Jul-15	131	$145,801
	XRDS - SH 183/NE 28th St.	17	10-Jul-15	05-Aug-15	126	$452,125
	Retaining Wall RW21A	15	10-Jul-15	31-Jul-15	120	$176,837
	Retaining Wall RW21B	17	10-Jul-15	05-Aug-15	126	$276,269
	Stage 3	195	09-Jul-15	06-Apr-16	512	$30,880,497
3AMSMS231000	Segment 3A- Phase 2 Stage 3 Finish	0		07-Mar-16	0	$0

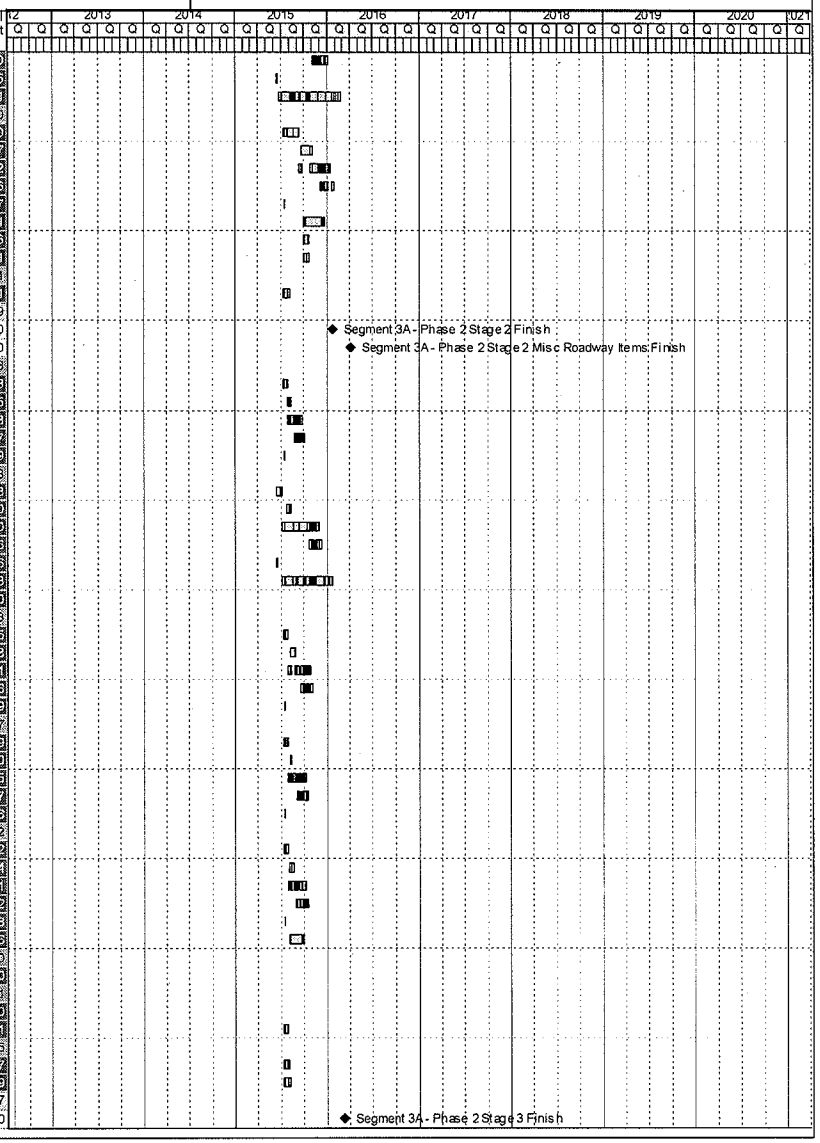

SUMMARY SCHEDULE — NTE - Segment 3A Interchange Project - FBS # 1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AMSRD1000	Segment 3A- Phase 2 Stage 3 Misc Roadway Items Finish	0		06-Apr-16	718	$0
NBRP - Meacham to Dewey		17	09-Jul-15	31-Jul-15	156	$544,858
TCP & Temp Work		17	09-Jul-15	31-Jul-15	156	$544,858
NBRP - Dewey to S. of Trinity River		0			0	$0
Retaining Wall RWN16-S		0			0	$0
NBGP - Meacham to Dewey		22	09-Jul-15	07-Aug-15	151	$701,664
TCP & Temp Work		22	09-Jul-15	07-Aug-15	151	$701,664
NBFR - Dewey to S. of Trinity River		46	09-Jul-15	10-Sep-15	127	$1,475,492
TCP & Temp Work		46	09-Jul-15	10-Sep-15	127	$1,475,492
NBGP - Dewey to S of Trinity River		54	09-Jul-15	22-Sep-15	119	$1,658,125
TCP & Temp Work		54	09-Jul-15	22-Sep-15	119	$1,658,125
SBGP - Meacham to Dewey		140	09-Jul-15	20-Jan-16	567	$9,257,340
TCP & Temp Work		140	09-Jul-15	20-Jan-16	33	$2,689,976
Drainage		11	27-Aug-15	16-Sep-15	48	$165,327
Roadworks		59	21-Aug-15	10-Dec-15	46	$1,606,896
ITS / Signs / Stripes / Electrical / MISC.		38	30-Oct-15	22-Dec-15	598	$327,371
Noise Wall		2	14-Jul-15	15-Jul-15	168	$13,293
B240 - SB 35W GP over Meacham		101	21-Aug-15	08-Jan-16	41	$1,482,075
Retaining Wall RWS01A		49	14-Sep-15	10-Dec-15	52	$1,212,420
Retaining Wall RWS02		72	14-Sep-15	20-Jan-16	29	$1,760,011
SBFR - Meacham to Dewey		112	10-Jul-15	15-Jan-16	31	$4,284,037
Retaining Wall RWS12		112	10-Jul-15	15-Jan-16	31	$4,284,037
SBGP - S. of Trinity River to IH-30		106	10-Oct-15	07-Mar-16	534	$3,053,997
TCP & Temp Work		106	10-Oct-15	07-Mar-16	0	$56,999
Drainage		9	10-Nov-15	25-Nov-15	24	$88,020
Roadworks		42	03-Nov-15	22-Jan-16	24	$825,075
ITS / Signs / Stripes / Electrical / MISC.		29	23-Dec-15	01-Feb-16	559	$99,777
Noise Wall		2	14-Oct-15	15-Oct-15	102	$7,076
B236 - SB 35W GP over RR (922+00)		90	03-Nov-15	07-Mar-16	0	$1,192,379
B234 - SB 35W GP over 4th St		78	03-Nov-15	18-Feb-16	12	$784,671
SBRP - Meacham to Dewey		73	09-Jul-15	19-Oct-15	634	$1,598,622
TCP & Temp Work		68	09-Jul-15	12-Oct-15	105	$22,562
Drainage		11	05-Aug-15	21-Aug-15	77	$135,376
Roadworks		42	28-Jul-15	12-Oct-15	77	$806,593
ITS / Signs / Stripes / Electrical / MISC.		35	01-Sep-15	19-Oct-15	634	$35,523
Noise Wall		2	14-Jul-15	15-Jul-15	168	$2,590
Retaining Wall RW13A		11	07-Aug-15	24-Aug-15	114	$53,476
Retaining Wall RWS13		25	07-Aug-15	14-Sep-15	100	$542,502
NSML - Dewey to S. of Trinity River		153	09-Jul-15	08-Feb-16	554	$8,133,625
TCP & Temp Work		147	09-Jul-15	29-Jan-16	25	$169,217
Drainage		19	24-Aug-15	25-Sep-15	33	$238,470
Roadworks		93	07-Aug-15	29-Jan-16	20	$2,885,576
ITS / Signs / Stripes / Electrical / MISC.		38	17-Dec-15	08-Feb-16	554	$396,923
Noise Wall		2	14-Jul-15	15-Jul-15	168	$18,651
Retaining Wall RWN15		87	14-Aug-15	12-Jan-16	33	$2,340,364
Retaining Wall RWS15-S		77	14-Aug-15	24-Dec-15	43	$2,024,424
XRDS - Meacham Blvd.		15	10-Jul-15	31-Jul-15	128	$172,737
Retaining Wall RW02A		15	10-Jul-15	31-Jul-15	128	$172,737
Phase 3		336	08-Mar-16	20-Jun-17	198	$145,242,545
3AMSMS31000	Segment 3A - Phase 3 Finish	0		27-Jan-17	2	$0
Stage 1		336	08-Mar-16	20-Jun-17	198	$52,217,688
3AMSMS311000	Segment 3A - Phase 3 Stage 1 Finish	0		27-Jan-17	2	$0
3AMS1001	Segment 3A - Phase 3 Stage 1 Misc Roadway Items Finish	0		20-Jun-17	278	$0
NBRP - S. of Trinity River to IH-30		15	08-Mar-16	28-Mar-16	219	$420,323
TCP & Temp Work		15	08-Mar-16	28-Mar-16	219	$420,323
NBRP - Dewey to S. of Trinity River		13	08-Mar-16	24-Mar-16	221	$398,446
TCP & Temp Work		13	08-Mar-16	24-Mar-16	221	$398,446
NBFR - Dewey to S. of Trinity River		95	08-Mar-16	18-Jul-16	439	$1,590,395
TCP & Temp Work		91	08-Mar-16	12-Jul-16	143	$544,186
Drainage		14	25-Apr-16	24-May-16	111	$121,874

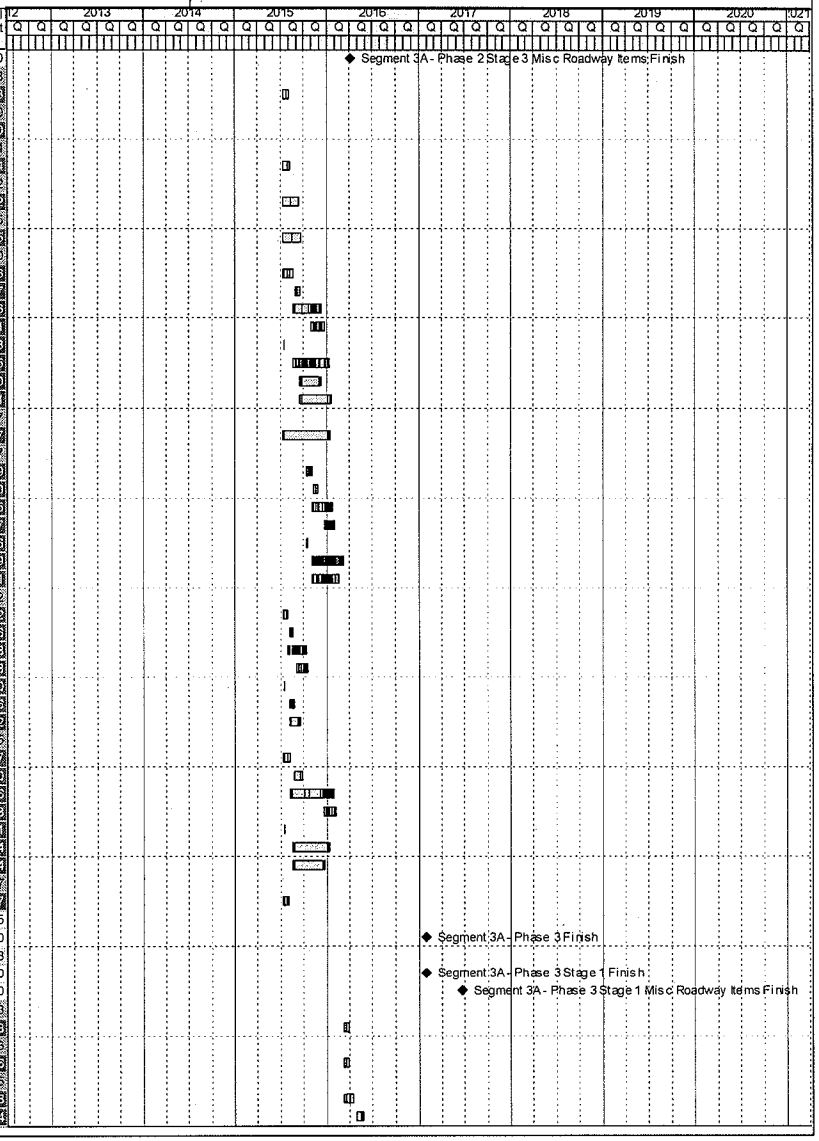

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Roadworks	48	12-Apr-16	12-Jul-16	111	$880,032
	ITS / Signs / Stripes / Electrical / MISC.	29	08-Jun-16	18-Jul-16	439	$40,882
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$3,420
	NBGP - S. of Trinity River to IH-30	28	08-Mar-16	14-Apr-16	0	$2,359,723
	TCP & Temp Work	28	08-Mar-16	14-Apr-16	0	$2,359,723
	NBFR - Meacham to Dewey	119	08-Mar-16	19-Aug-16	415	$9,266,426
	TCP & Temp Work	114	08-Mar-16	12-Aug-16	120	$60,486
	Drainage	26	20-Apr-16	10-Jun-16	91	$803,833
	Roadworks	76	28-Mar-16	12-Aug-16	91	$1,818,766
	ITS / Signs / Stripes / Electrical / MISC.	31	08-Jul-16	19-Aug-16	415	$123,010
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$8,521
	Retaining Wall RWN13-M1	0			0	$0
	Retaining Wall RWN13-M2	0			0	$0
	Retaining Wall RWN13-S	56	20-Apr-16	06-Jul-16	147	$940,809
	SBFR - Meacham to Dewey	61	08-Mar-16	31-May-16	473	$238,101
	TCP & Temp Work	56	08-Mar-16	24-May-16	178	$7,848
	Drainage	8	21-Mar-16	04-Apr-16	138	$30,554
	Roadworks	34	16-Mar-16	24-May-16	138	$176,585
	ITS / Signs / Stripes / Electrical / MISC.	34	14-Apr-16	31-May-16	473	$22,256
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$857
	NBGP - Meacham to Dewey	336	08-Mar-16	20-Jun-17	198	$31,747,483
	TCP & Temp Work	234	08-Mar-16	27-Jan-17	0	$1,884,235
	Drainage	30	06-Apr-16	03-Jun-16	2	$956,730
	Roadworks	170	16-Mar-16	24-Jan-17	2	$9,457,712
	ITS / Signs / Stripes / Electrical / MISC.	147	28-Nov-16	20-Jun-17	198	$1,830,622
	Noise Wall	4	16-Mar-16	21-Mar-16	224	$76,956
	B241 - NB 35W GP over Meacham	103	16-Mar-16	05-Aug-16	125	$1,551,910
	B210 - NB 35W GP over BNSF	196	16-Mar-16	14-Dec-16	32	$2,444,298
	B207 - NB 35W GP over FWWR	228	16-Mar-16	27-Jan-17	0	$4,437,805
	Retaining Wall RWN01	54	30-Jun-16	23-Sep-16	73	$1,460,342
	Retaining Wall RWN02	68	30-Jun-16	17-Oct-16	59	$1,692,150
	Retaining Wall RWN05	10	30-Jun-16	15-Jul-16	117	$152,542
	Retaining Wall RWN10-M	0			0	$0
	Retaining Wall RWN10-S	61	28-Mar-16	08-Jul-16	122	$1,577,643
	Retaining Wall RWN08	152	28-Mar-16	06-Dec-16	31	$4,244,537
	NBRP - Meacham to Dewey	156	08-Mar-16	11-Oct-16	378	$10,800,637
	TCP & Temp Work	155	08-Mar-16	11-Oct-16	78	$112,811
	Drainage	43	12-Apr-16	01-Jul-16	65	$573,857
	Roadworks	98	04-Apr-16	27-Sep-16	65	$2,132,226
	ITS / Signs / Stripes / Electrical / MISC.	38	16-Aug-16	06-Oct-16	381	$348,663
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$16,638
	B212 - SH183 Entrance Ramp to NB 35W ML	137	04-Apr-16	11-Oct-16	78	$2,386,255
	Retaining Wall RWN02A	66	05-May-16	19-Aug-16	94	$1,686,605
	Retaining Wall RWN04	67	05-May-16	22-Aug-16	93	$1,694,269
	Retaining Wall RW04A	13	05-May-16	25-May-16	147	$101,174
	Retaining Wall RWN07-M	51	05-May-16	28-Jul-16	109	$1,267,852
	Retaining Wall RWN07-S	0			0	$0
	Retaining Wall RWN12	20	05-May-16	08-Jun-16	140	$429,076
	Retaining Wall RW13B	11	05-May-16	23-May-16	149	$51,211
	XRDS - Meacham Blvd	21	08-Mar-16	11-Apr-16	173	$1,407,164
	Retaining Wall RW02A	16	08-Mar-16	01-Apr-16	178	$172,737
	Retaining Wall RW07A	21	08-Mar-16	11-Apr-16	173	$405,799
	Retaining Wall RW10A	19	08-Mar-16	06-Apr-16	175	$317,541
	Retaining Wall RW08A-S	21	08-Mar-16	11-Apr-16	173	$249,493
	Retaining Wall RW08B-S	21	08-Mar-16	11-Apr-16	173	$261,584
	Stage 2	336	08-Mar-16	20-Jun-17	198	$75,441,658
3AMSMS321000	Segment 3A- Phase 3 Stage 2 Finish	0		20-Jan-17	9	$0
3AMS	Segment 3A- Phase 3 Stage 2 Misc Roadway Items Finish	0		20-Jun-17	278	$0
	SBRP - S. of Trinity River to IH-30	208	08-Mar-16	22-Dec-16	326	$9,761,309
	TCP & Temp Work	208	08-Mar-16	22-Dec-16	26	$0

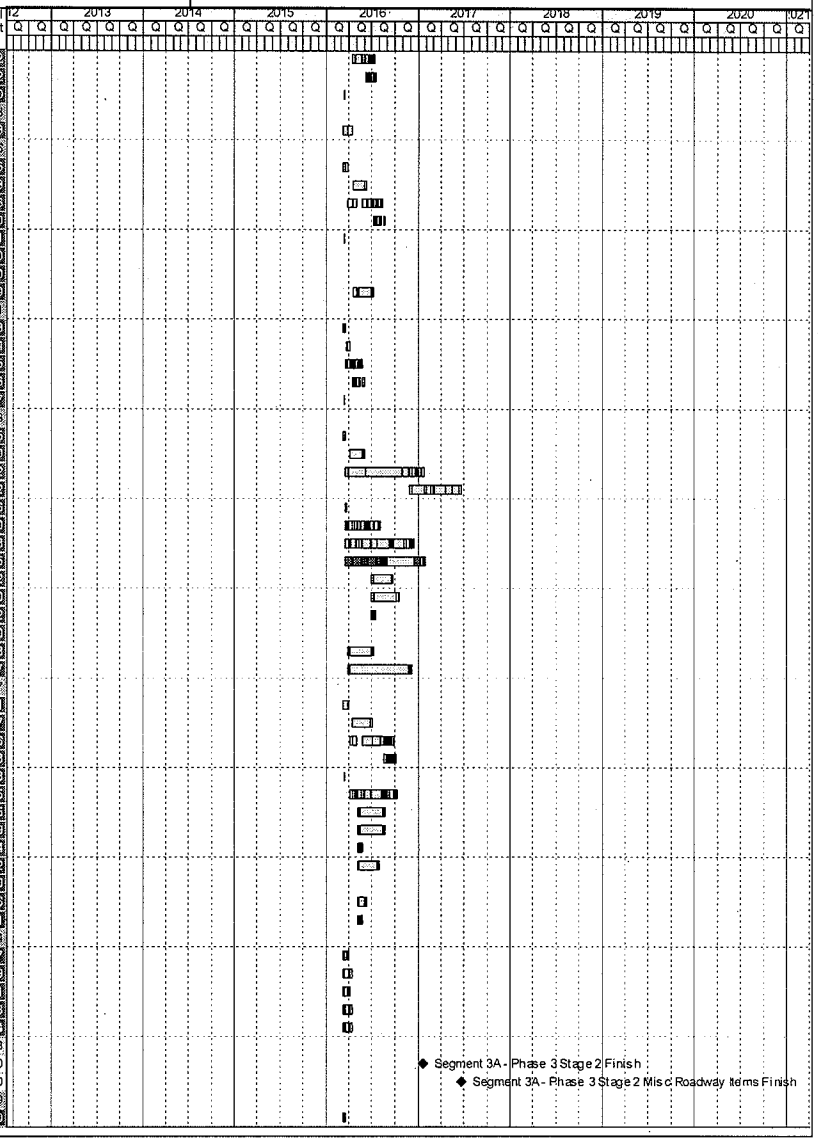

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Drainage	9	29-Mar-16	14-Apr-16	124	$0
	Roadworks	46	21-Mar-16	17-Jun-16	124	$0
	ITS / Signs / Stripes / Electrical / MISC.	38	29-Apr-16	21-Jun-16	458	$0
	Noise Wall	5	11-Mar-16	17-Mar-16	226	$0
	B232 - SB 35W ML Exit Ramp to Spur 280	199	21-Mar-16	22-Dec-16	26	$9,761,309
	NBFR - Dewey to S. of Trinity River	62	08-Mar-16	01-Jun-16	472	$363,777
	TCP & Temp Work	56	08-Mar-16	24-May-16	178	$15,042
	Drainage	8	24-Mar-16	08-Apr-16	138	$40,625
	Roadworks	33	18-Mar-16	24-May-16	138	$293,344
	ITS / Signs / Stripes / Electrical / MISC.	33	18-Apr-16	01-Jun-16	472	$13,627
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$1,140
	NBFR - Meacham to Dewey	49	08-Mar-16	13-May-16	185	$940,809
	Retaining Wall RWN13-M1	0			0	$0
	Retaining Wall RWN13-M2	0			0	$0
	Retaining Wall RWN13-S	40	08-Mar-16	13-May-16	154	$940,809
	NBGP - Meacham to Dewey	69	08-Mar-16	10-Jun-16	465	$951,736
	TCP & Temp Work	64	08-Mar-16	03-Jun-16	170	$46,414
	Drainage	8	23-Mar-16	06-Apr-16	132	$61,725
	Roadworks	40	16-Mar-16	03-Jun-16	132	$510,175
	ITS / Signs / Stripes / Electrical / MISC.	36	22-Apr-16	10-Jun-16	465	$75,916
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$4,965
	Retaining Wall RWN05	10	30-Mar-16	14-Apr-16	171	$152,542
	NBGP - Dewey to S. of Trinity River	253	08-Mar-16	23-Feb-17	281	$24,084,672
	TCP & Temp Work	228	08-Mar-16	19-Jan-17	6	$368,216
	Drainage	23	06-Apr-16	23-May-16	52	$495,064
	Roadworks	160	16-Mar-16	05-Jan-17	12	$6,054,927
	ITS / Signs / Stripes / Electrical / MISC.	73	15-Nov-16	23-Feb-17	281	$944,997
	Noise Wall	3	15-Mar-16	17-Mar-16	226	$39,832
	B219 - NB 35W GP over UPRR	222	16-Mar-16	19-Jan-17	6	$10,087,432
	B224 - NB 35W GP over Trinity River	218	16-Mar-16	13-Jan-17	10	$6,094,204
	NBGP - S. of Trinity River to IH-30	247	15-Apr-16	27-Mar-17	259	$18,261,247
	TCP & Temp Work	196	15-Apr-16	13-Jan-17	10	$1,487,162
	Drainage	20	20-May-16	22-Jun-16	7	$762,141
	Roadworks	144	27-Apr-16	13-Jan-17	7	$7,039,344
	ITS / Signs / Stripes / Electrical / MISC.	104	02-Nov-16	27-Mar-17	259	$1,533,454
	Noise Wall	4	25-Apr-16	28-Apr-16	196	$61,301
	B235 - NB 35W GP over RR (922+00)	136	27-Apr-16	02-Nov-16	62	$2,446,180
	B233 - NB 35W GP over 4th St.	148	27-Apr-16	16-Nov-16	50	$2,602,356
	Retaining Wall RWN23	33	30-Jun-16	19-Aug-16	94	$656,420
	Retaining Wall RWN25	35	30-Jun-16	24-Aug-16	92	$727,209
	Retaining Wall RWN26	37	30-Jun-16	26-Aug-16	90	$945,659
	NBRP - Meacham to Dewey	156	08-Mar-16	10-Oct-16	379	$4,191,229
	TCP & Temp Work	153	08-Mar-16	10-Oct-16	79	$13,537
	Drainage	10	29-Mar-16	15-Apr-16	131	$68,863
	Roadworks	40	18-Mar-16	06-Jun-16	131	$255,867
	ITS / Signs / Stripes / Electrical / MISC.	34	27-Apr-16	13-Jun-16	464	$26,145
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$1,997
	B203 - NB 35W ML Ramp to NB 35W GP	147	18-Mar-16	10-Oct-16	79	$3,824,820
	NBRP - Dewey to S. of Trinity River	164	08-Mar-16	21-Oct-16	370	$3,247,280
	TCP & Temp Work	160	08-Mar-16	17-Oct-16	74	$97,770
	Drainage	37	17-May-16	21-Jul-16	54	$481,336
	Roadworks	109	04-Apr-16	17-Oct-16	54	$2,340,554
	ITS / Signs / Stripes / Electrical / MISC.	36	02-Sep-16	21-Oct-16	370	$313,662
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$13,958
	Retaining Wall RWN19-M1	0			0	$0
	NBRP - S. of Trinity River to IH-30	229	08-Mar-16	20-Jan-17	305	$13,250,274
	TCP & Temp Work	223	08-Mar-16	20-Jan-17	5	$258,441
	Drainage	48	12-Apr-16	12-Jul-16	54	$635,822
	Roadworks	109	04-Apr-16	17-Oct-16	54	$1,980,736
	ITS / Signs / Stripes / Electrical / MISC.	41	29-Aug-16	24-Oct-16	369	$525,611

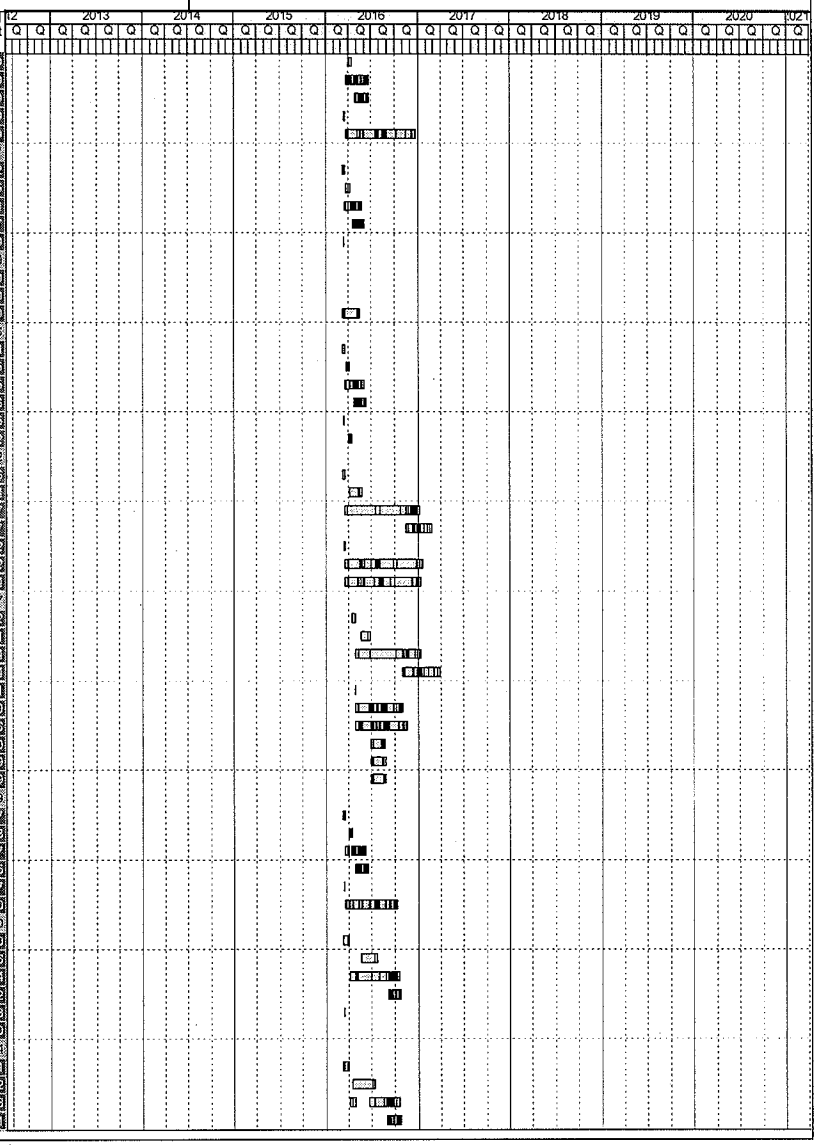

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Noise Wall	2	14-Mar-16	15-Mar-16	228	$18,448
	B231 - Spur 280 Entrance Ramp to NB 35W ML	210	04-Apr-16	20-Jan-17	5	$9,489,254
	Retaining Wall RWN31	22	28-Apr-16	03-Jun-16	142	$351,956
	Retaining Wall RW31A	0			0	$0
	XROS - SH 183/NE 28th St	25	08-Mar-16	18-Apr-16	169	$379,325
	Retaining Wall RW20A	25	08-Mar-16	18-Apr-16	169	$379,325
	Stage 3	336	08-Mar-16	20-Jun-17	198	$17,583,199
3AMSMS331000	Segment 3A - Phase 3 Stage 3 Finish	0		08-Nov-16	82	$0
3AMS1000	Segment 3A - Phase 3 Stage 3 Misc Roadway Items Finish	0		20-Jun-17	278	$0
	NBFR - Dewey to S. of Trinity River	69	08-Mar-16	10-Jun-16	465	$363,777
	TCP & Temp Work	64	08-Mar-16	03-Jun-16	170	$15,042
	Drainage	8	28-Mar-16	11-Apr-16	132	$40,625
	Roadworks	38	21-Mar-16	03-Jun-16	132	$293,344
	ITS / Signs / Stripes / Electrical / MISC.	38	20-Apr-16	10-Jun-16	465	$13,627
	Noise Wall	2	14-Mar-16	15-Mar-16	228	$1,140
	NBGP - Meacham to Dewey	79	08-Mar-16	24-Jun-16	455	$799,194
	TCP & Temp Work	74	08-Mar-16	17-Jun-16	160	$46,414
	Drainage	8	01-Apr-16	15-Apr-16	124	$61,725
	Roadworks	43	28-Mar-16	17-Jun-16	124	$610,175
	ITS / Signs / Stripes / Electrical / MISC.	37	05-May-16	24-Jun-16	455	$75,916
	Noise Wall	2	14-Mar-16	15-Mar-16	228	$4,965
	NBGP - Dewey to S. of Trinity River	176	08-Mar-16	08-Nov-16	358	$10,799,554
	TCP & Temp Work	176	08-Mar-16	08-Nov-16	58	$173,278
	Drainage	14	22-Apr-16	23-May-16	87	$232,971
	Roadworks	94	04-Apr-16	21-Sep-16	69	$2,849,377
	ITS / Signs / Stripes / Electrical / MISC.	38	12-Aug-16	04-Oct-16	383	$390,852
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$18,744
	B223 - NB 35W GP over Northside Dr/Yucca Ave	145	28-Mar-16	14-Oct-16	75	$2,532,599
	Retaining Wall RWN20	70	20-Jul-16	08-Nov-16	46	$3,475,527
	Retaining Wall RWN21	43	20-Jul-16	23-Sep-16	73	$1,126,205
	NBGP - S. of Trinity River to IH-30	111	14-Jun-16	15-Nov-16	353	$2,633,068
	TCP & Temp Work	99	14-Jun-16	28-Oct-16	65	$170,998
	Drainage	13	21-Jul-16	08-Aug-16	47	$203,238
	Roadworks	66	11-Jul-16	28-Oct-16	47	$1,877,158
	ITS / Signs / Stripes / Electrical / MISC.	38	23-Sep-16	15-Nov-16	353	$365,326
	Noise Wall	4	17-Jun-16	22-Jun-16	157	$16,347
	NBRP - Dewey to S. of Trinity River	105	08-Mar-16	01-Aug-16	429	$1,198,652
	TCP & Temp Work	101	08-Mar-16	26-Jul-16	133	$37,604
	Drainage	18	15-Apr-16	23-May-16	103	$185,129
	Roadworks	66	23-Mar-16	26-Jul-16	103	$900,213
	ITS / Signs / Stripes / Electrical / MISC.	32	17-Jun-16	01-Aug-16	429	$70,337
	Noise Wall	2	14-Mar-16	15-Mar-16	228	$5,369
	Retaining Wall RWN19-M1	0			0	$0
	NBRP - S. of Trinity River to IH-30	67	07-May-16	09-Aug-16	428	$150,957
	TCP & Temp Work	62	07-May-16	02-Aug-16	128	$12,307
	Drainage	8	01-Jun-16	13-Jun-16	98	$30,277
	Roadworks	41	24-May-16	02-Aug-16	98	$94,321
	ITS / Signs / Stripes / Electrical / MISC.	35	22-Jun-16	09-Aug-16	423	$12,573
	Noise Wall	4	16-May-16	19-May-16	181	$878
	NBLA - Meacham to Dewey	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	NBLA - Dewey to S. of Trinity River	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963

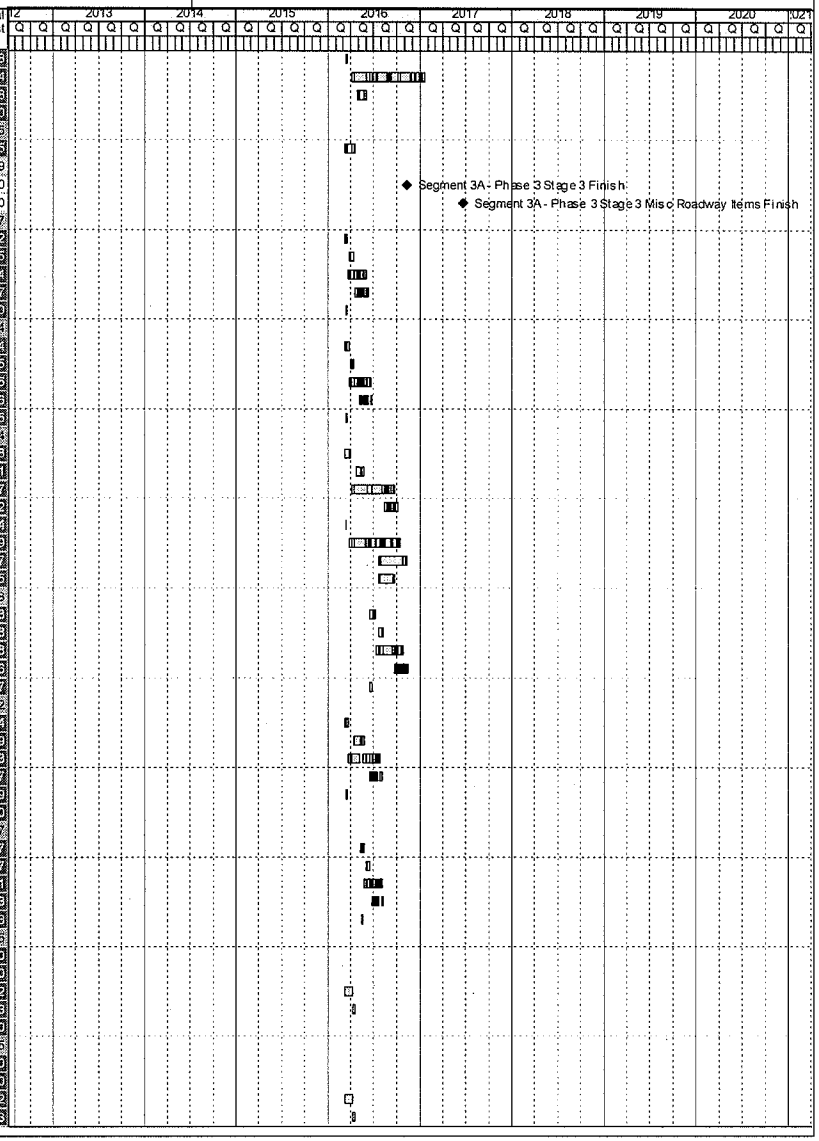

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Noise Wall	0			0	$0
	NBLA - S. of Trinity River to IH-30	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	SBLA - Meacham to Dewey	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	SBLA - Dewey to S. of Trinity River	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	SBLA - S. of Trinity River to IH-30	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	XRDS - SH 183/NE 28th St	23	08-Mar-16	14-Apr-16	171	$452,125
	Retaining Wall RW21A	20	08-Mar-16	08-Apr-16	174	$175,837
	Retaining Wall RW21B	23	08-Mar-16	14-Apr-16	171	$276,289
Phase 4		263	28-Jan-17	31-Jan-18	37	$198,122,135
3AMSMS41000	Segment 3A - Phase 4 Finish	0		31-Jan-18	53	$0
Stage 1		263	28-Jan-17	31-Jan-18	37	$198,122,135
3AMSMS411000	Segment 3A - Phase 4 Stage 1 Finish	0		31-Jan-18	53	$0
	SBRP - S. of Trinity River to IH-30	260	28-Jan-17	26-Jan-18	40	$9,761,309
	TCP & Temp Work	260	28-Jan-17	26-Jan-18	40	$0
	Drainage	8	20-Feb-17	03-Mar-17	188	$0
	Roadworks	44	10-Feb-17	04-May-17	188	$0
	ITS / Signs / Stripes / Electrical / MISC.	40	16-Mar-17	10-May-17	227	$0
	Noise Wall	5	03-Feb-17	09-Feb-17	291	$0
	B232 - SB 35W ML Exit Ramp to Spur 280	251	10-Feb-17	26-Jan-18	40	$9,761,309
	NBGP - Interchange to Meacham	144	28-Jan-17	17-Aug-17	156	$4,506,239
	TCP & Temp Work	144	28-Jan-17	17-Aug-17	156	$206,284
	Drainage	16	13-Mar-17	12-Apr-17	132	$662,628
	Roadworks	90	23-Feb-17	08-Aug-17	134	$3,098,024
	ITS / Signs / Stripes / Electrical / MISC.	39	26-Jun-17	17-Aug-17	156	$541,304
	Noise Wall	5	01-Feb-17	07-Feb-17	293	$0
	SBGP - S. of Trinity River to IH-30	96	28-Jan-17	12-Jun-17	204	$1,746,204
	TCP & Temp Work	96	28-Jan-17	12-Jun-17	204	$85,499
	Drainage	10	01-Mar-17	20-Mar-17	173	$182,030
	Roadworks	53	23-Feb-17	07-Jun-17	173	$1,237,612
	ITS / Signs / Stripes / Electrical / MISC.	36	24-Apr-17	12-Jun-17	204	$280,450
	Noise Wall	3	08-Feb-17	08-Feb-17	292	$10,613
	NSML - Meacham to Dewey	255	28-Jan-17	19-Jan-18	45	$72,429,188
	TCP & Temp Work	255	28-Jan-17	19-Jan-18	45	$1,489,111
	Drainage	60	27-Feb-17	21-Jun-17	23	$2,524,478
	Roadworks	179	08-Feb-17	02-Jan-18	54	$20,229,945
	ITS / Signs / Stripes / Electrical / MISC.	93	31-Aug-17	08-Jan-18	54	$3,741,374
	Noise Wall	9	08-Feb-17	20-Feb-17	284	$157,850
	B213 - 35W ML Transition (755+00)	146	08-Feb-17	30-Aug-17	147	$2,903,585
	B209 - 35W ML over BNSF	162	08-Feb-17	21-Sep-17	131	$2,862,489
	B206 - 35W ML over FWWR	243	08-Feb-17	12-Jan-18	50	$5,570,028

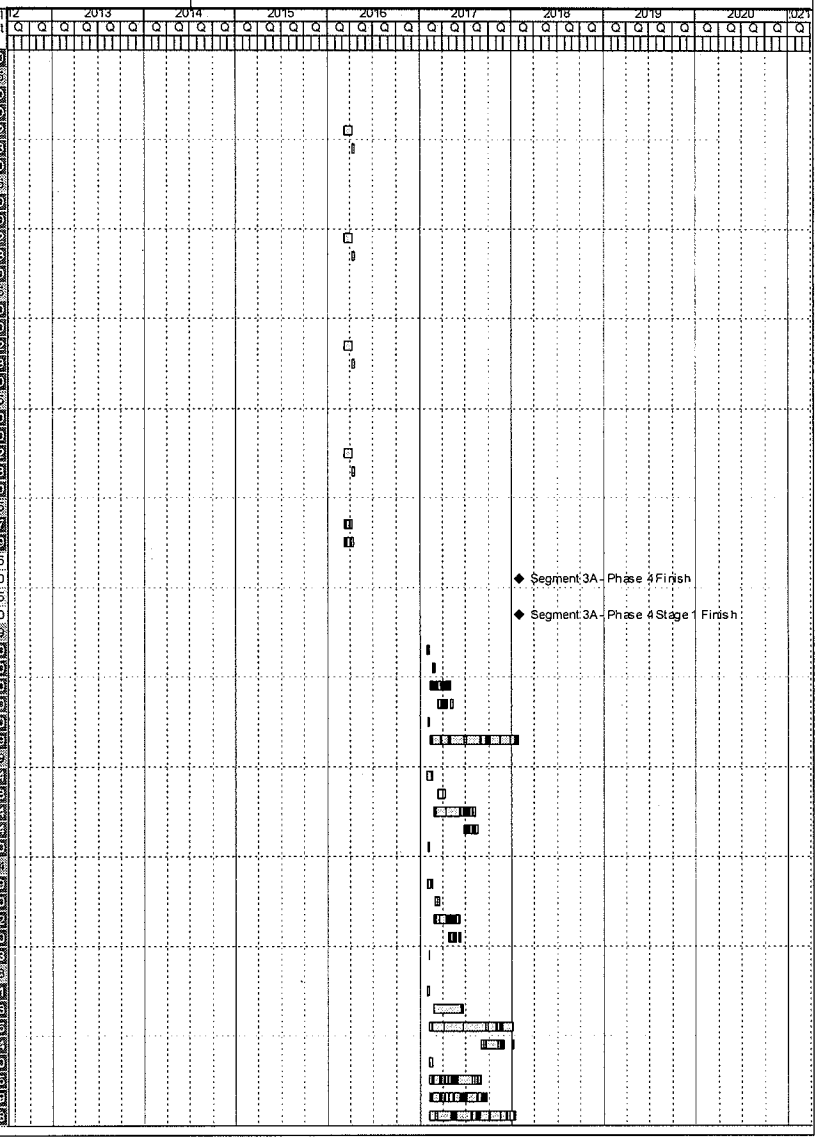

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	B204 - 35W ML Transition (713+00)	148	08-Feb-17	01-Sep-17	145	$2,035,195
	B201 - 35W ML over Meacham	129	08-Feb-17	07-Aug-17	164	$2,103,586
	Retaining Wall RWN03	118	03-Jul-17	12-Jan-18	50	$6,522,407
	Retaining Wall RWS03	118	03-Jul-17	12-Jan-18	50	$6,622,372
	Retaining Wall RW03A	20	03-Jul-17	02-Aug-17	148	$271,713
	Retaining Wall RWN06	49	03-Jul-17	20-Sep-17	119	$1,182,211
	Retaining Wall RW06A	20	03-Jul-17	02-Aug-17	148	$236,546
	Retaining Wall RWS06	49	03-Jul-17	20-Sep-17	119	$1,194,896
	Retaining Wall RWN09	101	03-Jul-17	15-Dec-17	67	$2,932,664
	Retaining Wall RWS09	96	03-Jul-17	07-Dec-17	72	$2,702,799
	Retaining Wall RW09A	24	03-Jul-17	08-Aug-17	144	$411,387
	Retaining Wall RWN11	101	03-Jul-17	15-Dec-17	67	$2,784,705
	Retaining Wall RW11A	22	03-Jul-17	04-Aug-17	146	$313,488
	Retaining Wall RWS11	123	03-Jul-17	19-Jan-18	45	$3,616,357
	NSML - Dewey to S. of Trinity River	263	28-Jan-17	31-Jan-18	37	$93,863,796
	TCP & Temp Work	263	28-Jan-17	31-Jan-18	37	$398,434
	Drainage	33	08-Mar-17	08-May-17	25	$596,940
	Roadworks	159	13-Feb-17	30-Nov-17	70	$5,771,152
	ITS / Signs / Stripes / Electrical / MISC.	68	14-Sep-17	18-Dec-17	69	$924,631
	Noise Wall	2	06-Feb-17	07-Feb-17	293	$37,302
	Bridge 225 - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	Bridge 243 - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	Bridge 242 - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	Bridge 232M - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	B222 - 35W ML over Northside Dr/Yucca Ave	199	13-Feb-17	16-Nov-17	91	$3,848,326
	Retaining Wall RWN19A	0			0	$0
	Retaining Wall RWN15	88	27-Feb-17	25-Jul-17	154	$2,340,364
	NSML - S. of Trinity River to IH-30	136	28-Jan-17	07-Aug-17	164	$1,987,366
	TCP & Temp Work	136	28-Jan-17	07-Aug-17	164	$135,374
	Drainage	13	26-Apr-17	19-May-17	139	$163,886
	Roadworks	86	23-Feb-17	02-Aug-17	140	$1,424,494
	ITS / Signs / Stripes / Electrical / MISC.	31	26-Jun-17	07-Aug-17	164	$253,396
	Noise Wall	3	01-Feb-17	03-Feb-17	295	$10,217
	Retaining Wall RWN29	0			0	$0
	NBRP - S. of Trinity River to IH-30	123	28-Jan-17	19-Jul-17	177	$1,764,709
	TCP & Temp Work	123	28-Jan-17	19-Jul-17	177	$135,374
	Drainage	28	01-Mar-17	24-Apr-17	152	$393,050
	Roadworks	73	23-Feb-17	11-Jul-17	152	$1,037,530
	ITS / Signs / Stripes / Electrical / MISC.	40	25-May-17	19-Jul-17	177	$289,092
	Noise Wall	3	01-Feb-17	03-Feb-17	295	$9,663
	SBRP - Meacham to Dewey	172	28-Jan-17	26-Sep-17	128	$4,106,927
	TCP & Temp Work	172	28-Jan-17	26-Sep-17	128	$22,662
	Drainage	11	17-Feb-17	08-Mar-17	189	$135,976
	Roadworks	43	09-Feb-17	02-May-17	190	$806,593
	ITS / Signs / Stripes / Electrical / MISC.	31	24-Mar-17	05-May-17	230	$35,523
	Noise Wall	3	03-Feb-17	07-Feb-17	293	$2,590
	B211 - SB 35W ML Exit Ramp to SH 183	164	09-Feb-17	26-Sep-17	128	$3,103,684
	SBRP - Dewey to S. of Trinity River	83	28-Jan-17	24-May-17	217	$751,499
	TCP & Temp Work	83	28-Jan-17	24-May-17	217	$32,490
	Drainage	13	24-Feb-17	20-Mar-17	181	$111,731
	Roadworks	49	13-Feb-17	16-May-17	181	$558,393
	ITS / Signs / Stripes / Electrical / MISC.	39	31-Mar-17	24-May-17	217	$45,647
	Noise Wall	3	06-Feb-17	08-Feb-17	292	$3,239
	XRDS - Meacham Blvd.	73	28-Jan-17	10-May-17	227	$1,449,530
	TCP & Temp Work	73	28-Jan-17	10-May-17	227	$0
	Drainage	8	20-Feb-17	03-Mar-17	188	$0
	Roadworks	44	10-Feb-17	04-May-17	188	$0
	ITS / Signs / Stripes / Electrical / MISC.	40	16-Mar-17	10-May-17	227	$0
	Noise Wall	5	03-Feb-17	09-Feb-17	291	$0
	Retaining Wall RW02A	16	28-Feb-17	24-Mar-17	225	$177,917

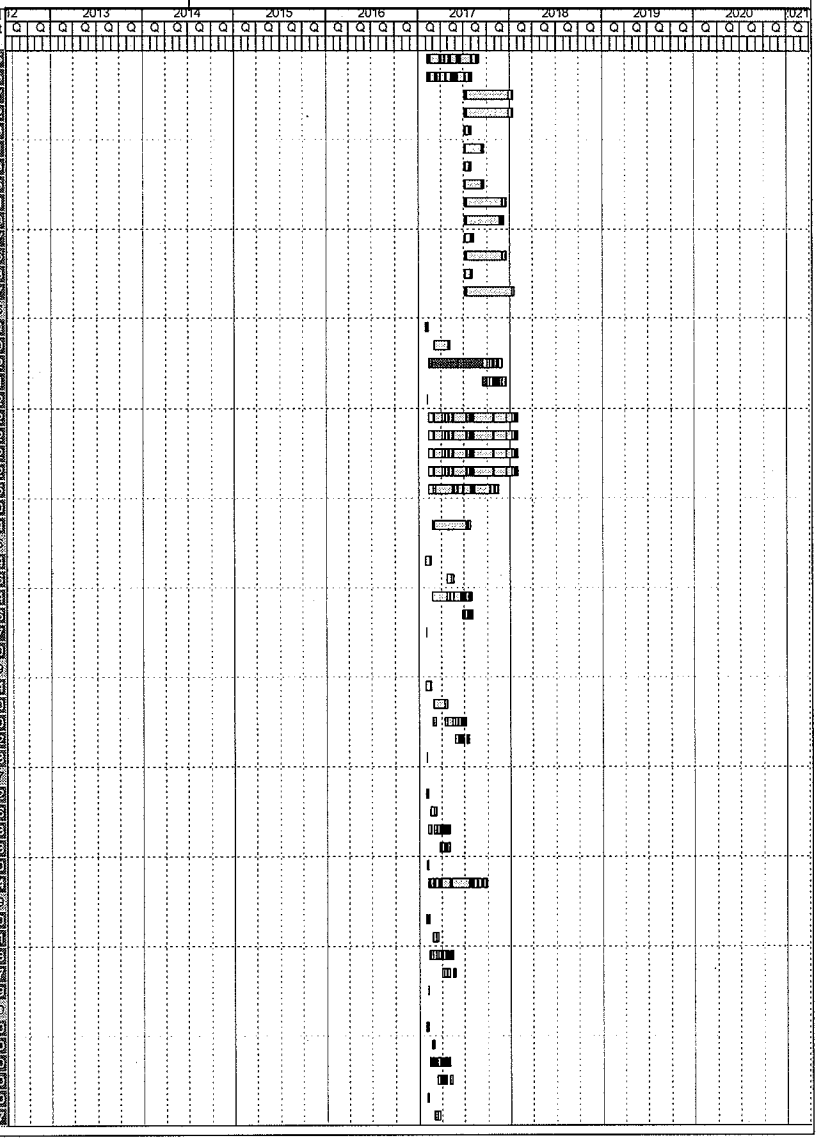

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Retaining Wall RW07A	22	28-Feb-17	04-Apr-17	219	$417,962
	Retaining Wall RW10A	19	28-Feb-17	29-Mar-17	222	$327,175
	Retaining Wall RW08A-S	20	20-Feb-17	23-Mar-17	226	$257,019
	Retaining Wall RW08B-S	20	20-Feb-17	23-Mar-17	226	$269,556
	XRDS - E. 4th St.	232	28-Jan-17	19-Dec-17	68	$3,888,488
	TCP & Temp Work	232	28-Jan-17	19-Dec-17	68	$0
	Drainage	8	20-Feb-17	03-Mar-17	188	$0
	Roadworks	44	10-Feb-17	04-May-17	188	$0
	ITS / Signs / Stripes / Electrical / MISC.	40	16-Mar-17	10-May-17	227	$0
	Noise Wall	5	03-Feb-17	09-Feb-17	291	$0
	B239 - Pedestrian Bridge over US 287	223	10-Feb-17	19-Dec-17	68	$3,422,964
	Retaining Wall RW21A	16	28-Feb-17	24-Mar-17	225	$180,965
	Retaining Wall RW21B	18	28-Feb-17	28-Mar-17	223	$284,559
	XRDS - Cypress St.	96	28-Jan-17	12-Jun-17	204	$1,845,481
	TCP & Temp Work	96	28-Jan-17	12-Jun-17	204	$0
	Drainage	17	20-Feb-17	21-Mar-17	178	$178,874
	Roadworks	53	10-Feb-17	22-May-17	178	$524,496
	ITS / Signs / Stripes / Electrical / MISC.	41	07-Apr-17	02-Jun-17	210	$551,601
	Noise Wall	2	03-Feb-17	06-Feb-17	294	$5,023
	B245 - Cypress St. over 290	87	10-Feb-17	12-Jun-17	204	$1,085,287
	Interchange Construction	1130	20-Apr-13	18-Aug-17	155	$297,383,286
	Phase 1	491	20-Apr-13	09-Mar-15	794	$158,465,857
ICMSMS1000	Interchange Phase 1 Finish	0		03-Feb-15	49	$0
ICMS1001	Interchange Phase 1 Misc Roadway Items Finish	0		09-Mar-15	1112	$0
	Stage 1	491	20-Apr-13	09-Mar-15	794	$158,465,857
	WBGP - Interchange to Meacham	25	20-Apr-13	24-May-13	477	$1,693,723
	TCP & Temp Work	25	20-Apr-13	24-May-13	477	$1,693,723
	NBFR - Interchange to Meacham	491	20-Apr-13	09-Mar-15	794	$10,845,939
	TCP & Temp Work	467	20-Apr-13	03-Feb-15	35	$270,747
	Drainage	224	27-Jun-13	12-Aug-14	26	$3,321,690
	Roadworks	339	20-May-13	03-Feb-15	26	$4,475,922
	ITS / Signs / Stripes / Electrical / MISC.	89	05-Nov-14	09-Mar-15	794	$1,518,298
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	Bridge (B33 - NB 35W FR over Little Fossil Creek)	323	20-May-13	13-Aug-14	159	$1,259,252
	SBFR - Interchange to Meacham	438	20-Apr-13	24-Dec-14	847	$9,722,314
	TCP & Temp Work	405	20-Apr-13	07-Nov-14	97	$270,747
	Drainage	192	27-Jun-13	19-Jun-14	70	$2,833,002
	Roadworks	295	20-May-13	07-Nov-14	70	$3,926,991
	ITS / Signs / Stripes / Electrical / MISC.	94	29-Aug-14	24-Dec-14	847	$1,457,506
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	Bridge (B34 - SB 35W FR over Little Fossil Creek)	238	20-May-13	16-Apr-14	244	$1,234,068
	NBGP - Interchange to Meacham	268	20-Apr-13	30-Apr-14	1017	$3,191,717
	TCP & Temp Work	268	20-Apr-13	30-Apr-14	234	$847,642
	Drainage	8	19-Jun-13	01-Jul-13	314	$82,828
	Roadworks	40	13-Jun-13	19-Aug-13	314	$387,253
	ITS / Signs / Stripes / Electrical / MISC.	30	15-Jul-13	23-Aug-13	1195	$34,967
	Noise Wall	5	24-Apr-13	30-Apr-13	495	$0
	Bridge (B1 - 35W NB GP over 820)	230	13-Jun-13	30-Apr-14	234	$1,839,026
	SBGP - Interchange to Meacham	260	20-Apr-13	16-Apr-14	1025	$5,568,301
	TCP & Temp Work	260	20-Apr-13	16-Apr-14	242	$1,550,410
	Drainage	11	22-Aug-13	09-Sep-13	252	$352,621
	Roadworks	78	25-Jul-13	09-Dec-13	252	$1,639,922
	ITS / Signs / Stripes / Electrical / MISC.	39	25-Oct-13	18-Dec-13	1112	$318,600
	Noise Wall	5	24-Apr-13	30-Apr-13	495	$0
	Bridge (B7 - 35W SB GP over 820	192	25-Jul-13	18-Apr-14	242	$1,696,748
	EBGP - Interchange to Meacham	228	20-Apr-13	05-Mar-14	1057	$7,466,384
	TCP & Temp Work	213	20-Apr-13	12-Feb-14	269	$1,673,208
	Drainage	19	19-Aug-13	19-Sep-13	217	$877,917
	Roadworks	108	01-Aug-13	12-Feb-14	217	$4,047,274
	ITS / Signs / Stripes / Electrical / MISC.	95	19-Dec-13	05-Mar-14	1057	$687,986

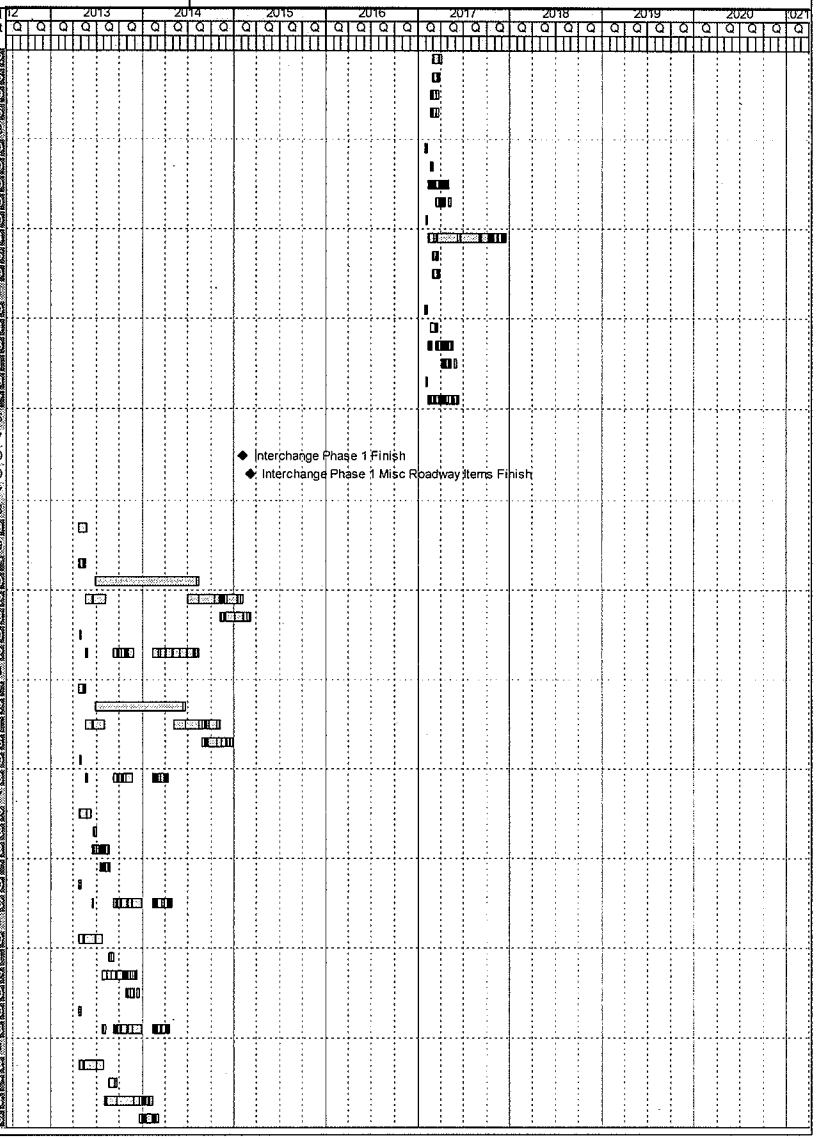

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	NSML - Interchange to Meacham	473	20-Apr-13	11-Feb-15	812	$19,527,318
	TCP & Temp Work	371	20-Apr-13	22-Sep-14	131	$741,612
	Drainage	61	11-Jun-13	29-Sep-13	98	$2,722,510
	Roadworks	267	20-May-13	22-Sep-14	98	$11,252,524
	ITS / Signs / Stripes / Electrical / MISC.	173	16-Jun-14	11-Feb-15	812	$2,247,472
	Noise Wall	5	03-May-13	09-May-13	488	$0
	Bridge (B4 - 35W ML over 820	281	20-May-13	19-May-14	221	$2,563,200
	EWML - Interchange to Meacham	210	20-Apr-13	07-Feb-14	1075	$7,129,497
	TCP & Temp Work	196	20-Apr-13	20-Jan-14	306	$369,932
	Drainage	29	11-Jun-13	30-Jul-13	230	$1,147,291
	Roadworks	135	20-May-13	20-Jan-14	230	$4,743,287
	ITS / Signs / Stripes / Electrical / MISC.	66	08-Nov-13	07-Feb-14	1075	$868,988
	Noise Wall	5	29-Apr-13	03-May-13	492	$0
	NBRP - Interchange to Meacham	406	20-Apr-13	10-Nov-14	873	$14,752,237
	TCP & Temp Work	406	20-Apr-13	10-Nov-14	98	$3,702,071
	Drainage	13	30-Oct-13	20-Nov-13	232	$173,468
	Roadworks	46	23-Oct-13	15-Jan-14	232	$483,419
	ITS / Signs / Stripes / Electrical / MISC.	34	09-Dec-13	23-Jan-14	1096	$72,938
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	Bridge (B35 - 35W NB GP Exit Ramp to Melody Hills)	119	23-Oct-13	07-Apr-14	251	$656,488
	Bridge (B16 - 35W NB - 820 EB GP DC)	274	23-Oct-13	10-Nov-14	98	$9,463,854
	SBRP - Interchange to Meacham	445	20-Apr-13	02-Jan-15	840	$26,529,491
	TCP & Temp Work	445	20-Apr-13	02-Jan-15	57	$3,615,374
	Drainage	35	31-Oct-13	05-Jan-14	183	$670,806
	Roadworks	93	25-Oct-13	18-Apr-14	183	$1,868,367
	ITS / Signs / Stripes / Electrical / MISC.	48	19-Feb-14	25-Apr-14	1020	$323,266
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	Bridge (B11 - 35W SB - 820 EB GP DC)	311	25-Oct-13	02-Jan-15	57	$9,198,148
	Bridge (B10 - 35W SB - 820 WB GP DC)	191	25-Oct-13	18-Jul-14	177	$6,005,897
	Retaining Wall EBRW-01	32	26-Nov-13	21-Jan-14	254	$791,577
	Retaining Wall EBRW-02	50	26-Nov-13	19-Feb-14	236	$1,535,365
	Retaining Wall EBRW-05	21	26-Nov-13	02-Jan-14	265	$450,715
	Retaining Wall EBRW-06	22	26-Nov-13	03-Jan-14	264	$481,926
	Retaining Wall WBRW-03	26	26-Nov-13	10-Jan-14	260	$579,799
	Retaining Wall WBRW-04	42	26-Nov-13	05-Feb-14	244	$1,028,250
	EBRP - Interchange to Meacham	393	20-Apr-13	22-Oct-14	892	$23,991,418
	TCP & Temp Work	393	20-Apr-13	22-Oct-14	109	$1,908,450
	Drainage	26	14-Aug-13	26-Sep-13	249	$479,896
	Roadworks	72	08-Aug-13	13-Dec-13	249	$1,397,659
	ITS / Signs / Stripes / Electrical / MISC.	42	28-Oct-13	24-Dec-13	1108	$182,973
	Noise Wall	5	24-Apr-13	30-Apr-13	495	$0
	Bridge (B14 - 820 EB - 35W SB GP DC)	315	08-Aug-13	22-Oct-14	109	$12,275,522
	Bridge (B13 - 820 EB - 35W NB GP DC)	234	08-Aug-13	01-Jul-14	190	$5,488,514
	Retaining Wall EBRW-11	51	09-Sep-13	02-Dec-13	283	$1,321,115
	Retaining Wall EBRW-12	51	09-Sep-13	02-Dec-13	283	$997,287
	WBRP - Interchange to Meacham	324	20-Apr-13	17-Jul-14	961	$28,027,518
	TCP & Temp Work	324	20-Apr-13	17-Jul-14	178	$3,576,507
	Drainage	10	31-Jul-13	15-Aug-13	276	$410,409
	Roadworks	77	18-Jul-13	26-Nov-13	257	$1,143,252
	ITS / Signs / Stripes / Electrical / MISC.	39	15-Oct-13	08-Dec-13	1120	$117,937
	Noise Wall	5	29-Apr-13	03-May-13	492	$0
	Bridge (B12 - 820 WB - 35W NB GP DC)	205	18-Jul-13	30-Apr-14	234	$9,671,429
	Bridge (B15 - 820 WB - 35W SB GP DC)	261	18-Jul-13	17-Jul-14	178	$7,162,605
	Bridge (B21 - 820 WB - 35W SB ML DC)	192	18-Jul-13	11-Apr-14	247	$2,022,770
	Retaining Wall WBRW-09	68	27-Sep-13	21-Jan-14	254	$1,917,920
	Retaining Wall WBRW-10	70	27-Sep-13	23-Jan-14	252	$2,004,690
	Phase 2	281	04-Feb-15	02-Mar-16	537	$98,596,108
ICMS1005	Interchange Phase 2 Misc Roadway Items Finish	0		01-Dec-15	845	$0
ICMS11001	Interchange Phase 2 Finish	0		02-Mar-16	46	$0

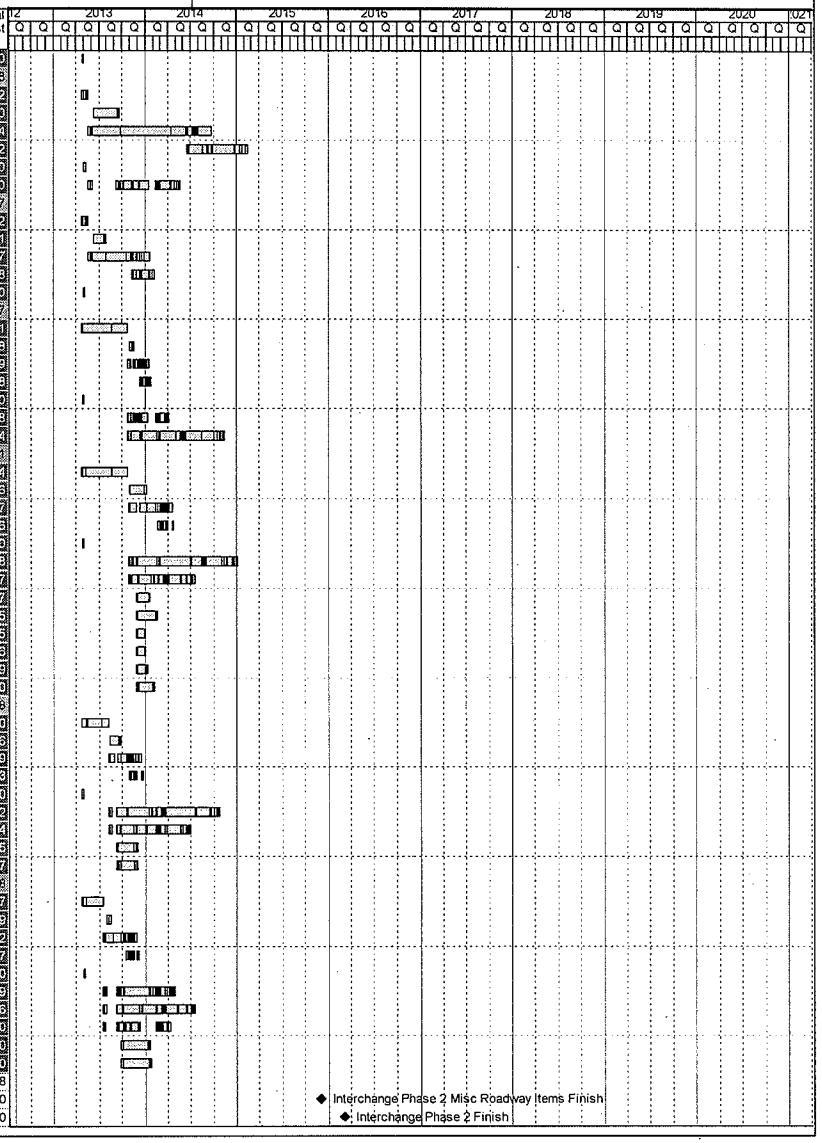

SUMMARY SCHEDULE | NTE - Segment 3A Interchange Project - FBS # 1 |

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Stage 1		281	04-Feb-15	02-Mar-16	537	$98,596,108
NBGP - Interchange to Meacham		170	04-Feb-15	29-Sep-15	648	$5,569,907
TCP & Temp Work		153	04-Feb-15	04-Sep-15	160	$257,855
Drainage		18	20-Mar-15	20-Apr-15	116	$828,285
Roadworks		103	27-Feb-15	04-Sep-15	116	$3,872,530
ITS / Signs / Stripes / Electrical / MISC.		50	22-Jul-15	29-Sep-15	648	$611,236
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
SBGP - Interchange to Meacham		215	04-Feb-15	01-Dec-15	603	$8,495,663
TCP & Temp Work		180	04-Feb-15	13-Oct-15	133	$309,426
Drainage		22	20-Mar-15	27-Apr-15	97	$1,057,862
Roadworks		122	27-Feb-15	13-Oct-15	97	$4,919,766
ITS / Signs / Stripes / Electrical / MISC.		76	18-Aug-15	01-Dec-15	603	$825,017
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
Bridge (B32GPL - 35W over Little Fossil Creek)		106	27-Feb-15	24-Jul-15	190	$1,383,593
EBGP - Interchange to Meacham		189	04-Feb-15	26-Oct-15	629	$6,239,107
TCP & Temp Work		168	04-Feb-15	25-Sep-15	145	$243,673
Drainage		20	20-Mar-15	23-Apr-15	106	$940,625
Roadworks		113	27-Feb-15	25-Sep-15	106	$4,336,365
ITS / Signs / Stripes / Electrical / MISC.		61	03-Aug-15	26-Oct-15	629	$718,444
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
WBGP - Interchange to Meacham		181	04-Feb-15	14-Oct-15	637	$6,118,217
TCP & Temp Work		157	04-Feb-15	10-Sep-15	156	$232,843
Drainage		20	11-Mar-15	15-Apr-15	114	$925,104
Roadworks		105	27-Feb-15	10-Sep-15	114	$4,256,102
ITS / Signs / Stripes / Electrical / MISC.		59	24-Jul-15	14-Oct-15	637	$704,168
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
NSML - Interchange to Meacham		169	04-Feb-15	28-Sep-15	649	$5,754,701
TCP & Temp Work		145	04-Feb-15	25-Aug-15	168	$206,003
Drainage		21	13-Mar-15	17-Apr-15	123	$756,253
Roadworks		96	27-Feb-15	25-Aug-15	123	$3,125,701
ITS / Signs / Stripes / Electrical / MISC.		59	08-Jul-15	28-Sep-15	649	$704,222
Noise Wall		5	03-Feb-15	12-Feb-15	306	$0
Bridge (B32ML - 35W over Little Fossil Creek)		90	27-Feb-15	02-Jul-15	206	$962,522
EWML - Interchange to Meacham		215	04-Feb-15	01-Dec-15	603	$7,422,417
TCP & Temp Work		199	04-Feb-15	09-Nov-15	114	$386,016
Drainage		30	20-Mar-15	18-May-15	83	$1,197,173
Roadworks		136	27-Feb-15	09-Nov-15	83	$4,949,516
ITS / Signs / Stripes / Electrical / MISC.		65	02-Sep-15	01-Dec-15	603	$889,711
Noise Wall		5	12-Feb-15	18-Feb-15	302	$0
NBRP - Interchange to Meacham		274	04-Feb-15	22-Feb-16	544	$19,918,529
TCP & Temp Work		274	04-Feb-15	22-Feb-16	39	$64,124
Drainage		28	04-Mar-15	23-Apr-15	143	$520,404
Roadworks		78	24-Feb-15	23-Jul-15	143	$1,450,257
ITS / Signs / Stripes / Electrical / MISC.		40	04-Jun-15	29-Jul-15	692	$218,819
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
Bridge (B16 - 35W NB - 820 EB GP DC)		137	24-Feb-15	02-Sep-15	162	$3,184,618
Bridge (B17 - 35W NB - 820 WB GP DC)		260	24-Feb-15	22-Feb-16	39	$10,550,920
Retaining Wall WBRW-05		56	25-Mar-15	26-Jun-15	174	$1,528,482
Retaining Wall WBRW-06		49	25-Mar-15	15-Jun-15	181	$1,272,437
Retaining Wall WBRW-04D		26	25-Mar-15	07-May-15	204	$579,287
Retaining Wall WBRW-04E		26	25-Mar-15	07-May-15	204	$579,287
SBRP - Interchange to Meacham		122	04-Feb-15	23-Jul-15	696	$3,383,408
TCP & Temp Work		122	04-Feb-15	23-Jul-15	191	$32,818
Drainage		17	25-Feb-15	30-Mar-15	169	$255,545
Roadworks		55	19-Feb-15	05-Jun-15	169	$711,759
ITS / Signs / Stripes / Electrical / MISC.		45	13-Apr-15	12-Jun-15	725	$73,326
Noise Wall		3	12-Feb-15	16-Feb-15	304	$0
Bridge (B10 - 35W SB - 820 WB GP DC)		111	19-Feb-15	23-Jul-15	191	$2,309,961
EBRP - Interchange to Meacham		61	04-Feb-15	29-Apr-15	757	$221,287
TCP & Temp Work		57	04-Feb-15	23-Apr-15	255	$13,537

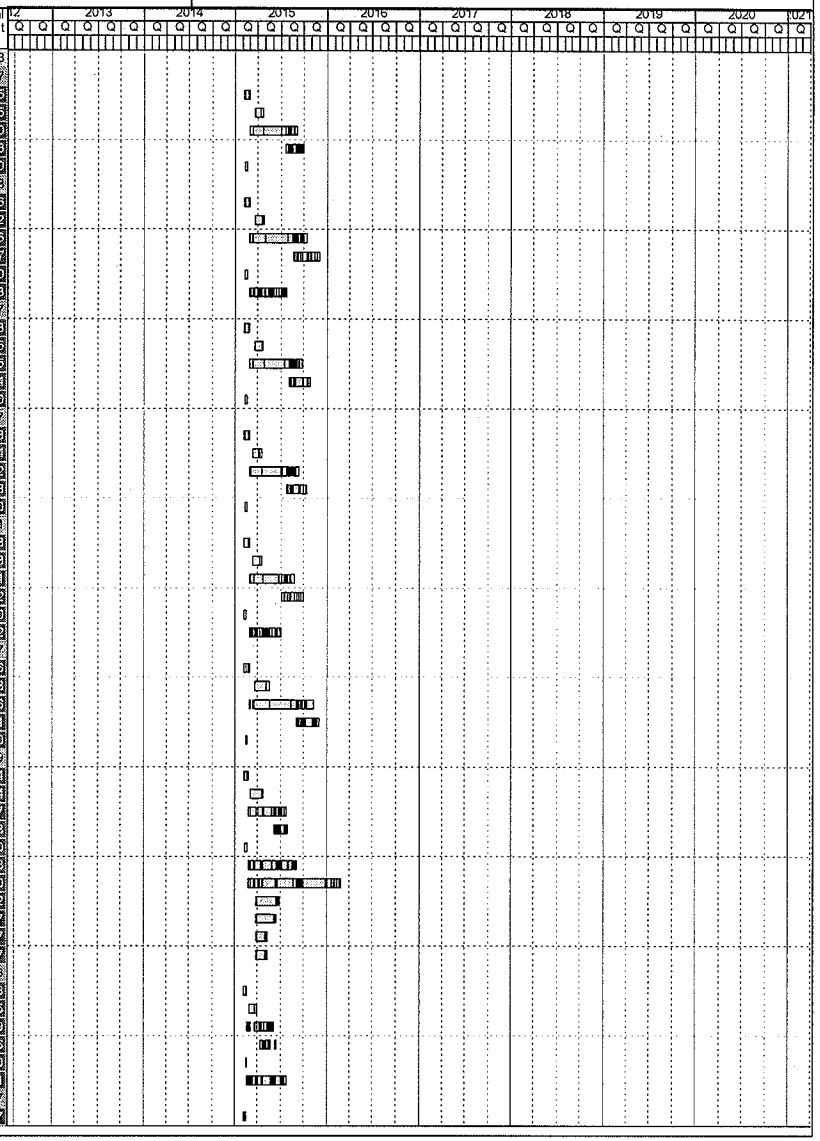

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Drainage	8	23-Feb-15	09-Mar-15	189	$53,922
	Roadworks	37	16-Feb-15	23-Apr-15	189	$148,629
	ITS / Signs / Stripes / Electrical / MISC.	30	19-Mar-15	29-Apr-15	757	$5,799
	Noise Wall	5	06-Feb-15	12-Feb-15	306	$0
	WBRP - Interchange to Meacham	281	04-Feb-15	02-Mar-16	537	$36,472,872
	TCP & Temp Work	281	04-Feb-15	02-Mar-16	32	$33,843
	Drainage	10	24-Feb-15	16-Mar-15	174	$263,083
	Roadworks	51	17-Feb-15	27-May-15	174	$732,854
	ITS / Signs / Stripes / Electrical / MISC.	47	01-Apr-15	04-Jun-15	731	$75,601
	Noise Wall	3	10-Feb-15	12-Feb-15	306	$0
	Bridge (B12 - 820 WB - 35W NB GP DC)	156	17-Feb-15	22-Sep-15	148	$6,447,736
	Bridge (B18 - 820 WB - 35W NB ML DC)	272	17-Feb-15	02-Mar-16	32	$12,083,218
	Bridge (B21 - 820 WB - 35W SB ML DC)	247	17-Feb-15	27-Jan-16	57	$11,462,361
	Retaining Wall WBRW-01	76	02-Mar-15	07-Jul-15	168	$2,357,414
	Retaining Wall WBRW-01A	65	02-Mar-15	18-Jun-15	179	$247,581
	Retaining Wall WBRW-02	63	02-Mar-15	15-Jun-15	181	$1,769,182
	Phase 3	154	03-Mar-16	04-Oct-16	383	$25,276,793
ICMS1000	Interchange Phase 3 Misc Roadway Items Finish	0		18-Aug-16	584	$0
ICMS11005	Interchange Phase 3 Finish	0		04-Oct-16	54	$0
	Stage 1	154	03-Mar-16	04-Oct-16	383	$25,276,793
	NBGP - Interchange to Meacham	93	03-Mar-16	11-Jul-16	444	$1,609,572
	TCP & Temp Work	89	03-Mar-16	05-Jul-16	103	$599,475
	Drainage	8	20-Apr-16	06-May-16	83	$165,657
	Roadworks	45	11-Apr-16	05-Jul-16	83	$774,506
	ITS / Signs / Stripes / Electrical / MISC.	30	31-May-16	11-Jul-16	444	$69,934
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	SBGP - Interchange to Meacham	121	03-Mar-16	18-Aug-16	416	$2,414,285
	TCP & Temp Work	114	03-Mar-16	09-Aug-16	78	$103,142
	Drainage	11	28-Apr-16	23-May-16	61	$352,621
	Roadworks	74	28-Mar-16	09-Aug-16	61	$1,639,922
	ITS / Signs / Stripes / Electrical / MISC.	29	11-Jul-16	18-Aug-16	416	$318,600
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	EBGP - Interchange to Meacham	76	03-Mar-16	16-Jun-16	461	$797,005
	TCP & Temp Work	70	03-Mar-16	08-Jun-16	122	$32,490
	Drainage	7	23-Mar-16	04-Apr-16	98	$125,417
	Roadworks	43	15-Mar-16	08-Jun-16	98	$578,182
	ITS / Signs / Stripes / Electrical / MISC.	42	20-Apr-16	16-Jun-16	461	$60,917
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	NBRP - Interchange to Meacham	147	03-Mar-16	23-Sep-16	390	$10,157,450
	TCP & Temp Work	147	03-Mar-16	23-Sep-16	45	$49,875
	Drainage	23	29-Mar-16	13-May-16	74	$404,759
	Roadworks	65	18-Mar-16	21-Jul-16	74	$1,127,978
	ITS / Signs / Stripes / Electrical / MISC.	35	10-Jun-16	28-Jul-16	431	$170,188
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	Bridge (B16 - 35W NB - 820 EB GP DC)	136	18-Mar-16	23-Sep-16	43	$3,154,618
	Bridge (B17 - 35W NB - 820 WB GP DC)	134	18-Mar-16	21-Sep-16	45	$3,768,150
	Retaining Wall EBRW-09	95	15-Apr-16	14-Jun-16	99	$748,656
	Retaining Wall EBRW-10	94	15-Apr-16	13-Jun-16	100	$733,327
	SBRP - Interchange to Meacham	154	03-Mar-16	04-Oct-16	383	$6,331,193
	TCP & Temp Work	154	03-Mar-16	04-Oct-16	38	$16,409
	Drainage	11	23-Mar-16	12-Apr-16	97	$127,778
	Roadworks	44	15-Mar-16	09-Jun-16	97	$355,879
	ITS / Signs / Stripes / Electrical / MISC.	37	27-Apr-16	16-Jun-16	461	$36,663
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	Retaining Wall EBRW-03	85	29-Mar-16	16-Aug-16	60	$2,362,956
	Retaining Wall EBRW-04	115	29-Mar-16	04-Oct-16	30	$3,431,513
	EBRP - Interchange to Meacham	138	03-Mar-16	12-Sep-16	54	$2,703,298
	Bridge (B13 - 820 EB - 35W NB GP DC)	138	03-Mar-16	12-Sep-16	54	$2,703,298
	WBRP - Interchange to Meacham	100	03-Mar-16	20-Jul-16	92	$1,263,989
	Bridge (B15 - 820 WB - 35W SB GP DC)	100	03-Mar-16	20-Jul-16	92	$1,263,989

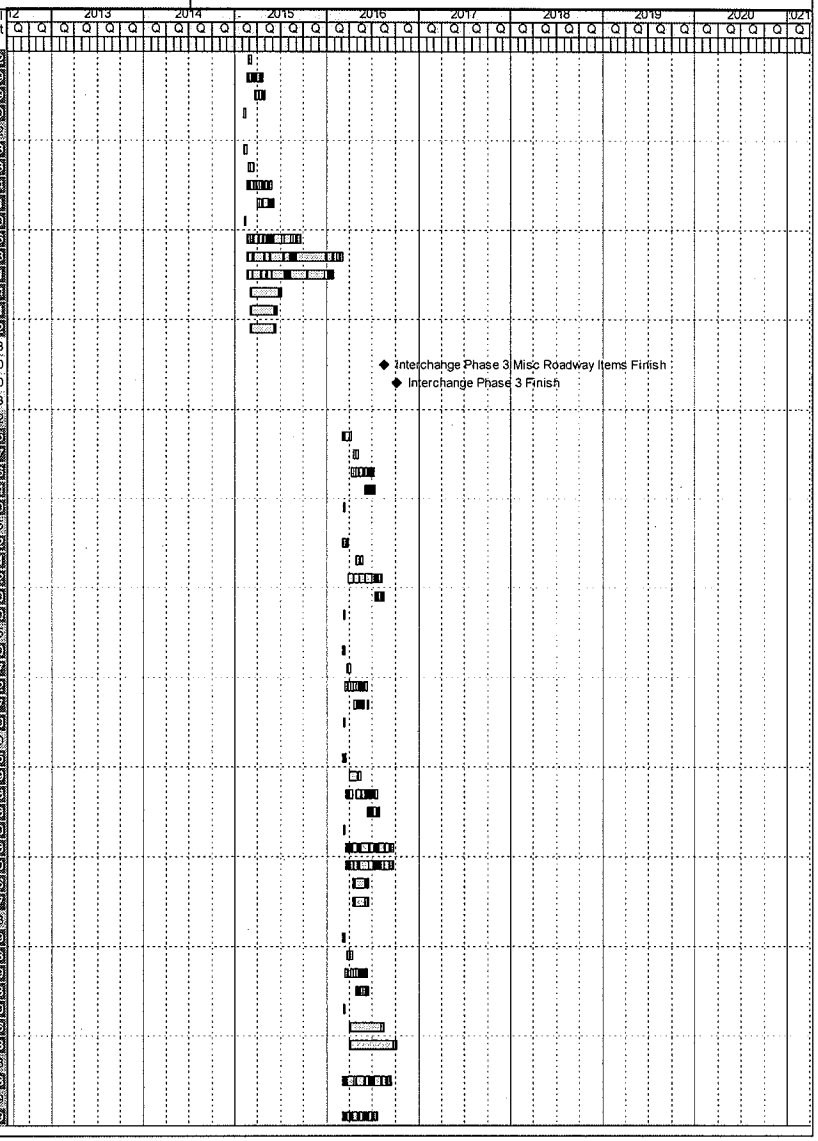

SUMMARY SCHEDULE | NTE - Segment 3A Interchange Project - FBS # 1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Phase 4		228	05-Oct-16	18-Aug-17	155	$15,044,528
ICMS11000	Interchange Phase 4 Finish	0		18-Aug-17	219	$0
Stage 1		228	05-Oct-16	18-Aug-17	155	$15,044,528
SBGP - Interchange to Meacham		61	05-Oct-16	28-Dec-16	322	$570,875
TCP & Temp Work		61	05-Oct-16	28-Dec-16	322	$25,795
Drainage		7	24-Oct-16	03-Nov-16	257	$86,165
Roadworks		37	17-Oct-16	22-Dec-16	257	$409,980
ITS / Signs / Stripes / Electrical / MISC.		32	15-Nov-16	28-Dec-16	322	$48,954
Noise Wall		5	07-Oct-16	13-Oct-16	376	$0
EBGP - Interchange to Meacham		70	05-Oct-16	10-Jan-17	313	$929,839
TCP & Temp Work		70	05-Oct-16	10-Jan-17	313	$37,905
Drainage		8	27-Oct-16	08-Nov-16	251	$146,319
Roadworks		41	18-Oct-16	03-Jan-17	251	$674,546
ITS / Signs / Stripes / Electrical / MISC.		32	28-Nov-16	10-Jan-17	313	$71,069
Noise Wall		5	07-Oct-16	13-Oct-16	376	$0
WBGP - Interchange to Meacham		228	05-Oct-16	18-Aug-17	155	$8,025,032
TCP & Temp Work		228	05-Oct-16	18-Aug-17	155	$308,652
Drainage		25	14-Nov-16	30-Dec-16	30	$1,226,300
Roadworks		136	27-Oct-16	13-Jul-17	151	$5,641,810
ITS / Signs / Stripes / Electrical / MISC.		72	11-May-17	18-Aug-17	155	$848,270
Noise Wall		5	10-Oct-16	14-Oct-16	375	$0
EWML - Interchange to Meacham		74	05-Oct-16	16-Jan-17	309	$1,025,216
TCP & Temp Work		74	05-Oct-16	16-Jan-17	309	$56,294
Drainage		9	28-Oct-16	11-Nov-16	248	$174,588
Roadworks		43	21-Oct-16	10-Jan-17	248	$721,804
ITS / Signs / Stripes / Electrical / MISC.		32	02-Dec-16	16-Jan-17	309	$72,531
Noise Wall		5	07-Oct-16	13-Oct-16	376	$0
WBRP - Interchange to Meacham		100	05-Oct-16	21-Feb-17	283	$1,591,748
TCP & Temp Work		100	05-Oct-16	21-Feb-17	283	$48,735
Drainage		22	27-Oct-16	06-Dec-16	229	$378,639
Roadworks		63	19-Oct-16	15-Feb-17	229	$1,055,310
ITS / Signs / Stripes / Electrical / MISC.		36	03-Jan-17	21-Feb-17	283	$108,865
Noise Wall		5	07-Oct-16	13-Oct-16	376	$0
SBRP - Interchange to Meacham		87	05-Oct-16	02-Feb-17	296	$923,984
Bridge (B10 - 35W SB - 820 WB GP DC)		87	05-Oct-16	02-Feb-17	296	$923,984
NBRP - Interchange to Meacham		78	05-Oct-16	20-Jan-17	305	$753,630
Bridge (B17 - 35W NB - 820 WB GP DC)		78	05-Oct-16	20-Jan-17	305	$753,630
NBLA - Interchange to Meacham		47	05-Oct-16	08-Dec-16	336	$306,050
TCP & Temp Work		65	05-Oct-16	08-Dec-16	472	$0
Roadworks		26	05-Oct-16	16-Nov-16	268	$241,665
ITS / Signs / Stripes / Electrical / MISC.		10	18-Nov-16	08-Dec-16	268	$64,385
SBLA - Interchange to Meacham		47	05-Oct-16	08-Dec-16	336	$306,052
TCP & Temp Work		65	05-Oct-16	08-Dec-16	472	$0
Roadworks		26	05-Oct-16	16-Nov-16	268	$241,668
ITS / Signs / Stripes / Electrical / MISC.		10	18-Nov-16	08-Dec-16	268	$64,385
EBLA - Interchange to Meacham		47	05-Oct-16	08-Dec-16	336	$306,050
TCP & Temp Work		65	05-Oct-16	08-Dec-16	472	$0
Roadworks		26	05-Oct-16	16-Nov-16	268	$241,665
ITS / Signs / Stripes / Electrical / MISC.		10	18-Nov-16	08-Dec-16	268	$64,385
WBLA - Interchange to Meacham		47	05-Oct-16	08-Dec-16	336	$306,050
TCP & Temp Work		65	05-Oct-16	08-Dec-16	472	$0
Roadworks		26	05-Oct-16	16-Nov-16	268	$241,665
ITS / Signs / Stripes / Electrical / MISC.		10	18-Nov-16	08-Dec-16	268	$64,385

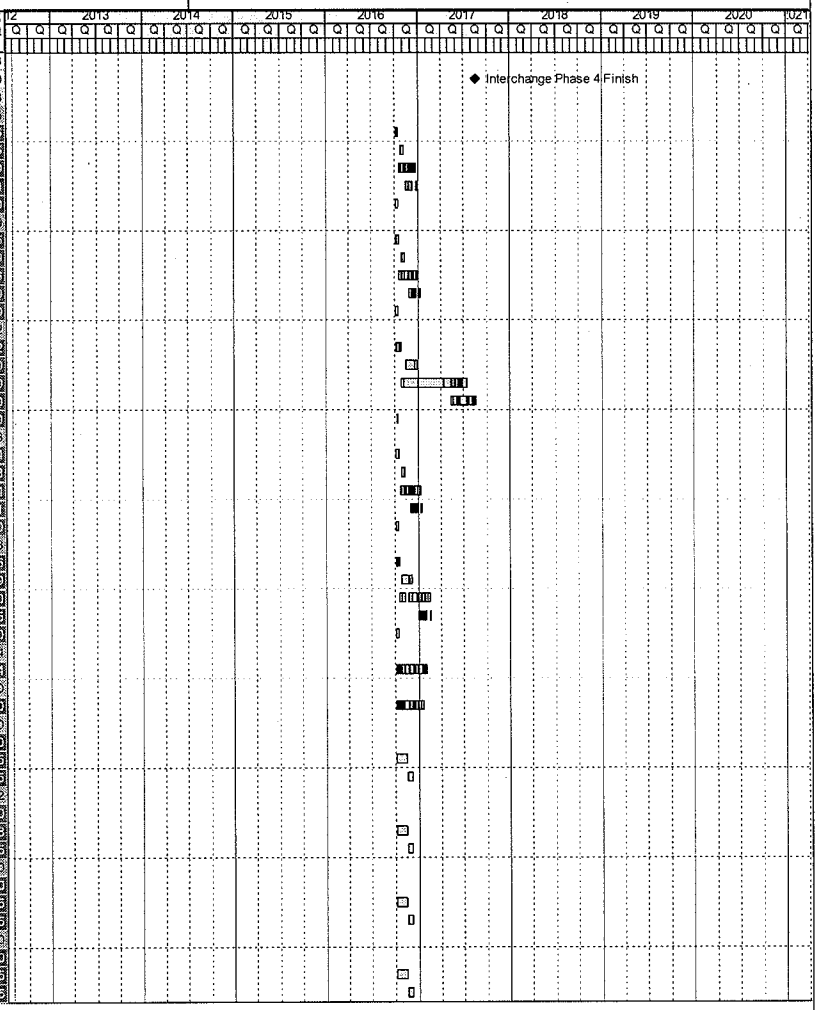

ATTACHMENT 03 - DETAILED PROGRAM SCHEDULE | NTE - Segment 3A Interchange Project - FBS # 1 |

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Total		1543	01-Aug-12	29-Jun-18	0	$1,037,614,340
NTE - Segment 3A & Interchange Project - FBS # 1		1543	01-Aug-12	29-Jun-18	0	$1,037,614,340
Project Administration		1500	01-Oct-12	29-Jun-18	0	$53,014,340
Project Milestones		1500	01-Oct-12	29-Jun-18	0	$0
NTE-NTP1	Notice To Proceed # 1	0	01-Oct-12*		53	$0
NTE-NTP2	Notice to Proceed # 2	0	01-Apr-13		269	$0
NTE-PROJFINISH3B	Substantial Completion Segment 3B (By others)	0		31-Mar-16*	593	$0
NTE-ITSFINISH	Completion of ITS (Civil) Work	0		06-Oct-17	2	$0
NTE-SC-NOTICE1	Substantial Completion Notiifcation Period to TxDOT	20	26-Feb-18	23-Mar-18	20	$0
NTE-SC-NOTICE2	Notification to TxDOT / IE of Developer's Anticipated Substantial Completion	0	26-Feb-18		20	$0
NTE-SCOMP-1000	Substantial Completion Segment 3A	0		23-Mar-18	2	$0
NTE-SCOMP-1010	TxDOT Issue Substantial Completion Certificate	5	26-Mar-18	30-Mar-18	0	$0
NTE-SCOMP-1020	Open Traffic / Service Commencement	0		30-Mar-18*	1	$0
NTE-FCOMP-1000	Completion of Punchlist Works	70	31-Mar-18	08-Jun-18	1	$0
NTE-FCOMP-1010	Review and Approval of Punchlist Works by TxDOT / IE	15	09-Jun-18	23-Jun-18	1	$0
NTE-FCOMP-1005	Notification to TxDOT / IE of Develpoer's Final Completion	0	11-Jun-18		10	$0
NTE-FCOMP-1015	TxDOT Issue Final Completion Certificate	5	25-Jun-18	29-Jun-18	0	$0
NTE-FCOMP-1020	Project Final Acceptance	0		29-Jun-18	0	$0
Management Submittals		391	01-Oct-12	31-Mar-14	1035	$0
Project Schedules		391	01-Oct-12	31-Mar-14	1035	$0
NTE3AIC-FBS2-1000	Development of FBS # 2	95	01-Oct-12	13-Feb-13	188	$0
NTE3AIC-FBS2-1010	TxDOT Review and Approval of FBS # 2	30	14-Feb-13	28-Mar-13	187	$0
NTE3AIC-FBS3-1000	Development of FBS # 3	255	01-Apr-13	31-Mar-14	1018	$0
Quality Management Plans		128	01-Oct-12	27-Mar-13	193	$0
NTE-3AIC-QMP-1000	Develop Quality management Plan (QMP)	110	01-Oct-12	06-Mar-13	189	$0
NTE-3AIC-QMP-1010	TxDOT Approval of QMP	15	07-Mar-13	27-Mar-13	188	$0
Developer Deliverables for NTP # 2		120	01-Oct-12	20-Mar-13	195	$0
NTE3AIC-DVLP-1000	Submit Developer Deliverables required for NTP # 2 (Letter of Credit, Insurance etc)	120	01-Oct-12	20-Mar-13	195	$0
Developer Activities		1017	01-May-14	23-Mar-18	0	$53,014,340
Segment 3A		1017	01-May-14	23-Mar-18	0	$32,338,747
Project System Design		280	01-May-14	27-May-15	447	$6,467,749
3A-CINT-DGN1	NCS / ITS / TCS System Design - Segment 3A	260	01-May-14	27-May-15	447	$6,467,749
Network Communication System (NCS)		105	09-Oct-17	02-Mar-18	10	$3,880,650
3A-CINT-NCS1	Pulling Fiber-Optic Backbone - Segment 3A	60	09-Oct-17	29-Dec-17	0	$1,616,937
3A-CINT-NCS2	NCS equipment installation - Segment 3A	30	09-Oct-17	17-Nov-17	40	$646,775
3A-CINT-NCS3	NCS Equipment Commissioning Test - Segment 3A	15	01-Jan-18	19-Jan-18	10	$646,775
3A-CINT-NCS4	NCS Site Integration Testing - Segment 3A	15	22-Jan-18	09-Feb-18	10	$323,387
3A-CINT-NCS5	NCS Operational Test - Segment 3A	10	12-Feb-18	23-Feb-18	10	$323,387
3A-CINT-NCS6	NCS/Central end-to-end Testing - Segment 3A	5	26-Feb-18	02-Mar-18	10	$323,387
Intelligent Transportation System (ITS)		120	09-Oct-17	23-Mar-18	0	$10,186,705
3A-CINT-ITS1	Microwave Vehicle Detector (MVD) - Segment 3A	60	09-Oct-17	29-Dec-17	0	$1,616,937
3A-CINT-ITS2	Traffic RFID Devices - Segment 3A	40	09-Oct-17	01-Dec-17	25	$970,162
3A-CINT-ITS3	CCTV Camera - Segment 3A	25	09-Oct-17	10-Nov-17	40	$970,162
3A-CINT-ITS4	Dynamic Message Sign (DMS) - Segment 3A	25	09-Oct-17	10-Nov-17	40	$1,616,937
3A-CINT-ITS5	Toll Rate DMS (TRDMS) - Segment 3A	10	09-Oct-17	20-Oct-17	55	$1,616,937
3A-CINT-ITS6	Weather Station - Segment 3A	5	09-Oct-17	13-Oct-17	0	$1,455,244
3A-CINT-ITS7	ITS Equipment Commissioning Testing - Segment 3A	60	16-Oct-17	05-Jan-18	0	$646,775
3A-CINT-ITS8	ITS System Integration Testing - Segment 3A	40	08-Jan-18	02-Mar-18	0	$646,775
3A-CINT-ITS9	ITS Operational Test - Segment 3A	10	05-Mar-18	16-Mar-18	0	$323,387
3A-CINT-ITS10	ITS/Central end-to-end testing - Segment 3A	5	19-Mar-18	23-Mar-18	0	$323,387
Toll Collection System (TCS)		120	09-Oct-17	23-Mar-18	0	$11,803,643
3A-CINT-TCS1	Gantry Structure Installation - Segment 3A	40	09-Oct-17	01-Dec-17	0	$2,102,019
3A-CINT-TCS3	TCS Central Equipment Installation - Segment 3A	30	09-Oct-17	17-Nov-17	55	$2,587,100
3A-CINT-TCS2	TCS Field Equipment installation - Segment 3A	45	04-Dec-17	02-Feb-18	0	$3,233,875

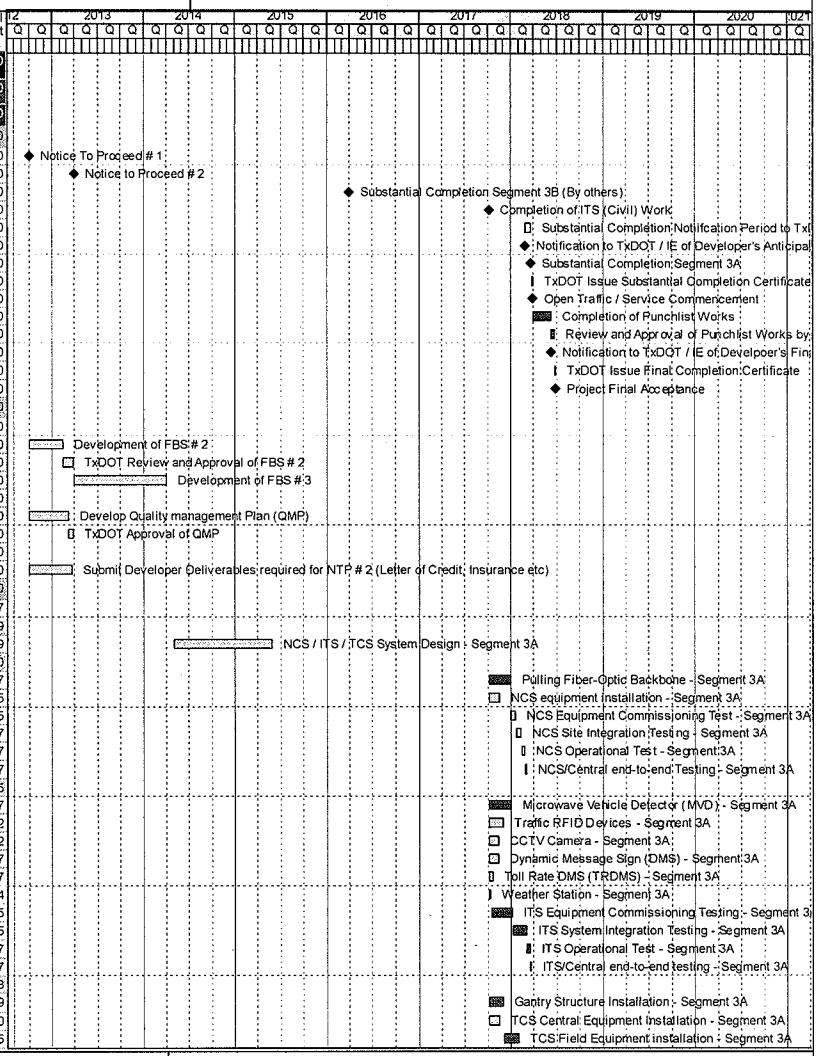

Remaining Level of Effort | Remaining Work
Actual Level of Effort | Critical Remaining Work
Actual Work | Milestone

NTE 3A / Interchange Project

DETAILED PROGRAM SCHEDULE
FBS1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3A-CINT-TCS4	TCS Equipment Commissioning Test - Segment 3A	10	05-Feb-18	16-Feb-18	0	$1,293,550
3A-CINT-TCS5	TCS Site Integration Testing - Segment 3A	10	19-Feb-18	02-Mar-18	0	$1,293,550
3A-CINT-TCS6	TCS Operational Test - Segment 3A	10	05-Mar-18	16-Mar-18	0	$646,775
3A-CINT-TCS7	TCS/Central end-to-end Testing - Segment 3A	5	19-Mar-18	23-Mar-18	0	$646,775
Segment 3B		594	01-May-14	09-Aug-16	423	$20,675,593
Project System Design		280	01-May-14	27-May-15	447	$4,135,119
3B-CINT-DGN1	NCS / ITS / TCS System Design - Segment 3B	280	01-May-14	27-May-15	447	$4,135,119
Network Communication System (NCS)		75	01-Jul-15	13-Oct-15	633	$2,481,071
3B-CINT-NCS1	Pulling Fiber-Optic Backbone - Segment 3B	30	01-Jul-15	11-Aug-15	423	$1,033,780
3B-CINT-NCS2	NCS equipment installation - Segment 3B	30	01-Jul-15	11-Aug-15	633	$413,512
3B-CINT-NCS3	NCS Equipment Commissioning Test - Segment 3B	15	12-Aug-15	01-Sep-15	633	$413,512
3B-CINT-NCS4	NCS Site Integration Testing - Segment 3B	15	02-Sep-15	22-Sep-15	633	$206,756
3B-CINT-NCS5	NCS Operational Test - Segment 3B	10	23-Sep-15	06-Oct-15	633	$206,756
3B-CINT-NCS6	NCS/Central end-to-end Testing - Segment 3B	5	07-Oct-15	13-Oct-15	633	$206,756
Intelligent Transportation System (ITS)		290	01-Jul-15	09-Aug-16	423	$6,512,812
3B-CINT-ITS1	Microwave Vehicle Detector (MVD) - Segment 3B	95	01-Jul-15	10-Nov-15	423	$1,033,780
3B-CINT-ITS2	Traffic RFID Devices - Segment 3B	38	11-Nov-15	01-Jan-16	490	$620,268
3B-CINT-ITS3	CCTV Camera - Segment 3B	15	11-Nov-15	01-Dec-15	513	$620,268
3B-CINT-ITS4	Dynamic Message Sign (DMS) - Segment 3B	20	11-Nov-15	08-Dec-15	508	$1,033,780
3B-CINT-ITS5	Toll Rate DMS (TRDMS) - Segment 3B	25	11-Nov-15	15-Dec-15	503	$1,033,780
3B-CINT-ITS6	Weather Station - Segment 3B	10	11-Nov-15	24-Nov-15	423	$930,402
3B-CINT-ITS7	ITS Equipment Commissioning Testing - Segment 3B	95	25-Nov-15	05-Apr-16	423	$413,512
3B-CINT-ITS8	ITS System Integration Testing - Segment 3B	75	06-Apr-16	19-Jul-16	423	$413,512
3B-CINT-ITS9	ITS Operational Test - Segment 3B	10	20-Jul-16	02-Aug-16	423	$206,756
3B-CINT-ITS10	ITS/Central end-to-end testing - Segment 3B	5	03-Aug-16	09-Aug-16	423	$206,756
Toll Collection System (TCS)		150	01-Jul-15	26-Jan-16	563	$7,546,591
3B-CINT-TCS1	Gantry Structure Installation - Segment 3B	45	01-Jul-15	01-Sep-15	563	$1,343,914
3B-CINT-TCS3	TCS Central Equipment Installation - Segment 3B	45	01-Jul-15	01-Sep-15	623	$1,654,047
3B-CINT-TCS2	TCS Field Equipment installation - Segment 3B	60	02-Sep-15	24-Nov-15	563	$2,067,559
3B-CINT-TCS4	TCS Equipment Commissioning Test - Segment 3B	15	25-Nov-15	15-Dec-15	563	$827,024
3B-CINT-TCS5	TCS Site Integration Testing - Segment 3B	15	16-Dec-15	05-Jan-16	563	$827,024
3B-CINT-TCS6	TCS Operational Test - Segment 3B	10	06-Jan-16	19-Jan-16	563	$413,512
3B-CINT-TCS7	TCS/Central end-to-end Testing - Segment 3B	5	20-Jan-16	26-Jan-16	563	$413,512
Right-of-Way Acquisition		548	01-Aug-12	05-Sep-14	925	$0
Acquisition by Developer		548	01-Aug-12	05-Sep-14	925	$0
NTE-ROWSTART	Start Right of Way Process	0	01-Aug-12*		1	$0
NTE-ROW-BATCH1	Finish ROW Batch 1 Review by TxDOT	0		14-Dec-12	13	$0
NTE-ROW-BATCH2	Start ROW Batch 2 Review by TxDOT	0	17-Dec-12		13	$0
NTE-ROW-BATCH2-1	Finish ROW Batch 2 Review by TxDOT	0		10-Jan-13	12	$0
NTE-ROW-BATCH3	Start ROW Batch 3 Review by TxDOT	0	11-Jan-13		12	$0
NTE-ROW-BATCH3-1	Finish ROW Batch 3 Review by TxDOT	0		01-Feb-13	12	$0
NTE-ROW-BATCH4	Start ROW Batch 4 Review by TxDOT	0	04-Feb-13		12	$0
NTE-ROW-BATCH4-1	Finish ROW Batch 4 Review by TxDOT	0		25-Feb-13	11	$0
NTE-ROW-BATCH5	Start ROW Batch 5 Review by TxDOT	0	26-Feb-13		11	$0
NTE-ROW-BATCH5-1	Finish ROW Batch 5 Review by TxDOT	0		01-Apr-13	1	$0
NTE-ROW-BATCH6	Start ROW Batch 6 Review by TxDOT	0	02-Apr-13		1	$0
NTE-ROW-BATCH6-1	Finish ROW Batch 6 Review by TxDOT	0		15-Apr-13	1	$0
NTE-ROW-BATCH7	Start ROW Batch 7 Review by TxDOT	0	16-Apr-13		1	$0
NTE-ROW-BATCH7-1	Finish ROW Batch 7 Review by TxDOT	0		29-Apr-13	11	$0
NTE-ROW-BATCH8	Start ROW Batch 8 Review by TxDOT	0	30-Apr-13		11	$0
NTE-ROW-BATCH8-1	Finish ROW Batch 8 Review by TxDOT	0		28-May-13	140	$0
NTE-ROW-BATCH9	Start ROW Batch 9 Review by TxDOT	0	29-May-13		140	$0
NTE-ROWFINISH	Complete Right of Way Process	0		05-Sep-14	1297	$0
Parcels Needing Relocation		548	01-Aug-12	05-Sep-14	382	$0
Parcel #8 SBFR - Meacham to Dewey (STA 679+00 to STA 687+00)		400	01-Aug-12	11-Feb-14	141	$0
3ASBFRMDMSRO810	Parcel #8 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO81010	Parcel #8 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO81020	Parcel #8 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRMDRO81030	Parcel #8 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRMDRO81050	Parcel #8 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0

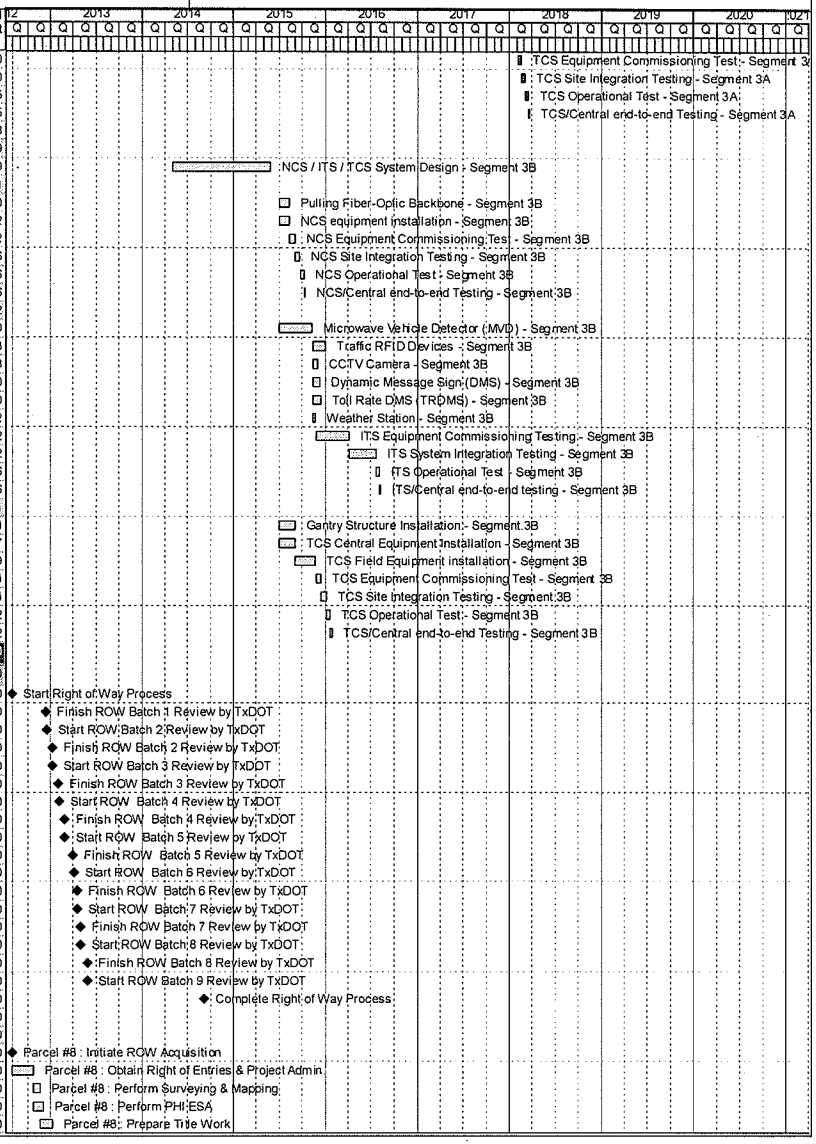

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRMDRO81040	Parcel #8 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRMDRO81060	Parcel #8 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRMDRO81070	Parcel #8 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRMDRO81080	Parcel #8 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRMDRO81090	Parcel #8 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	139	$0
3ASBFRMDRO81100	Parcel #8 : Parcel closing	20	30-Apr-13	28-May-13	229	$0
3ASBFRMDRO81110	Parcel #8 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	139	$0
3ASBFRMDRO81120	Parcel #8 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	139	$0
3ASBFRMDRO81130	Parcel #8 : Execute Relocation	20	15-Nov-13	13-Dec-13	139	$0
3ASBFRMDRO81140	Parcel #8 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	139	$0
3ASBFRMDRO81150	Parcel #8 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	139	$0
3ASBFRMDMSRO811	Parcel #8 : Cleared for Construction	0		11-Feb-14	197	$0
Parcel #15 SBFR - Meacham to Dewey (STA 700+00 to STA 700+00)		400	01-Aug-12	11-Feb-14	141	$0
3ASBFRMDMSRO151	Parcel #15 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO151010	Parcel #15 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO151020	Parcel #15 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRMDRO151030	Parcel #15 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRMDRO151050	Parcel #15 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRMDRO151040	Parcel #15 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRMDRO151060	Parcel #15 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRMDRO151070	Parcel #15 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRMDRO151080	Parcel #15 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRMDRO151090	Parcel #15 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	139	$0
3ASBFRMDRO151100	Parcel #15 : Parcel closing	20	30-Apr-13	28-May-13	229	$0
3ASBFRMDRO151110	Parcel #15 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	139	$0
3ASBFRMDRO151120	Parcel #15 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	139	$0
3ASBFRMDRO151130	Parcel #15 : Execute Relocation	20	15-Nov-13	13-Dec-13	139	$0
3ASBFRMDRO151140	Parcel #15 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	139	$0
3ASBFRMDRO151150	Parcel #15 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	139	$0
3ASBFRMDMSRO151	Parcel #15 : Cleared for Construction	0		11-Feb-14	197	$0
Parcel #25 SBGP - Meacham to Dewey (STA 730+00 to STA 730+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBGPMDMSRO251	Parcel #25 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPMDRO251010	Parcel #25 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPMDRO251020	Parcel #25 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBGPMDRO251030	Parcel #25 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBGPMDRO251050	Parcel #25 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBGPMDRO251040	Parcel #25 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBGPMDRO251060	Parcel #25 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBGPMDRO251070	Parcel #25 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBGPMDRO251080	Parcel #25 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBGPMDRO251090	Parcel #25 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBGPMDRO251100	Parcel #25 : Parcel closing	20	30-Apr-13	28-May-13	228	$0
3ASBGPMDRO251110	Parcel #25 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBGPMDRO251120	Parcel #25 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBGPMDRO251130	Parcel #25 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBGPMDRO251140	Parcel #25 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBGPMDRO251150	Parcel #25 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBGPMDMSRO251	Parcel #25 : Cleared for Construction	0		11-Feb-14	196	$0
Parcel #27 SBGP - Meacham to Dewey (STA 735+00 to STA 735+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBGPMDMSRO271	Parcel #27 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPMDRO271010	Parcel #27 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPMDRO271020	Parcel #27 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBGPMDRO271030	Parcel #27 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBGPMDRO271050	Parcel #27 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBGPMDRO271040	Parcel #27 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBGPMDRO271060	Parcel #27 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBGPMDRO271070	Parcel #27 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBGPMDRO271080	Parcel #27 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBGPMDRO271090	Parcel #27 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBGPMDRO271100	Parcel #27 : Parcel closing	20	30-Apr-13	28-May-13	228	$0

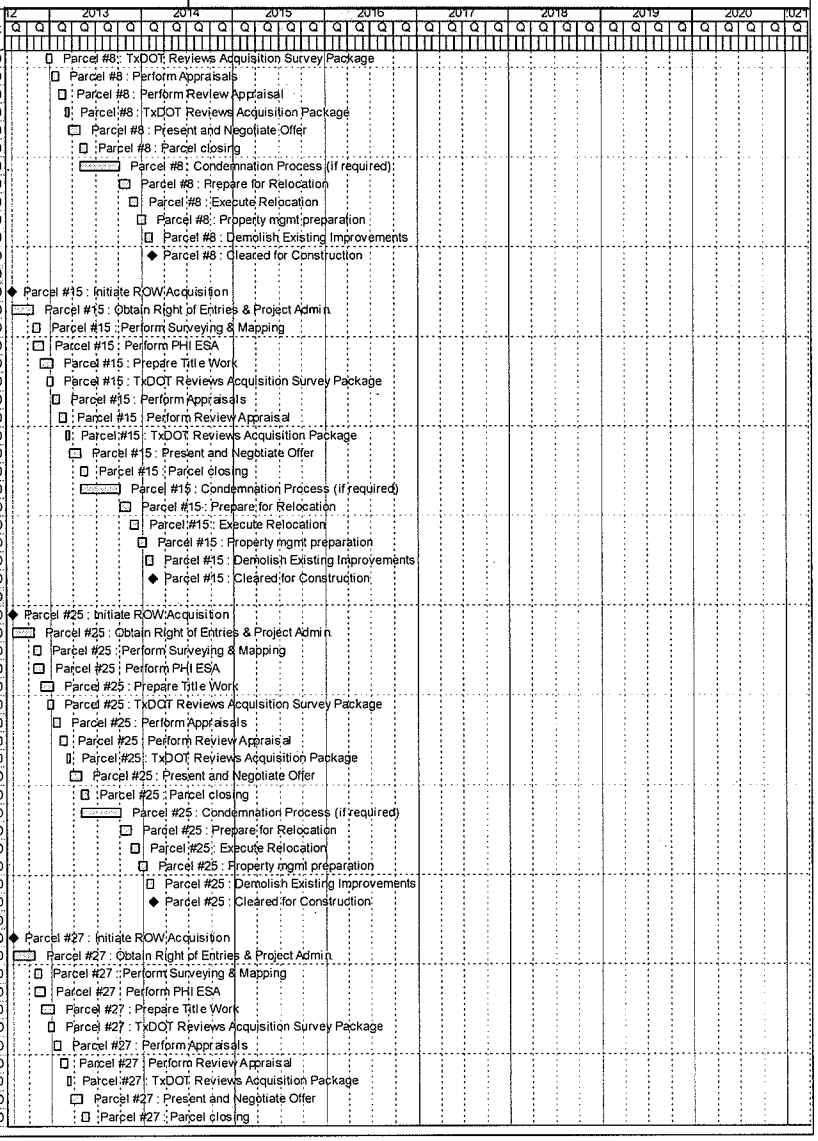

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBGPMDRO271110	Parcel #27 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBGPMDRO271120	Parcel #27 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBGPMDRO271130	Parcel #27 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBGPMDRO271140	Parcel #27 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBGPMDRO271150	Parcel #27 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBGPMDMSRO271	Parcel #27 : Cleared for Construction	0		11-Feb-14	196	$0
Parcel #29 SBGP - Meacham to Dewey (STA 737+00 to STA 737+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBGPMDMSRO291	Parcel #29 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPMDRO291010	Parcel #29 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPMDRO291020	Parcel #29 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBGPMDRO291030	Parcel #29 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBGPMDRO291050	Parcel #29 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBGPMDRO291040	Parcel #29 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBGPMDRO291060	Parcel #29 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBGPMDRO291070	Parcel #29 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBGPMDRO291080	Parcel #29 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBGPMDRO291090	Parcel #29 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBGPMDRO291100	Parcel #29 : Parcel closing	20	30-Apr-13	28-May-13	228	$0
3ASBGPMDRO291110	Parcel #29 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBGPMDRO291120	Parcel #29 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBGPMDRO291130	Parcel #29 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBGPMDRO291140	Parcel #29 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBGPMDRO291150	Parcel #29 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBGPMDMSRO291	Parcel #29 : Cleared for Construction	0		11-Feb-14	196	$0
Parcel #31 NBGP - Meacham to Dewey (STA 736+00 to STA 736+00)		476	01-Aug-12	28-May-14	440	$0
3ANBGPMDMSRO311	Parcel #31 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ANBGPMDRO311010	Parcel #31 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	46	$0
3ANBGPMDRO311020	Parcel #31 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ANBGPMDRO311030	Parcel #31 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	180	$0
3ANBGPMDRO311050	Parcel #31 : Prepare Title Work	30	08-Jan-13	18-Feb-13	160	$0
3ANBGPMDRO311060	Parcel #31 : Perform Appraisals	20	19-Feb-13	18-Mar-13	160	$0
3ANBGPMDRO311040	Parcel #31 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ANBGPMDRO311070	Parcel #31 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	160	$0
3ANBGPMDRO311080	Parcel #31 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPMDRO311090	Parcel #31 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	430	$0
3ANBGPMDRO311100	Parcel #31 : Parcel closing	20	18-Jul-13	14-Aug-13	540	$0
3ANBGPMDRO311110	Parcel #31 : Condemnation Process (if required)	130	18-Jul-13	21-Jan-14	430	$0
3ANBGPMDRO311120	Parcel #31 : Prepare for Relocation	30	22-Jan-14	04-Mar-14	430	$0
3ANBGPMDRO311130	Parcel #31 : Execute Relocation	20	05-Mar-14	01-Apr-14	430	$0
3ANBGPMDRO311140	Parcel #31 : Property mgmt preparation	20	02-Apr-14	29-Apr-14	430	$0
3ANBGPMDRO311150	Parcel #31 : Demolish Existing Improvements	20	30-Apr-14	28-May-14	430	$0
3ANBGPMDMSRO311	Parcel #31 : Cleared for Construction	0		28-May-14	616	$0
Parcel #34 SBFR - Meacham to Dewey (STA 743+00 to STA 743+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBFRMDMSRO341	Parcel #34 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO341010	Parcel #34 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO341020	Parcel #34 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRMDRO341030	Parcel #34 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRMDRO341050	Parcel #34 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRMDRO341040	Parcel #34 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRMDRO341060	Parcel #34 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRMDRO341070	Parcel #34 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRMDRO341080	Parcel #34 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRMDRO341090	Parcel #34 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBFRMDRO341100	Parcel #34 : Parcel closing	20	30-Apr-13	28-May-13	228	$0
3ASBFRMDRO341110	Parcel #34 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBFRMDRO341120	Parcel #34 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBFRMDRO341130	Parcel #34 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBFRMDRO341140	Parcel #34 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBFRMDRO341150	Parcel #34 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBFRMDMSRO341	Parcel #34 : Cleared for Construction	0		11-Feb-14	196	$0

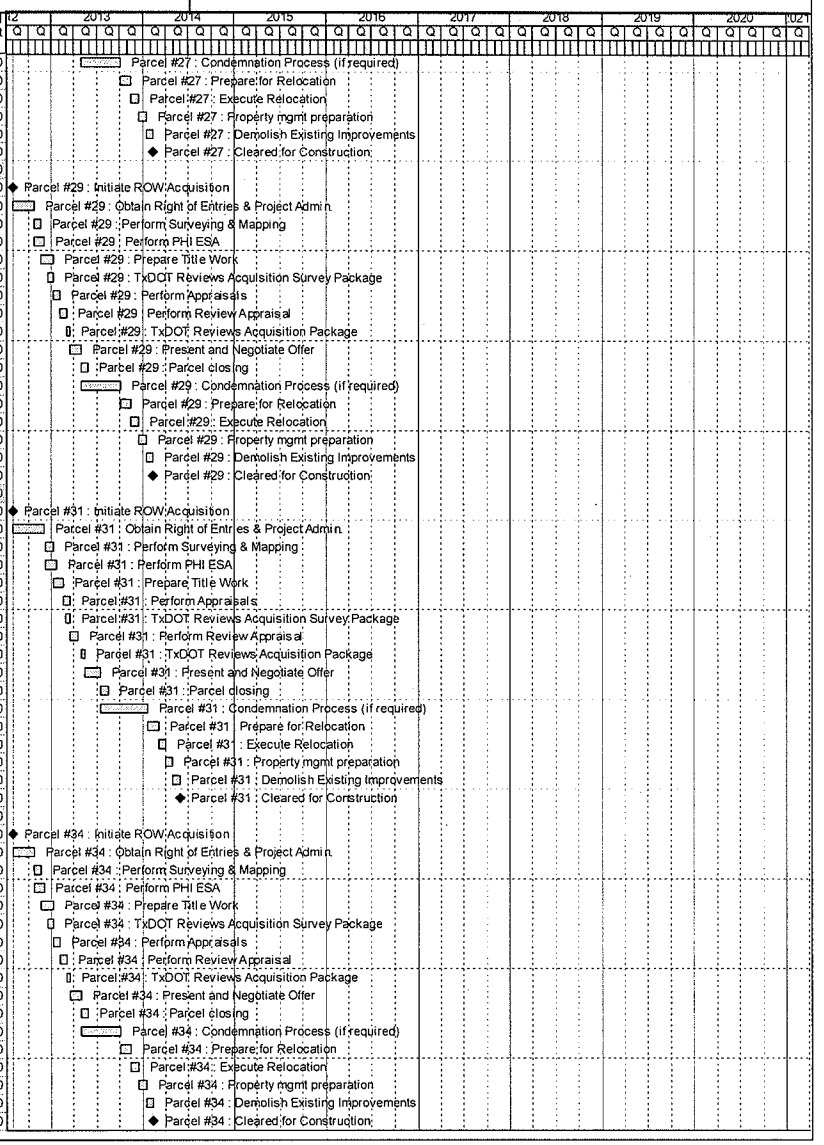

ATTACHMENT 03 - DETAILED PROGRAM SCHEDULE

NTE - Segment 3A Interchange Project - FBS # 1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Parcel #39 SBFR - Meacham to Dewey (STA 746+00 to STA 746+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBFRMDMSRO391	Parcel #39 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO391010	Parcel #39 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO391020	Parcel #39 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRMDRO391030	Parcel #39 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRMDRO391050	Parcel #39 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRMDRO391040	Parcel #39 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRMDRO391060	Parcel #39 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRMDRO391070	Parcel #39 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRMDRO391080	Parcel #39 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRMDRO391090	Parcel #39 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBFRMDRO391100	Parcel #39 : Parcel closing	20	30-Apr-13	28-May-13	228	$0
3ASBFRMDRO391110	Parcel #39 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBFRMDRO391120	Parcel #39 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBFRMDRO391130	Parcel #39 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBFRMDRO391140	Parcel #39 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBFRMDRO391150	Parcel #39 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBFRMDMSRO391	Parcel #39 : Cleared for Construction	0		11-Feb-14	196	$0
Parcel #41 (TxDOT #821) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 747+00 to STA 747+00)		537	01-Aug-12	21-Aug-14	3	$0
3ASBFRMDMSRO411	Parcel #41 : Initiate ROW Acquisition	0	01-Aug-12		5	$0
3ASBFRMDRO411010	Parcel #41 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	3	$0
3ASBFRMDRO411020	Parcel #41 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	3	$0
3ASBFRMDRO411030	Parcel #41 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	23	$0
3ASBFRMDRO411050	Parcel #41 : Prepare Title Work	30	08-Jan-13	18-Feb-13	3	$0
3ASBFRMDRO411040	Parcel #41 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRMDRO411060	Parcel #41 : Perform Appraisals	20	19-Feb-13	18-Mar-13	3	$0
3ASBFRMDRO411070	Parcel #41 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	3	$0
3ASBFRMDRO411080	Parcel #41 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	3	$0
3ASBFRMDRO411090	Parcel #41 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	3	$0
3ASBFRMDRO411100	Parcel #41 : Parcel closing	60	06-Sep-13	29-Nov-13	98	$0
3ASBFRMDRO411110	Parcel #41 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	3	$0
3ASBFRMDRO411120	Parcel #41 : Prepare for Relocation	30	16-Apr-14	28-May-14	3	$0
3ASBFRMDRO411130	Parcel #41 : Execute Relocation	20	29-May-14	25-Jun-14	3	$0
3ASBFRMDRO411140	Parcel #41 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	3	$0
3ASBFRMDRO411150	Parcel #41 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	3	$0
3ASBFRMDMSRO411	Parcel #41 : Cleared for Construction	0		21-Aug-14	5	$0
Parcel #43 SBFR - Meacham to Dewey (STA 750+00 to STA 750+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBFRMDMSRO431	Parcel #43 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO431010	Parcel #43 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO431020	Parcel #43 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRMDRO431030	Parcel #43 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRMDRO431050	Parcel #43 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRMDRO431040	Parcel #43 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRMDRO431060	Parcel #43 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRMDRO431070	Parcel #43 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRMDRO431080	Parcel #43 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRMDRO431090	Parcel #43 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBFRMDRO431100	Parcel #43 : Parcel closing	20	30-Apr-13	28-May-13	228	$0
3ASBFRMDRO431110	Parcel #43 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBFRMDRO431120	Parcel #43 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBFRMDRO431130	Parcel #43 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBFRMDRO431140	Parcel #43 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBFRMDRO431150	Parcel #43 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBFRMDMSRO431	Parcel #43 : Cleared for Construction	0		11-Feb-14	196	$0
Parcel #44 (TxDOT #825) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 752+00 to STA 752+00)		537	01-Aug-12	21-Aug-14	3	$0
3ASBFRMDMSRO441	Parcel #44 : Initiate ROW Acquisition	0	01-Aug-12		5	$0
3ASBFRMDRO441010	Parcel #44 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	3	$0
3ASBFRMDRO441020	Parcel #44 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	3	$0
3ASBFRMDRO441030	Parcel #44 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	23	$0
3ASBFRMDRO441050	Parcel #44 : Prepare Title Work	30	08-Jan-13	18-Feb-13	3	$0

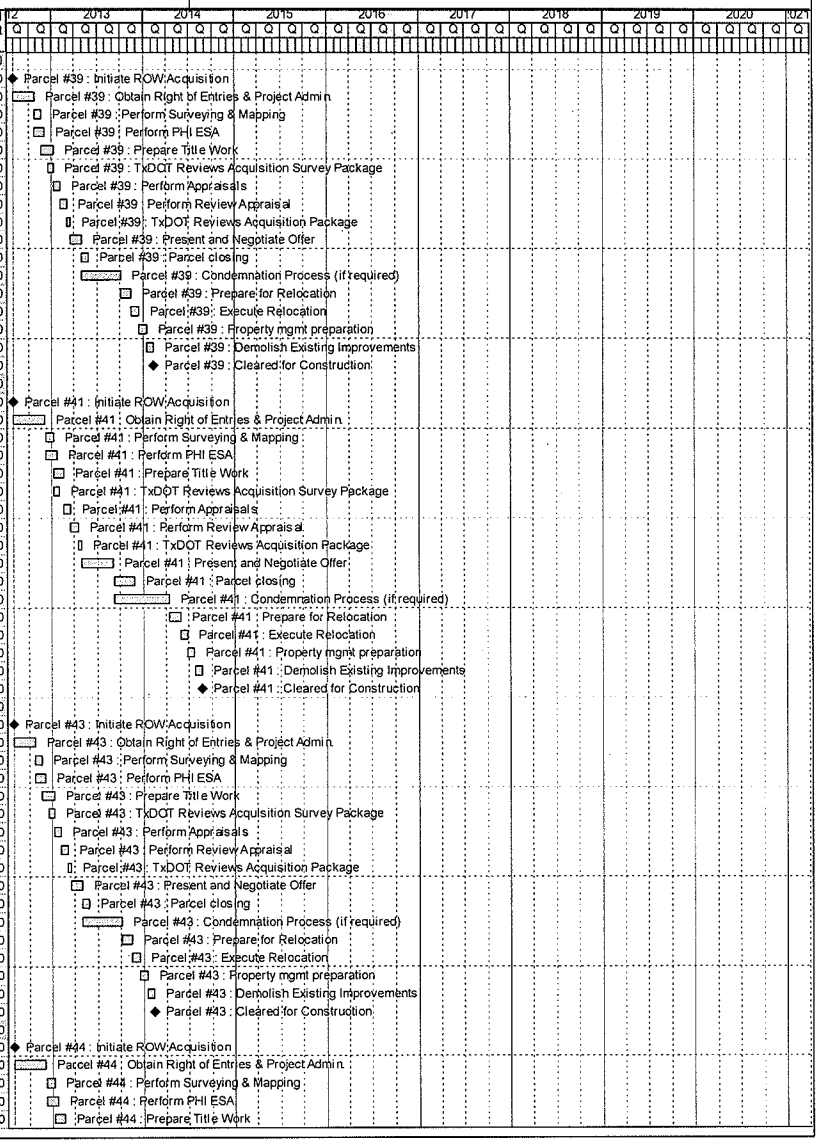

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRMDRO441040	Parcel #44 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRMDRO441060	Parcel #44 : Perform Appraisals	20	19-Feb-13	18-Mar-13	3	$0
3ASBFRMDRO441070	Parcel #44 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	3	$0
3ASBFRMDRO441080	Parcel #44 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	3	$0
3ASBFRMDRO441090	Parcel #44 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	3	$0
3ASBFRMDRO441100	Parcel #44 : Parcel closing	60	06-Sep-13	29-Nov-13	98	$0
3ASBFRMDRO441110	Parcel #44 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	3	$0
3ASBFRMDRO441120	Parcel #44 : Prepare for Relocation	30	16-Apr-14	28-May-14	3	$0
3ASBFRMDRO441130	Parcel #44 : Execute Relocation	20	29-May-14	25-Jun-14	3	$0
3ASBFRMDRO441140	Parcel #44 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	3	$0
3ASBFRMDRO441150	Parcel #44 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	3	$0
3ASBFRMDMSRO441	Parcel #44 : Cleared for Construction	0		21-Aug-14	5	$0
Parcel #51 SBFR - Meacham to Dewey (STA 757+00 to STA 757+00)		400	01-Aug-12	11-Feb-14	140	$0
3ASBFRMDMSRO511	Parcel #51 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO511010	Parcel #51 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO511020	Parcel #51 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRMDRO511030	Parcel #51 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRMDRO511050	Parcel #51 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRMDRO511040	Parcel #51 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRMDRO511060	Parcel #51 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRMDRO511070	Parcel #51 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRMDRO511080	Parcel #51 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRMDRO511090	Parcel #51 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	138	$0
3ASBFRMDRO511100	Parcel #51 : Parcel closing	20	30-Apr-13	28-May-13	228	$0
3ASBFRMDRO511110	Parcel #51 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	138	$0
3ASBFRMDRO511120	Parcel #51 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	138	$0
3ASBFRMDRO511130	Parcel #51 : Execute Relocation	20	15-Nov-13	13-Dec-13	138	$0
3ASBFRMDRO511140	Parcel #51 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	138	$0
3ASBFRMDRO511150	Parcel #51 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	138	$0
3ASBFRMDMSRO511	Parcel #51 : Cleared for Construction	0		11-Feb-14	196	$0
Parcel #52 (TxDOT #830) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 757+00 to STA 762+50)		537	01-Aug-12	21-Aug-14	3	$0
3ASBFRMDMSRO521	Parcel #52 : Initiate ROW Acquisition	0	01-Aug-12		5	$0
3ASBFRMDRO521010	Parcel #52 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	3	$0
3ASBFRMDRO521020	Parcel #52 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	3	$0
3ASBFRMDRO521030	Parcel #52 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	23	$0
3ASBFRMDRO521050	Parcel #52 : Prepare Title Work	30	08-Jan-13	18-Feb-13	3	$0
3ASBFRMDRO521040	Parcel #52 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRMDRO521060	Parcel #52 : Perform Appraisals	20	19-Feb-13	18-Mar-13	3	$0
3ASBFRMDRO521070	Parcel #52 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	3	$0
3ASBFRMDRO521080	Parcel #52 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	3	$0
3ASBFRMDRO521090	Parcel #52 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	3	$0
3ASBFRMDRO521100	Parcel #52 : Parcel closing	60	06-Sep-13	29-Nov-13	98	$0
3ASBFRMDRO521110	Parcel #52 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	3	$0
3ASBFRMDRO521120	Parcel #52 : Prepare for Relocation	30	16-Apr-14	28-May-14	3	$0
3ASBFRMDRO521130	Parcel #52 : Execute Relocation	20	29-May-14	25-Jun-14	3	$0
3ASBFRMDRO521140	Parcel #52 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	3	$0
3ASBFRMDRO521150	Parcel #52 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	3	$0
3ASBFRMDMSRO521	Parcel #52 : Cleared for Construction	0		21-Aug-14	5	$0
Parcel #61 (TxDOT #835) - COMPLEX PARCEL - SBFR - Meacham to Dewey (STA 771+50 to STA 776+00)		537	01-Aug-12	21-Aug-14	3	$0
3ASBFRMDMSRO611	Parcel #61 : Initiate ROW Acquisition	0	01-Aug-12		5	$0
3ASBFRMDRO611010	Parcel #61 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	3	$0
3ASBFRMDRO611020	Parcel #61 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	3	$0
3ASBFRMDRO611030	Parcel #61 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	23	$0
3ASBFRMDRO611050	Parcel #61 : Prepare Title Work	30	08-Jan-13	18-Feb-13	3	$0
3ASBFRMDRO611040	Parcel #61 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRMDRO611060	Parcel #61 : Perform Appraisals	20	19-Feb-13	18-Mar-13	3	$0
3ASBFRMDRO611070	Parcel #61 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	3	$0
3ASBFRMDRO611080	Parcel #61 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	3	$0
3ASBFRMDRO611090	Parcel #61 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	3	$0
3ASBFRMDRO611100	Parcel #61 : Parcel closing	60	06-Sep-13	29-Nov-13	98	$0

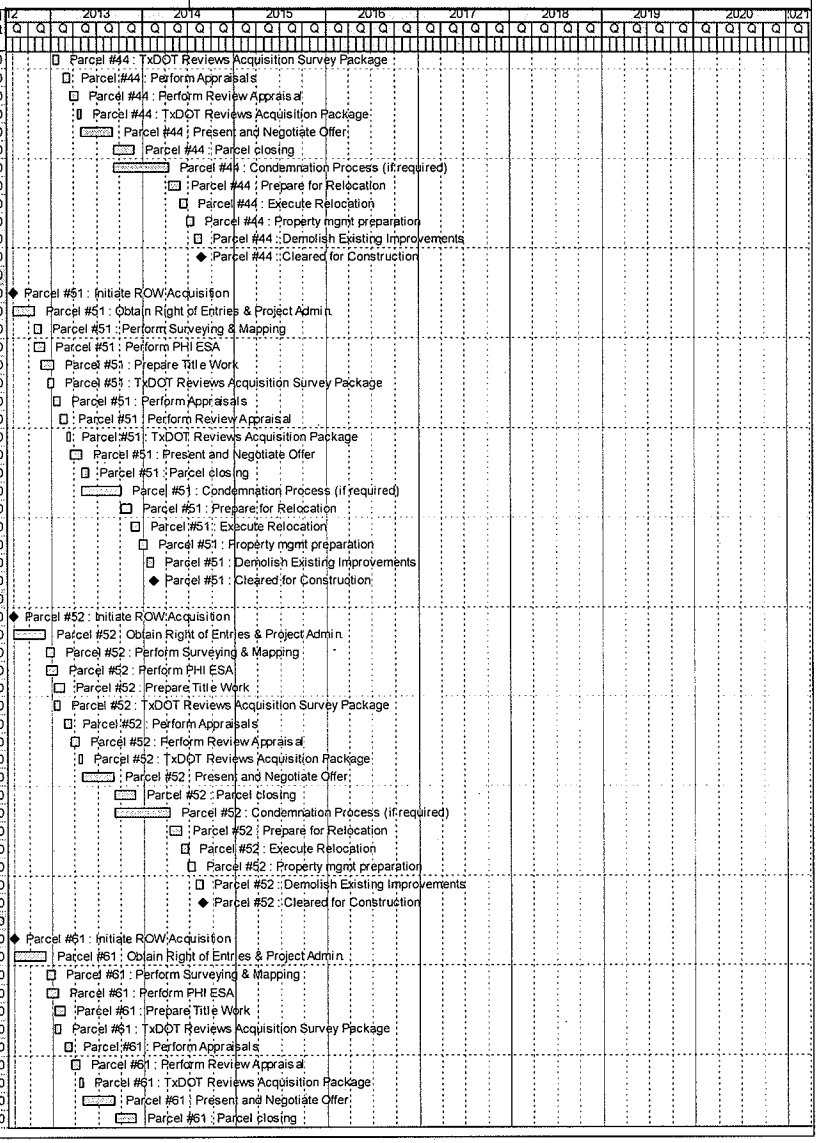

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRMDRO611110	Parcel #61 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	3	$0
3ASBFRMDRO611120	Parcel #61 : Prepare for Relocation	30	16-Apr-14	28-May-14	3	$0
3ASBFRMDRO611130	Parcel #61 : Execute Relocation	20	29-May-14	25-Jun-14	3	$0
3ASBFRMDRO611140	Parcel #61 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	3	$0
3ASBFRMDRO611150	Parcel #61 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	3	$0
3ASBFRMDMSRO611	Parcel #61 : Cleared for Construction	0		21-Aug-14	5	$0
Parcel #64 SBFR - Dewey to S. of trinity River (STA 777+00 to STA 777+00)		400	01-Aug-12	11-Feb-14	141	$0
3ASBFRDTMSRO641	Parcel #64 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRDTRO641010	Parcel #64 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRDTRO641020	Parcel #64 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRDTRO641030	Parcel #64 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRDTRO641050	Parcel #64 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRDTRO641040	Parcel #64 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRDTRO641060	Parcel #64 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRDTRO641070	Parcel #64 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRDTRO641080	Parcel #64 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRDTRO641090	Parcel #64 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	139	$0
3ASBFRDTRO641100	Parcel #64 : Parcel closing	20	30-Apr-13	28-May-13	229	$0
3ASBFRDTRO641110	Parcel #64 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	139	$0
3ASBFRDTRO641120	Parcel #64 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	139	$0
3ASBFRDTRO641130	Parcel #64 : Execute Relocation	20	15-Nov-13	13-Dec-13	139	$0
3ASBFRDTRO641140	Parcel #64 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	139	$0
3ASBFRDTRO641150	Parcel #64 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	139	$0
3ASBFRDTMSRO641	Parcel #64 : Cleared for Construction	0		11-Feb-14	197	$0
Parcel #65 (TxDOT #836) - COMPLEX - SBFR - Dewey to S. of Trinity River (STA 781+00 to STA 781+00)		537	01-Aug-12	21-Aug-14	4	$0
3ASBFRDTMSRO651	Parcel #65 : Initiate ROW Acquisition	0	01-Aug-12		6	$0
3ASBFRDTRO651010	Parcel #65 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	4	$0
3ASBFRDTRO651020	Parcel #65 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	4	$0
3ASBFRDTRO651030	Parcel #65 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	24	$0
3ASBFRDTRO651050	Parcel #65 : Prepare Title Work	30	08-Jan-13	18-Feb-13	4	$0
3ASBFRDTRO651040	Parcel #65 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRDTRO651060	Parcel #65 : Perform Appraisals	20	19-Feb-13	18-Mar-13	4	$0
3ASBFRDTRO651070	Parcel #65 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	4	$0
3ASBFRDTRO651080	Parcel #65 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	4	$0
3ASBFRDTRO651090	Parcel #65 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	4	$0
3ASBFRDTRO651100	Parcel #65 : Parcel closing	60	06-Sep-13	29-Nov-13	99	$0
3ASBFRDTRO651110	Parcel #65 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	4	$0
3ASBFRDTRO651120	Parcel #65 : Prepare for Relocation	30	16-Apr-14	28-May-14	4	$0
3ASBFRDTRO651130	Parcel #65 : Execute Relocation	20	29-May-14	25-Jun-14	4	$0
3ASBFRDTRO651140	Parcel #65 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	4	$0
3ASBFRDTRO651150	Parcel #65 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	4	$0
3ASBFRDTMSRO651	Parcel #65 : Cleared for Construction	0		21-Aug-14	6	$0
Parcel #71 SBFR - Dewey to S. of trinity River (STA 788+00 to STA 788+00)		400	01-Aug-12	11-Feb-14	200	$0
3ASBFRDTMSRO711	Parcel #71 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRDTRO711010	Parcel #71 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRDTRO711020	Parcel #71 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRDTRO711030	Parcel #71 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRDTRO711050	Parcel #71 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRDTRO711060	Parcel #71 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRDTRO711040	Parcel #71 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRDTRO711070	Parcel #71 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRDTRO711080	Parcel #71 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRDTRO711090	Parcel #71 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	197	$0
3ASBFRDTRO711100	Parcel #71 : Parcel closing	20	30-Apr-13	28-May-13	287	$0
3ASBFRDTRO711110	Parcel #71 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	197	$0
3ASBFRDTRO711120	Parcel #71 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	197	$0
3ASBFRDTRO711130	Parcel #71 : Execute Relocation	20	15-Nov-13	13-Dec-13	197	$0
3ASBFRDTRO711140	Parcel #71 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	197	$0
3ASBFRDTRO711150	Parcel #71 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	197	$0
3ASBFRDTMSRO711	Parcel #71 : Cleared for Construction	0		11-Feb-14	280	$0

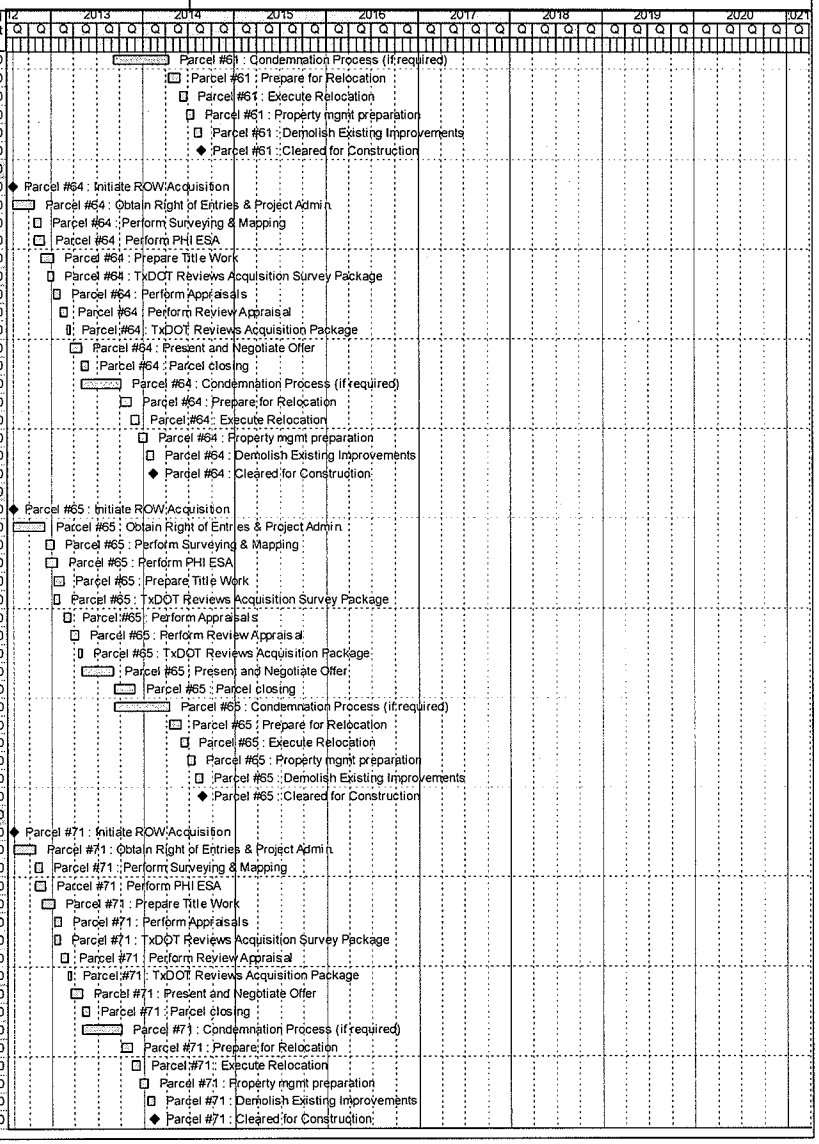

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Parcel #72 (TxDOT #841) - COMPLEX - SBFR - Dewey to S. of Trinity River (STA 790+00 to STA 795+00)		537	01-Aug-12	21-Aug-14	4	$0
3ASBFRDTMSRO721	Parcel #72 : Initiate ROW Acquisition	0	01-Aug-12		6	$0
3ASBFRDTRO721010	Parcel #72 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	4	$0
3ASBFRDTRO721020	Parcel #72 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	4	$0
3ASBFRDTRO721030	Parcel #72 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	24	$0
3ASBFRDTRO721050	Parcel #72 : Prepare Title Work	30	08-Jan-13	18-Feb-13	4	$0
3ASBFRDTRO721040	Parcel #72 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRDTRO721060	Parcel #72 : Perform Appraisals	20	19-Feb-13	18-Mar-13	4	$0
3ASBFRDTRO721070	Parcel #72 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	4	$0
3ASBFRDTRO721080	Parcel #72 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	4	$0
3ASBFRDTRO721090	Parcel #72 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	4	$0
3ASBFRDTRO721100	Parcel #72 : Parcel closing	60	06-Sep-13	29-Nov-13	99	$0
3ASBFRDTRO721110	Parcel #72 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	4	$0
3ASBFRDTRO721120	Parcel #72 : Prepare for Relocation	30	16-Apr-14	28-May-14	4	$0
3ASBFRDTRO721130	Parcel #72 : Execute Relocation	20	29-May-14	25-Jun-14	4	$0
3ASBFRDTRO721140	Parcel #72 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	4	$0
3ASBFRDTRO721150	Parcel #72 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	4	$0
3ASBFRDTMSRO721	Parcel #72 : Cleared for Construction	0		21-Aug-14	6	$0
Parcel #73 (TxDOT #842) - COMPLEX - SBRP - Dewey to S. of Trinity River (STA 795+00 to STA 800+00)		537	01-Aug-12	21-Aug-14	4	$0
3ASBRPDTMSRO731	Parcel #73 : Initiate ROW Acquisition	0	01-Aug-12		6	$0
3ASBRPDTRO731010	Parcel #73 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	4	$0
3ASBRPDTRO731020	Parcel #73 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	4	$0
3ASBRPDTRO731030	Parcel #73 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	24	$0
3ASBRPDTRO731050	Parcel #73 : Prepare Title Work	30	08-Jan-13	18-Feb-13	4	$0
3ASBRPDTRO731040	Parcel #73 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBRPDTRO731060	Parcel #73 : Perform Appraisals	20	19-Feb-13	18-Mar-13	4	$0
3ASBRPDTRO731070	Parcel #73 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	4	$0
3ASBRPDTRO731080	Parcel #73 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	4	$0
3ASBRPDTRO731090	Parcel #73 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	4	$0
3ASBRPDTRO731100	Parcel #73 : Parcel closing	60	06-Sep-13	29-Nov-13	99	$0
3ASBRPDTRO731110	Parcel #73 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	4	$0
3ASBRPDTRO731120	Parcel #73 : Prepare for Relocation	30	16-Apr-14	28-May-14	4	$0
3ASBRPDTRO731130	Parcel #73 : Execute Relocation	20	29-May-14	25-Jun-14	4	$0
3ASBRPDTRO731140	Parcel #73 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	4	$0
3ASBRPDTRO731150	Parcel #73 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	4	$0
3ASBRPDTMSRO731	Parcel #73 : Cleared for Construction	0		21-Aug-14	6	$0
Parcel #76 SBML - Dewey to S. of trinity River (STA 805+00 to STA 806+00)		400	01-Aug-12	11-Feb-14	200	$0
3ANSMLDTMSRO761	Parcel #76 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANSMLDTRO761010	Parcel #76 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANSMLDTRO761020	Parcel #76 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ANSMLDTRO761030	Parcel #76 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANSMLDTRO761050	Parcel #76 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ANSMLDTRO761060	Parcel #76 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ANSMLDTRO761040	Parcel #76 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANSMLDTRO761070	Parcel #76 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ANSMLDTRO761080	Parcel #76 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ANSMLDTRO761090	Parcel #76 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	197	$0
3ANSMLDTRO761100	Parcel #76 : Parcel closing	20	30-Apr-13	28-May-13	287	$0
3ANSMLDTRO761110	Parcel #76 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	197	$0
3ANSMLDTRO761120	Parcel #76 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	197	$0
3ANSMLDTRO761130	Parcel #76 : Execute Relocation	20	15-Nov-13	13-Dec-13	197	$0
3ANSMLDTRO761140	Parcel #76 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	197	$0
3ANSMLDTRO761150	Parcel #76 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	197	$0
3ANSMLDTMSRO761	Parcel #76 : Cleared for Construction	0		11-Feb-14	280	$0
Parcel #77 (TxDOT #846) - COMPLEX - SBGP - Dewey to S. of Trinity River (STA 805+00 to STA 810+00)		537	01-Aug-12	21-Aug-14	4	$0
3ASBGPDTMSRO771	Parcel #77 : Initiate ROW Acquisition	0	01-Aug-12		6	$0
3ASBGPDTRO771010	Parcel #77 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	4	$0
3ASBGPDTRO771020	Parcel #77 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	4	$0
3ASBGPDTRO771030	Parcel #77 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	24	$0
3ASBGPDTRO771050	Parcel #77 : Prepare Title Work	30	08-Jan-13	18-Feb-13	4	$0

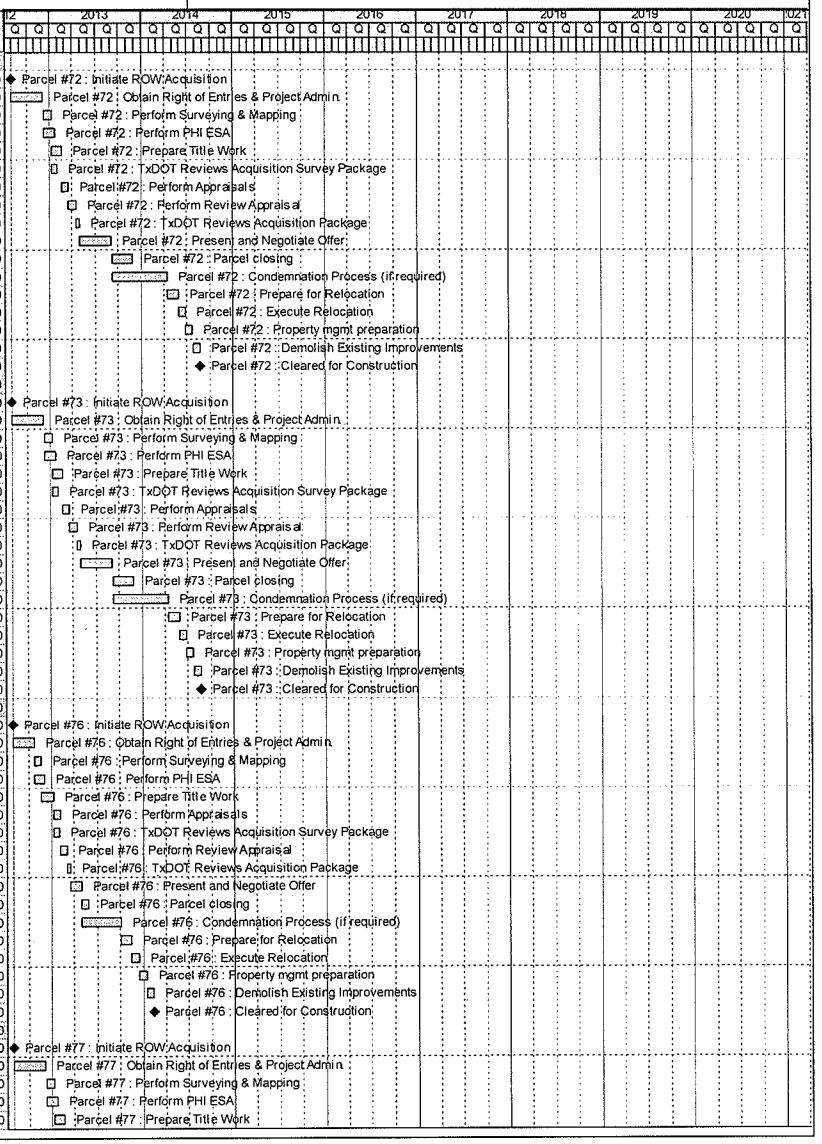

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBGPDTRO771040	Parcel #77 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBGPDTRO771060	Parcel #77 : Perform Appraisals	20	19-Feb-13	18-Mar-13	4	$0
3ASBGPDTRO771070	Parcel #77 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	4	$0
3ASBGPDTRO771080	Parcel #77 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	4	$0
3ASBGPDTRO771090	Parcel #77 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	4	$0
3ASBGPDTRO771100	Parcel #77 : Parcel closing	60	06-Sep-13	29-Nov-13	99	$0
3ASBGPDTRO771110	Parcel #77 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	4	$0
3ASBGPDTRO771120	Parcel #77 : Prepare for Relocation	30	16-Apr-14	28-May-14	4	$0
3ASBGPDTRO771130	Parcel #77 : Execute Relocation	20	29-May-14	25-Jun-14	4	$0
3ASBGPDTRO771140	Parcel #77 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	4	$0
3ASBGPDTRO771150	Parcel #77 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	4	$0
3ASBGPDTMSRO771	Parcel #77 : Cleared for Construction	0		21-Aug-14	6	$0
Parcel #88/80(TxDOT #847/848) COMPLEX - SBML - Dewey to S. of Trinity (STA 811+00 to STA 825+00)		537	01-Aug-12	21-Aug-14	4	$0
3ANSMLDTMSRO881	Parcel #88 : Initiate ROW Acquisition	0	01-Aug-12		6	$0
3ANSMLDTRO881010	Parcel #88 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	4	$0
3ANSMLDTRO881020	Parcel #88 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	4	$0
3ANSMLDTRO881030	Parcel #88 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	24	$0
3ANSMLDTRO881050	Parcel #88 : Prepare Title Work	30	08-Jan-13	18-Feb-13	4	$0
3ANSMLDTRO881040	Parcel #88 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANSMLDTRO881060	Parcel #88 : Perform Appraisals	20	19-Feb-13	18-Mar-13	4	$0
3ANSMLDTRO881070	Parcel #88 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	4	$0
3ANSMLDTRO881080	Parcel #88 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	4	$0
3ANSMLDTRO881090	Parcel #88 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	4	$0
3ANSMLDTRO881100	Parcel #88 : Parcel closing	60	06-Sep-13	29-Nov-13	99	$0
3ANSMLDTRO881110	Parcel #88 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	4	$0
3ANSMLDTRO881120	Parcel #88 : Prepare for Relocation	30	16-Apr-14	28-May-14	4	$0
3ANSMLDTRO881130	Parcel #88 : Execute Relocation	20	29-May-14	25-Jun-14	4	$0
3ANSMLDTRO881140	Parcel #88 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	4	$0
3ANSMLDTRO881150	Parcel #88 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	4	$0
3ANSMLDTMSRO881	Parcel #88 : Cleared for Construction	0		21-Aug-14	6	$0
Parcel #97 SBFR - Dewey to S. of trinity River (STA 862+00 to STA 862+00)		400	01-Aug-12	11-Feb-14	200	$0
3ASBFRDTMSRO971	Parcel #97 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRDTRO971010	Parcel #97 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRDTRO971020	Parcel #97 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRDTRO971030	Parcel #97 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRDTRO971050	Parcel #97 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRDTRO971060	Parcel #97 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRDTRO971040	Parcel #97 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRDTRO971070	Parcel #97 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRDTRO971080	Parcel #97 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRDTRO971090	Parcel #97 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	197	$0
3ASBFRDTRO971100	Parcel #97 : Parcel closing	20	30-Apr-13	28-May-13	287	$0
3ASBFRDTRO971110	Parcel #97 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	197	$0
3ASBFRDTRO971120	Parcel #97 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	197	$0
3ASBFRDTRO971130	Parcel #97 : Execute Relocation	20	15-Nov-13	13-Dec-13	197	$0
3ASBFRDTRO971140	Parcel #97 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	197	$0
3ASBFRDTRO971150	Parcel #97 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	197	$0
3ASBFRDTMSRO971	Parcel #97 : Cleared for Construction	0		11-Feb-14	280	$0
Parcel #99 SBFR - Dewey to S. of trinity River (STA 862+50 to STA)		400	01-Aug-12	11-Feb-14	200	$0
3ASBFRDTMSRO991	Parcel #99 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRDTRO991010	Parcel #99 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRDTRO991020	Parcel #99 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRDTRO991030	Parcel #99 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRDTRO991050	Parcel #99 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRDTRO991060	Parcel #99 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRDTRO991040	Parcel #99 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRDTRO991070	Parcel #99 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRDTRO991080	Parcel #99 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRDTRO991090	Parcel #99 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	197	$0
3ASBFRDTRO991100	Parcel #99 : Parcel closing	20	30-Apr-13	28-May-13	287	$0

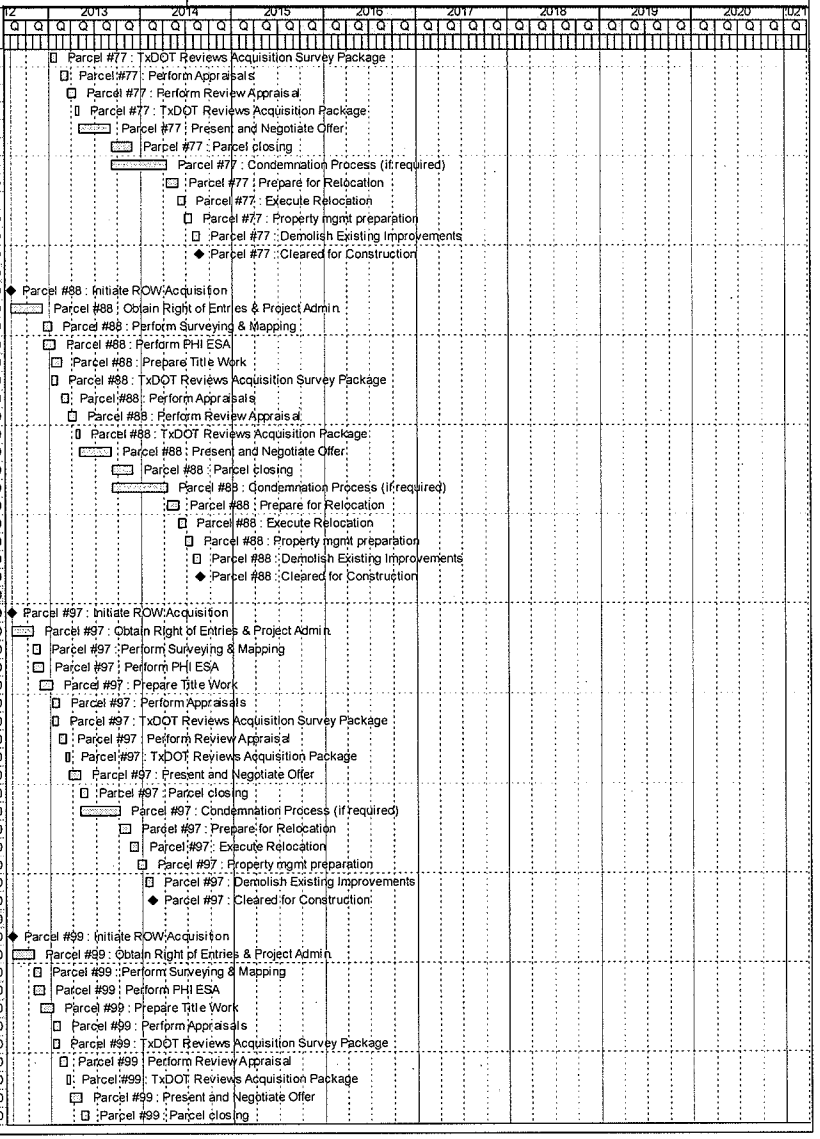

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRDTRO991110	Parcel #99 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	197	$0
3ASBFRDTRO991120	Parcel #99 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	197	$0
3ASBFRDTRO991130	Parcel #99 : Execute Relocation	20	15-Nov-13	13-Dec-13	197	$0
3ASBFRDTRO991140	Parcel #99 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	197	$0
3ASBFRDTRO991150	Parcel #99 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	197	$0
3ASBFRDTMSRO991	Parcel #99 : Cleared for Construction	0		11-Feb-14	280	$0
Parcel #100 SBFR - S. of trinity River to IH 30 (STA 863+00 to STA 863+00)		400	01-Aug-12	11-Feb-14	187	$0
3ASBFRSIMSRO1001	Parcel #100 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRSIRO1001010	Parcel #100 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRSIRO1001020	Parcel #100 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRSIRO1001030	Parcel #100 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRSIRO1001050	Parcel #100 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRSIRO1001060	Parcel #100 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRSIRO1001040	Parcel #100 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1001070	Parcel #100 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRSIRO1001080	Parcel #100 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRSIRO1001090	Parcel #100 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	184	$0
3ASBFRSIRO1001100	Parcel #100 : Parcel closing	20	30-Apr-13	28-May-13	274	$0
3ASBFRSIRO1001110	Parcel #100 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	184	$0
3ASBFRSIRO1001120	Parcel #100 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	184	$0
3ASBFRSIRO1001130	Parcel #100 : Execute Relocation	20	15-Nov-13	13-Dec-13	184	$0
3ASBFRSIRO1001140	Parcel #100 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	184	$0
3ASBFRSIRO1001150	Parcel #100 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	184	$0
3ASBFRSIMSRO1001	Parcel #100 : Cleared for Construction	0		11-Feb-14	261	$0
Parcel #108 (TxDOT #866) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 866+00 to STA 866+00)		537	01-Aug-12	21-Aug-14	1	$0
3ANBFRSIMSRO1081	Parcel #108 : Initiate ROW Acquisition	0	01-Aug-12		1	$0
3ANBFRSIRO1081010	Parcel #108 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	1	$0
3ANBFRSIRO1081020	Parcel #108 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	1	$0
3ANBFRSIRO1081030	Parcel #108 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	21	$0
3ANBFRSIRO1081050	Parcel #108 : Prepare Title Work	30	08-Jan-13	18-Feb-13	1	$0
3ANBFRSIRO1081040	Parcel #108 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANBFRSIRO1081060	Parcel #108 : Perform Appraisals	20	19-Feb-13	18-Mar-13	1	$0
3ANBFRSIRO1081070	Parcel #108 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	1	$0
3ANBFRSIRO1081080	Parcel #108 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	1	$0
3ANBFRSIRO1081090	Parcel #108 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	1	$0
3ANBFRSIRO1081100	Parcel #108 : Parcel closing	20	06-Sep-13	03-Oct-13	136	$0
3ANBFRSIRO1081110	Parcel #108 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	1	$0
3ANBFRSIRO1081120	Parcel #108 : Prepare for Relocation	30	16-Apr-14	28-May-14	1	$0
3ANBFRSIRO1081130	Parcel #108 : Execute Relocation	20	29-May-14	25-Jun-14	1	$0
3ANBFRSIRO1081140	Parcel #108 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	1	$0
3ANBFRSIRO1081150	Parcel #108 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	1	$0
3ANBFRSIMSRO1081	Parcel #108 : Cleared for Construction	0		21-Aug-14	3	$0
Parcel #109 (TxDOT #867) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 867+00 to STA 867+00)		537	01-Aug-12	21-Aug-14	1	$0
3ANBFRSIMSRO1091	Parcel #109 : Initiate ROW Acquisition	0	01-Aug-12		1	$0
3ANBFRSIRO1091010	Parcel #109 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	1	$0
3ANBFRSIRO1091020	Parcel #109 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	1	$0
3ANBFRSIRO1091030	Parcel #109 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	21	$0
3ANBFRSIRO1091050	Parcel #109 : Prepare Title Work	30	08-Jan-13	18-Feb-13	1	$0
3ANBFRSIRO1091040	Parcel #109 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANBFRSIRO1091060	Parcel #109 : Perform Appraisals	20	19-Feb-13	18-Mar-13	1	$0
3ANBFRSIRO1091070	Parcel #109 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	1	$0
3ANBFRSIRO1091080	Parcel #109 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	1	$0
3ANBFRSIRO1091090	Parcel #109 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	1	$0
3ANBFRSIRO1091100	Parcel #109 : Parcel closing	20	06-Sep-13	03-Oct-13	136	$0
3ANBFRSIRO1091110	Parcel #109 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	1	$0
3ANBFRSIRO1091120	Parcel #109 : Prepare for Relocation	30	16-Apr-14	28-May-14	1	$0
3ANBFRSIRO1091130	Parcel #109 : Execute Relocation	20	29-May-14	25-Jun-14	1	$0
3ANBFRSIRO1091140	Parcel #109 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	1	$0
3ANBFRSIRO1091150	Parcel #109 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	1	$0
3ANBFRSIMSRO1091	Parcel #109 : Cleared for Construction	0		21-Aug-14	3	$0

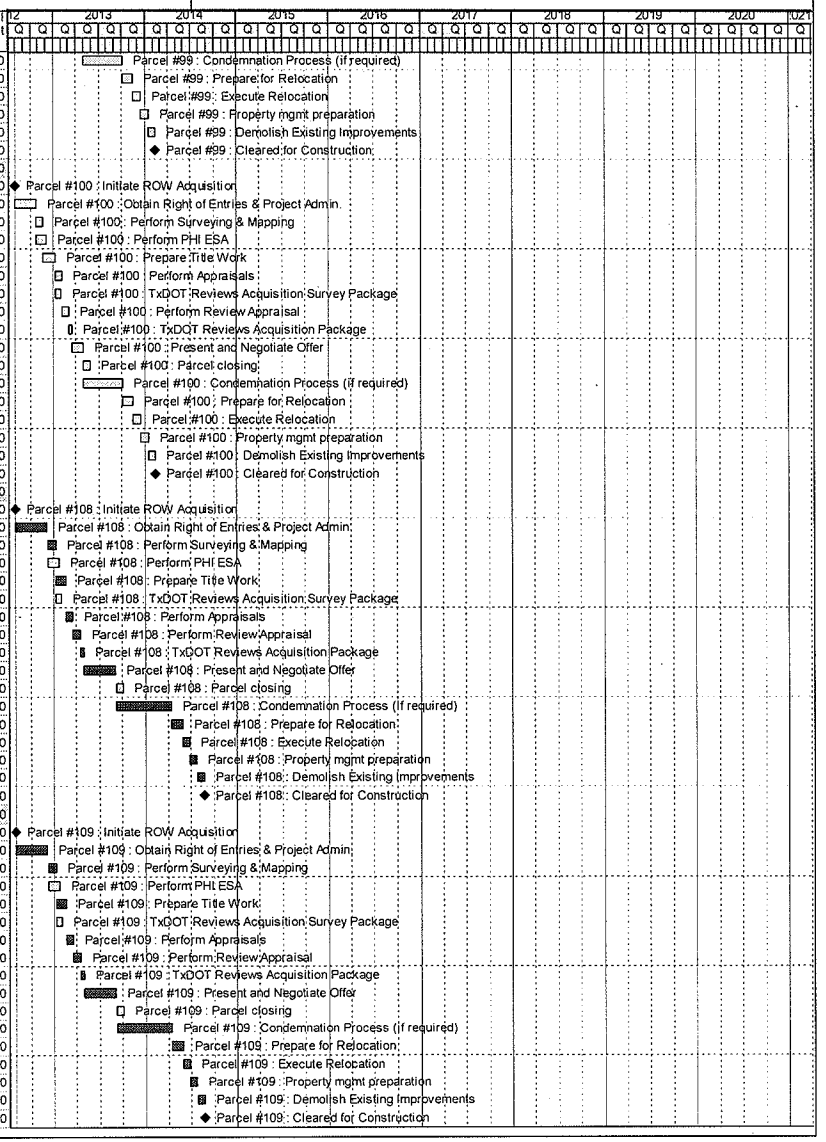

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Parcel #110 (TxDOT #874) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 867+00 to STA 867+00)		537	01-Aug-12	21-Aug-14	1	$0
3ANBFRSIMSRO1101	Parcel #110 : Initiate ROW Acquisition	0	01-Aug-12		1	$0
3ANBFRSIRO1101010	Parcel #110 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	1	$0
3ANBFRSIRO1101020	Parcel #110 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	1	$0
3ANBFRSIRO1101030	Parcel #110 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	21	$0
3ANBFRSIRO1101050	Parcel #110 : Prepare Title Work	30	08-Jan-13	18-Feb-13	1	$0
3ANBFRSIRO1101040	Parcel #110 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANBFRSIRO1101060	Parcel #110 : Perform Appraisals	20	19-Feb-13	18-Mar-13	1	$0
3ANBFRSIRO1101070	Parcel #110 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	1	$0
3ANBFRSIRO1101080	Parcel #110 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	1	$0
3ANBFRSIRO1101090	Parcel #110 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	1	$0
3ANBFRSIRO1101100	Parcel #110 : Parcel closing	20	06-Sep-13	03-Oct-13	136	$0
3ANBFRSIRO1101110	Parcel #110 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	1	$0
3ANBFRSIRO1101120	Parcel #110 : Prepare for Relocation	30	16-Apr-14	28-May-14	1	$0
3ANBFRSIRO1101130	Parcel #110 : Execute Relocation	20	29-May-14	25-Jun-14	1	$0
3ANBFRSIRO1101140	Parcel #110 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	1	$0
3ANBFRSIRO1101150	Parcel #110 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	1	$0
3ANBFRSIMSRO1101	Parcel #110 : Cleared for Construction	0		21-Aug-14	3	$0
Parcel #115 (TxDOT #880) - COMPLEX - SBFR - S. of Trinity to IH 30 (STA 872+00 to STA 872+00)		537	01-Aug-12	21-Aug-14	50	$0
3ASBFRSIMSRO1151	Parcel #115 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRSIRO1151010	Parcel #115 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	11	$0
3ASBFRSIRO1151020	Parcel #115 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	11	$0
3ASBFRSIRO1151030	Parcel #115 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	31	$0
3ASBFRSIRO1151050	Parcel #115 : Prepare Title Work	30	08-Jan-13	18-Feb-13	11	$0
3ASBFRSIRO1151040	Parcel #115 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1151060	Parcel #115 : Perform Appraisals	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRSIRO1151070	Parcel #115 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	11	$0
3ASBFRSIRO1151080	Parcel #115 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ASBFRSIRO1151090	Parcel #115 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	49	$0
3ASBFRSIRO1151100	Parcel #115 : Parcel closing	60	06-Sep-13	29-Nov-13	144	$0
3ASBFRSIRO1151110	Parcel #115 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	49	$0
3ASBFRSIRO1151120	Parcel #115 : Prepare for Relocation	30	16-Apr-14	28-May-14	49	$0
3ASBFRSIRO1151130	Parcel #115 : Execute Relocation	20	29-May-14	25-Jun-14	49	$0
3ASBFRSIRO1151140	Parcel #115 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	49	$0
3ASBFRSIRO1151150	Parcel #115 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	49	$0
3ASBFRSIMSRO1151	Parcel #115 : Cleared for Construction	0		21-Aug-14	70	$0
Parcel #116 SBFR - S. of Trinity River to IH 30 (STA 875+00 to STA 876+00)		400	01-Aug-12	11-Feb-14	167	$0
3ASBFRSIMSRO1161	Parcel #116 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRSIRO1161010	Parcel #116 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRSIRO1161020	Parcel #116 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRSIRO1161030	Parcel #116 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRSIRO1161050	Parcel #116 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRSIRO1161060	Parcel #116 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRSIRO1161040	Parcel #116 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1161070	Parcel #116 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRSIRO1161080	Parcel #116 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRSIRO1161090	Parcel #116 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	184	$0
3ASBFRSIRO1161100	Parcel #116 : Parcel closing	20	30-Apr-13	28-May-13	274	$0
3ASBFRSIRO1161110	Parcel #116 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	184	$0
3ASBFRSIRO1161120	Parcel #116 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	184	$0
3ASBFRSIRO1161130	Parcel #116 : Execute Relocation	20	15-Nov-13	13-Dec-13	184	$0
3ASBFRSIRO1161140	Parcel #116 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	184	$0
3ASBFRSIRO1161150	Parcel #116 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	184	$0
3ASBFRSIMSRO1161	Parcel #116 : Cleared for Construction	0		11-Feb-14	261	$0
Parcel #117 (TxDOT #883) - COMPLEX - SBFR - S. of Trinity to IH 30 (STA 878+00 to STA 878+00)		537	01-Aug-12	21-Aug-14	50	$0
3ASBFRSIMSRO1171	Parcel #117 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRSIRO1171010	Parcel #117 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	11	$0
3ASBFRSIRO1171020	Parcel #117 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	11	$0
3ASBFRSIRO1171030	Parcel #117 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	31	$0
3ASBFRSIRO1171050	Parcel #117 : Prepare Title Work	30	08-Jan-13	18-Feb-13	11	$0

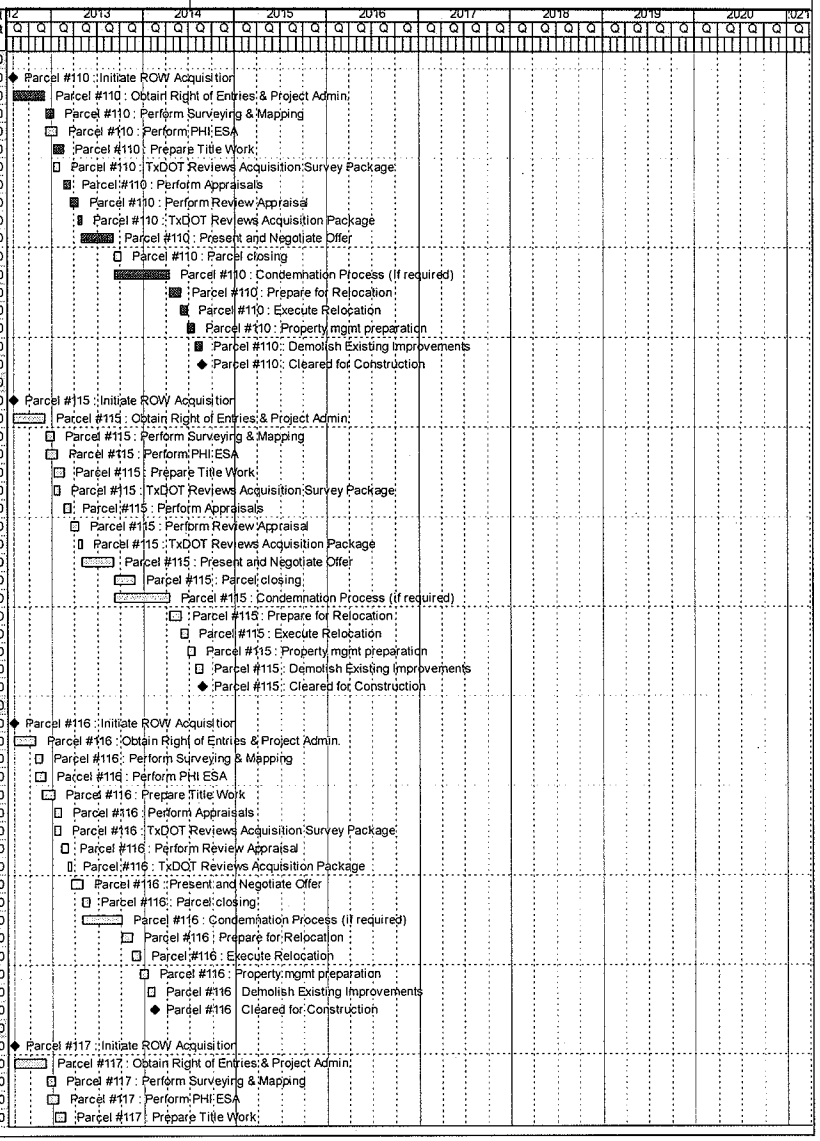

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRSIRO1171040	Parcel #117 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1171060	Parcel #117 : Perform Appraisals	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRSIRO1171070	Parcel #117 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	11	$0
3ASBFRSIRO1171080	Parcel #117 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ASBFRSIRO1171090	Parcel #117 : Present and Negotiate Offer	90	30-Apr-13	05-Sep-13	49	$0
3ASBFRSIRO1171100	Parcel #117 : Parcel closing	60	06-Sep-13	29-Nov-13	144	$0
3ASBFRSIRO1171110	Parcel #117 : Condemnation Process (if required)	155	06-Sep-13	15-Apr-14	49	$0
3ASBFRSIRO1171120	Parcel #117 : Prepare for Relocation	30	16-Apr-14	28-May-14	49	$0
3ASBFRSIRO1171130	Parcel #117 : Execute Relocation	20	29-May-14	25-Jun-14	49	$0
3ASBFRSIRO1171140	Parcel #117 : Property mgmt preparation	20	26-Jun-14	24-Jul-14	49	$0
3ASBFRSIRO1171150	Parcel #117 : Demolish Existing Improvements	20	25-Jul-14	21-Aug-14	49	$0
3ASBFRSIMSRO1171	Parcel #117 : Cleared for Construction	0		21-Aug-14	70	$0
Parcel #118 (TxDOT #885) - COMPLEX - SBFR - S. of Trinity to IH 30 (STA 881+00 to STA 884+00)		548	01-Aug-12	05-Sep-14	39	$0
3ASBFRSIMSRO1181	Parcel #118 : Initiate ROW Acquisition	0	01-Aug-12		21	$0
3ASBFRSIRO1181010	Parcel #118 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	15	$0
3ASBFRSIRO1181020	Parcel #118 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	15	$0
3ASBFRSIRO1181030	Parcel #118 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	69	$0
3ASBFRSIRO1181050	Parcel #118 : Prepare Title Work	30	08-Jan-13	18-Feb-13	49	$0
3ASBFRSIRO1181040	Parcel #118 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1181060	Parcel #118 : Perform Appraisals	20	19-Feb-13	18-Mar-13	49	$0
3ASBFRSIRO1181070	Parcel #118 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	49	$0
3ASBFRSIRO1181080	Parcel #118 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	39	$0
3ASBFRSIRO1181090	Parcel #118 : Present and Negotiate Offer	90	14-May-13	19-Sep-13	39	$0
3ASBFRSIRO1181100	Parcel #118 : Parcel closing	60	20-Sep-13	13-Dec-13	134	$0
3ASBFRSIRO1181110	Parcel #118 : Condemnation Process (if required)	155	20-Sep-13	29-Apr-14	39	$0
3ASBFRSIRO1181120	Parcel #118 : Prepare for Relocation	30	30-Apr-14	11-Jun-14	39	$0
3ASBFRSIRO1181130	Parcel #118 : Execute Relocation	20	12-Jun-14	10-Jul-14	39	$0
3ASBFRSIRO1181140	Parcel #118 : Property mgmt preparation	20	11-Jul-14	07-Aug-14	39	$0
3ASBFRSIRO1181150	Parcel #118 : Demolish Existing Improvements	20	08-Aug-14	05-Sep-14	39	$0
3ASBFRSIMSRO1181	Parcel #118 : Cleared for Construction	0		05-Sep-14	55	$0
Parcel #120 SBFR - S. of Trinity River to IH 30 (STA 884+00 to STA 887+00)		400	01-Aug-12	11-Feb-14	187	$0
3ASBFRSIMSRO1201	Parcel #120 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRSIRO1201010	Parcel #120 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRSIRO1201020	Parcel #120 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ASBFRSIRO1201030	Parcel #120 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRSIRO1201050	Parcel #120 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ASBFRSIRO1201060	Parcel #120 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ASBFRSIRO1201040	Parcel #120 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1201070	Parcel #120 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ASBFRSIRO1201080	Parcel #120 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ASBFRSIRO1201090	Parcel #120 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	184	$0
3ASBFRSIRO1201100	Parcel #120 : Parcel closing	20	30-Apr-13	28-May-13	274	$0
3ASBFRSIRO1201110	Parcel #120 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	184	$0
3ASBFRSIRO1201120	Parcel #120 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	184	$0
3ASBFRSIRO1201130	Parcel #120 : Execute Relocation	20	15-Nov-13	13-Dec-13	184	$0
3ASBFRSIRO1201140	Parcel #120 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	184	$0
3ASBFRSIRO1201150	Parcel #120 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	184	$0
3ASBFRSIMSRO1201	Parcel #120 : Cleared for Construction	0		11-Feb-14	261	$0
Parcel #122 SBGP - S. of Trinity River to IH 30 (STA 887+00 to STA 890+00)		476	01-Aug-12	28-May-14	454	$0
3ASBGPSIMSRO1221	Parcel #122 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ASBGPSIRO1221010	Parcel #122 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	46	$0
3ASBGPSIRO1221020	Parcel #122 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ASBGPSIRO1221030	Parcel #122 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	180	$0
3ASBGPSIRO1221050	Parcel #122 : Prepare Title Work	30	08-Jan-13	18-Feb-13	160	$0
3ASBGPSIRO1221060	Parcel #122 : Perform Appraisals	20	19-Feb-13	18-Mar-13	160	$0
3ASBGPSIRO1221040	Parcel #122 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ASBGPSIRO1221070	Parcel #122 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	160	$0
3ASBGPSIRO1221080	Parcel #122 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ASBGPSIRO1221090	Parcel #122 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	444	$0
3ASBGPSIRO1221100	Parcel #122 : Parcel closing	20	18-Jul-13	14-Aug-13	554	$0

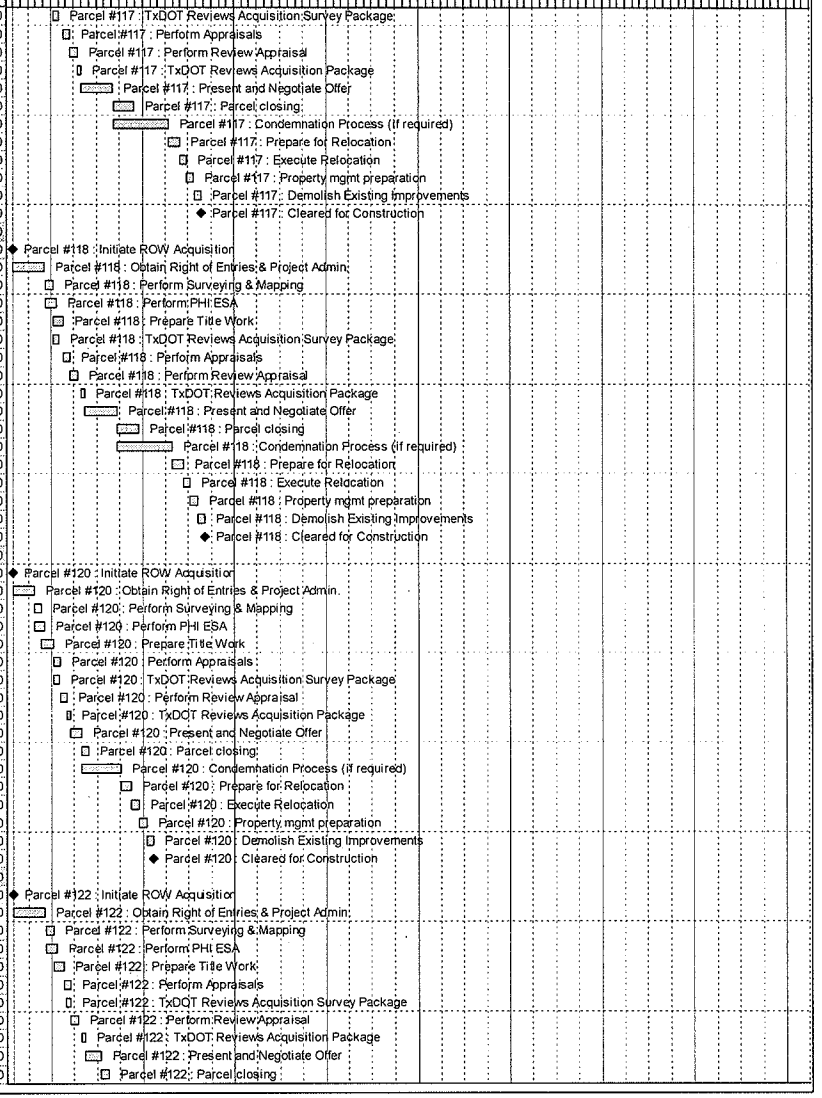

ATTACHMENT 03 - DETAILED PROGRAM SCHEDULE

NTE - Segment 3A Interchange Project - FBS # 1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBGPSIRO1221110	Parcel #122 : Condemnation Process (if required)	130	18-Jul-13	21-Jan-14	444	$0
3ASBGPSIRO1221120	Parcel #122 : Prepare for Relocation	30	22-Jan-14	04-Mar-14	444	$0
3ASBGPSIRO1221130	Parcel #122 : Execute Relocation	20	05-Mar-14	01-Apr-14	444	$0
3ASBGPSIRO1221140	Parcel #122 : Property mgmt preparation	20	02-Apr-14	29-Apr-14	444	$0
3ASBGPSIRO1221150	Parcel #122 : Demolish Existing Improvements	20	30-Apr-14	28-May-14	444	$0
3ASBGPSIMSRO1221	Parcel #122 : Cleared for Construction	0		28-May-14	636	$0
Parcel #126 (TxDOT #897) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 915+00 to STA 915+00)		548	01-Aug-12	05-Sep-14	382	$0
3ASBGPSIMSRO1261	Parcel #126 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBGPSIRO1261010	Parcel #126 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ASBGPSIRO1261020	Parcel #126 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBGPSIRO1261030	Parcel #126 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	180	$0
3ASBGPSIRO1261050	Parcel #126 : Prepare Title Work	30	08-Jan-13	18-Feb-13	160	$0
3ASBGPSIRO1261040	Parcel #126 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBGPSIRO1261060	Parcel #126 : Perform Appraisals	20	19-Feb-13	18-Mar-13	160	$0
3ASBGPSIRO1261070	Parcel #126 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	160	$0
3ASBGPSIRO1261080	Parcel #126 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ASBGPSIRO1261090	Parcel #126 : Present and Negotiate Offer	90	14-May-13	19-Sep-13	374	$0
3ASBGPSIRO1261100	Parcel #126 : Parcel closing	60	20-Sep-13	13-Dec-13	469	$0
3ASBGPSIRO1261110	Parcel #126 : Condemnation Process (if required)	155	20-Sep-13	29-Apr-14	374	$0
3ASBGPSIRO1261120	Parcel #126 : Prepare for Relocation	30	30-Apr-14	11-Jun-14	374	$0
3ASBGPSIRO1261130	Parcel #126 : Execute Relocation	20	12-Jun-14	10-Jul-14	374	$0
3ASBGPSIRO1261140	Parcel #126 : Property mgmt preparation	20	11-Jul-14	07-Aug-14	374	$0
3ASBGPSIRO1261150	Parcel #126 : Demolish Existing Improvements	20	08-Aug-14	05-Sep-14	374	$0
3ASBGPSIMSRO1261	Parcel #126 : Cleared for Construction	0		05-Sep-14	536	$0
Parcel #128 (TxDOT #903) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 917+00 to STA 917+00)		548	01-Aug-12	05-Sep-14	382	$0
3ASBGPSIMSRO1281	Parcel #128 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBGPSIRO1281010	Parcel #128 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ASBGPSIRO1281020	Parcel #128 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBGPSIRO1281030	Parcel #128 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	180	$0
3ASBGPSIRO1281050	Parcel #128 : Prepare Title Work	30	08-Jan-13	18-Feb-13	160	$0
3ASBGPSIRO1281040	Parcel #128 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBGPSIRO1281060	Parcel #128 : Perform Appraisals	20	19-Feb-13	18-Mar-13	160	$0
3ASBGPSIRO1281070	Parcel #128 : Perform Review Appraisal	20	19-Mar-13	15-Apr-13	160	$0
3ASBGPSIRO1281080	Parcel #128 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ASBGPSIRO1281090	Parcel #128 : Present and Negotiate Offer	90	14-May-13	19-Sep-13	374	$0
3ASBGPSIRO1281100	Parcel #128 : Parcel closing	60	20-Sep-13	13-Dec-13	469	$0
3ASBGPSIRO1281110	Parcel #128 : Condemnation Process (if required)	155	20-Sep-13	29-Apr-14	374	$0
3ASBGPSIRO1281120	Parcel #128 : Prepare for Relocation	30	30-Apr-14	11-Jun-14	374	$0
3ASBGPSIRO1281130	Parcel #128 : Execute Relocation	20	12-Jun-14	10-Jul-14	374	$0
3ASBGPSIRO1281140	Parcel #128 : Property mgmt preparation	20	11-Jul-14	07-Aug-14	374	$0
3ASBGPSIRO1281150	Parcel #128 : Demolish Existing Improvements	20	08-Aug-14	05-Sep-14	374	$0
3ASBGPSIMSRO1281	Parcel #128 : Cleared for Construction	0		05-Sep-14	536	$0
Parcel #161 NBFR - S. of Trinity River to IH 30 (STA 915+00 to STA 915+00)		400	01-Aug-12	11-Feb-14	138	$0
3ANBFRSIMSRO1611	Parcel #161 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRSIRO1611010	Parcel #161 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRSIRO1611020	Parcel #161 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ANBFRSIRO1611030	Parcel #161 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRSIRO1611050	Parcel #161 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ANBFRSIRO1611040	Parcel #161 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRSIRO1611060	Parcel #161 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ANBFRSIRO1611070	Parcel #161 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ANBFRSIRO1611080	Parcel #161 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ANBFRSIRO1611090	Parcel #161 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	136	$0
3ANBFRSIRO1611100	Parcel #161 : Parcel closing	20	30-Apr-13	28-May-13	226	$0
3ANBFRSIRO1611110	Parcel #161 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	136	$0
3ANBFRSIRO1611120	Parcel #161 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	136	$0
3ANBFRSIRO1611130	Parcel #161 : Execute Relocation	20	15-Nov-13	13-Dec-13	136	$0
3ANBFRSIRO1611140	Parcel #161 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	136	$0
3ANBFRSIRO1611150	Parcel #161 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	136	$0
3ANBFRSIMSRO1611	Parcel #161 : Cleared for Construction	0		11-Feb-14	194	$0

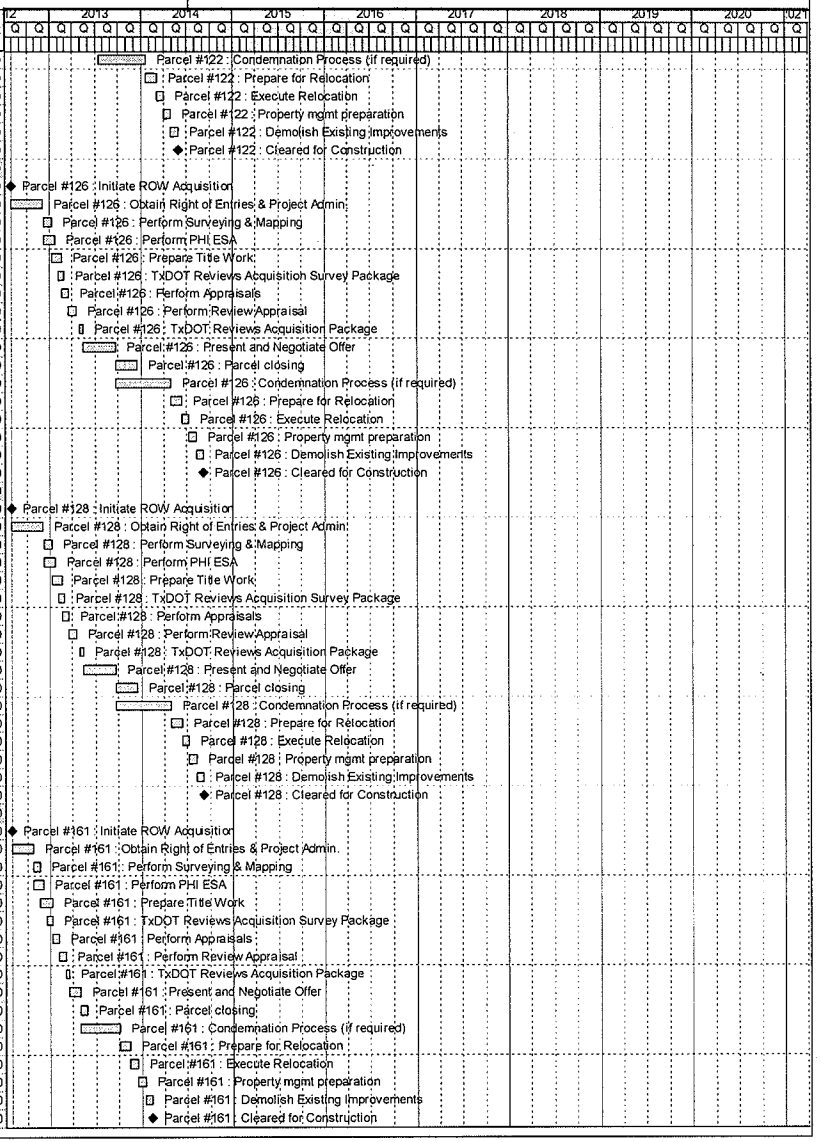

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Parcel #163 NBFR - S. of Trinity River to IH 30 (STA 914+00 to STA 914+00)		400	01-Aug-12	11-Feb-14	136	$0
3ANBFRSIMSRO1631	Parcel #163 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRSIRO1631010	Parcel #163 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRSIRO1631020	Parcel #163 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ANBFRSIRO1631030	Parcel #163 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRSIRO1631050	Parcel #163 : Prepare Title Work	30	23-Nov-12	07-Jan-13	11	$0
3ANBFRSIRO1631040	Parcel #163 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRSIRO1631060	Parcel #163 : Perform Appraisals	20	08-Jan-13	04-Feb-13	11	$0
3ANBFRSIRO1631070	Parcel #163 : Perform Review Appraisal	20	05-Feb-13	04-Mar-13	11	$0
3ANBFRSIRO1631080	Parcel #163 : TxDOT Reviews Acquisition Package	10	05-Mar-13	18-Mar-13	11	$0
3ANBFRSIRO1631090	Parcel #163 : Present and Negotiate Offer	30	19-Mar-13	29-Apr-13	136	$0
3ANBFRSIRO1631100	Parcel #163 : Parcel closing	20	30-Apr-13	28-May-13	226	$0
3ANBFRSIRO1631110	Parcel #163 : Condemnation Process (if required)	110	30-Apr-13	03-Oct-13	136	$0
3ANBFRSIRO1631120	Parcel #163 : Prepare for Relocation	30	04-Oct-13	14-Nov-13	136	$0
3ANBFRSIRO1631130	Parcel #163 : Execute Relocation	20	15-Nov-13	13-Dec-13	136	$0
3ANBFRSIRO1631140	Parcel #163 : Property mgmt preparation	20	16-Dec-13	14-Jan-14	136	$0
3ANBFRSIRO1631150	Parcel #163 : Demolish Existing Improvements	20	15-Jan-14	11-Feb-14	136	$0
3ANBFRSIMSRO1631	Parcel #163 : Cleared for Construction	0		11-Feb-14	194	$0
Parcels Not Needing Relocation		548	01-Aug-12	05-Sep-14	382	$0
Parcel #1 SBFR - Meacham to Dewey (STA 666+00 to STA 671+20)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRMDMSRO011	Parcel #1 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO011010	Parcel #1 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO011030	Parcel #1 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO011020	Parcel #1 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO011040	Parcel #1 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO011050	Parcel #1 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO011060	Parcel #1 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO011070	Parcel #1 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO011080	Parcel #1 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO011090	Parcel #1 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBFRMDRO011100	Parcel #1 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRMDRO011110	Parcel #1 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRMDMSRO011	Parcel #1 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #2 SBFR - Meacham to Dewey (STA 671+20 to STA 674+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRMDMSRO021	Parcel #2 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO021010	Parcel #2 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO021020	Parcel #2 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO021030	Parcel #2 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO021040	Parcel #2 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO021050	Parcel #2 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO021060	Parcel #2 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO021070	Parcel #2 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO021080	Parcel #2 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO021090	Parcel #2 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBFRMDRO021100	Parcel #2 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRMDRO021110	Parcel #2 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRMDMSRO021	Parcel #2 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #3 NBFR - Meacham to Dewey (STA 665+00 to STA 665+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO03	Parcel #3 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO031010	Parcel #3 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO031020	Parcel #3 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO031030	Parcel #3 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO031050	Parcel #3 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO031040	Parcel #3 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO031060	Parcel #3 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO031070	Parcel #3 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO031080	Parcel #3 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO031090	Parcel #3 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO031100	Parcel #3 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO031110	Parcel #3 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0

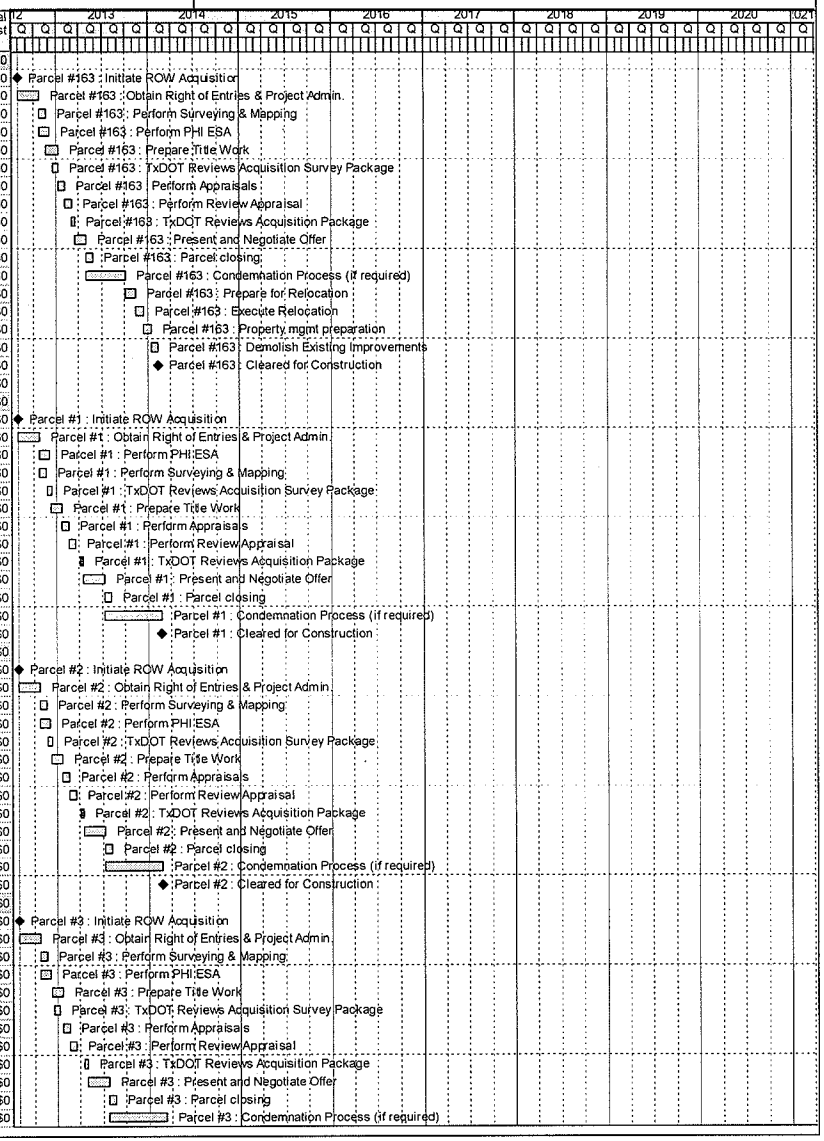

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRMDMSRO03	Parcel #3 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #4 NBFR - Meacham to Dewey (STA 665+00 to STA 668+50)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO04	Parcel #4 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO041010	Parcel #4 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO041020	Parcel #4 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO041030	Parcel #4 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO041050	Parcel #4 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO041040	Parcel #4 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO041060	Parcel #4 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO041070	Parcel #4 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO041080	Parcel #4 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO041090	Parcel #4 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO041100	Parcel #4 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO041110	Parcel #4 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO04	Parcel #4 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #5 NBFR - Meacham to Dewey (STA 669+50 to STA 671+50)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO05	Parcel #5 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO051010	Parcel #5 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO051020	Parcel #5 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO051030	Parcel #5 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO051050	Parcel #5 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO051040	Parcel #5 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO051060	Parcel #5 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO051070	Parcel #5 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO051080	Parcel #5 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO051090	Parcel #5 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO051100	Parcel #5 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO051110	Parcel #5 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO05	Parcel #5 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #6 NBFR - Meacham to Dewey (STA 671+50 to STA 674+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO06	Parcel #6 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO061010	Parcel #6 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO061020	Parcel #6 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO061030	Parcel #6 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO061050	Parcel #6 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO061040	Parcel #6 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO061060	Parcel #6 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO061070	Parcel #6 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO061080	Parcel #6 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO061090	Parcel #6 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO061100	Parcel #6 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO061110	Parcel #6 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO06	Parcel #6 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #7 SBFR - Meacham to Dewey (STA 676+00 to STA 679+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRMDMSRO071	Parcel #7 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO071010	Parcel #7 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO071020	Parcel #7 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO071030	Parcel #7 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO071040	Parcel #7 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO071050	Parcel #7 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO071060	Parcel #7 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO071070	Parcel #7 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO071080	Parcel #7 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO071090	Parcel #7 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBFRMDRO071100	Parcel #7 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRMDRO071110	Parcel #7 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRMDMSRO071	Parcel #7 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #9 NBFR - Meacham to Dewey (STA 676+00 to STA 680+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO09	Parcel #9 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO091010	Parcel #9 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0

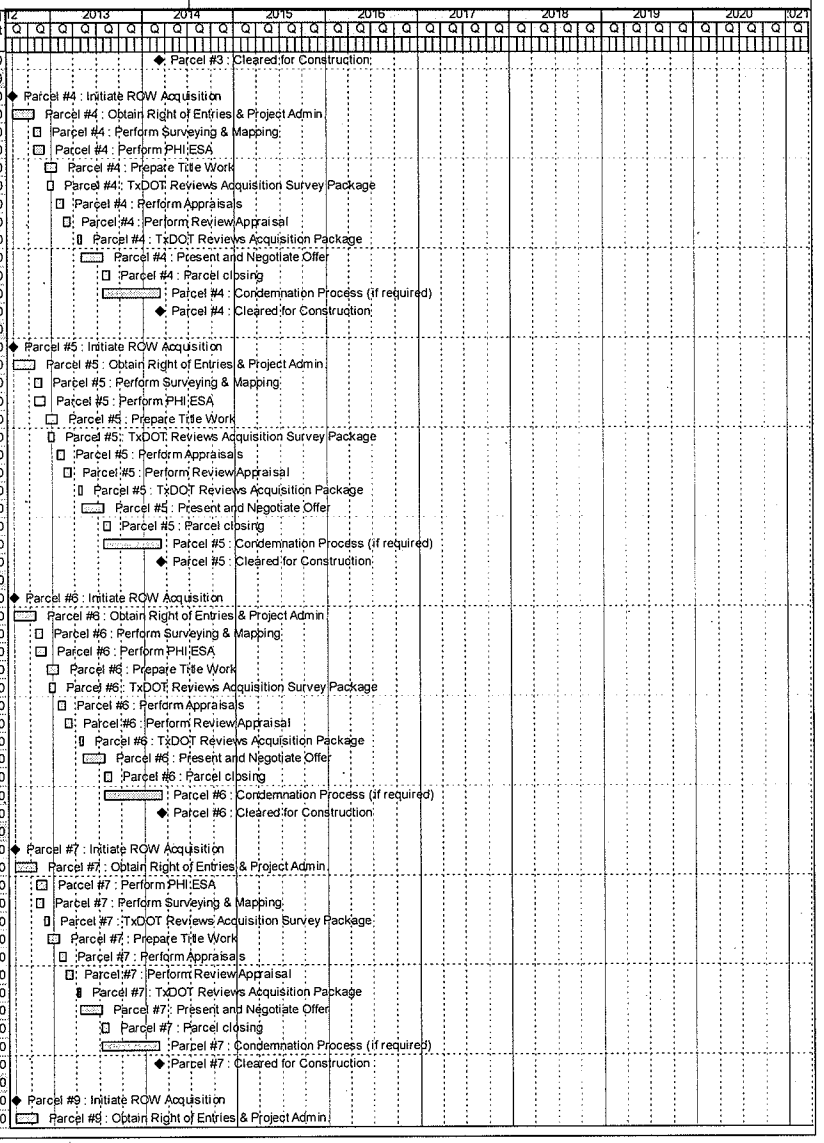

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRMDRO091020	Parcel #9 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO091030	Parcel #9 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO091050	Parcel #9 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO091040	Parcel #9 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO091060	Parcel #9 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO091070	Parcel #9 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO091080	Parcel #9 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO091090	Parcel #9 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO091100	Parcel #9 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO091110	Parcel #9 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO09	Parcel #9 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #10 NBFR - Meacham to Dewey (STA 681+00 to STA 685+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO10	Parcel #10 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO101010	Parcel #10 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO101020	Parcel #10 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO101030	Parcel #10 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO101050	Parcel #10 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO101040	Parcel #10 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO101060	Parcel #10 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO101070	Parcel #10 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO101080	Parcel #10 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO101090	Parcel #10 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO101100	Parcel #10 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO101110	Parcel #10 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO10	Parcel #10 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #11 NBFR - Meacham to Dewey (STA 685+00 to STA 686+50)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO111	Parcel #11 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO111010	Parcel #11 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO111020	Parcel #11 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO111030	Parcel #11 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO111050	Parcel #11 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO111040	Parcel #11 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO111060	Parcel #11 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO111070	Parcel #11 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO111080	Parcel #11 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO111090	Parcel #11 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO111100	Parcel #11 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO111110	Parcel #11 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO111	Parcel #11 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #13 SBFR - Meacham to Dewey (STA 689+00 to STA 694+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRMDMSRO131	Parcel #13 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO131010	Parcel #13 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO131020	Parcel #13 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO131030	Parcel #13 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO131040	Parcel #13 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO131050	Parcel #13 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO131060	Parcel #13 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO131070	Parcel #13 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO131080	Parcel #13 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO131090	Parcel #13 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBFRMDRO131100	Parcel #13 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRMDRO131110	Parcel #13 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRMDMSRO131	Parcel #13 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #14 SBFR - Meacham to Dewey (STA 695+00 to STA 701+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRMDMSRO141	Parcel #14 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO141010	Parcel #14 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO141020	Parcel #14 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO141030	Parcel #14 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO141040	Parcel #14 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO141050	Parcel #14 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0

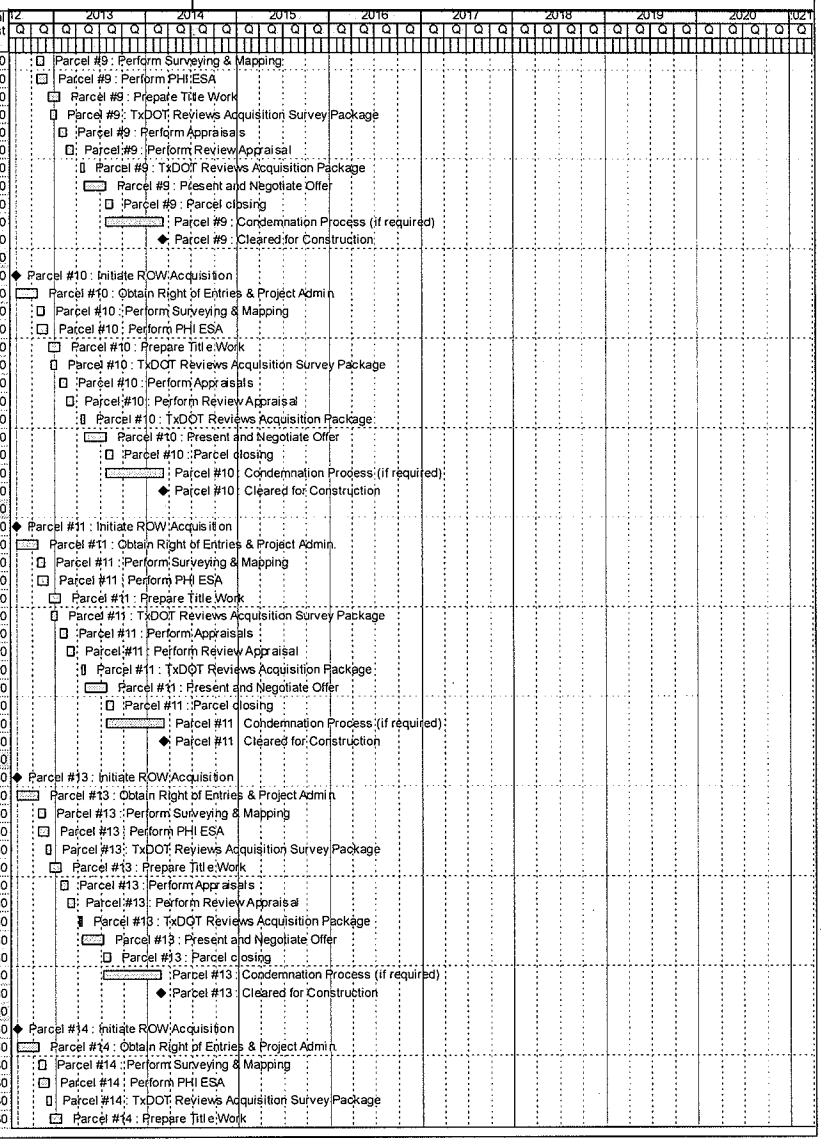

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRMDRO141060	Parcel #14 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO141070	Parcel #14 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO141080	Parcel #14 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO141090	Parcel #14 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBFRMDRO141100	Parcel #14 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRMDRO141110	Parcel #14 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRMDMSRO141	Parcel #14 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #16 SBFR - Meacham to Dewey (STA 701+00 to STA 725+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRMDMSRO161	Parcel #16 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO161010	Parcel #16 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO161020	Parcel #16 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO161030	Parcel #16 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO161040	Parcel #16 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO161050	Parcel #16 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO161060	Parcel #16 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO161070	Parcel #16 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO161080	Parcel #16 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO161090	Parcel #16 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBFRMDRO161100	Parcel #16 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRMDRO161110	Parcel #16 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRMDMSRO161	Parcel #16 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #17 NBFR - Meacham to Dewey (STA 690+00 to STA 695+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO17	Parcel #17 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO171010	Parcel #17 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO171020	Parcel #17 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRMDRO171030	Parcel #17 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO171040	Parcel #17 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRMDRO171050	Parcel #17 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO171060	Parcel #17 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO171070	Parcel #17 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO171080	Parcel #17 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO171090	Parcel #17 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO171110	Parcel #17 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDRO171100	Parcel #17 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDMSRO17	Parcel #17 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #18 NBFR - Meacham to Dewey (STA 695+00 to STA 669+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO18	Parcel #18 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO181010	Parcel #18 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO181020	Parcel #18 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRMDRO181030	Parcel #18 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO181040	Parcel #18 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRMDRO181050	Parcel #18 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO181060	Parcel #18 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO181070	Parcel #18 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO181080	Parcel #18 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO181090	Parcel #18 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO181100	Parcel #18 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDRO181110	Parcel #18 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDMSRO18	Parcel #18 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #19 NBFR - Meacham to Dewey (STA 669+00 to STA 703+50)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO19	Parcel #19 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO191010	Parcel #19 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO191020	Parcel #19 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRMDRO191030	Parcel #19 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO191040	Parcel #19 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRMDRO191050	Parcel #19 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO191060	Parcel #19 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO191070	Parcel #19 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO191080	Parcel #19 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO191090	Parcel #19 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0

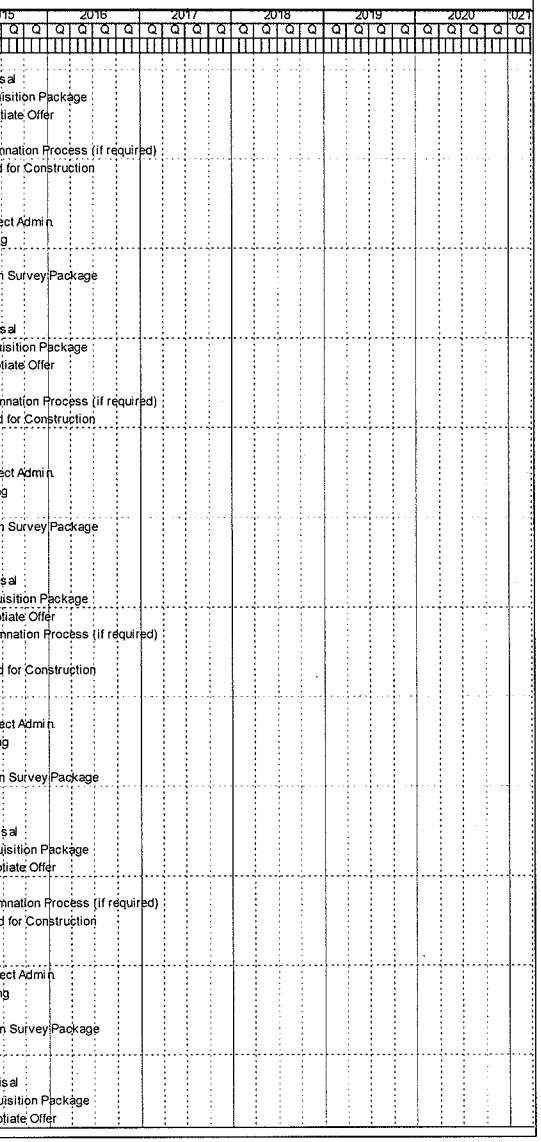

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRMDRO191100	Parcel #19 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDRO191110	Parcel #19 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDMSRO19`	Parcel #19 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #20 NBFR - Meacham to Dewey (STA 704+00 to STA 725+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO20`	Parcel #20 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO201010	Parcel #20 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO201020	Parcel #20 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRMDRO201030	Parcel #20 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO201040	Parcel #20 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRMDRO201050	Parcel #20 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO201060	Parcel #20 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO201070	Parcel #20 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO201080	Parcel #20 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO201090	Parcel #20 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO201100	Parcel #20 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDRO201110	Parcel #20 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDMSRO20`	Parcel #20 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #23 NBGP - Meacham to Dewey (STA 728+00 to STA 728+00)		486	01-Aug-12	11-Jun-14	430	$0
3ANBGPMDMSRO23`	Parcel #23 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPMDRO231010	Parcel #23 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPMDRO231020	Parcel #23 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPMDRO231030	Parcel #23 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	440	$0
3ANBGPMDRO231050	Parcel #23 : Prepare Title Work	30	22-Jan-13	04-Mar-13	440	$0
3ANBGPMDRO231040	Parcel #23 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPMDRO231060	Parcel #23 : Perform Appraisals	20	05-Mar-13	01-Apr-13	440	$0
3ANBGPMDRO231070	Parcel #23 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	440	$0
3ANBGPMDRO231080	Parcel #23 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	411	$0
3ANBGPMDRO231090	Parcel #23 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	420	$0
3ANBGPMDRO231100	Parcel #23 : Parcel closing	20	15-Aug-13	12-Sep-13	610	$0
3ANBGPMDRO231110	Parcel #23 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	420	$0
3ANBGPMDMSRO23`	Parcel #23 : Cleared for Construction	0		11-Jun-14	602	$0
Parcel #24 NBGP - Meacham to Dewey (STA 728+00 to STA 728+00)		486	01-Aug-12	11-Jun-14	430	$0
3ANBGPMDMSRO24`	Parcel #24 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPMDRO241010	Parcel #24 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPMDRO241020	Parcel #24 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPMDRO241030	Parcel #24 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	440	$0
3ANBGPMDRO241050	Parcel #24 : Prepare Title Work	30	22-Jan-13	04-Mar-13	440	$0
3ANBGPMDRO241040	Parcel #24 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPMDRO241060	Parcel #24 : Perform Appraisals	20	05-Mar-13	01-Apr-13	440	$0
3ANBGPMDRO241070	Parcel #24 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	440	$0
3ANBGPMDRO241080	Parcel #24 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	411	$0
3ANBGPMDRO241090	Parcel #24 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	420	$0
3ANBGPMDRO241100	Parcel #24 : Parcel closing	20	15-Aug-13	12-Sep-13	610	$0
3ANBGPMDRO241110	Parcel #24 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	420	$0
3ANBGPMDMSRO24`	Parcel #24 : Cleared for Construction	0		11-Jun-14	602	$0
Parcel #26 NBGP - Meacham to Dewey (STA 731+00 to STA 735+00)		486	01-Aug-12	11-Jun-14	430	$0
3ANBGPMDMSRO26`	Parcel #26 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPMDRO261010	Parcel #26 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPMDRO261020	Parcel #26 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPMDRO261030	Parcel #26 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	440	$0
3ANBGPMDRO261050	Parcel #26 : Prepare Title Work	30	22-Jan-13	04-Mar-13	440	$0
3ANBGPMDRO261040	Parcel #26 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPMDRO261060	Parcel #26 : Perform Appraisals	20	05-Mar-13	01-Apr-13	440	$0
3ANBGPMDRO261070	Parcel #26 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	440	$0
3ANBGPMDRO261080	Parcel #26 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	411	$0
3ANBGPMDRO261090	Parcel #26 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	420	$0
3ANBGPMDRO261100	Parcel #26 : Parcel closing	20	15-Aug-13	12-Sep-13	610	$0
3ANBGPMDRO261110	Parcel #26 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	420	$0
3ANBGPMDMSRO26`	Parcel #26 : Cleared for Construction	0		11-Jun-14	602	$0
Parcel #28 SBGP - Meacham to Dewey (STA 736+00 to STA 736+00)		410	01-Aug-12	25-Feb-14	130	$0

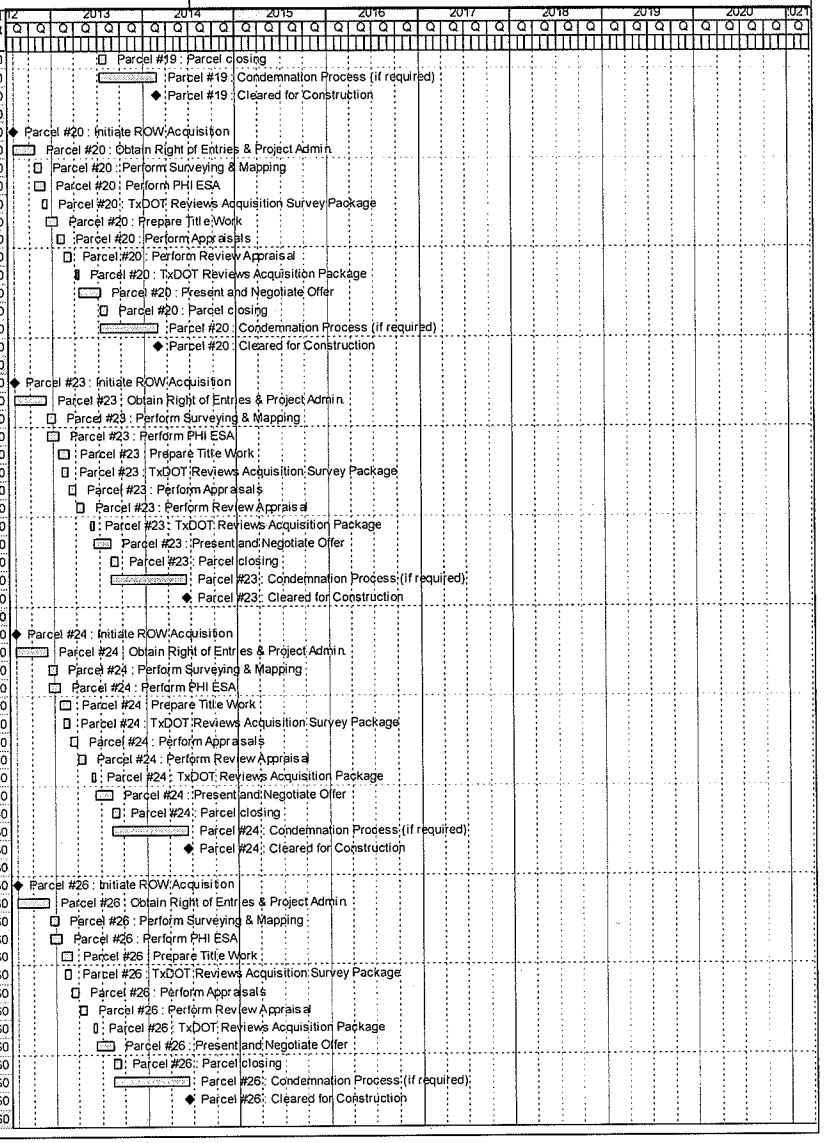

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBGPMDMSRO281	Parcel #28 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPMDRO281010	Parcel #28 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPMDRO281020	Parcel #28 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBGPMDRO281030	Parcel #28 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBGPMDRO281040	Parcel #28 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBGPMDRO281050	Parcel #28 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBGPMDRO281060	Parcel #28 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBGPMDRO281070	Parcel #28 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBGPMDRO281080	Parcel #28 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBGPMDRO281090	Parcel #28 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBGPMDRO281100	Parcel #28 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBGPMDRO281110	Parcel #28 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBGPMDMSRO281	Parcel #28 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #30 NBGP - Meacham to Dewey (STA 735+00 to STA 735+00)		486	01-Aug-12	11-Jun-14	430	$0
3ANBGPMDMSRO30	Parcel #30 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ANBGPMDRO301010	Parcel #30 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	46	$0
3ANBGPMDRO301020	Parcel #30 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ANBGPMDRO301030	Parcel #30 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	440	$0
3ANBGPMDRO301050	Parcel #30 : Prepare Title Work	30	22-Jan-13	04-Mar-13	440	$0
3ANBGPMDRO301040	Parcel #30 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ANBGPMDRO301060	Parcel #30 : Perform Appraisals	20	19-Mar-13	15-Apr-13	430	$0
3ANBGPMDRO301070	Parcel #30 : Perform Review Appraisal	20	16-Apr-13	13-May-13	430	$0
3ANBGPMDRO301080	Parcel #30 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	411	$0
3ANBGPMDRO301090	Parcel #30 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	420	$0
3ANBGPMDRO301100	Parcel #30 : Parcel closing	20	15-Aug-13	12-Sep-13	610	$0
3ANBGPMDRO301110	Parcel #30 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	420	$0
3ANBGPMDMSRO30	Parcel #30 : Cleared for Construction	0		11-Jun-14	602	$0
Parcel #32 NBGP - Meacham to Dewey (STA 736+00 to STA 740+00)		486	01-Aug-12	11-Jun-14	430	$0
3ANBGPMDRO321010	Parcel #32 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	46	$0
3ANBGPMDMSRO32	Parcel #32 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ANBGPMDRO321020	Parcel #32 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ANBGPMDRO321030	Parcel #32 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	440	$0
3ANBGPMDRO321050	Parcel #32 : Prepare Title Work	30	22-Jan-13	04-Mar-13	440	$0
3ANBGPMDRO321040	Parcel #32 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ANBGPMDRO321060	Parcel #32 : Perform Appraisals	20	19-Mar-13	15-Apr-13	430	$0
3ANBGPMDRO321070	Parcel #32 : Perform Review Appraisal	20	16-Apr-13	13-May-13	430	$0
3ANBGPMDRO321080	Parcel #32 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	411	$0
3ANBGPMDRO321090	Parcel #32 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	420	$0
3ANBGPMDRO321100	Parcel #32 : Parcel closing	20	15-Aug-13	12-Sep-13	610	$0
3ANBGPMDRO321110	Parcel #32 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	420	$0
3ANBGPMDMSRO32	Parcel #32 : Cleared for Construction	0		11-Jun-14	602	$0
Parcel #35 SBFR - Meacham to Dewey (STA 743+00 to STA 743+00)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO351	Parcel #35 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO351010	Parcel #35 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO351020	Parcel #35 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO351030	Parcel #35 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO351040	Parcel #35 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO351050	Parcel #35 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO351060	Parcel #35 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO351070	Parcel #35 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO351080	Parcel #35 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO351090	Parcel #35 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO351100	Parcel #35 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO351110	Parcel #35 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO351	Parcel #35 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #36 SBFR - Meacham to Dewey (STA 744+00 to STA 744+00)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO361	Parcel #36 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO361010	Parcel #36 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO361020	Parcel #36 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO361030	Parcel #36 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0

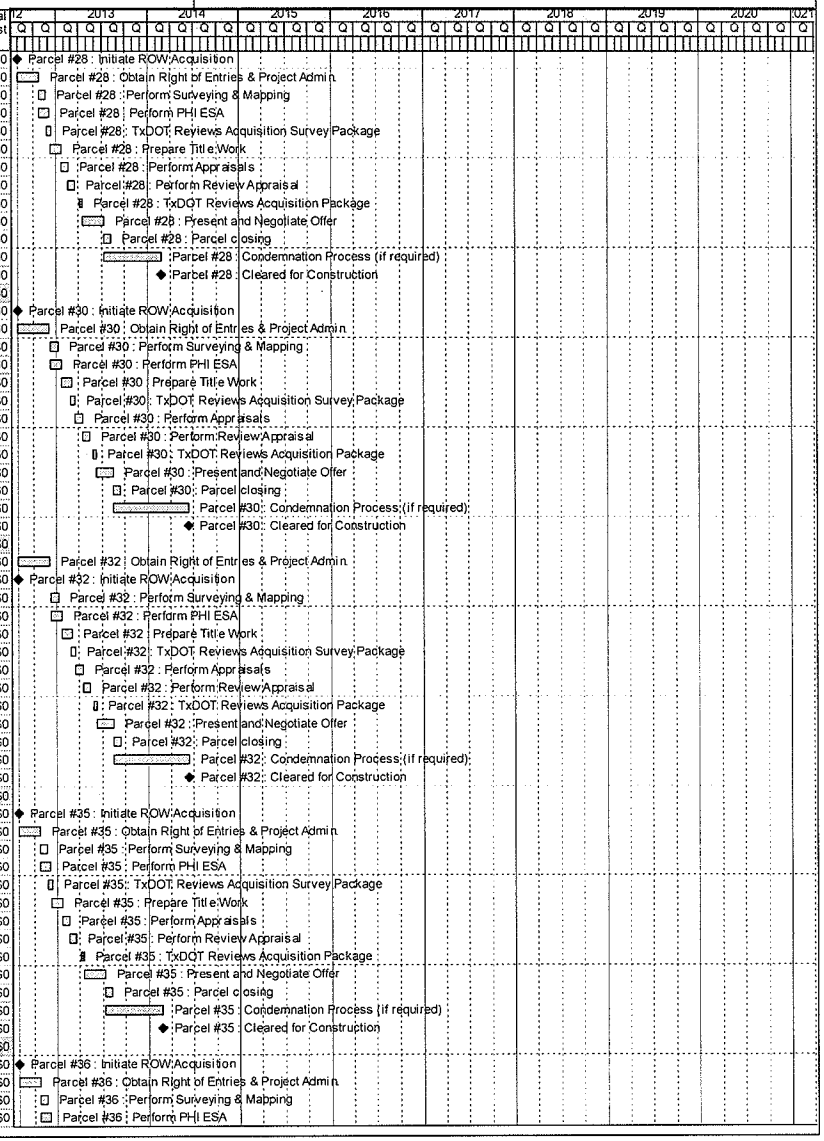

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRMDRO361040	Parcel #36 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO361050	Parcel #36 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO361060	Parcel #36 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO361070	Parcel #36 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO361080	Parcel #36 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO361090	Parcel #36 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO361100	Parcel #36 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO361110	Parcel #36 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO361	Parcel #36 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #37 SBFR - Meacham to Dewey (STA 745+00 to STA 745+00)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO371	Parcel #37 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO371010	Parcel #37 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO371020	Parcel #37 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO371030	Parcel #37 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO371040	Parcel #37 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO371050	Parcel #37 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO371060	Parcel #37 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO371070	Parcel #37 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO371080	Parcel #37 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO371090	Parcel #37 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO371100	Parcel #37 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO371110	Parcel #37 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO371	Parcel #37 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #38 SBFR - Meacham to Dewey (STA 745+00 to STA 745+00)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO381	Parcel #38 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO381010	Parcel #38 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO381020	Parcel #38 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO381030	Parcel #38 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO381040	Parcel #38 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO381050	Parcel #38 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO381060	Parcel #38 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO381070	Parcel #38 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO381080	Parcel #38 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO381090	Parcel #38 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO381100	Parcel #38 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO381110	Parcel #38 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO381	Parcel #38 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #40 SBFR - Meacham to Dewey (STA 746+00 to STA 746+00)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO401	Parcel #40 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO401010	Parcel #40 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO401020	Parcel #40 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO401030	Parcel #40 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO401040	Parcel #40 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO401050	Parcel #40 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO401060	Parcel #40 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO401070	Parcel #40 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO401080	Parcel #40 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO401090	Parcel #40 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO401100	Parcel #40 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO401110	Parcel #40 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO401	Parcel #40 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #42 (TxDOT #921) - COMPLEX - SBFR - Meacham to Dewey (STA 750+00 to STA 750+00)		537	01-Aug-12	21-Aug-14	3	$0
3ASBFRMDMSRO421	Parcel #42 : Initiate ROW Acquisition	0	01-Aug-12		5	$0
3ASBFRMDRO421010	Parcel #42 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	3	$0
3ASBFRMDRO421030	Parcel #42 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	3	$0
3ASBFRMDRO421020	Parcel #42 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	13	$0
3ASBFRMDRO421040	Parcel #42 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRMDRO421050	Parcel #42 : Prepare Title Work	30	22-Jan-13	04-Mar-13	3	$0
3ASBFRMDRO421060	Parcel #42 : Perform Appraisals	20	05-Mar-13	01-Apr-13	3	$0
3ASBFRMDRO421070	Parcel #42 : Perform Review Appraisal	30	02-Apr-13	13-May-13	3	$0

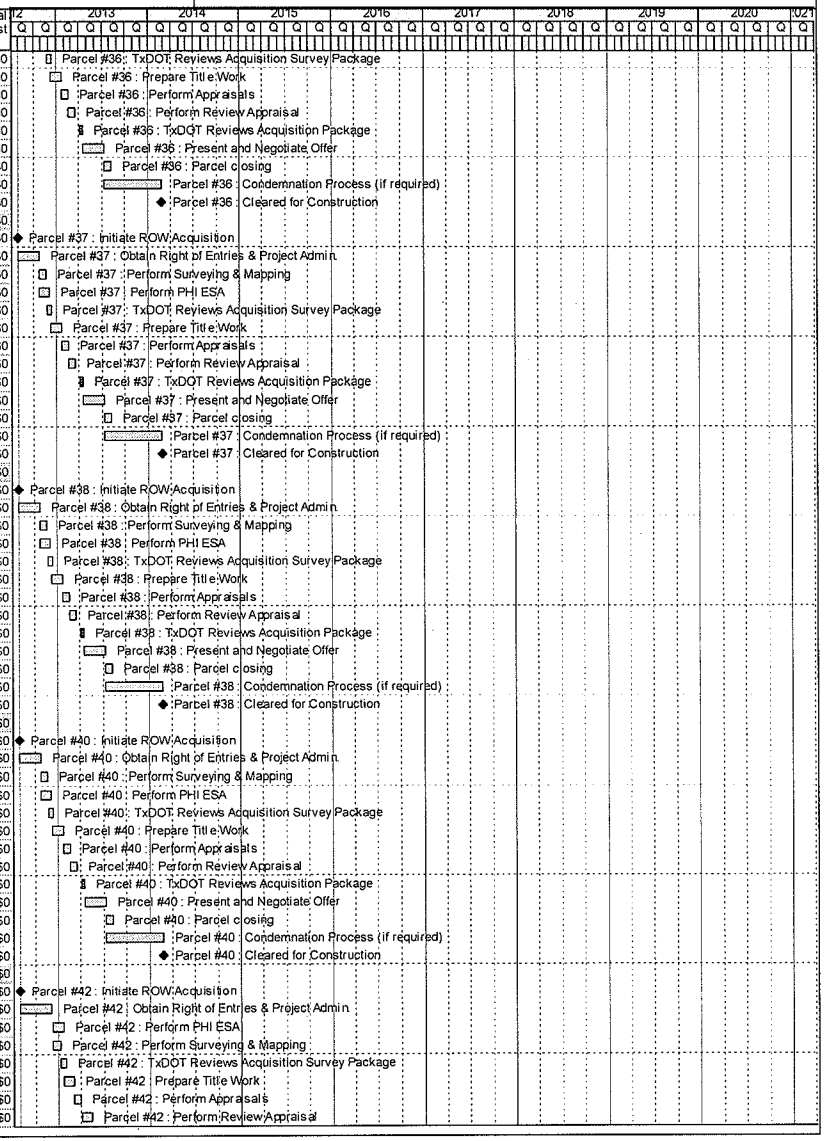

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRMDRO421080	Parcel #42 : TxDOT Reviews Acquisition Package	10	14-May-13	28-May-13	3	$0
3ASBFRMDRO421090	Parcel #42 : Present and Negotiate Offer	90	29-May-13	03-Oct-13	3	$0
3ASBFRMDRO421100	Parcel #42 : Parcel closing	60	04-Oct-13	30-Dec-13	168	$0
3ASBFRMDRO421110	Parcel #42 : Condemnation Process (if required)	225	04-Oct-13	21-Aug-14	3	$0
3ASBFRMDMSRO421	Parcel #42 : Cleared for Construction	0		21-Aug-14	5	$0
Parcel #45 NBGP - Meacham to Dewey (STA 743+00 to STA 743+00)		486	01-Aug-12	11-Jun-14	430	$0
3ANBGPMDMSRO45	Parcel #45 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ANBGPMDRO451010	Parcel #45 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	46	$0
3ANBGPMDRO451020	Parcel #45 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ANBGPMDRO451030	Parcel #45 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	440	$0
3ANBGPMDRO451050	Parcel #45 : Prepare Title Work	30	22-Jan-13	04-Mar-13	440	$0
3ANBGPMDRO451040	Parcel #45 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ANBGPMDRO451060	Parcel #45 : Perform Appraisals	20	19-Mar-13	15-Apr-13	430	$0
3ANBGPMDRO451070	Parcel #45 : Perform Review Appraisal	20	16-Apr-13	13-May-13	430	$0
3ANBGPMDRO451080	Parcel #45 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	411	$0
3ANBGPMDRO451090	Parcel #45 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	420	$0
3ANBGPMDRO451100	Parcel #45 : Parcel closing	20	15-Aug-13	12-Sep-13	610	$0
3ANBGPMDRO451110	Parcel #45 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	420	$0
3ANBGPMDMSRO45	Parcel #45 : Cleared for Construction	0		11-Jun-14	602	$0
Parcel #46 NBFR - Meacham to Dewey (STA 743+00 to STA 745+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO46	Parcel #46 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO461010	Parcel #46 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO461020	Parcel #46 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRMDRO461030	Parcel #46 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO461040	Parcel #46 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRMDRO461050	Parcel #46 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO461060	Parcel #46 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO461070	Parcel #46 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO461080	Parcel #46 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO461090	Parcel #46 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO461100	Parcel #46 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDRO461110	Parcel #46 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDMSRO46	Parcel #46 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #47 NBFR - Meacham to Dewey (STA 746+00 to STA 750+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO47	Parcel #47 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO471010	Parcel #47 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO471020	Parcel #47 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRMDRO471030	Parcel #47 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO471040	Parcel #47 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRMDRO471050	Parcel #47 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO471060	Parcel #47 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO471070	Parcel #47 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO471080	Parcel #47 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO471090	Parcel #47 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO471110	Parcel #47 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDRO471100	Parcel #47 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDMSRO47	Parcel #47 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #48 NBFR - Meacham to Dewey (STA 750+50 to STA 751+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO48	Parcel #48 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO481010	Parcel #48 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO481020	Parcel #48 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	21	$0
3ANBFRMDRO481030	Parcel #48 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO481050	Parcel #48 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO481040	Parcel #48 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO481060	Parcel #48 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO481070	Parcel #48 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO481080	Parcel #48 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO481090	Parcel #48 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO481100	Parcel #48 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDRO481110	Parcel #48 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0

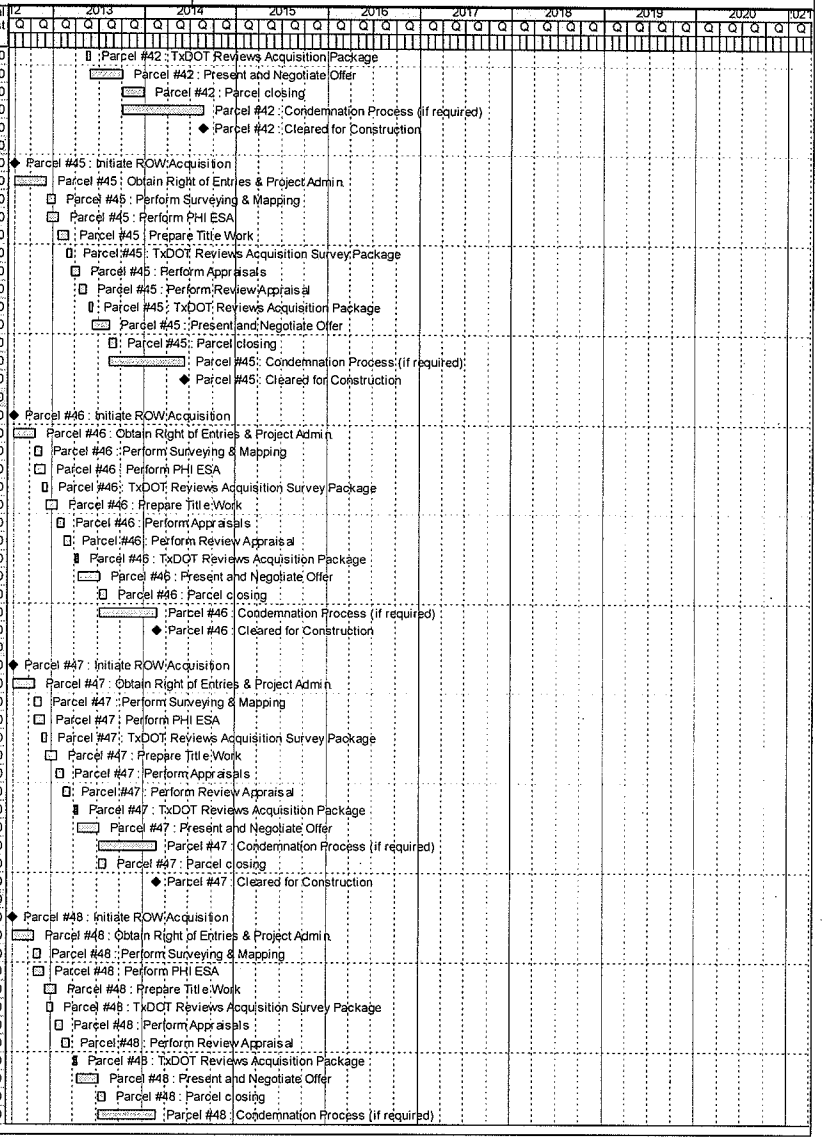

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRMDMSRO48	Parcel #48 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #49 NBFR - Meacham to Dewey (STA 751+00 to STA 756+00)		410	01-Aug-12	25-Feb-14	147	$0
3ANBFRMDMSRO49	Parcel #49 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRMDRO491010	Parcel #49 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRMDRO491020	Parcel #49 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	21	$0
3ANBFRMDRO491030	Parcel #49 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRMDRO491050	Parcel #49 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRMDRO491040	Parcel #49 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO491060	Parcel #49 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRMDRO491070	Parcel #49 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRMDRO491080	Parcel #49 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRMDRO491090	Parcel #49 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	144	$0
3ANBFRMDRO491100	Parcel #49 : Parcel closing	20	11-Jul-13	07-Aug-13	284	$0
3ANBFRMDRO491110	Parcel #49 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	144	$0
3ANBFRMDMSRO49	Parcel #49 : Cleared for Construction	0		25-Feb-14	205	$0
Parcel #50 SBFR - Meacham to Dewey (STA 756+00 to STA 756+00)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO501	Parcel #50 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO501010	Parcel #50 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO501020	Parcel #50 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO501030	Parcel #50 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO501040	Parcel #50 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO501050	Parcel #50 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO501060	Parcel #50 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO501070	Parcel #50 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO501080	Parcel #50 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO501090	Parcel #50 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO501100	Parcel #50 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO501110	Parcel #50 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO501	Parcel #50 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #53 SBFR - Meacham to Dewey (STA 762+50 to STA 766+50)		410	01-Aug-12	25-Feb-14	130	$0
3ASBFRMDMSRO531	Parcel #53 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRMDRO531010	Parcel #53 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRMDRO531020	Parcel #53 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRMDRO531030	Parcel #53 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRMDRO531040	Parcel #53 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRMDRO531050	Parcel #53 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRMDRO531060	Parcel #53 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRMDRO531070	Parcel #53 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRMDRO531080	Parcel #53 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRMDRO531090	Parcel #53 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	128	$0
3ASBFRMDRO531100	Parcel #53 : Parcel closing	20	11-Jul-13	07-Aug-13	268	$0
3ASBFRMDRO531110	Parcel #53 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	128	$0
3ASBFRMDMSRO531	Parcel #53 : Cleared for Construction	0		25-Feb-14	182	$0
Parcel #54 NBFR - Meacham to Dewey (STA 755+00 to STA 759+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO54	Parcel #54 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO541010	Parcel #54 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO541020	Parcel #54 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO541030	Parcel #54 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO541050	Parcel #54 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO541040	Parcel #54 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO541060	Parcel #54 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO541070	Parcel #54 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO541080	Parcel #54 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO541090	Parcel #54 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO541100	Parcel #54 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO541110	Parcel #54 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO54	Parcel #54 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #55 NBFR - Meacham to Dewey (STA 755+00 to STA 760+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO55	Parcel #55 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO551010	Parcel #55 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0

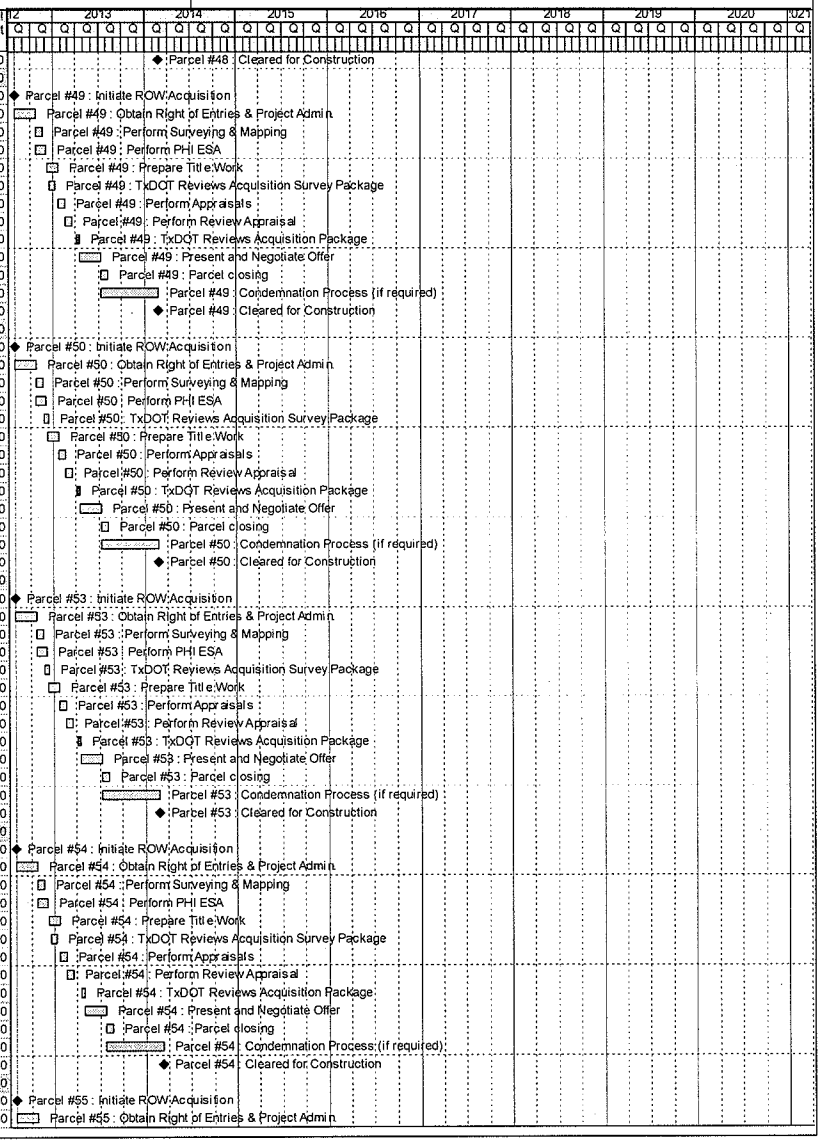

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRMDRO551020	Parcel #55 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO551030	Parcel #55 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO551050	Parcel #55 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO551040	Parcel #55 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO551060	Parcel #55 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO551070	Parcel #55 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO551080	Parcel #55 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO551090	Parcel #55 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO551100	Parcel #55 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO551110	Parcel #55 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO55'	Parcel #55 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #56 NBFR - Meacham to Dewey (STA 761+00 to STA 761+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO56'	Parcel #56 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO561010	Parcel #56 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO561020	Parcel #56 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO561030	Parcel #56 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO561050	Parcel #56 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO561040	Parcel #56 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO561060	Parcel #56 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO561070	Parcel #56 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO561080	Parcel #56 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO561090	Parcel #56 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO561100	Parcel #56 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO561110	Parcel #56 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO56'	Parcel #56 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #57 NBFR - Meacham to Dewey (STA 762+00 to STA 762+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO57'	Parcel #57 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO571010	Parcel #57 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO571020	Parcel #57 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO571030	Parcel #57 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO571050	Parcel #57 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO571040	Parcel #57 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO571060	Parcel #57 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO571070	Parcel #57 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO571080	Parcel #57 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO571090	Parcel #57 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO571100	Parcel #57 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO571110	Parcel #57 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO57'	Parcel #57 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #58 NBFR - Meacham to Dewey (STA 762+00 to STA 771+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO58'	Parcel #58 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO581010	Parcel #58 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO581020	Parcel #58 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO581030	Parcel #58 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO581050	Parcel #58 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO581040	Parcel #58 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ANBFRMDRO581060	Parcel #58 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO581070	Parcel #58 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO581080	Parcel #58 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO581090	Parcel #58 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO581100	Parcel #58 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO581110	Parcel #58 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO58'	Parcel #58 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #59 NBFR - Meacham to Dewey (STA 771+00 to STA 776+00)		420	01-Aug-12	11-Mar-14	137	$0
3ANBFRMDMSRO59'	Parcel #59 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ANBFRMDRO591010	Parcel #59 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	29	$0
3ANBFRMDRO591020	Parcel #59 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ANBFRMDRO591030	Parcel #59 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ANBFRMDRO591050	Parcel #59 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ANBFRMDRO591040	Parcel #59 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0

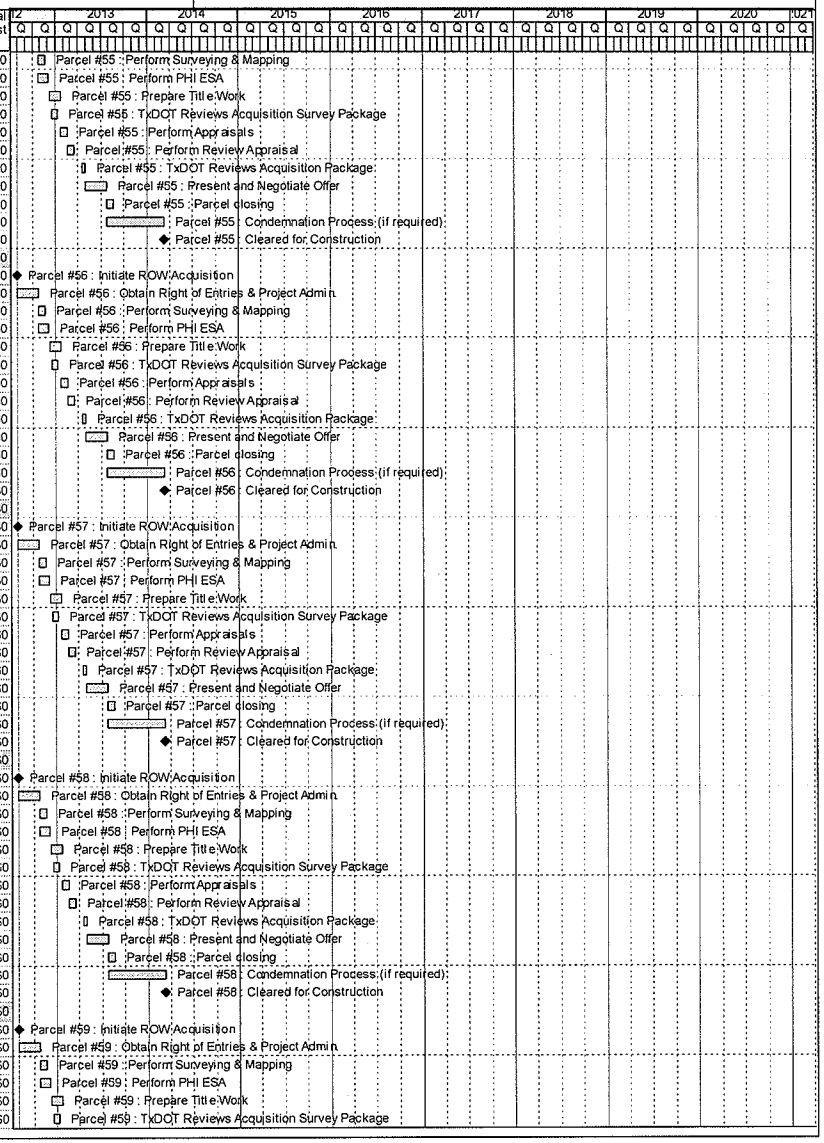

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRMDRO591060	Parcel #59 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ANBFRMDRO591070	Parcel #59 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ANBFRMDRO591080	Parcel #59 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ANBFRMDRO591090	Parcel #59 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	134	$0
3ANBFRMDRO591100	Parcel #59 : Parcel closing	20	25-Jul-13	21-Aug-13	274	$0
3ANBFRMDRO591110	Parcel #59 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	134	$0
3ANBFRMDMSRO59	Parcel #59 : Cleared for Construction	0		11-Mar-14	191	$0
Parcel #60 (TxDOT #833) - COMPLEX - SBFR - Meacham to Dewey (STA 767+00 to STA 771+00)		537	01-Aug-12	21-Aug-14	3	$0
3ASBFRMDMSRO601	Parcel #60 : Initiate ROW Acquisition	0	01-Aug-12		5	$0
3ASBFRMDRO601010	Parcel #60 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	3	$0
3ASBFRMDRO601020	Parcel #60 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	13	$0
3ASBFRMDRO601030	Parcel #60 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	3	$0
3ASBFRMDRO601040	Parcel #60 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRMDRO601050	Parcel #60 : Prepare Title Work	30	22-Jan-13	04-Mar-13	3	$0
3ASBFRMDRO601060	Parcel #60 : Perform Appraisals	20	05-Mar-13	01-Apr-13	3	$0
3ASBFRMDRO601070	Parcel #60 : Perform Review Appraisal	30	02-Apr-13	13-May-13	3	$0
3ASBFRMDRO601080	Parcel #60 : TxDOT Reviews Acquisition Package	10	14-May-13	28-May-13	3	$0
3ASBFRMDRO601090	Parcel #60 : Present and Negotiate Offer	90	29-May-13	03-Oct-13	3	$0
3ASBFRMDRO601100	Parcel #60 : Parcel closing	20	04-Oct-13	31-Oct-13	208	$0
3ASBFRMDRO601110	Parcel #60 : Condemnation Process (if required)	225	04-Oct-13	21-Aug-14	3	$0
3ASBFRMDMSRO601	Parcel #60 : Cleared for Construction	0		21-Aug-14	5	$0
Parcel #62 NBFR - Dewey to S. of trinity River (STA 776+00 to STA 776+00)		465	01-Aug-12	13-May-14	296	$0
3ANBFRDTMSRO621	Parcel #62 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBFRDTRO621010	Parcel #62 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBFRDTRO621020	Parcel #62 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBFRDTRO621030	Parcel #62 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBFRDTRO621050	Parcel #62 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBFRDTRO621040	Parcel #62 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBFRDTRO621060	Parcel #62 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBFRDTRO621070	Parcel #62 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBFRDTRO621080	Parcel #62 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBFRDTRO621090	Parcel #62 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	289	$0
3ANBFRDTRO621100	Parcel #62 : Parcel closing	20	18-Jul-13	14-Aug-13	479	$0
3ANBFRDTRO621110	Parcel #62 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	289	$0
3ANBFRDTMSRO621	Parcel #62 : Cleared for Construction	0		13-May-14	414	$0
Parcel #63 NBFR - Dewey to S. of trinity River (STA 776+00 to STA 785+00)		465	01-Aug-12	13-May-14	296	$0
3ANBFRDTMSRO631	Parcel #63 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBFRDTRO631010	Parcel #63 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBFRDTRO631020	Parcel #63 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBFRDTRO631030	Parcel #63 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBFRDTRO631050	Parcel #63 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBFRDTRO631040	Parcel #63 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBFRDTRO631060	Parcel #63 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBFRDTRO631070	Parcel #63 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBFRDTRO631080	Parcel #63 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBFRDTRO631090	Parcel #63 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	289	$0
3ANBFRDTRO631100	Parcel #63 : Parcel closing	20	18-Jul-13	14-Aug-13	479	$0
3ANBFRDTRO631110	Parcel #63 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	289	$0
3ANBFRDTMSRO631	Parcel #63 : Cleared for Construction	0		13-May-14	414	$0
Parcel #66 SBFR - Dewey to S. of trinity River (STA 782+00 to STA 782+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBFRDTMSRO661	Parcel #66 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBFRDTRO661010	Parcel #66 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBFRDTRO661020	Parcel #66 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBFRDTRO661030	Parcel #66 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBFRDTRO661040	Parcel #66 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBFRDTRO661050	Parcel #66 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBFRDTRO661060	Parcel #66 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBFRDTRO661070	Parcel #66 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBFRDTRO661080	Parcel #66 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBFRDTRO661090	Parcel #66 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0

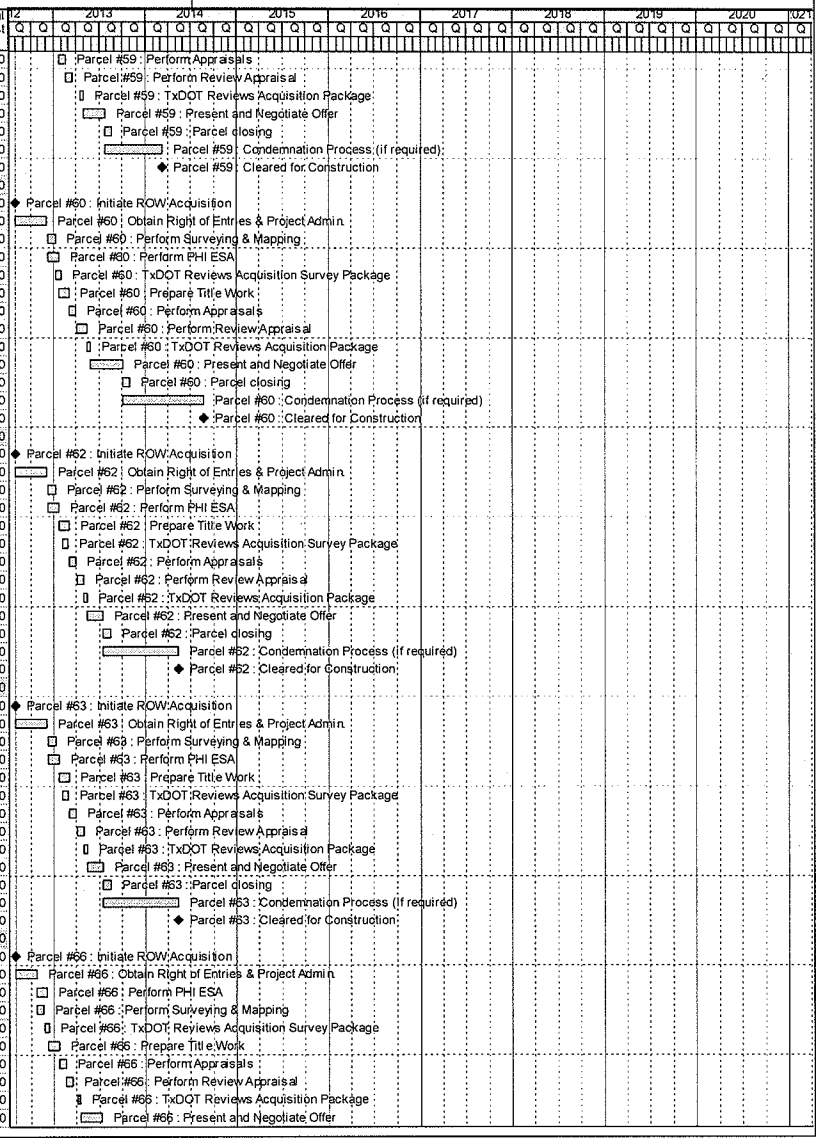

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRDTRO661100	Parcel #66 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBFRDTRO661110	Parcel #66 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBFRDTMSRO661	Parcel #66 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #67 SBFR - Dewey to S. of trinity River (STA 783+00 to STA 783+00)		465	01-Aug-12	13-May-14	135	$0
3ASBFRDTMSRO671	Parcel #67 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBFRDTRO671010	Parcel #67 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ASBFRDTRO671020	Parcel #67 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBFRDTRO671030	Parcel #67 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	132	$0
3ASBFRDTRO671050	Parcel #67 : Prepare Title Work	30	22-Jan-13	04-Mar-13	132	$0
3ASBFRDTRO671040	Parcel #67 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBFRDTRO671060	Parcel #67 : Perform Appraisals	20	05-Mar-13	01-Apr-13	132	$0
3ASBFRDTRO671070	Parcel #67 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	132	$0
3ASBFRDTRO671080	Parcel #67 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	132	$0
3ASBFRDTRO671090	Parcel #67 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	132	$0
3ASBFRDTRO671100	Parcel #67 : Parcel closing	20	18-Jul-13	14-Aug-13	322	$0
3ASBFRDTRO671110	Parcel #67 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	132	$0
3ASBFRDTMSRO671	Parcel #67 : Cleared for Construction	0		13-May-14	189	$0
Parcel #70 (TxDOT #839) - COMPLEX - NBGP - Dewey to S. of Trinity (STA 788+00 to STA 788+00)		548	01-Aug-12	05-Sep-14	145	$0
3ANBGPDTMSRO701	Parcel #70 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPDTRO701010	Parcel #70 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPDTRO701020	Parcel #70 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPDTRO701030	Parcel #70 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPDTRO701050	Parcel #70 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPDTRO701040	Parcel #70 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPDTRO701060	Parcel #70 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPDTRO701070	Parcel #70 : Perform Review Appraisal	30	02-Apr-13	13-May-13	150	$0
3ANBGPDTRO701080	Parcel #70 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	139	$0
3ANBGPDTRO701090	Parcel #70 : Present and Negotiate Offer	90	12-Jun-13	17-Oct-13	142	$0
3ANBGPDTRO701100	Parcel #70 : Parcel closing	20	18-Oct-13	14-Nov-13	347	$0
3ANBGPDTRO701110	Parcel #70 : Condemnation Process (if required)	225	18-Oct-13	05-Sep-14	142	$0
3ANBGPDTMSRO701	Parcel #70 : Cleared for Construction	0		05-Sep-14	205	$0
Parcel #74 NBFR - Dewey to S. of trinity River (STA 788+00 to STA 804+00)		465	01-Aug-12	13-May-14	296	$0
3ANBFRDTMSRO741	Parcel #74 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBFRDTRO741010	Parcel #74 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBFRDTRO741020	Parcel #74 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBFRDTRO741030	Parcel #74 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBFRDTRO741050	Parcel #74 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBFRDTRO741040	Parcel #74 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBFRDTRO741060	Parcel #74 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBFRDTRO741070	Parcel #74 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBFRDTRO741080	Parcel #74 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBFRDTRO741090	Parcel #74 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	289	$0
3ANBFRDTRO741100	Parcel #74 : Parcel closing	20	18-Jul-13	14-Aug-13	479	$0
3ANBFRDTRO741110	Parcel #74 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	289	$0
3ANBFRDTMSRO741	Parcel #74 : Cleared for Construction	0		13-May-14	414	$0
Parcel #75 (TxDOT #843/844) - COMPLEX - NBGP - Dewey to S. of Trinity (STA 805+00 to STA 805+00)		548	01-Aug-12	05-Sep-14	145	$0
3ANBGPDTMSRO751	Parcel #75 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPDTRO751010	Parcel #75 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPDTRO751020	Parcel #75 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPDTRO751030	Parcel #75 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPDTRO751050	Parcel #75 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPDTRO751040	Parcel #75 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPDTRO751060	Parcel #75 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPDTRO751070	Parcel #75 : Perform Review Appraisal	30	02-Apr-13	13-May-13	150	$0
3ANBGPDTRO751080	Parcel #75 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	139	$0
3ANBGPDTRO751090	Parcel #75 : Present and Negotiate Offer	90	12-Jun-13	17-Oct-13	142	$0
3ANBGPDTRO751100	Parcel #75 : Parcel closing	20	18-Oct-13	14-Nov-13	347	$0
3ANBGPDTRO751110	Parcel #75 : Condemnation Process (if required)	225	18-Oct-13	05-Sep-14	142	$0
3ANBGPDTMSRO751	Parcel #75 : Cleared for Construction	0		05-Sep-14	205	$0
Parcel #78 NBGP - Dewey to S. of Trinity River (STA 810+00 to STA 811+00)		465	01-Aug-12	13-May-14	226	$0

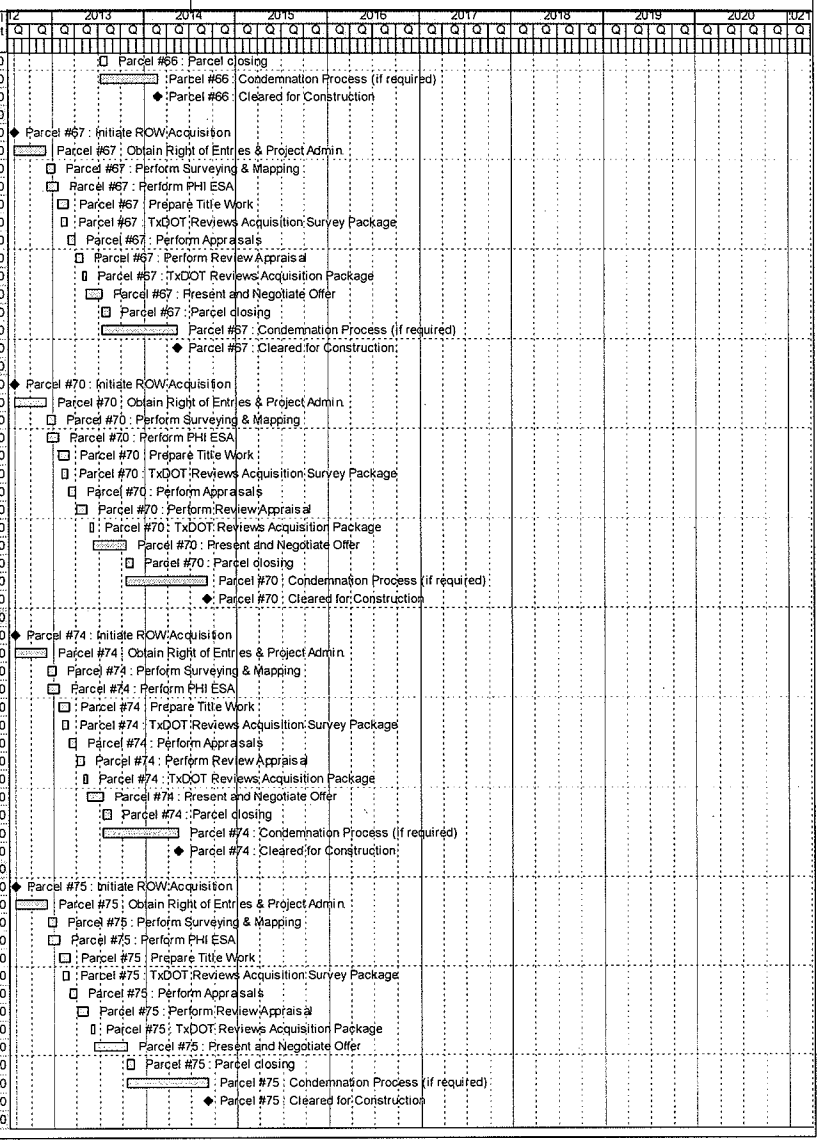

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBGPDTMSRO781	Parcel #78 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPDTRO781010	Parcel #78 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPDTRO781020	Parcel #78 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPDTRO781030	Parcel #78 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPDTRO781050	Parcel #78 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPDTRO781040	Parcel #78 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPDTRO781060	Parcel #78 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPDTRO781070	Parcel #78 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBGPDTRO781080	Parcel #78 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPDTRO781090	Parcel #78 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	222	$0
3ANBGPDTRO781100	Parcel #78 : Parcel closing	20	18-Jul-13	14-Aug-13	412	$0
3ANBGPDTRO781110	Parcel #78 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	222	$0
3ANBGPDTMSRO781	Parcel #78 : Cleared for Construction	0		13-May-14	320	$0
Parcel #87 NBGP - Dewey to S. of Trinity River (STA 815+00 to STA 829+00)		465	01-Aug-12	13-May-14	228	$0
3ANBGPDTMSRO871	Parcel #87 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPDTRO871010	Parcel #87 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPDTRO871020	Parcel #87 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPDTRO871030	Parcel #87 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPDTRO871050	Parcel #87 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPDTRO871040	Parcel #87 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPDTRO871060	Parcel #87 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPDTRO871070	Parcel #87 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBGPDTRO871080	Parcel #87 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPDTRO871090	Parcel #87 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	222	$0
3ANBGPDTRO871100	Parcel #87 : Parcel closing	20	18-Jul-13	14-Aug-13	412	$0
3ANBGPDTRO871110	Parcel #87 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	222	$0
3ANBGPDTMSRO871	Parcel #87 : Cleared for Construction	0		13-May-14	320	$0
Parcel #89 SBGP - Dewey to S. of trinity River (STA 830+00 to STA 835+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBGPDTMSRO891	Parcel #89 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPDTRO891010	Parcel #89 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPDTRO891020	Parcel #89 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBGPDTRO891030	Parcel #89 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBGPDTRO891040	Parcel #89 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBGPDTRO891050	Parcel #89 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBGPDTRO891060	Parcel #89 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBGPDTRO891070	Parcel #89 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBGPDTRO891080	Parcel #89 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBGPDTRO891090	Parcel #89 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBGPDTRO891100	Parcel #89 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBGPDTRO891110	Parcel #89 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBGPDTMSRO891	Parcel #89 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #90 SBGP - Dewey to S. of trinity River (STA 830+00 to STA 835+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBGPDTMSRO901	Parcel #90 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPDTRO901010	Parcel #90 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPDTRO901020	Parcel #90 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBGPDTRO901030	Parcel #90 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBGPDTRO901040	Parcel #90 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBGPDTRO901050	Parcel #90 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBGPDTRO901060	Parcel #90 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBGPDTRO901070	Parcel #90 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBGPDTRO901080	Parcel #90 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBGPDTRO901090	Parcel #90 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBGPDTRO901100	Parcel #90 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBGPDTRO901110	Parcel #90 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBGPDTMSRO901	Parcel #90 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #91 NBFR - Dewey to S. of trinity River (STA 830+00 to STA 835+00)		465	01-Aug-12	13-May-14	296	$0
3ANBFRDTMSRO911	Parcel #91 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBFRDTRO911010	Parcel #91 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ANBFRDTRO911020	Parcel #91 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBFRDTRO911030	Parcel #91 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0

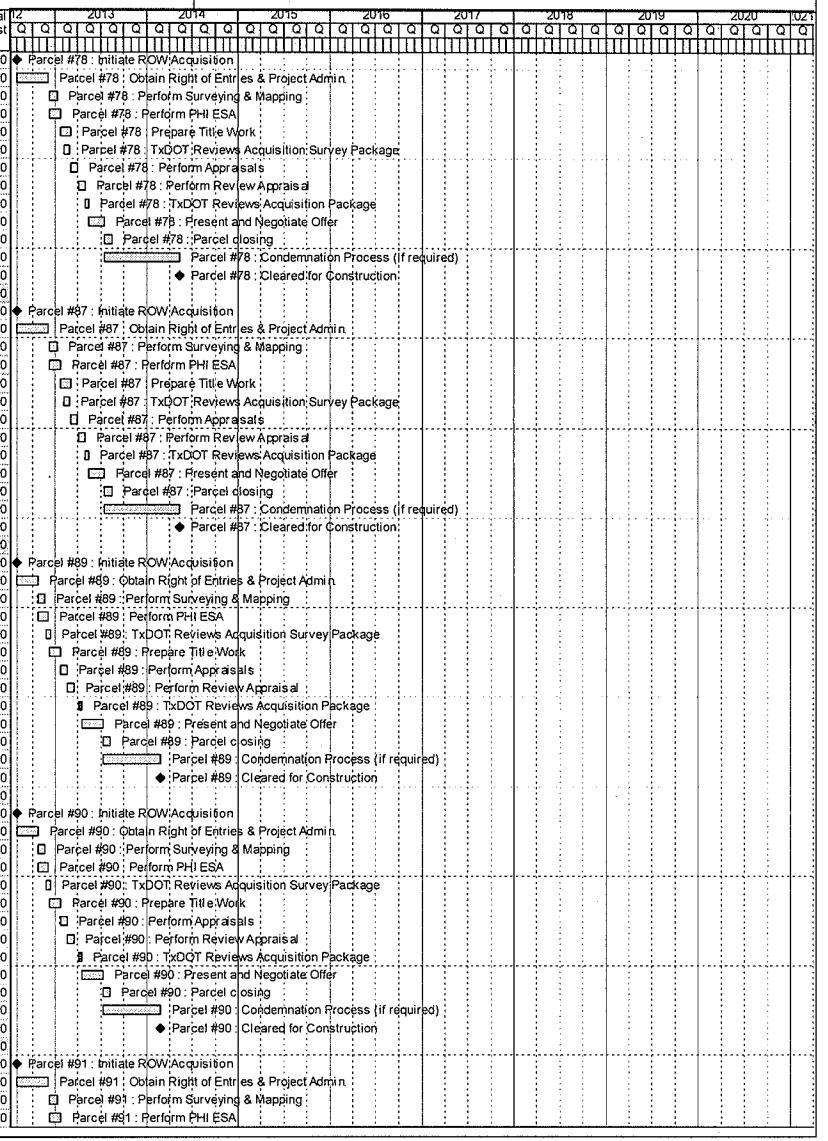

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRDTRO911050	Parcel #91 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBFRDTRO911040	Parcel #91 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBFRDTRO911060	Parcel #91 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBFRDTRO911070	Parcel #91 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBFRDTRO911080	Parcel #91 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBFRDTRO911090	Parcel #91 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	289	$0
3ANBFRDTRO911100	Parcel #91 : Parcel closing	20	18-Jul-13	14-Aug-13	479	$0
3ANBFRDTRO911110	Parcel #91 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	289	$0
3ANBFRDTMSRO911	Parcel #91 : Cleared for Construction	0		13-May-14	414	$0
Parcel #92 SBRP - Dewey to S. of trinity River (STA 839+00 to STA 842+00)		465	01-Aug-12	13-May-14	135	$0
3ASBRPDTMSRO921	Parcel #92 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBRPDTRO921010	Parcel #92 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ASBRPDTRO921020	Parcel #92 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBRPDTRO921030	Parcel #92 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	132	$0
3ASBRPDTRO921050	Parcel #92 : Prepare Title Work	30	22-Jan-13	04-Mar-13	132	$0
3ASBRPDTRO921040	Parcel #92 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBRPDTRO921060	Parcel #92 : Perform Appraisals	20	05-Mar-13	01-Apr-13	132	$0
3ASBRPDTRO921070	Parcel #92 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	132	$0
3ASBRPDTRO921080	Parcel #92 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	132	$0
3ASBRPDTRO921090	Parcel #92 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	132	$0
3ASBRPDTRO921100	Parcel #92 : Parcel closing	20	18-Jul-13	14-Aug-13	322	$0
3ASBRPDTRO921110	Parcel #92 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	132	$0
3ASBRPDTMSRO921	Parcel #92 : Cleared for Construction	0		13-May-14	189	$0
Parcel #95 SBGP - Dewey to S. of trinity River (STA 861+00 to STA 861+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBGPDTRO951000	Parcel #95 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPDTMSRO951	Parcel #95 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPDTRO951020	Parcel #95 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBGPDTRO951030	Parcel #95 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBGPDTRO951040	Parcel #95 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBGPDTRO951050	Parcel #95 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBGPDTRO951060	Parcel #95 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBGPDTRO951070	Parcel #95 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBGPDTRO951080	Parcel #95 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBGPDTRO951090	Parcel #95 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBGPDTRO951100	Parcel #95 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBGPDTRO951110	Parcel #95 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBGPDTMSRO951	Parcel #95 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #96 SBGP - Dewey to S. of trinity River (STA 861+00 to STA 861+00)		410	01-Aug-12	25-Feb-14	131	$0
3ASBGPDTMSRO961	Parcel #96 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ASBGPDTRO961010	Parcel #96 : Obtain Right of Entries & Project Admin	60	01-Aug-12	24-Oct-12	11	$0
3ASBGPDTRO961020	Parcel #96 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ASBGPDTRO961030	Parcel #96 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ASBGPDTRO961040	Parcel #96 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ASBGPDTRO961050	Parcel #96 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ASBGPDTRO961060	Parcel #96 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ASBGPDTRO961070	Parcel #96 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ASBGPDTRO961080	Parcel #96 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ASBGPDTRO961090	Parcel #96 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	129	$0
3ASBGPDTRO961100	Parcel #96 : Parcel closing	20	11-Jul-13	07-Aug-13	269	$0
3ASBGPDTRO961110	Parcel #96 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	129	$0
3ASBGPDTMSRO961	Parcel #96 : Cleared for Construction	0		25-Feb-14	183	$0
Parcel #98 SBFR - Dewey to S. of trinity River (STA 862+00 to STA 862+00)		465	01-Aug-12	13-May-14	135	$0
3ASBFRDTMSRO981	Parcel #98 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBFRDTRO981010	Parcel #98 : Obtain Right of Entries & Project Admin	90	01-Aug-12	06-Dec-12	31	$0
3ASBFRDTRO981020	Parcel #98 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBFRDTRO981030	Parcel #98 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	132	$0
3ASBFRDTRO981050	Parcel #98 : Prepare Title Work	30	22-Jan-13	04-Mar-13	132	$0
3ASBFRDTRO981040	Parcel #98 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBFRDTRO981060	Parcel #98 : Perform Appraisals	20	05-Mar-13	01-Apr-13	132	$0
3ASBFRDTRO981070	Parcel #98 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	132	$0

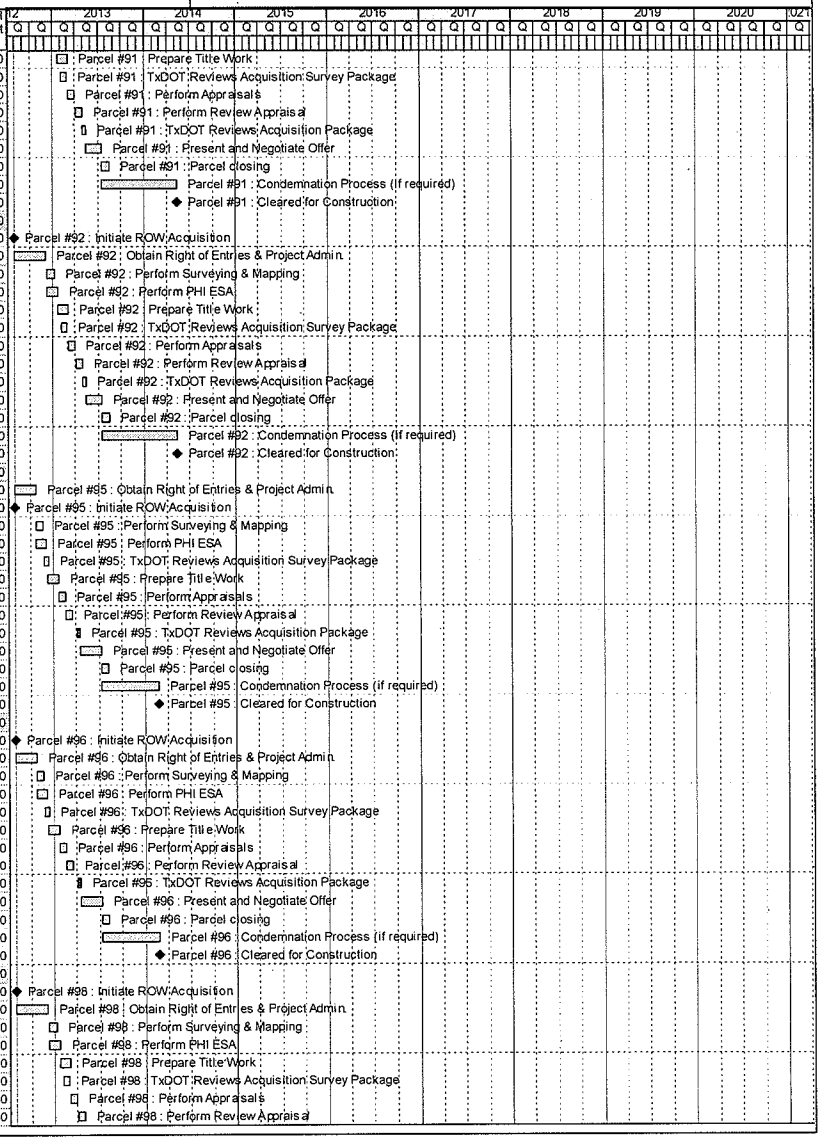

ATTACHMENT 03 - DETAILED PROGRAM SCHEDULE

NTE - Segment 3A Interchange Project - FBS # 1

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBFRDTRO981080	Parcel #98 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	132	$0
3ASBFRDTRO981090	Parcel #98 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	132	$0
3ASBFRDTRO981100	Parcel #98 : Parcel closing	20	18-Jul-13	14-Aug-13	322	$0
3ASBFRDTRO981110	Parcel #98 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	132	$0
3ASBFRDTMSRO981	Parcel #98 : Cleared for Construction	0		13-May-14	189	$0
Parcel #101 SBFR - S. of trinity River to IH 30 (STA 863+00 to STA 863+00)		420	01-Aug-12	11-Mar-14	167	$0
3ASBFRSIMSRO1011	Parcel #101 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ASBFRSIRO1011010	Parcel #101 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ASBFRSIRO1011030	Parcel #101 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRSIRO1011020	Parcel #101 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ASBFRSIRO1011050	Parcel #101 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ASBFRSIRO1011040	Parcel #101 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRSIRO1011060	Parcel #101 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ASBFRSIRO1011070	Parcel #101 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ASBFRSIRO1011080	Parcel #101 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ASBFRSIRO1011090	Parcel #101 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	164	$0
3ASBFRSIRO1011100	Parcel #101 : Parcel closing	20	25-Jul-13	21-Aug-13	304	$0
3ASBFRSIRO1011110	Parcel #101 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	164	$0
3ASBFRSIMSRO1011	Parcel #101 : Cleared for Construction	0		11-Mar-14	233	$0
Parcel #102 SBFR - S. of trinity River to IH 30 (STA 864+00 to STA 864+00)		420	01-Aug-12	11-Mar-14	167	$0
3ASBFRSIMSRO1021	Parcel #102 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ASBFRSIRO1021010	Parcel #102 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ASBFRSIRO1021020	Parcel #102 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ASBFRSIRO1021030	Parcel #102 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRSIRO1021050	Parcel #102 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ASBFRSIRO1021040	Parcel #102 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRSIRO1021060	Parcel #102 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ASBFRSIRO1021070	Parcel #102 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ASBFRSIRO1021080	Parcel #102 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ASBFRSIRO1021090	Parcel #102 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	164	$0
3ASBFRSIRO1021100	Parcel #102 : Parcel closing	20	25-Jul-13	21-Aug-13	304	$0
3ASBFRSIRO1021110	Parcel #102 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	164	$0
3ASBFRSIMSRO1021	Parcel #102 : Cleared for Construction	0		11-Mar-14	233	$0
Parcel #103 SBFR - S. of trinity River to IH 30 (STA 865+00 to STA 865+00)		420	01-Aug-12	11-Mar-14	167	$0
3ASBFRSIMSRO1031	Parcel #103 : Initiate ROW Acquisition	0	01-Aug-12		42	$0
3ASBFRSIRO1031010	Parcel #103 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	29	$0
3ASBFRSIRO1031020	Parcel #103 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	29	$0
3ASBFRSIRO1031030	Parcel #103 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	31	$0
3ASBFRSIRO1031050	Parcel #103 : Prepare Title Work	30	07-Dec-12	21-Jan-13	31	$0
3ASBFRSIRO1031040	Parcel #103 : TxDOT Reviews Acquisition Survey Package	15	17-Dec-12	10-Jan-13	11	$0
3ASBFRSIRO1031060	Parcel #103 : Perform Appraisals	20	22-Jan-13	18-Feb-13	31	$0
3ASBFRSIRO1031070	Parcel #103 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	31	$0
3ASBFRSIRO1031080	Parcel #103 : TxDOT Reviews Acquisition Package	10	16-Apr-13	29-Apr-13	11	$0
3ASBFRSIRO1031090	Parcel #103 : Present and Negotiate Offer	60	30-Apr-13	24-Jul-13	164	$0
3ASBFRSIRO1031100	Parcel #103 : Parcel closing	20	25-Jul-13	21-Aug-13	304	$0
3ASBFRSIRO1031110	Parcel #103 : Condemnation Process (if required)	160	25-Jul-13	11-Mar-14	164	$0
3ASBFRSIMSRO1031	Parcel #103 : Cleared for Construction	0		11-Mar-14	233	$0
Parcel #111 NBFR - S. of trinity River to IH 30 (STA 867+00 to STA 871+00)		465	01-Aug-12	13-May-14	296	$0
3ANBFRSIMSRO1111	Parcel #111 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBFRSIRO1111010	Parcel #111 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBFRSIRO1111020	Parcel #111 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBFRSIRO1111030	Parcel #111 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBFRSIRO1111050	Parcel #111 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBFRSIRO1111040	Parcel #111 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBFRSIRO1111060	Parcel #111 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBFRSIRO1111070	Parcel #111 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBFRSIRO1111080	Parcel #111 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBFRSIRO1111090	Parcel #111 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	289	$0
3ANBFRSIRO1111100	Parcel #111 : Parcel closing	20	18-Jul-13	14-Aug-13	479	$0
3ANBFRSIRO1111110	Parcel #111 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	289	$0

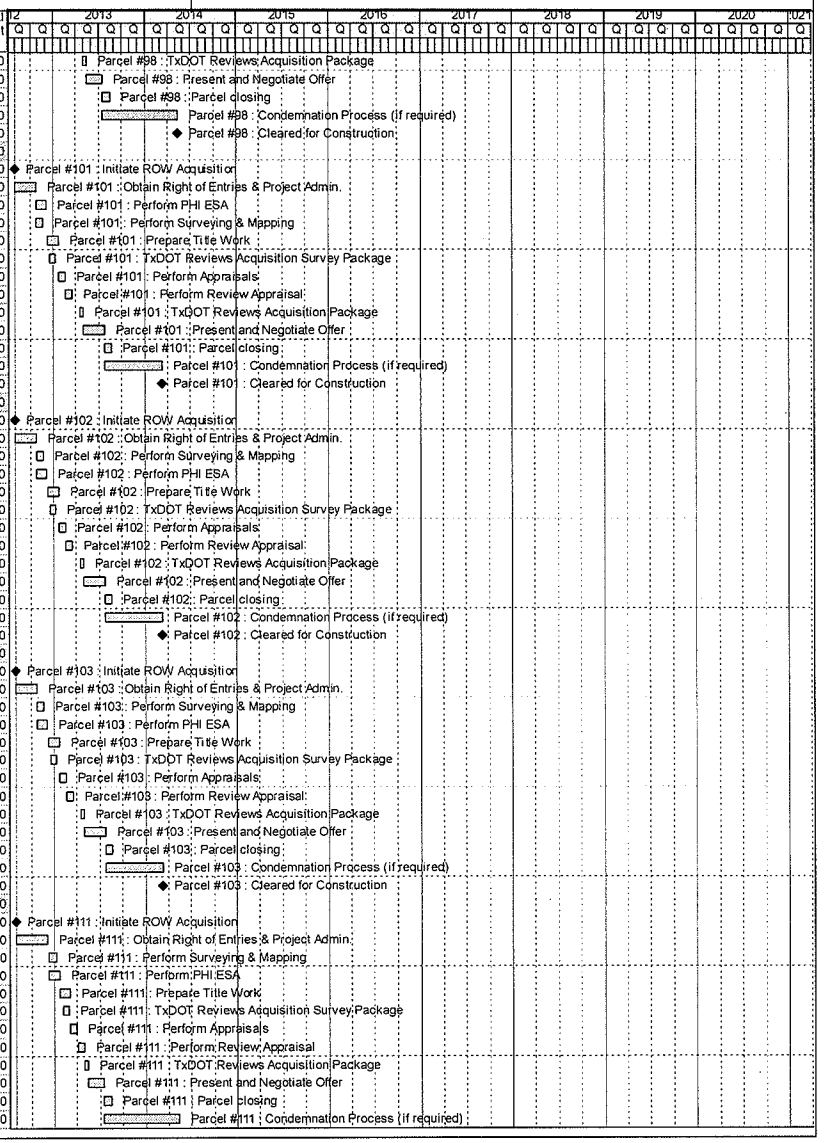

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRSIMSRO1111	Parcel #111 : Cleared for Construction	0		13-May-14	414	$0
Parcel #112 NBFR - S. of trinity River to IH 30 (STA 871+00 to STA 876+00)		465	01-Aug-12	13-May-14	296	$0
3ANBFRSIMSRO1121	Parcel #112 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBFRSIRO1121010	Parcel #112 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBFRSIRO1121020	Parcel #112 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBFRSIRO1121030	Parcel #112 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBFRSIRO1121050	Parcel #112 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBFRSIRO1121040	Parcel #112 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBFRSIRO1121060	Parcel #112 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBFRSIRO1121070	Parcel #112 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBFRSIRO1121080	Parcel #112 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBFRSIRO1121090	Parcel #112 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	289	$0
3ANBFRSIRO1121100	Parcel #112 : Parcel closing	20	18-Jul-13	14-Aug-13	479	$0
3ANBFRSIRO1121110	Parcel #112 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	289	$0
3ANBFRSIMSRO1121	Parcel #112 : Cleared for Construction	0		13-May-14	414	$0
Parcel #113 SBFR - S. of trinity River to IH 30 (STA 870+00 to STA 870+00)		465	01-Aug-12	13-May-14	122	$0
3ASBFRSIMSRO1131	Parcel #113 : Initiate ROW Acquisition	0	01-Aug-12		21	$0
3ASBFRSIRO1131010	Parcel #113 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	15	$0
3ASBFRSIRO1131020	Parcel #113 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	15	$0
3ASBFRSIRO1131030	Parcel #113 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	119	$0
3ASBFRSIRO1131040	Parcel #113 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1131050	Parcel #113 : Prepare Title Work	30	22-Jan-13	04-Mar-13	119	$0
3ASBFRSIRO1131060	Parcel #113 : Perform Appraisals	20	05-Mar-13	01-Apr-13	119	$0
3ASBFRSIRO1131070	Parcel #113 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	119	$0
3ASBFRSIRO1131080	Parcel #113 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	119	$0
3ASBFRSIRO1131090	Parcel #113 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	119	$0
3ASBFRSIRO1131100	Parcel #113 : Parcel closing	20	18-Jul-13	14-Aug-13	309	$0
3ASBFRSIRO1131110	Parcel #113 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	119	$0
3ASBFRSIMSRO1131	Parcel #113 : Cleared for Construction	0		13-May-14	170	$0
Parcel #114 SBFR - S. of trinity River to IH 30 (STA 871+00 to STA 871+00)		465	01-Aug-12	13-May-14	122	$0
3ASBFRSIMSRO1141	Parcel #114 : Initiate ROW Acquisition	0	01-Aug-12		21	$0
3ASBFRSIRO1141010	Parcel #114 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	15	$0
3ASBFRSIRO1141020	Parcel #114 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	15	$0
3ASBFRSIRO1141030	Parcel #114 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	119	$0
3ASBFRSIRO1141040	Parcel #114 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1141050	Parcel #114 : Prepare Title Work	30	22-Jan-13	04-Mar-13	119	$0
3ASBFRSIRO1141060	Parcel #114 : Perform Appraisals	20	05-Mar-13	01-Apr-13	119	$0
3ASBFRSIRO1141070	Parcel #114 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	119	$0
3ASBFRSIRO1141080	Parcel #114 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	119	$0
3ASBFRSIRO1141090	Parcel #114 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	119	$0
3ASBFRSIRO1141100	Parcel #114 : Parcel closing	20	18-Jul-13	14-Aug-13	309	$0
3ASBFRSIRO1141110	Parcel #114 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	119	$0
3ASBFRSIMSRO1141	Parcel #114 : Cleared for Construction	0		13-May-14	170	$0
Parcel #119 SBFR - S. of trinity River to IH 30 (STA 881+00 to STA 884+00)		465	01-Aug-12	13-May-14	122	$0
3ASBFRSIRO1191000	Parcel #119 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	15	$0
3ASBFRSIMSRO1191	Parcel #119 : Initiate ROW Acquisition	0	01-Aug-12		21	$0
3ASBFRSIRO1191020	Parcel #119 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	15	$0
3ASBFRSIRO1191030	Parcel #119 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	119	$0
3ASBFRSIRO1191040	Parcel #119 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO1191050	Parcel #119 : Prepare Title Work	30	22-Jan-13	04-Mar-13	119	$0
3ASBFRSIRO1191060	Parcel #119 : Perform Appraisals	20	05-Mar-13	01-Apr-13	119	$0
3ASBFRSIRO1191070	Parcel #119 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	119	$0
3ASBFRSIRO1191080	Parcel #119 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	119	$0
3ASBFRSIRO1191090	Parcel #119 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	119	$0
3ASBFRSIRO1191100	Parcel #119 : Parcel closing	20	18-Jul-13	14-Aug-13	309	$0
3ASBFRSIRO1191110	Parcel #119 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	119	$0
3ASBFRSIMSRO1191	Parcel #119 : Cleared for Construction	0		13-May-14	170	$0
Parcel #123 SBGP - S. of trinity River to IH 30 (STA 900+00 to STA 903+00)		486	01-Aug-12	11-Jun-14	444	$0
3ASBGPSIMSRO1231	Parcel #123 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ASBGPSIRO1231010	Parcel #123 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	46	$0

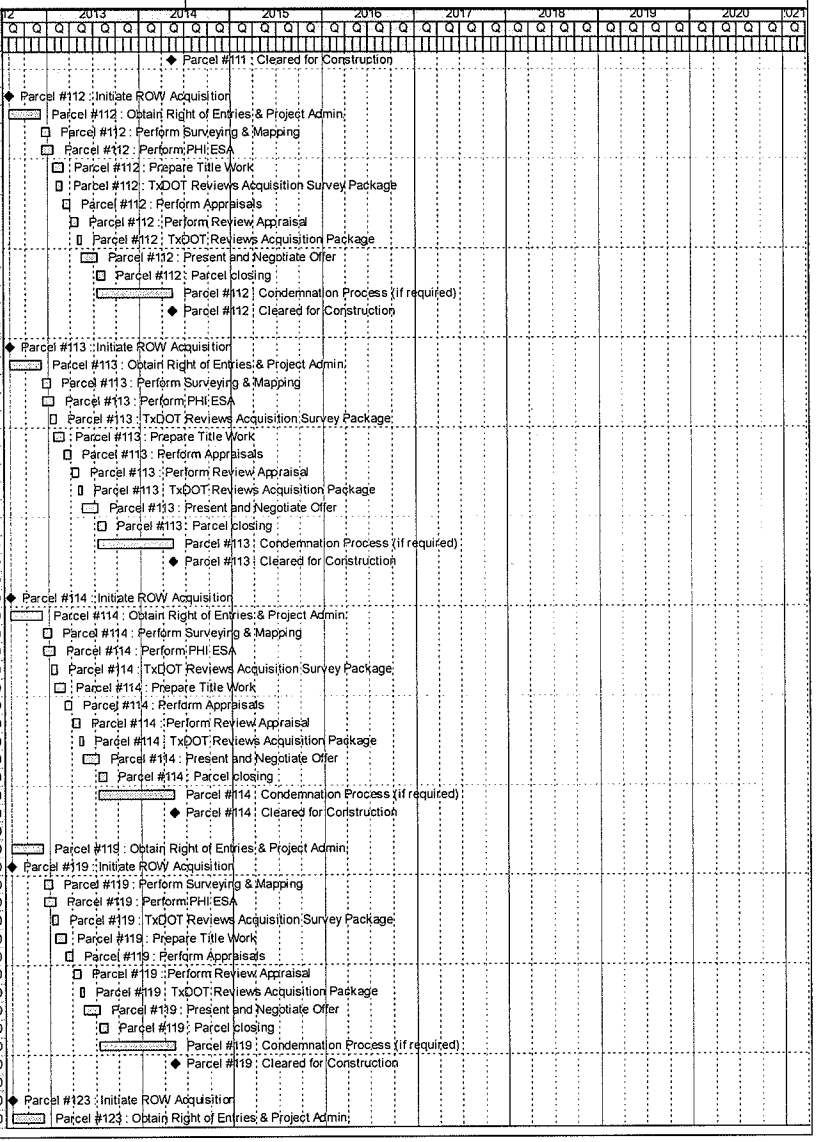

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBGPSIRO1231020	Parcel #123 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ASBGPSIRO1231030	Parcel #123 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	453	$0
3ASBGPSIRO1231050	Parcel #123 : Prepare Title Work	30	22-Jan-13	04-Mar-13	453	$0
3ASBGPSIRO1231040	Parcel #123 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ASBGPSIRO1231060	Parcel #123 : Perform Appraisals	20	19-Mar-13	15-Apr-13	443	$0
3ASBGPSIRO1231070	Parcel #123 : Perform Review Appraisal	20	16-Apr-13	13-May-13	443	$0
3ASBGPSIRO1231080	Parcel #123 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	424	$0
3ASBGPSIRO1231090	Parcel #123 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	434	$0
3ASBGPSIRO1231100	Parcel #123 : Parcel closing	20	15-Aug-13	12-Sep-13	624	$0
3ASBGPSIRO1231110	Parcel #123 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	434	$0
3ASBGPSIMSRO1231	Parcel #123 : Cleared for Construction	0		11-Jun-14	622	$0
Parcel #124 (TxDOT #—) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 903+00 to STA 910+00)		548	01-Aug-12	05-Sep-14	382	$0
3ASBGPSIMSRO1241	Parcel #124 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBGPSIRO1241010	Parcel #124 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ASBGPSIRO1241020	Parcel #124 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBGPSIRO1241030	Parcel #124 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	383	$0
3ASBGPSIRO1241050	Parcel #124 : Prepare Title Work	30	22-Jan-13	04-Mar-13	383	$0
3ASBGPSIRO1241040	Parcel #124 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBGPSIRO1241060	Parcel #124 : Perform Appraisals	20	05-Mar-13	01-Apr-13	383	$0
3ASBGPSIRO1241070	Parcel #124 : Perform Review Appraisal	30	02-Apr-13	13-May-13	383	$0
3ASBGPSIRO1241080	Parcel #124 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	368	$0
3ASBGPSIRO1241090	Parcel #124 : Present and Negotiate Offer	90	12-Jun-13	17-Oct-13	374	$0
3ASBGPSIRO1241100	Parcel #124 : Parcel closing	60	18-Oct-13	14-Jan-14	539	$0
3ASBGPSIRO1241110	Parcel #124 : Condemnation Process (if required)	225	18-Oct-13	05-Sep-14	374	$0
3ASBGPSIMSRO1241	Parcel #124 : Cleared for Construction	0		05-Sep-14	536	$0
Parcel #125 (TxDOT #896) - COMPLEX - SBGP - S. of Trinity to IH 30 (STA 912+00 to STA 912+00)		548	01-Aug-12	05-Sep-14	382	$0
3ASBGPSIMSRO1251	Parcel #125 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBGPSIRO1251010	Parcel #125 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ASBGPSIRO1251020	Parcel #125 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBGPSIRO1251030	Parcel #125 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	383	$0
3ASBGPSIRO1251050	Parcel #125 : Prepare Title Work	30	22-Jan-13	04-Mar-13	383	$0
3ASBGPSIRO1251040	Parcel #125 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBGPSIRO1251060	Parcel #125 : Perform Appraisals	20	05-Mar-13	01-Apr-13	383	$0
3ASBGPSIRO1251070	Parcel #125 : Perform Review Appraisal	30	02-Apr-13	13-May-13	383	$0
3ASBGPSIRO1251080	Parcel #125 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	368	$0
3ASBGPSIRO1251090	Parcel #125 : Present and Negotiate Offer	90	12-Jun-13	17-Oct-13	374	$0
3ASBGPSIRO1251100	Parcel #125 : Parcel closing	60	18-Oct-13	14-Jan-14	539	$0
3ASBGPSIRO1251110	Parcel #125 : Condemnation Process (if required)	225	18-Oct-13	05-Sep-14	374	$0
3ASBGPSIMSRO1251	Parcel #125 : Cleared for Construction	0		05-Sep-14	536	$0
Parcel #127 SBGP - S. of Trinity River to IH 30 (STA 916+00 to STA 916+00)		486	01-Aug-12	11-Jun-14	444	$0
3ASBGPSIMSRO1271	Parcel #127 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ASBGPSIRO1271010	Parcel #127 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	46	$0
3ASBGPSIRO1271020	Parcel #127 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ASBGPSIRO1271030	Parcel #127 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	453	$0
3ASBGPSIRO1271050	Parcel #127 : Prepare Title Work	30	22-Jan-13	04-Mar-13	453	$0
3ASBGPSIRO1271040	Parcel #127 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ASBGPSIRO1271060	Parcel #127 : Perform Appraisals	20	19-Mar-13	15-Apr-13	443	$0
3ASBGPSIRO1271070	Parcel #127 : Perform Review Appraisal	20	16-Apr-13	13-May-13	443	$0
3ASBGPSIRO1271080	Parcel #127 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	424	$0
3ASBGPSIRO1271090	Parcel #127 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	434	$0
3ASBGPSIRO1271100	Parcel #127 : Parcel closing	20	15-Aug-13	12-Sep-13	624	$0
3ASBGPSIRO1271110	Parcel #127 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	434	$0
3ASBGPSIMSRO1271	Parcel #127 : Cleared for Construction	0		11-Jun-14	622	$0
Parcel #129 SBGP - S. of Trinity River to IH 30 (STA 918+00 to STA 918+00)		486	01-Aug-12	11-Jun-14	444	$0
3ASBGPSIMSRO1291	Parcel #129 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ASBGPSIRO1291010	Parcel #129 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	46	$0
3ASBGPSIRO1291020	Parcel #129 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ASBGPSIRO1291030	Parcel #129 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	453	$0
3ASBGPSIRO1291050	Parcel #129 : Prepare Title Work	30	22-Jan-13	04-Mar-13	453	$0
3ASBGPSIRO1291040	Parcel #129 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0

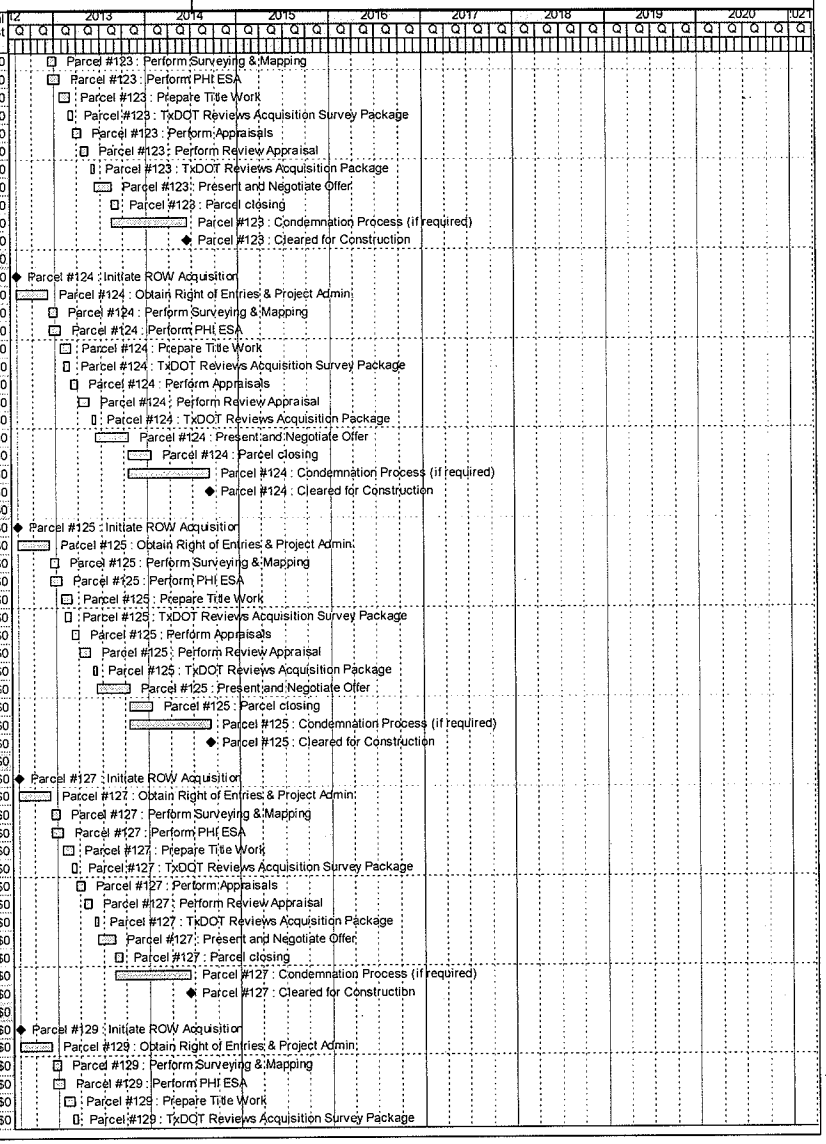

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBGPSIRO1291060	Parcel #129 : Perform Appraisals	20	19-Mar-13	15-Apr-13	443	$0
3ASBGPSIRO1291070	Parcel #129 : Perform Review Appraisal	20	16-Apr-13	13-May-13	443	$0
3ASBGPSIRO1291080	Parcel #129 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	424	$0
3ASBGPSIRO1291090	Parcel #129 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	434	$0
3ASBGPSIRO1291100	Parcel #129 : Parcel closing	20	15-Aug-13	12-Sep-13	624	$0
3ASBGPSIRO1291110	Parcel #129 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	434	$0
3ASBGPSIMSRO1291	Parcel #129 : Cleared for Construction	0		11-Jun-14	622	$0
Parcel #130 SBGP - S. of Trinity River to IH 30 (STA 918+00 to STA 923+00)		486	01-Aug-12	11-Jun-14	444	$0
3ASBGPSIMSRO1301	Parcel #130 : Initiate ROW Acquisition	0	01-Aug-12		65	$0
3ASBGPSIRO1301010	Parcel #130 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	46	$0
3ASBGPSIRO1301020	Parcel #130 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	46	$0
3ASBGPSIRO1301030	Parcel #130 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	453	$0
3ASBGPSIRO1301050	Parcel #130 : Prepare Title Work	30	22-Jan-13	04-Mar-13	453	$0
3ASBGPSIRO1301040	Parcel #130 : TxDOT Reviews Acquisition Survey Package	15	26-Feb-13	18-Mar-13	11	$0
3ASBGPSIRO1301060	Parcel #130 : Perform Appraisals	20	19-Mar-13	15-Apr-13	443	$0
3ASBGPSIRO1301070	Parcel #130 : Perform Review Appraisal	20	16-Apr-13	13-May-13	443	$0
3ASBGPSIRO1301080	Parcel #130 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	424	$0
3ASBGPSIRO1301090	Parcel #130 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	434	$0
3ASBGPSIRO1301100	Parcel #130 : Parcel closing	20	15-Aug-13	12-Sep-13	624	$0
3ASBGPSIRO1301110	Parcel #130 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	434	$0
3ASBGPSIMSRO1301	Parcel #130 : Cleared for Construction	0		11-Jun-14	622	$0
Parcel #153 NBGP - S. of Trinity River to IH 30 (STA 925+00 to STA 925+00)		465	01-Aug-12	13-May-14	432	$0
3ANBGPSIMSRO1531	Parcel #153 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1531010	Parcel #153 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1531020	Parcel #153 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1531030	Parcel #153 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPSIRO1531050	Parcel #153 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPSIRO1531040	Parcel #153 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1531060	Parcel #153 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPSIRO1531070	Parcel #153 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBGPSIRO1531080	Parcel #153 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPSIRO1531090	Parcel #153 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	421	$0
3ANBGPSIRO1531100	Parcel #153 : Parcel closing	20	18-Jul-13	14-Aug-13	611	$0
3ANBGPSIRO1531110	Parcel #153 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	421	$0
3ANBGPSIMSRO1531	Parcel #153 : Cleared for Construction	0		13-May-14	604	$0
Parcel #154 NBGP - S. of Trinity River to IH 30 (STA 924+00 to STA 924+00)		465	01-Aug-12	13-May-14	432	$0
3ANBGPSIMSRO1541	Parcel #154 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1541010	Parcel #154 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1541020	Parcel #154 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1541030	Parcel #154 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPSIRO1541050	Parcel #154 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPSIRO1541040	Parcel #154 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1541060	Parcel #154 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPSIRO1541070	Parcel #154 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBGPSIRO1541080	Parcel #154 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPSIRO1541090	Parcel #154 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	421	$0
3ANBGPSIRO1541100	Parcel #154 : Parcel closing	20	18-Jul-13	14-Aug-13	611	$0
3ANBGPSIRO1541110	Parcel #154 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	421	$0
3ANBGPSIMSRO1541	Parcel #154 : Cleared for Construction	0		13-May-14	604	$0
Parcel #155 NBGP - S. of Trinity River to IH 30 (STA 924+00 to STA 922+00)		465	01-Aug-12	13-May-14	432	$0
3ANBGPSIMSRO1551	Parcel #155 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1551010	Parcel #155 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1551020	Parcel #155 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1551030	Parcel #155 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPSIRO1551050	Parcel #155 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPSIRO1551040	Parcel #155 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1551060	Parcel #155 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPSIRO1551070	Parcel #155 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBGPSIRO1551080	Parcel #155 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPSIRO1551090	Parcel #155 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	421	$0

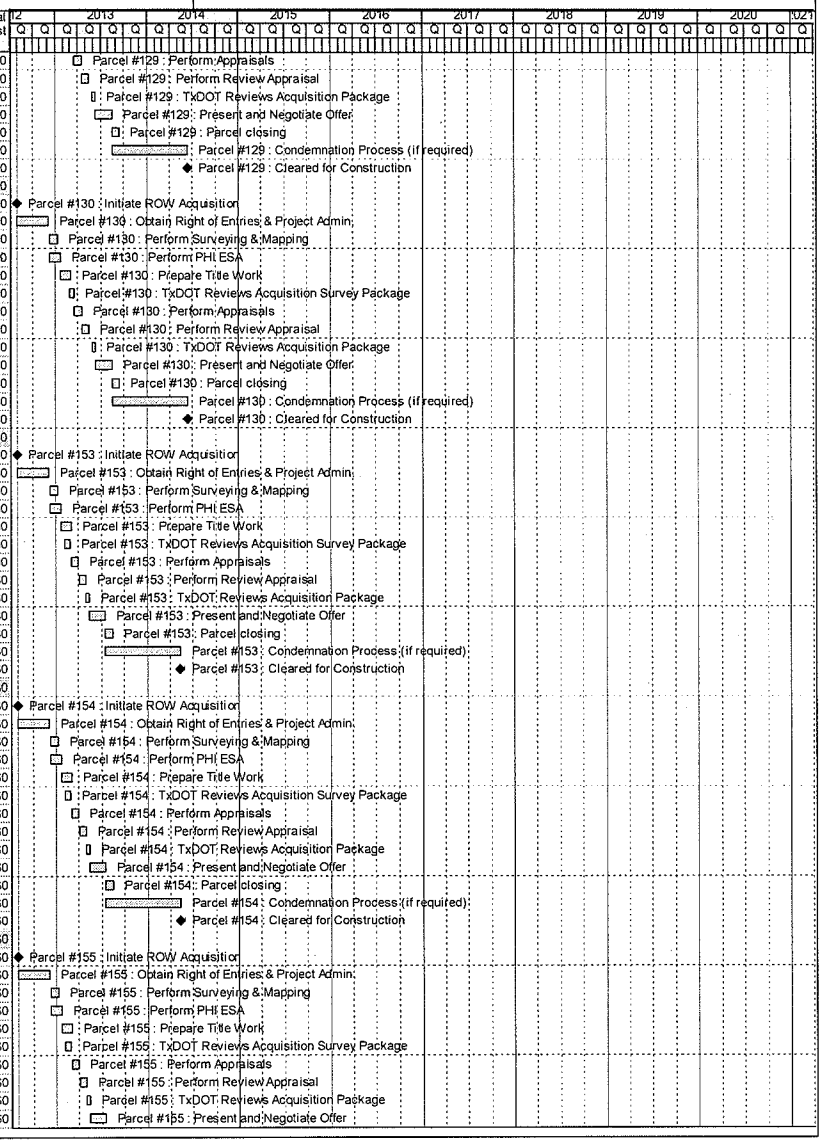

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBGPSIRO1551100	Parcel #155 : Parcel closing	20	18-Jul-13	14-Aug-13	611	$0
3ANBGPSIRO1551110	Parcel #155 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	421	$0
3ANBGPSIMSRO1551	Parcel #155 : Cleared for Construction	0		13-May-14	604	$0
Parcel #156 NBGP - S. of Trinity River to IH 30 (STA 920+00 to STA 920+00)		465	01-Aug-12	13-May-14	432	$0
3ANBGPSIMSRO1561	Parcel #156 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1561010	Parcel #156 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1561020	Parcel #156 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1561030	Parcel #156 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	150	$0
3ANBGPSIRO1561050	Parcel #156 : Prepare Title Work	30	22-Jan-13	04-Mar-13	150	$0
3ANBGPSIRO1561040	Parcel #156 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1561060	Parcel #156 : Perform Appraisals	20	05-Mar-13	01-Apr-13	150	$0
3ANBGPSIRO1561070	Parcel #156 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	150	$0
3ANBGPSIRO1561080	Parcel #156 : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	149	$0
3ANBGPSIRO1561090	Parcel #156 : Present and Negotiate Offer	45	14-May-13	17-Jul-13	421	$0
3ANBGPSIRO1561100	Parcel #156 : Parcel closing	20	18-Jul-13	14-Aug-13	611	$0
3ANBGPSIRO1561110	Parcel #156 : Condemnation Process (if required)	210	18-Jul-13	13-May-14	421	$0
3ANBGPSIMSRO1561	Parcel #156 : Cleared for Construction	0		13-May-14	604	$0
Parcel #157 NBGP - S. of Trinity River to IH 30 (STA 919+00 to STA 919+00)		486	01-Aug-12	11-Jun-14	411	$0
3ANBGPSIMSRO1571	Parcel #157 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1571010	Parcel #157 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1571020	Parcel #157 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1571030	Parcel #157 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	419	$0
3ANBGPSIRO1571050	Parcel #157 : Prepare Title Work	30	22-Jan-13	04-Mar-13	419	$0
3ANBGPSIRO1571040	Parcel #157 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1571060	Parcel #157 : Perform Appraisals	20	05-Mar-13	01-Apr-13	419	$0
3ANBGPSIRO1571070	Parcel #157 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	419	$0
3ANBGPSIRO1571080	Parcel #157 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	393	$0
3ANBGPSIRO1571090	Parcel #157 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	401	$0
3ANBGPSIRO1571100	Parcel #157 : Parcel closing	20	15-Aug-13	12-Sep-13	591	$0
3ANBGPSIRO1571110	Parcel #157 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	401	$0
3ANBGPSIMSRO1571	Parcel #157 : Cleared for Construction	0		11-Jun-14	575	$0
Parcel #158 NBFR - S. of Trinity River to IH 30 (STA 918+00 to STA 918+00)		400	01-Aug-12	11-Feb-14	138	$0
3ANBFRSIMSRO1581	Parcel #158 : Initiate ROW Acquisition	0	01-Aug-12		1	$0
3ANBFRSIRO1581010	Parcel #158 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	1	$0
3ANBFRSIRO1581020	Parcel #158 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ANBFRSIRO1581030	Parcel #158 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	1	$0
3ANBFRSIRO1581040	Parcel #158 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRSIRO1581050	Parcel #158 : Prepare Title Work	30	07-Dec-12	21-Jan-13	1	$0
3ANBFRSIRO1581060	Parcel #158 : Perform Appraisals	20	22-Jan-13	18-Feb-13	1	$0
3ANBFRSIRO1581070	Parcel #158 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	1	$0
3ANBFRSIRO1581080	Parcel #158 : TxDOT Reviews Acquisition Package	10	19-Mar-13	01-Apr-13	1	$0
3ANBFRSIRO1581090	Parcel #158 : Present and Negotiate Offer	60	02-Apr-13	25-Jun-13	136	$0
3ANBFRSIRO1581100	Parcel #158 : Parcel closing	20	26-Jun-13	24-Jul-13	276	$0
3ANBFRSIRO1581110	Parcel #158 : Condemnation Process (if required)	160	26-Jun-13	11-Feb-14	136	$0
3ANBFRSIMSRO1581	Parcel #158 : Cleared for Construction	0		11-Feb-14	194	$0
Parcel #159 NBFR - S. of Trinity River to IH 30 (STA 916+00 to STA 916+00)		400	01-Aug-12	11-Feb-14	138	$0
3ANBFRSIMSRO1591	Parcel #159 : Initiate ROW Acquisition	0	01-Aug-12		1	$0
3ANBFRSIRO1591010	Parcel #159 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	1	$0
3ANBFRSIRO1591020	Parcel #159 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	11	$0
3ANBFRSIRO1591030	Parcel #159 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	1	$0
3ANBFRSIRO1591040	Parcel #159 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRSIRO1591050	Parcel #159 : Prepare Title Work	30	07-Dec-12	21-Jan-13	1	$0
3ANBFRSIRO1591060	Parcel #159 : Perform Appraisals	20	22-Jan-13	18-Feb-13	1	$0
3ANBFRSIRO1591070	Parcel #159 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	1	$0
3ANBFRSIRO1591080	Parcel #159 : TxDOT Reviews Acquisition Package	10	19-Mar-13	01-Apr-13	1	$0
3ANBFRSIRO1591090	Parcel #159 : Present and Negotiate Offer	60	02-Apr-13	25-Jun-13	136	$0
3ANBFRSIRO1591100	Parcel #159 : Parcel closing	20	26-Jun-13	24-Jul-13	276	$0
3ANBFRSIRO1591110	Parcel #159 : Condemnation Process (if required)	160	26-Jun-13	11-Feb-14	136	$0
3ANBFRSIMSRO1591	Parcel #159 : Cleared for Construction	0		11-Feb-14	194	$0
Parcel #160 NBFR - S. of Trinity River to IH 30 (STA 915+00 to STA 915+00)		410	01-Aug-12	25-Feb-14	128	$0

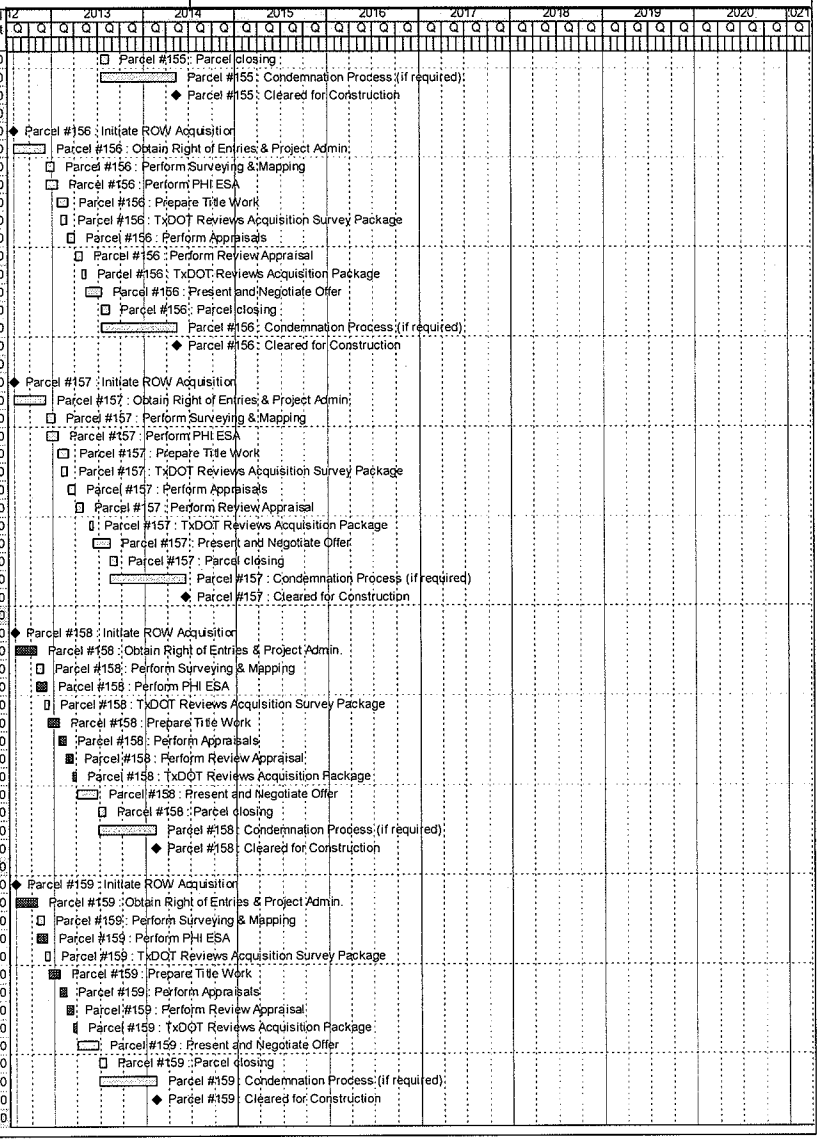

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBFRSIMSRO1601	Parcel #160 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRSIRO1601010	Parcel #160 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRSIRO1601020	Parcel #160 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRSIRO1601030	Parcel #160 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRSIRO1601040	Parcel #160 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRSIRO1601050	Parcel #160 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRSIRO1601060	Parcel #160 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRSIRO1601070	Parcel #160 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRSIRO1601080	Parcel #160 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRSIRO1601090	Parcel #160 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	126	$0
3ANBFRSIRO1601100	Parcel #160 : Parcel closing	20	11-Jul-13	07-Aug-13	266	$0
3ANBFRSIRO1601110	Parcel #160 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	126	$0
3ANBFRSIMSRO1601	Parcel #160 : Cleared for Construction	0		25-Feb-14	180	$0
Parcel #162 NBFR - S. of Trinity River to IH 30 (STA 914+00 to STA 914+00)		410	01-Aug-12	25-Feb-14	128	$0
3ANBFRSIMSRO1621	Parcel #162 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRSIRO1621010	Parcel #162 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRSIRO1621020	Parcel #162 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRSIRO1621030	Parcel #162 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRSIRO1621040	Parcel #162 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRSIRO1621050	Parcel #162 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRSIRO1621060	Parcel #162 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRSIRO1621070	Parcel #162 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRSIRO1621080	Parcel #162 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRSIRO1621090	Parcel #162 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	126	$0
3ANBFRSIRO1621100	Parcel #162 : Parcel closing	20	11-Jul-13	07-Aug-13	266	$0
3ANBFRSIRO1621110	Parcel #162 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	126	$0
3ANBFRSIMSRO1621	Parcel #162 : Cleared for Construction	0		25-Feb-14	180	$0
Parcel #166 NBFR - S. of Trinity River to IH 30 (STA 910+00 to STA 908+00)		410	01-Aug-12	25-Feb-14	128	$0
3ANBFRSIMSRO1661	Parcel #166 : Initiate ROW Acquisition	0	01-Aug-12		15	$0
3ANBFRSIRO1661010	Parcel #166 : Obtain Right of Entries & Project Admin.	60	01-Aug-12	24-Oct-12	11	$0
3ANBFRSIRO1661020	Parcel #166 : Perform Surveying & Mapping	20	25-Oct-12	21-Nov-12	12	$0
3ANBFRSIRO1661030	Parcel #166 : Perform PHI ESA	30	25-Oct-12	06-Dec-12	11	$0
3ANBFRSIRO1661040	Parcel #166 : TxDOT Reviews Acquisition Survey Package	15	26-Nov-12	14-Dec-12	11	$0
3ANBFRSIRO1661050	Parcel #166 : Prepare Title Work	30	07-Dec-12	21-Jan-13	11	$0
3ANBFRSIRO1661060	Parcel #166 : Perform Appraisals	20	22-Jan-13	18-Feb-13	11	$0
3ANBFRSIRO1661070	Parcel #166 : Perform Review Appraisal	20	19-Feb-13	18-Mar-13	11	$0
3ANBFRSIRO1661080	Parcel #166 : TxDOT Reviews Acquisition Package	10	02-Apr-13	15-Apr-13	1	$0
3ANBFRSIRO1661090	Parcel #166 : Present and Negotiate Offer	60	16-Apr-13	10-Jul-13	126	$0
3ANBFRSIRO1661100	Parcel #166 : Parcel closing	20	11-Jul-13	07-Aug-13	266	$0
3ANBFRSIRO1661110	Parcel #166 : Condemnation Process (if required)	160	11-Jul-13	25-Feb-14	126	$0
3ANBFRSIMSRO1661	Parcel #166 : Cleared for Construction	0		25-Feb-14	180	$0
Parcel #167 (TxDOT #889) - COMPLEX - NBFR - S. of Trinity to IH 30 (STA 905+00 to STA 905+00)		537	01-Aug-12	21-Aug-14	1	$0
3ANBFRSIMSRO1671	Parcel #167 : Initiate ROW Acquisition	0	01-Aug-12		1	$0
3ANBFRSIRO1671010	Parcel #167 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	1	$0
3ANBFRSIRO1671020	Parcel #167 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	11	$0
3ANBFRSIRO1671030	Parcel #167 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	1	$0
3ANBFRSIRO1671040	Parcel #167 : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANBFRSIRO1671050	Parcel #167 : Prepare Title Work	30	22-Jan-13	04-Mar-13	1	$0
3ANBFRSIRO1671060	Parcel #167 : Perform Appraisals	20	05-Mar-13	01-Apr-13	1	$0
3ANBFRSIRO1671070	Parcel #167 : Perform Review Appraisal	30	02-Apr-13	13-May-13	1	$0
3ANBFRSIRO1671080	Parcel #167 : TxDOT Reviews Acquisition Package	10	14-May-13	28-May-13	1	$0
3ANBFRSIRO1671090	Parcel #167 : Present and Negotiate Offer	90	29-May-13	03-Oct-13	1	$0
3ANBFRSIRO1671100	Parcel #167 : Parcel closing	20	04-Oct-13	31-Oct-13	206	$0
3ANBFRSIRO1671110	Parcel #167 : Condemnation Process (if required)	225	04-Oct-13	21-Aug-14	1	$0
3ANBFRSIMSRO1671	Parcel #167 : Cleared for Construction	0		21-Aug-14	3	$0
Parcel #168 NBGP - S. of Trinity River to IH 30 (STA 903+00 to STA 903+00)		486	01-Aug-12	11-Jun-14	411	$0
3ANBGPSIMSRO1681	Parcel #168 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1681010	Parcel #168 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1681020	Parcel #168 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1681030	Parcel #168 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	419	$0

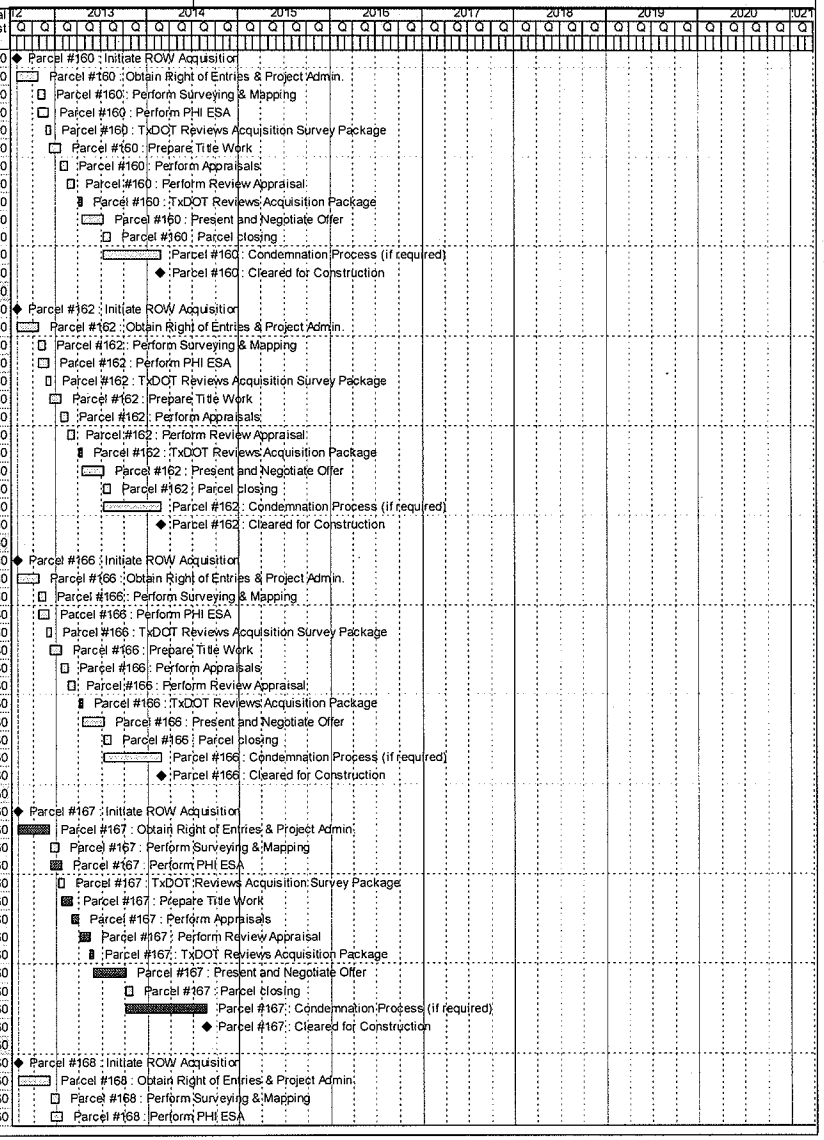

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBGPSIRO1681050	Parcel #168 : Prepare Title Work	30	22-Jan-13	04-Mar-13	419	$0
3ANBGPSIRO1681040	Parcel #168 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1681060	Parcel #168 : Perform Appraisals	20	05-Mar-13	01-Apr-13	419	$0
3ANBGPSIRO1681070	Parcel #168 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	419	$0
3ANBGPSIRO1681080	Parcel #168 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	393	$0
3ANBGPSIRO1681090	Parcel #168 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	401	$0
3ANBGPSIRO1681100	Parcel #168 : Parcel closing	20	15-Aug-13	12-Sep-13	591	$0
3ANBGPSIRO1681110	Parcel #168 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	401	$0
3ANBGPSIMSRO1681	Parcel #168 : Cleared for Construction	0		11-Jun-14	575	$0
Parcel #169 NBGP - S. of Trinity River to IH 30 (STA 900+00 to STA 900+00)		486	01-Aug-12	11-Jun-14	411	$0
3ANBGPSIMSRO1691	Parcel #169 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1691010	Parcel #169 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1691020	Parcel #169 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1691030	Parcel #169 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	419	$0
3ANBGPSIRO1691050	Parcel #169 : Prepare Title Work	30	22-Jan-13	04-Mar-13	419	$0
3ANBGPSIRO1691040	Parcel #169 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1691060	Parcel #169 : Perform Appraisals	20	05-Mar-13	01-Apr-13	419	$0
3ANBGPSIRO1691070	Parcel #169 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	419	$0
3ANBGPSIRO1691080	Parcel #169 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	393	$0
3ANBGPSIRO1691090	Parcel #169 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	401	$0
3ANBGPSIRO1691100	Parcel #169 : Parcel closing	20	15-Aug-13	12-Sep-13	591	$0
3ANBGPSIRO1691110	Parcel #169 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	401	$0
3ANBGPSIMSRO1691	Parcel #169 : Cleared for Construction	0		11-Jun-14	575	$0
Parcel #12 EAST (TxDOT #804) - COMPLEX - NBFR - Meacham to Dewey (STA 688+00 to STA)		537	01-Aug-12	21-Aug-14	20	$0
3ANBFRSIMSRO12E*	Parcel #12 EAST : Initiate ROW Acquisition	0	01-Aug-12		21	$0
3ANBFRSIRO12E1010	Parcel #12 EAST : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	15	$0
3ANBFRSIRO12E1020	Parcel #12 EAST : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	15	$0
3ANBFRSIRO12E1030	Parcel #12 EAST : Perform PHI ESA	30	07-Dec-12	21-Jan-13	19	$0
3ANBFRSIRO12E1040	Parcel #12 EAST : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ANBFRSIRO12E1050	Parcel #12 EAST : Prepare Title Work	30	22-Jan-13	04-Mar-13	19	$0
3ANBFRSIRO12E1060	Parcel #12 EAST : Perform Appraisals	20	05-Mar-13	01-Apr-13	19	$0
3ANBFRSIRO12E1070	Parcel #12 EAST : Perform Review Appraisal	30	02-Apr-13	13-May-13	19	$0
3ANBFRSIRO12E1080	Parcel #12 EAST : TxDOT Reviews Acquisition Package	10	14-May-13	28-May-13	19	$0
3ANBFRSIRO12E1090	Parcel #12 EAST : Present and Negotiate Offer	90	29-May-13	03-Oct-13	19	$0
3ANBFRSIRO12E1100	Parcel #12 EAST : Parcel closing	20	04-Oct-13	31-Oct-13	224	$0
3ANBFRSIRO12E1110	Parcel #12 EAST : Condemnation Process (if required)	225	04-Oct-13	21-Aug-14	19	$0
3ANBFRSIMSRO12E*	Parcel #12 EAST : Cleared for Construction	0		21-Aug-14	28	$0
Parcel #12 WEST (TxDOT #805) - COMPLEX - SBFR - Meacham to Dewey (STA 688+00 to STA)		537	01-Aug-12	21-Aug-14	4	$0
3ASBFRSIMSRO12W	Parcel #12 WEST : Initiate ROW Acquisition	0	01-Aug-12		6	$0
3ASBFRSIRO12W101	Parcel #12 WEST : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	4	$0
3ASBFRSIRO12W102	Parcel #12 WEST : Perform PHI ESA	30	07-Dec-12	21-Jan-13	4	$0
3ASBFRSIRO12W103	Parcel #12 WEST : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	14	$0
3ASBFRSIRO12W104	Parcel #12 WEST : TxDOT Reviews Acquisition Survey Package	15	11-Jan-13	01-Feb-13	11	$0
3ASBFRSIRO12W105	Parcel #12 WEST : Prepare Title Work	30	22-Jan-13	04-Mar-13	4	$0
3ASBFRSIRO12W106	Parcel #12 WEST : Perform Appraisals	20	05-Mar-13	01-Apr-13	4	$0
3ASBFRSIRO12W107	Parcel #12 WEST : Perform Review Appraisal	30	02-Apr-13	13-May-13	4	$0
3ASBFRSIRO12W108	Parcel #12 WEST : TxDOT Reviews Acquisition Package	10	14-May-13	28-May-13	4	$0
3ASBFRSIRO12W109	Parcel #12 WEST : Present and Negotiate Offer	90	29-May-13	03-Oct-13	4	$0
3ASBFRSIRO12W110	Parcel #12 WEST : Parcel closing	20	04-Oct-13	31-Oct-13	209	$0
3ASBFRSIRO12W111	Parcel #12 WEST : Condemnation Process (if required)	225	04-Oct-13	21-Aug-14	4	$0
3ASBFRSIMSRO12W	Parcel #12 WEST : Cleared for Construction	0		21-Aug-14	6	$0
Parcel #149 / 150 NBGP - S. of Trinity River to IH 30 (STA 934+00 to STA)		486	01-Aug-12	11-Jun-14	411	$0
3ANBGPSIMSRO1491	Parcel #149 / 150 : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ANBGPSIRO1491010	Parcel #149 / 150 : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ANBGPSIRO1491020	Parcel #149 / 150 : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ANBGPSIRO1491030	Parcel #149 / 150 : Perform PHI ESA	30	07-Dec-12	21-Jan-13	419	$0
3ANBGPSIRO1491050	Parcel #149 / 150 : Prepare Title Work	30	22-Jan-13	04-Mar-13	419	$0
3ANBGPSIRO1491040	Parcel #149 / 150 : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ANBGPSIRO1491060	Parcel #149 / 150 : Perform Appraisals	20	05-Mar-13	01-Apr-13	419	$0
3ANBGPSIRO1491070	Parcel #149 / 150 : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	419	$0

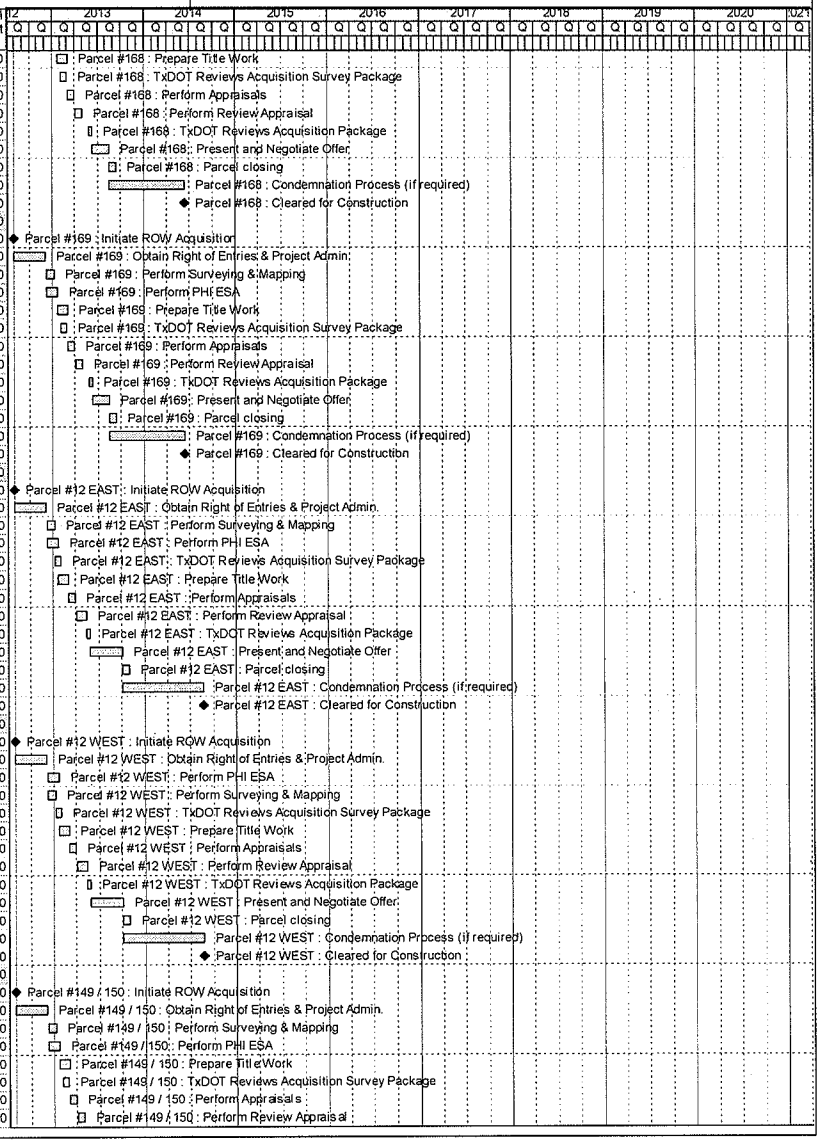

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ANBGPSIRO1491080	Parcel #149 / 150 : TxDOT Reviews Acquisition Package	10	29-May-13	11-Jun-13	393	$0
3ANBGPSIRO1491090	Parcel #149 / 150 : Present and Negotiate Offer	45	12-Jun-13	14-Aug-13	401	$0
3ANBGPSIRO1491100	Parcel #149 / 150 : Parcel closing	20	15-Aug-13	12-Sep-13	591	$0
3ANBGPSIRO1491110	Parcel #149 / 150 : Condemnation Process (if required)	210	15-Aug-13	11-Jun-14	401	$0
3ANBGPSIMSRO1491	Parcel #149 / 150 : Cleared for Construction	0		11-Jun-14	575	$0
Parcel #93A SBFR - Dewey to S. of Trinity River (STA 848+00 to STA)		465	01-Aug-12	13-May-14	135	$0
3ASBFRDTMSRO93A	Parcel #93A : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBFRDTRO93A10	Parcel #93A : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ASBFRDTRO93A10	Parcel #93A : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBFRDTRO93A10	Parcel #93A : Perform PHI ESA	30	07-Dec-12	21-Jan-13	132	$0
3ASBFRDTRO93A10	Parcel #93A : Prepare Title Work	30	22-Jan-13	04-Mar-13	132	$0
3ASBFRDTRO93A10	Parcel #93A : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBFRDTRO93A10	Parcel #93A : Perform Appraisals	20	05-Mar-13	01-Apr-13	132	$0
3ASBFRDTRO93A10	Parcel #93A : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	132	$0
3ASBFRDTRO93A10	Parcel #93A : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	132	$0
3ASBFRDTRO93A10	Parcel #93A : Present and Negotiate Offer	45	14-May-13	17-Jul-13	132	$0
3ASBFRDTRO93A11	Parcel #93A : Parcel closing	20	18-Jul-13	14-Aug-13	322	$0
3ASBFRDTRO93A111	Parcel #93A : Condemnation Process (if required)	210	18-Jul-13	13-May-14	132	$0
3ASBFRDTMSRO93A	Parcel #93A : Cleared for Construction	0		13-May-14	189	$0
Parcel #93B SBFR - Dewey to S. of Trinity River (STA 848+00 to STA)		465	01-Aug-12	13-May-14	135	$0
3ASBFRDTMSRO93B	Parcel #93B : Initiate ROW Acquisition	0	01-Aug-12		44	$0
3ASBFRDTRO93B10	Parcel #93B : Obtain Right of Entries & Project Admin.	90	01-Aug-12	06-Dec-12	31	$0
3ASBFRDTRO93B10	Parcel #93B : Perform Surveying & Mapping	20	07-Dec-12	07-Jan-13	31	$0
3ASBFRDTRO93B10	Parcel #93B : Perform PHI ESA	30	07-Dec-12	21-Jan-13	132	$0
3ASBFRDTRO93B10	Parcel #93B : Prepare Title Work	30	22-Jan-13	04-Mar-13	132	$0
3ASBFRDTRO93B10	Parcel #93B : TxDOT Reviews Acquisition Survey Package	15	04-Feb-13	25-Feb-13	11	$0
3ASBFRDTRO93B10	Parcel #93B : Perform Appraisals	20	05-Mar-13	01-Apr-13	132	$0
3ASBFRDTRO93B10	Parcel #93B : Perform Review Appraisal	20	02-Apr-13	29-Apr-13	132	$0
3ASBFRDTRO93B10	Parcel #93B : TxDOT Reviews Acquisition Package	10	30-Apr-13	13-May-13	132	$0
3ASBFRDTRO93B10	Parcel #93B : Present and Negotiate Offer	45	14-May-13	17-Jul-13	132	$0
3ASBFRDTRO93B11	Parcel #93B : Parcel closing	20	18-Jul-13	14-Aug-13	322	$0
3ASBFRDTRO93B111	Parcel #93B : Condemnation Process (if required)	210	18-Jul-13	13-May-14	132	$0
3ASBFRDTMSRO93B	Parcel #93B : Cleared for Construction	0		13-May-14	189	$0
Utility Adjustments		362	01-Oct-12	18-Feb-14	858	$20,469,314
Utility Coordination		215	01-Oct-12	26-Jul-13	514	$0
MSUT 1000	Start of Utility Coordination Process	0	01-Oct-12		178	$0
MSUT 1010	TxDOT Review of Utility Submission - Calendar Week 1	0	05-Nov-12		178	$0
MSUT 1020	TxDOT Review of Utility Submission - Calendar Week 2	0	12-Nov-12		178	$0
MSUT 1030	TxDOT Review of Utility Submission - Calendar Week 3	0	19-Nov-12		178	$0
MSUT 1040	TxDOT Review of Utility Submission - Calendar Week 4	0	26-Nov-12		178	$0
MSUT 1050	TxDOT Review of Utility Submission - Calendar Week 5	0	03-Dec-12		178	$0
MSUT 1060	TxDOT Review of Utility Submission - Calendar Week 6	0	10-Dec-12		178	$0
MSUT 1070	TxDOT Review of Utility Submission - Calendar Week 7	0	17-Dec-12		178	$0
MSUT 1080	TxDOT Review of Utility Submission - Calendar Week 8	0	24-Dec-12		178	$0
MSUT 1090	TxDOT Review of Utility Submission - Calendar Week 9	0	31-Dec-12		178	$0
MSUT 1100	TxDOT Review of Utility Submission - Calendar Week 10	0	07-Jan-13		178	$0
MSUT 1110	TxDOT Review of Utility Submission - Calendar Week 11	0	14-Jan-13		178	$0
MSUT 1120	TxDOT Review of Utility Submission - Calendar Week 12	0	21-Jan-13		178	$0
MSUT 1130	TxDOT Review of Utility Submission - Calendar Week 13	0	28-Jan-13		178	$0
MSUT 1140	TxDOT Review of Utility Submission - Calendar Week 14	0	04-Feb-13		178	$0
MSUT 1150	TxDOT Review of Utility Submission - Calendar Week 15	0	11-Feb-13		178	$0
MSUT 1160	TxDOT Review of Utility Submission - Calendar Week 16	0	18-Feb-13		178	$0
MSUT 1170	TxDOT Review of Utility Submission - Calendar Week 17	0	25-Feb-13		178	$0
MSUT 1180	TxDOT Review of Utility Submission - Calendar Week 18	0	04-Mar-13		178	$0
MSUT 1190	TxDOT Review of Utility Submission - Calendar Week 19	0	11-Mar-13		178	$0
MSUT 1200	TxDOT Review of Utility Submission - Calendar Week 20	0	18-Mar-13		178	$0
MSUT 1210	TxDOT Review of Utility Submission - Calendar Week 21	0	25-Mar-13		178	$0
MSUT 1220	TxDOT Review of Utility Submission - Calendar Week 22	0	01-Apr-13		178	$0
MSUT 1230	TxDOT Review of Utility Submission - Calendar Week 23	0	08-Apr-13		178	$0
MSUT 1240	TxDOT Review of Utility Submission - Calendar Week 24	0	15-Apr-13		178	$0

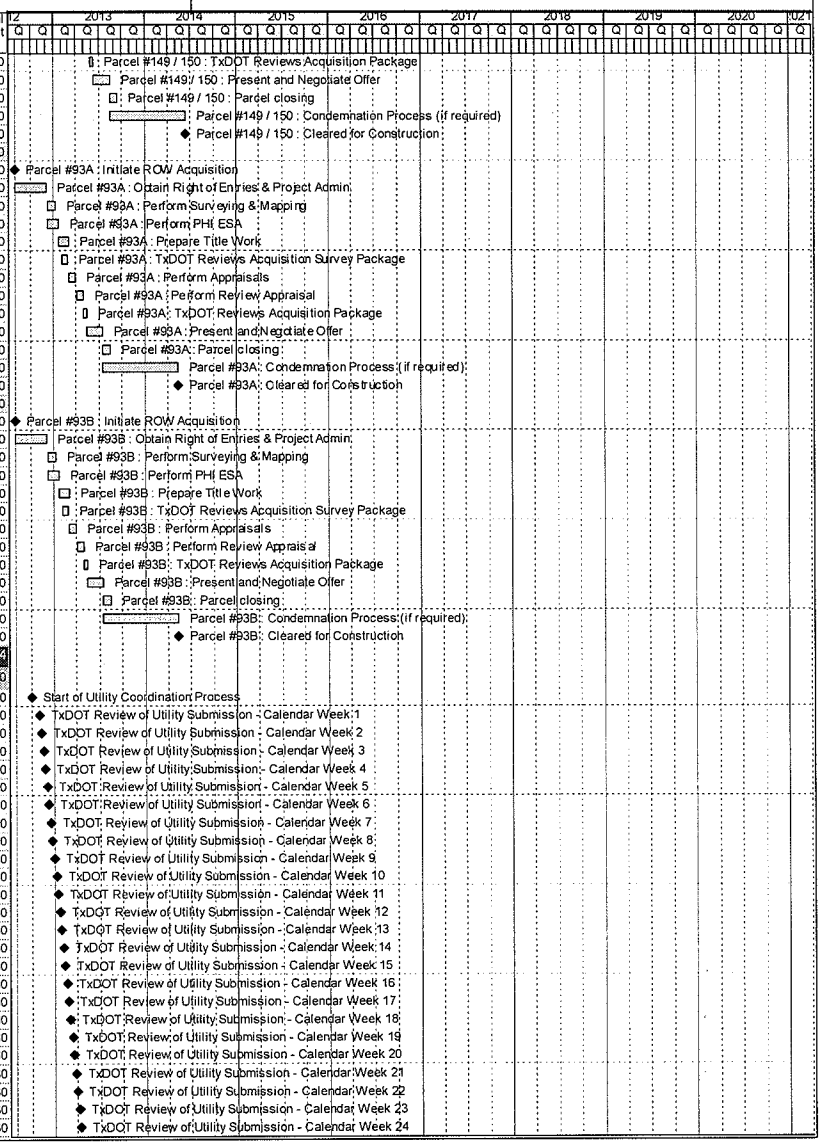

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
MSUT1250	TxDOT Review of Utility Submission - Calendar Week 25	0	22-Apr-13		375	$0
MSUT1260	TxDOT Review of Utility Submission - Calendar Week 26	0	29-Apr-13		381	$0
MSUT1270	TxDOT Review of Utility Submission - Calendar Week 27	0	06-May-13		455	$0
MSUT1280	TxDOT Review of Utility Submission - Calendar Week 28	0	13-May-13		721	$0
AT&T		194	01-Oct-12	27-Jun-13	266	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	266	$0
3AAT&TMSUT1005	Start of Utility Assembly Package Relocation Process - AT&T	0	01-Oct-12		422	$0
3AAT&TMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - AT&T	0		27-Jun-13	374	$0
MUAA Process		155	01-Oct-12	03-May-13	265	$0
3AAT&TMSUT1020	Start of MUAA Process - AT&T	0	01-Oct-12		422	$0
3AAT&TDSUT1030	Develop MUAA - AT&T	20	01-Oct-12	26-Oct-12	295	$0
3AAT&TDSUT1040	Prepare & Deliver MUAA - AT&T	5	29-Oct-12	02-Nov-12	295	$0
3AAT&TDSUT1050	MUAA Interim Comments by TxDOT (round 1) - AT&T	10	05-Nov-12	16-Nov-12	291	$0
3AAT&TDSUT1060	MUAA Comments by Owner (round 1) - AT&T	15	05-Nov-12	26-Nov-12	295	$0
3AAT&TDSUT1070	Address Comments from Owner & TxDOT (round 1) - AT&T	10	27-Nov-12	10-Dec-12	295	$0
3AAT&TDSUT1080	MUAA Comments by Owner (round 2) - AT&T	15	11-Dec-12	02-Jan-13	296	$0
3AAT&TDSUT1090	MUAA Interim Comments by TxDOT (round 2) - AT&T	15	17-Dec-12	10-Jan-13	283	$0
3AAT&TDSUT1100	Address Comments from Owner & TxDOT (round 2) - AT&T	10	11-Jan-13	24-Jan-13	290	$0
3AAT&TDSUT1110	MUAA Comments by Owner (round 3) - AT&T	15	25-Jan-13	14-Feb-13	290	$0
3AAT&TDSUT1120	MUAA Interim Comments by TxDOT (round 3) - AT&T	10	19-Feb-13	04-Mar-13	273	$0
3AAT&TDSUT1130	Address Comments from Owner & TxDOT (round 3) - AT&T	10	05-Mar-13	18-Mar-13	278	$0
3AAT&TDSUT1140	Final Submittal to TxDOT - AT&T	15	15-Apr-13	03-May-13	259	$0
3AAT&TMSUT1150	MUAA Process Complete and Ready for Assembly Package - AT&T	0		03-May-13	373	$0
3AAT&TMSUT1160	TxDOT Final Approval - AT&T	0		03-May-13	254	$0
Utility Design		122	01-Oct-12	19-Mar-13	298	$0
3AAT&TMSUT1170	Start of Utility Design Process - AT&T	0	01-Oct-12		470	$0
3AAT&TDSUT1180	Utility Design Kick-Off Meeting - AT&T	2	01-Oct-12	02-Oct-12	327	$0
3AAT&TDSUT1190	Utility Design - 60% - AT&T	30	03-Oct-12	13-Nov-12	327	$0
3AAT&TDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - AT&T	20	14-Nov-12	12-Dec-12	327	$0
3AAT&TDSUT1200	Utility Design - 90% - AT&T	20	10-Dec-12	08-Jan-13	310	$0
3AAT&TDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - AT&T	10	10-Dec-12	21-Dec-12	310	$0
3AAT&TDSUT1230	Utility Design Final Comments Incorporated - AT&T	5	09-Jan-13	15-Jan-13	310	$0
3AAT&TDSUT1240	TxDOT and OTS Review of Final Plans - AT&T	10	11-Feb-13	22-Feb-13	292	$0
3AAT&TDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - AT&T	10	25-Feb-13	08-Mar-13	292	$0
3AAT&TDSUT1260	Final Plans to be Incorporated in the Assembly Package - AT&T	7	11-Mar-13	19-Mar-13	292	$0
3AAT&TMSUT1270	Final Utility Design Ready for Assembly Package - AT&T	0		19-Mar-13	418	$0
Signature Process		38	06-May-13	27-Jun-13	259	$0
3AAT&TDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - AT&T	10	06-May-13	17-May-13	259	$0
3AAT&TDSUT1290	Owner Review & Signature - AT&T	10	20-May-13	03-Jun-13	259	$0
3AAT&TDSUT1300	Contractor Review & Signature - AT&T	3	04-Jun-13	06-Jun-13	259	$0
3AAT&TDSUT1310	Developer Review & Signature - AT&T	5	07-Jun-13	13-Jun-13	259	$0
3AAT&TDSUT1320	TxDOT Review & Approval - AT&T	10	14-Jun-13	27-Jun-13	259	$0
Procurement		28	06-May-13	12-Jun-13	277	$0
3AAT&TDSUT1330	R.F.P. Preparation - AT&T	5	06-May-13	10-May-13	270	$0
3AAT&TDSUT1340	R.F.P. Solicitation - AT&T	15	13-May-13	03-Jun-13	270	$0
3AAT&TDSUT1350	Review and Selection of Contractor (s) - AT&T	5	04-Jun-13	10-Jun-13	270	$0
3AAT&TDSUT1360	Executed Agreement with Contractor(s) - AT&T	2	11-Jun-13	12-Jun-13	270	$0
3AAT&TMSUT1370	Issuance of NTP to Contractor(s) - AT&T	0		12-Jun-13	389	$0
Atmos		200	01-Oct-12	05-Jul-13	269	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	269	$0
3AATMOMSUT1320	Start of Utility Assembly Package Relocation Process - ATMOS	0	01-Oct-12		436	$0
3AATMOMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - ATMOS	0		05-Jul-13	377	$0
MUAA Process		160	01-Oct-12	10-May-13	269	$0
3AATMOMSUT1020	Start of MUAA Process - ATMOS	0	01-Oct-12		436	$0
3AATMODSUT1030	Develop MUAA - ATMOS	20	01-Oct-12	26-Oct-12	305	$0
3AATMODSUT1040	Prepare & Deliver MUAA - ATMOS	5	29-Oct-12	02-Nov-12	305	$0
3AATMODSUT1060	MUAA Comments by Owner (round 1) - ATMOS	15	05-Nov-12	26-Nov-12	305	$0
3AATMODSUT1050	MUAA Interim Comments by TxDOT (round 1) - ATMOS	10	12-Nov-12	27-Nov-12	296	$0
3AATMODSUT1070	Address Comments from Owner & TxDOT (round 1) - ATMOS	10	28-Nov-12	11-Dec-12	304	$0
3AATMODSUT1080	MUAA Comments by Owner (round 2) - ATMOS	15	12-Dec-12	03-Jan-13	304	$0

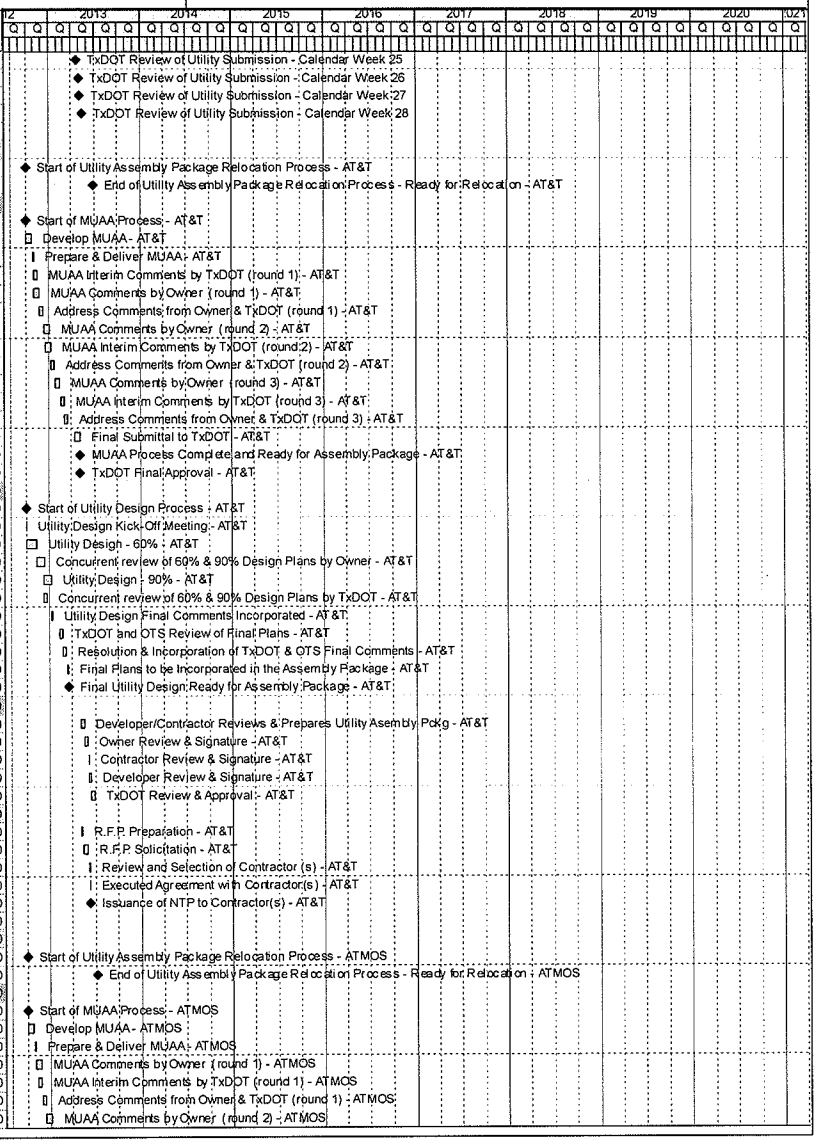

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AATMODSUT1090	MUAA Interim Comments by TxDOT (round 2) - ATMOS	15	27-Dec-12	17-Jan-13	287	$0
3AATMODSUT1100	Address Comments from Owner & TxDOT (round 2) - ATMOS	10	18-Jan-13	31-Jan-13	294	$0
3AATMODSUT1110	MUAA Comments by Owner (round 3) - ATMOS	15	01-Feb-13	21-Feb-13	294	$0
3AATMODSUT1120	MUAA Interim Comments by TxDOT (round 3) - ATMOS	10	19-Feb-13	04-Mar-13	282	$0
3AATMODSUT1130	Address Comments from Owner & TxDOT (round 3) - ATMOS	10	05-Mar-13	18-Mar-13	287	$0
3AATMODSUT1140	Final Submittal to TxDOT - ATMOS	15	22-Apr-13	10-May-13	263	$0
3AATMOMSUT1150	MUAA Process Complete and Ready for Assembly Package - ATMOS	0		10-May-13	377	$0
3AATMOMSUT1160	TxDOT Final Approval - ATMOS	0		10-May-13	258	$0
Utility Design		122	01-Oct-12	19-Mar-13	307	$0
3AATMOMSUT1170	Start of Utility Design Process - ATMOS	0	01-Oct-12		483	$0
3AATMODSUT1180	Utility Design Kick-Off Meeting - ATMOS	2	01-Oct-12	02-Oct-12	336	$0
3AATMODSUT1190	Utility Design - 60% - ATMOS	30	03-Oct-12	13-Nov-12	336	$0
3AATMODSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - ATMOS	20	14-Nov-12	12-Dec-12	336	$0
3AATMODSUT1200	Utility Design - 90% - ATMOS	20	10-Dec-12	08-Jan-13	319	$0
3AATMODSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - ATMOS	10	10-Dec-12	21-Dec-12	319	$0
3AATMODSUT1230	Utility Design Final Comments Incorporated - ATMOS	5	09-Jan-13	15-Jan-13	319	$0
3AATMODSUT1240	TxDOT and OTS Review of Final Plans - ATMOS	10	11-Feb-13	22-Feb-13	301	$0
3AATMODSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - ATMOS	10	25-Feb-13	08-Mar-13	301	$0
3AATMODSUT1260	Final Plans to be Incorporated in the Assembly Package - ATMOS	7	11-Mar-13	19-Mar-13	301	$0
3AATMOMSUT1270	Final Utility Design Ready for Assembly Package - ATMOS	0		19-Mar-13	429	$0
Signature Process		36	13-May-13	05-Jul-13	263	$0
3AATMODSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - ATMOS	10	13-May-13	24-May-13	263	$0
3AATMODSUT1290	Owner Review & Signature - ATMOS	10	28-May-13	10-Jun-13	263	$0
3AATMODSUT1300	Contractor Review & Signature - ATMOS	3	11-Jun-13	13-Jun-13	263	$0
3AATMODSUT1310	Developer Review & Signature - ATMOS	5	14-Jun-13	20-Jun-13	263	$0
3AATMODSUT1320	TxDOT Review & Approval - ATMOS	10	21-Jun-13	05-Jul-13	263	$0
Procurement		28	13-May-13	19-Jun-13	281	$0
3AATMODSUT1330	R.F.P. Preparation - ATMOS	5	13-May-13	17-May-13	274	$0
3AATMODSUT1340	R.F.P. Solicitation - ATMOS	15	20-May-13	10-Jun-13	274	$0
3AATMODSUT1350	Review and Selection of Contractor (s) - ATMOS	5	11-Jun-13	17-Jun-13	274	$0
3AATMODSUT1360	Executed Agreement with Contractor(s) - ATMOS	2	18-Jun-13	19-Jun-13	274	$0
3AATMOMSUT1370	Issuance of NTP to Contractor(s) - ATMOS	0		19-Jun-13	393	$0
Barnett Gathering		210	01-Oct-12	19-Jul-13	331	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	331	$0
ICBARNMSUT1000	Start of Utility Assembly Package Relocation Process - Barnett Gathering	0	01-Oct-12		539	$0
ICBARNMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Barnett Gathering	0		19-Jul-13	465	$0
MUAA Process		170	01-Oct-12	24-May-13	333	$0
ICBARNMSUT1020	Start of MUAA Process - Barnett Gathering	0	01-Oct-12		539	$0
ICBARNDSUT1030	Develop MUAA - Barnett Gathering	20	01-Oct-12	26-Oct-12	376	$0
ICBARNDSUT1040	Prepare & Deliver MUAA - Barnett Gathering	5	29-Oct-12	02-Nov-12	376	$0
ICBARNDSUT1060	MUAA Comments by Owner (round 1) - Barnett Gathering	15	05-Nov-12	26-Nov-12	376	$0
ICBARNDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Barnett Gathering	10	26-Nov-12	07-Dec-12	358	$0
ICBARNDSUT1070	Address Comments from Owner & TxDOT (round 1) - Barnett Gathering	10	10-Dec-12	21-Dec-12	367	$0
ICBARNDSUT1080	MUAA Comments by Owner (round 2) - Barnett Gathering	15	24-Dec-12	15-Jan-13	367	$0
ICBARNDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Barnett Gathering	15	22-Jan-13	11-Feb-13	342	$0
ICBARNDSUT1100	Address Comments from Owner & TxDOT (round 2) - Barnett Gathering	10	12-Feb-13	25-Feb-13	348	$0
ICBARNDSUT1110	MUAA Comments by Owner (round 3) - Barnett Gathering	15	26-Feb-13	18-Mar-13	348	$0
ICBARNDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Barnett Gathering	10	25-Mar-13	05-Apr-13	329	$0
ICBARNDSUT1130	Address Comments from Owner & TxDOT (round 3) - Barnett Gathering	10	08-Apr-13	19-Apr-13	334	$0
ICBARNDSUT1140	Final Submittal to TxDOT - Barnett Gathering	15	06-May-13	24-May-13	324	$0
ICBARNMSUT1150	MUAA Process Complete and Ready for Assembly Package - Barnett Gathering	0		24-May-13	467	$0
ICBARNMSUT1160	TxDOT Final Approval - Barnett Gathering	0		24-May-13	319	$0
Utility Design		142	01-Oct-12	16-Apr-13	361	$0
ICBARNMSUT1170	Start of Utility Design Process - Barnett Gathering	0	01-Oct-12		582	$0
ICBARNDSUT1180	Utility Design Kick-Off Meeting - Barnett Gathering	2	01-Oct-12	02-Oct-12	407	$0
ICBARNDSUT1190	Utility Design - 60% - Barnett Gathering	30	03-Oct-12	13-Nov-12	407	$0
ICBARNDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Barnett Gathering	20	14-Nov-12	12-Dec-12	407	$0
ICBARNDSUT1200	Utility Design - 90% - Barnett Gathering	20	14-Jan-13	08-Feb-13	367	$0
ICBARNDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Barnett Gathering	10	14-Jan-13	25-Jan-13	367	$0
ICBARNDSUT1230	Utility Design Final Comments Incorporated - Barnett Gathering	5	11-Feb-13	15-Feb-13	367	$0

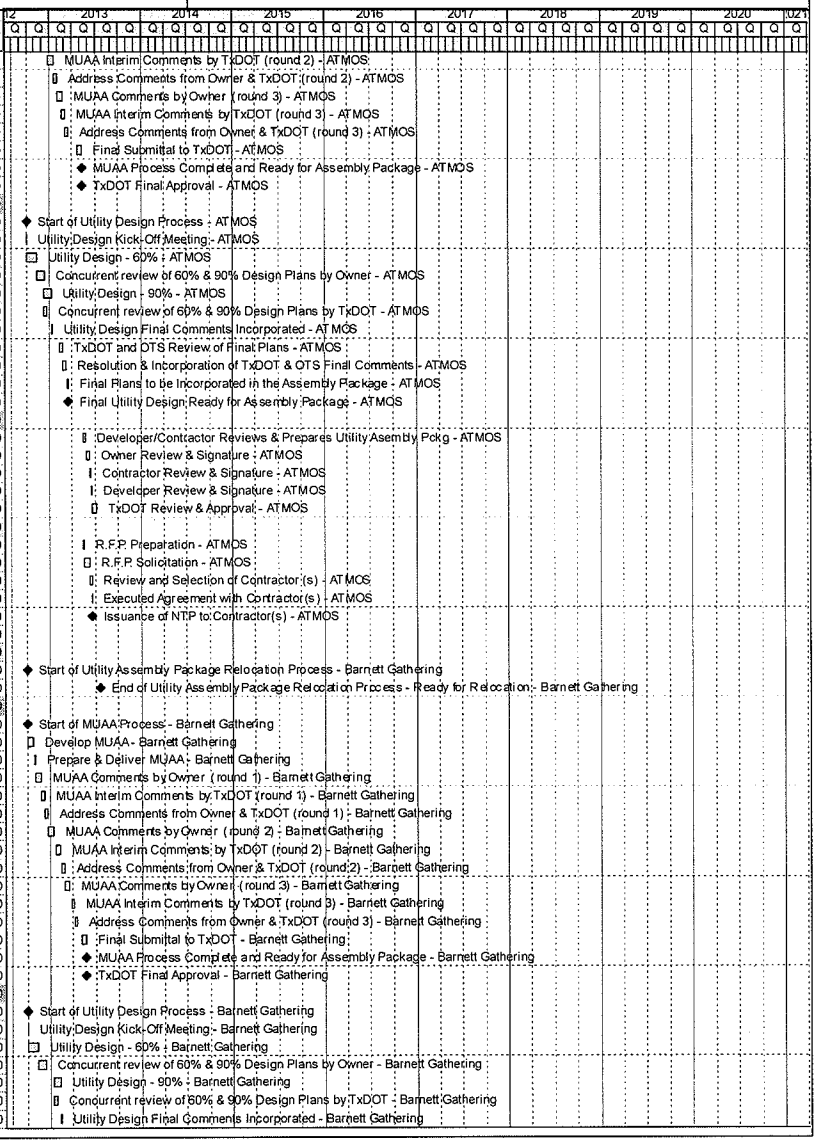

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
ICBARNDSUT1240	TxDOT and OTS Review of Final Plans - Barnett Gathering	10	11-Mar-13	22-Mar-13	352	$0
ICBARNDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Barnett Gathering	10	25-Mar-13	05-Apr-13	352	$0
ICBARNDSUT1260	Final Plans to be Incorporated in the Assembly Package - Barnett Gathering	7	08-Apr-13	16-Apr-13	352	$0
ICBARNMSUT1270	Final Utility Design Ready for Assembly Package - Barnett Gathering	0		16-Apr-13	505	$0
Signature Process		38	28-May-13	19-Jul-13	324	$0
ICBARNDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Barnett Gathering	10	28-May-13	10-Jun-13	324	$0
ICBARNDSUT1290	Owner Review & Signature - Barnett Gathering	10	11-Jun-13	24-Jun-13	324	$0
ICBARNDSUT1300	Contractor Review & Signature - Barnett Gathering	3	25-Jun-13	27-Jun-13	324	$0
ICBARNDSUT1310	Developer Review & Signature - Barnett Gathering	5	28-Jun-13	05-Jul-13	324	$0
ICBARNDSUT1320	TxDOT Review & Approval - Barnett Gathering	10	08-Jul-13	19-Jul-13	324	$0
Procurement		27	28-May-13	03-Jul-13	343	$0
ICBARNDSUT1330	R.F.P. Preparation - Barnett Gathering	5	28-May-13	03-Jun-13	335	$0
ICBARNDSUT1340	R.F.P. Solicitation - Barnett Gathering	15	04-Jun-13	24-Jun-13	335	$0
ICBARNDSUT1350	Review and Selection of Contractor (s) - Barnett Gathering	5	25-Jun-13	01-Jul-13	335	$0
ICBARNDSUT1360	Executed Agreement with Contractor(s) - Barnett Gathering	2	02-Jul-13	03-Jul-13	335	$0
ICBARNMSUT1370	Issuance of NTP to Contractor(s) - Barnett Gathering	0		03-Jul-13	481	$0
Broadwing / Level 3		200	01-Oct-12	05-Jul-13	277	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	277	$0
3ALVL3MSUT1000	Start of Utility Assembly Package Relocation Process - Broadwing / Level 23	0	01-Oct-12		448	$0
3ALVL3MSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Broadwing / Level 9	0		05-Jul-13	389	$0
MUAA Process		160	01-Oct-12	10-May-13	278	$0
3ALVL3MSUT1020	Start of MUAA Process - Broadwing / Level 22	0	01-Oct-12		448	$0
3ALVL3DSUT1030	Develop MUAA - Broadwing / Level 6	20	01-Oct-12	26-Oct-12	313	$0
3ALVL3DSUT1040	Prepare & Deliver MUAA - Broadwing / Level 17	5	29-Oct-12	02-Nov-12	313	$0
3ALVL3DSUT1060	MUAA Comments by Owner (round 1) - Broadwing / Level 6	15	05-Nov-12	26-Nov-12	313	$0
3ALVL3DSUT1050	MUAA Interim Comments by TxDOT (round 1) - Broadwing / Level 9	10	12-Nov-12	27-Nov-12	303	$0
3ALVL3DSUT1070	Address Comments from Owner & TxDOT (round 1) - Broadwing / Level 3	10	28-Nov-12	11-Dec-12	312	$0
3ALVL3DSUT1080	MUAA Comments by Owner (round 2) - Broadwing / Level 7	15	12-Dec-12	03-Jan-13	312	$0
3ALVL3DSUT1090	MUAA Interim Comments by TxDOT (round 2) - Broadwing / Level 11	15	27-Dec-12	17-Jan-13	295	$0
3ALVL3DSUT1100	Address Comments from Owner & TxDOT (round 2) - Broadwing / Level 4	10	18-Jan-13	31-Jan-13	302	$0
3ALVL3DSUT1110	MUAA Comments by Owner (round 3) - Broadwing / Level 8	15	01-Feb-13	21-Feb-13	302	$0
3ALVL3DSUT1120	MUAA Interim Comments by TxDOT (round 3) - Broadwing / Level 10	10	04-Mar-13	15-Mar-13	281	$0
3ALVL3DSUT1130	Address Comments from Owner & TxDOT (round 3) - Broadwing / Level 5	10	18-Mar-13	29-Mar-13	286	$0
3ALVL3DSUT1140	Final Submittal to TxDOT - Broadwing / Level 12	15	22-Apr-13	10-May-13	271	$0
3ALVL3MSUT1150	MUAA Process Complete and Ready for Assembly Package - Broadwing / Level 15	0		10-May-13	390	$0
3ALVL3MSUT1160	TxDOT Final Approval - Broadwing / Level 26	0		10-May-13	266	$0
Utility Design		137	01-Oct-12	09-Apr-13	301	$0
3ALVL3MSUT1170	Start of Utility Design Process - Broadwing / Level 24	0	01-Oct-12		493	$0
3ALVL3DSUT1180	Utility Design Kick-Off Meeting - Broadwing / Level 31	2	01-Oct-12	02-Oct-12	344	$0
3ALVL3DSUT1190	Utility Design - 60% - Broadwing / Level 28	30	03-Oct-12	13-Nov-12	344	$0
3ALVL3DSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Broadwing / Level 3	20	14-Nov-12	12-Dec-12	344	$0
3ALVL3DSUT1200	Utility Design - 90% - Broadwing / Level 29	20	31-Dec-12	28-Jan-13	313	$0
3ALVL3DSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Broadwing / Level 4	10	31-Dec-12	14-Jan-13	313	$0
3ALVL3DSUT1230	Utility Design Final Comments Incorporated - Broadwing / Level 30	5	29-Jan-13	04-Feb-13	313	$0
3ALVL3DSUT1240	TxDOT and OTS Review of Final Plans - Broadwing / Level 25	10	04-Mar-13	15-Mar-13	294	$0
3ALVL3DSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Broadwing / Level 20	10	18-Mar-13	29-Mar-13	294	$0
3ALVL3DSUT1260	Final Plans to be Incorporated in the Assembly Package - Broadwing / Level 11	7	01-Apr-13	09-Apr-13	294	$0
3ALVL3MSUT1270	Final Utility Design Ready for Assembly Package - Broadwing / Level 13	0		09-Apr-13	421	$0
Signature Process		38	13-May-13	05-Jul-13	271	$0
3ALVL3DSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Broadwing / Level 8	10	13-May-13	24-May-13	271	$0
3ALVL3DSUT1290	Owner Review & Signature - Broadwing / Level 16	10	28-May-13	10-Jun-13	271	$0
3ALVL3DSUT1300	Contractor Review & Signature - Broadwing / Level 5	3	11-Jun-13	13-Jun-13	271	$0
3ALVL3DSUT1310	Developer Review & Signature - Broadwing / Level 7	5	14-Jun-13	20-Jun-13	271	$0
3ALVL3DSUT1320	TxDOT Review & Approval - Broadwing / Level 27	10	21-Jun-13	05-Jul-13	271	$0
Procurement		28	13-May-13	19-Jun-13	289	$0
3ALVL3DSUT1330	R.F.P. Preparation - Broadwing / Level 18	5	13-May-13	17-May-13	282	$0
3ALVL3DSUT1340	R.F.P. Solicitation - Broadwing / Level 19	15	20-May-13	10-Jun-13	282	$0
3ALVL3DSUT1350	Review and Selection of Contractor (s) - Broadwing / Level 21	5	11-Jun-13	17-Jun-13	282	$0
3ALVL3DSUT1360	Executed Agreement with Contractor(s) - Broadwing / Level 10	2	18-Jun-13	19-Jun-13	282	$0
3ALVL3MSUT1370	Issuance of NTP to Contractor(s) - Broadwing / Level 14	0		19-Jun-13	405	$0

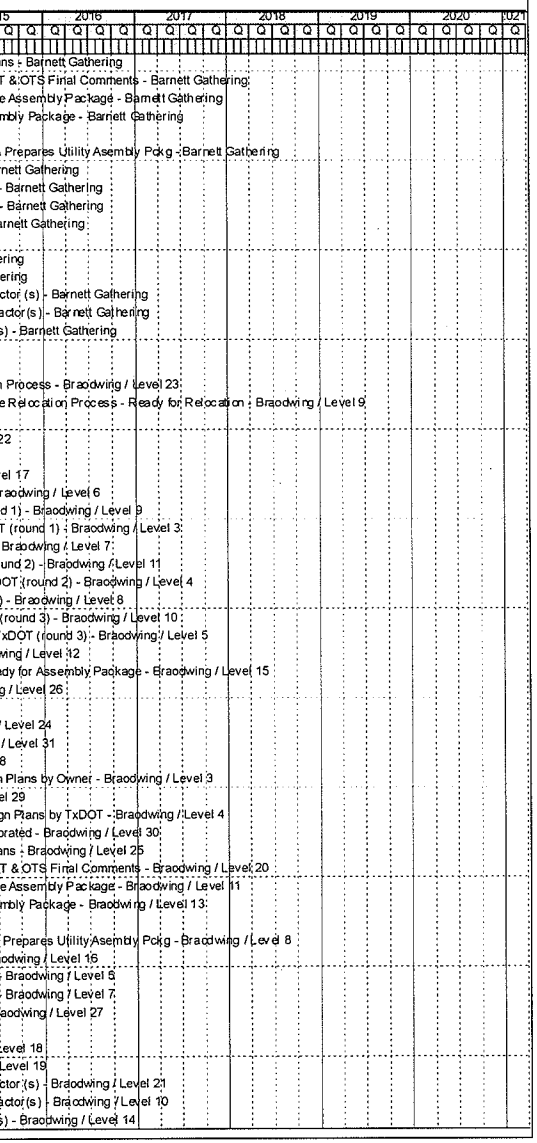

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Charter Communication		200	01-Oct-12	05-Jul-13	270	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	270	$0
3ACHARMSUT1000	Start of Utility Assembly Package Relocation Process - Charter Communication	0	01-Oct-12		437	$0
3ACHARMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Charter Communi	0		05-Jul-13	380	$0
MUAA Process		160	01-Oct-12	10-May-13	271	$0
3ACHARMSUT1020	Start of MUAA Process - Charter Communication	0	01-Oct-12		437	$0
3ACHARDSUT1030	Develop MUAA - Charter Communication	20	01-Oct-12	26-Oct-12	306	$0
3ACHARDSUT1040	Prepare & Deliver MUAA - Charter Communication	5	29-Oct-12	02-Nov-12	306	$0
3ACHARDSUT1060	MUAA Comments by Owner (round 1) - Charter Communication	15	05-Nov-12	26-Nov-12	306	$0
3ACHARDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Charter Communication	10	12-Nov-12	27-Nov-12	297	$0
3ACHARDSUT1070	Address Comments from Owner & TxDOT (round 1) - Charter Communication	10	28-Nov-12	11-Dec-12	305	$0
3ACHARDSUT1080	MUAA Comments by Owner (round 2) - Charter Communication	15	12-Dec-12	03-Jan-13	305	$0
3ACHARDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Charter Communication	15	27-Dec-12	17-Jan-13	288	$0
3ACHARDSUT1100	Address Comments from Owner & TxDOT (round 2) - Charter Communication	10	18-Jan-13	31-Jan-13	295	$0
3ACHARDSUT1110	MUAA Comments by Owner (round 3) - Charter Communication	15	01-Feb-13	21-Feb-13	295	$0
3ACHARDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Charter Communication	10	25-Feb-13	08-Mar-13	279	$0
3ACHARDSUT1130	Address Comments from Owner & TxDOT (round 3) - Charter Communication	10	11-Mar-13	22-Mar-13	284	$0
3ACHARDSUT1140	Final Submittal to TxDOT - Charter Communication	15	22-Apr-13	10-May-13	264	$0
3ACHARMSUT1150	MUAA Process Complete and Ready for Assembly Package - Charter Communication	0		10-May-13	381	$0
3ACHARMSUT1160	TxDOT Final Approval - Charter Communication	0		10-May-13	259	$0
Utility Design		122	01-Oct-12	19-Mar-13	309	$0
3ACHARMSUT1170	Start of Utility Design Process - Charter Communication	0	01-Oct-12		484	$0
3ACHARDSUT1180	Utility Design Kick-Off Meeting - Charter Communication	2	01-Oct-12	02-Oct-12	337	$0
3ACHARDSUT1190	Utility Design - 60% - Charter Communication	30	03-Oct-12	13-Nov-12	337	$0
3ACHARDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Charter Communication	20	14-Nov-12	12-Dec-12	337	$0
3ACHARDSUT1200	Utility Design - 90% - Charter Communication	20	10-Dec-12	08-Jan-13	320	$0
3ACHARDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Charter Communication	10	10-Dec-12	21-Dec-12	320	$0
3ACHARDSUT1230	Utility Design Final Comments Incorporated - Charter Communication	5	09-Jan-13	15-Jan-13	320	$0
3ACHARDSUT1240	TxDOT and OTS Review of Final Plans - Charter Communication	10	11-Feb-13	22-Feb-13	302	$0
3ACHARDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Charter Communication	10	25-Feb-13	08-Mar-13	302	$0
3ACHARDSUT1260	Final Plans to be Incorporated in the Assembly Package - Charter Communication	7	11-Mar-13	19-Mar-13	302	$0
3ACHARMSUT1270	Final Utility Design Ready for Assembly Package - Charter Communication	0		19-Mar-13	433	$0
Signature Process		38	13-May-13	05-Jul-13	264	$0
3ACHARDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Charter Communication	10	13-May-13	24-May-13	264	$0
3ACHARDSUT1290	Owner Review & Signature - Charter Communication	10	28-May-13	10-Jun-13	264	$0
3ACHARDSUT1300	Contractor Review & Signature - Charter Communication	3	11-Jun-13	13-Jun-13	264	$0
3ACHARDSUT1310	Developer Review & Signature - Charter Communication	5	14-Jun-13	20-Jun-13	264	$0
3ACHARDSUT1320	TxDOT Review & Approval - Charter Communication	10	21-Jun-13	05-Jul-13	264	$0
Procurement		28	13-May-13	19-Jun-13	282	$0
3ACHARDSUT1330	R.F.P. Preparation - Charter Communication	5	13-May-13	17-May-13	275	$0
3ACHARDSUT1340	R.F.P. Solicitation - Charter Communication	15	20-May-13	10-Jun-13	275	$0
3ACHARDSUT1350	Review and Selection of Contractor (s) - Charter Communication	5	11-Jun-13	17-Jun-13	275	$0
3ACHARDSUT1360	Executed Agreement with Contractor(s) - Charter Communication	2	18-Jun-13	19-Jun-13	275	$0
3ACHARMSUT1370	Issuance of NTP to Contractor(s) - Charter Communication	0		19-Jun-13	396	$0
Chevron		210	01-Oct-12	19-Jul-13	361	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	361	$0
3ACHEVMSUT1001	Start of Utility Assembly Package Relocation Process - Chevron	0	01-Oct-12		578	$0
3ACHEVMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Chevron	0		19-Jul-13	507	$0
MUAA Process		170	01-Oct-12	24-May-13	362	$0
3ACHEVMSUT1020	Start of MUAA Process - Chevron	0	01-Oct-12		578	$0
3ACHEVDSUT1030	Develop MUAA - Chevron	20	01-Oct-12	26-Oct-12	405	$0
3ACHEVDSUT1040	Prepare & Deliver MUAA - Chevron	5	29-Oct-12	02-Nov-12	405	$0
3ACHEVDSUT1060	MUAA Comments by Owner (round 1) - Chevron	15	05-Nov-12	26-Nov-12	405	$0
3ACHEVDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Chevron	10	26-Nov-12	07-Dec-12	387	$0
3ACHEVDSUT1070	Address Comments from Owner & TxDOT (round 1) - Chevron	10	10-Dec-12	21-Dec-12	396	$0
3ACHEVDSUT1080	MUAA Comments by Owner (round 2) - Chevron	15	24-Dec-12	15-Jan-13	396	$0
3ACHEVDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Chevron	15	22-Jan-13	11-Feb-13	371	$0
3ACHEVDSUT1100	Address Comments from Owner & TxDOT (round 2) - Chevron	10	12-Feb-13	25-Feb-13	377	$0
3ACHEVDSUT1110	MUAA Comments by Owner (round 3) - Chevron	15	26-Feb-13	18-Mar-13	377	$0
3ACHEVDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Chevron	10	08-Apr-13	19-Apr-13	348	$0

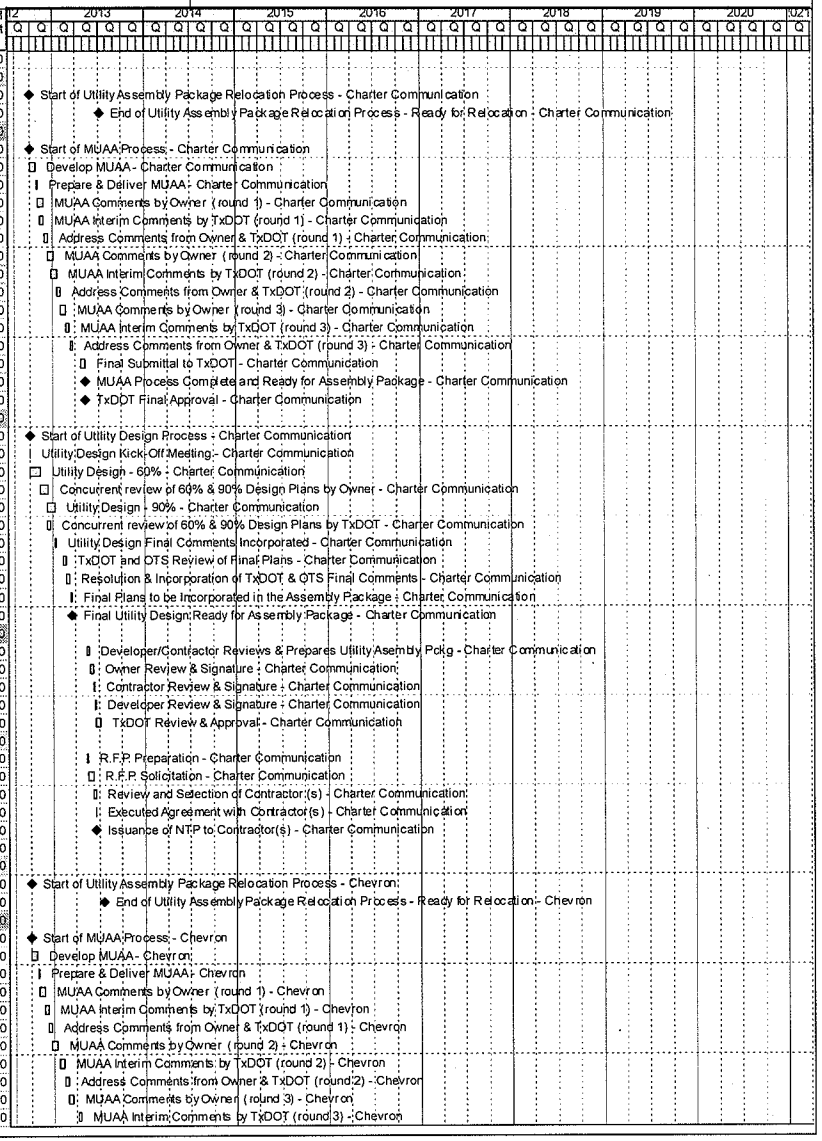

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ACHEVDSUT1130	Address Comments from Owner & TxDOT (round 3) - Chevron	10	22-Apr-13	03-May-13	353	$0
3ACHEVDSUT1140	Final Submittal to TxDOT - Chevron	15	06-May-13	24-May-13	353	$0
3ACHEVMSUT1150	MUAA Process Complete and Ready for Assembly Package - Chevron	0		24-May-13	508	$0
3ACHEVMSUT1160	TxDOT Final Approval - Chevron	0		24-May-13	348	$0
Utility Design		147	01-Oct-12	23-Apr-13	385	$0
3ACHEVDSUT1170	Utility Design Kick-Off Meeting - Chevron	2	01-Oct-12	02-Oct-12	436	$0
3ACHEVMSUT1170	Start of Utility Design Process - Chevron	0	01-Oct-12		624	$0
3ACHEVDSUT1190	Utility Design - 60% - Chevron	30	03-Oct-12	13-Nov-12	436	$0
3ACHEVDSUT1200	Concurrent review of 60% & 90% Design Plans by Owner - Chevron	20	14-Nov-12	12-Dec-12	436	$0
3ACHEVDSUT1210	Utility Design - 90% - Chevron	20	14-Jan-13	08-Feb-13	396	$0
3ACHEVDSUT1220	Concurrent review of 60% & 90% Design Plans by TxDOT - Chevron	10	14-Jan-13	25-Jan-13	396	$0
3ACHEVDSUT1230	Utility Design Final Comments Incorporated - Chevron	5	11-Feb-13	15-Feb-13	396	$0
3ACHEVDSUT1240	TxDOT and OTS Review of Final Plans - Chevron	10	18-Mar-13	29-Mar-13	376	$0
3ACHEVDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Chevron	10	01-Apr-13	12-Apr-13	376	$0
3ACHEVDSUT1260	Final Plans to be Incorporated in the Assembly Package - Chevron	7	15-Apr-13	23-Apr-13	376	$0
3ACHEVMSUT1270	Final Utility Design Ready for Assembly Package - Chevron	0		23-Apr-13	539	$0
Signature Process		36	26-May-13	19-Jul-13	353	$0
3ACHEVDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Chevron	10	26-May-13	10-Jun-13	353	$0
3ACHEVDSUT1290	Owner Review & Signature - Chevron	10	11-Jun-13	24-Jun-13	353	$0
3ACHEVDSUT1300	Contractor Review & Signature - Chevron	3	25-Jun-13	27-Jun-13	353	$0
3ACHEVDSUT1310	Developer Review & Signature - Chevron	5	28-Jun-13	05-Jul-13	353	$0
3ACHEVDSUT1320	TxDOT Review & Approval - Chevron	10	08-Jul-13	19-Jul-13	353	$0
Procurement		27	28-May-13	03-Jul-13	373	$0
3ACHEVDSUT1330	R.F.P. Preparation - Chevron	5	28-May-13	03-Jun-13	364	$0
3ACHEVDSUT1340	R.F.P. Solicitation - Chevron	15	04-Jun-13	24-Jun-13	364	$0
3ACHEVDSUT1350	Review and Selection of Contractor (s) - Chevron	5	25-Jun-13	01-Jul-13	364	$0
3ACHEVDSUT1360	Executed Agreement with Contractor(s) - Chevron	2	02-Jul-13	03-Jul-13	364	$0
3ACHEVMSUT1370	Issuance of NTP to Contractor(s) - Chevron	0		03-Jul-13	523	$0
City of Fort Worth		194	01-Oct-12	27-Jun-13	260	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	260	$0
3ACFTWMSUT1001	Start of Utility Assembly Package Relocation Process - City of Fort Worth	0	01-Oct-12		414	$0
3ACFTWMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - City of Fort Worth	0		27-Jun-13	364	$0
MUAA Process		155	01-Oct-12	03-May-13	260	$0
3ACFTWMSUT1020	Start of MUAA Process - City of Fort Worth	0	01-Oct-12		414	$0
3ACFTWDSUT1030	Develop MUAA - City of Fort Worth	20	01-Oct-12	26-Oct-12	290	$0
3ACFTWDSUT1040	Prepare & Deliver MUAA - City of Fort Worth	5	29-Oct-12	02-Nov-12	290	$0
3ACFTWDSUT1050	MUAA Interim Comments by TxDOT (round 1) - City of Fort Worth	10	05-Nov-12	16-Nov-12	287	$0
3ACFTWDSUT1060	MUAA Comments by Owner (round 1) - City of Fort Worth	15	05-Nov-12	26-Nov-12	290	$0
3ACFTWDSUT1070	Address Comments from Owner & TxDOT (round 1) - City of Fort Worth	10	27-Nov-12	10-Dec-12	290	$0
3ACFTWDSUT1080	MUAA Comments by Owner (round 2) - City of Fort Worth	15	11-Dec-12	02-Jan-13	291	$0
3ACFTWDSUT1090	MUAA Interim Comments by TxDOT (round 2) - City of Fort Worth	15	17-Dec-12	10-Jan-13	278	$0
3ACFTWDSUT1100	Address Comments from Owner & TxDOT (round 2) - City of Fort Worth	10	11-Jan-13	24-Jan-13	285	$0
3ACFTWDSUT1110	MUAA Comments by Owner (round 3) - City of Fort Worth	15	25-Jan-13	14-Feb-13	285	$0
3ACFTWDSUT1120	MUAA Interim Comments by TxDOT (round 3) - City of Fort Worth	10	25-Feb-13	08-Mar-13	264	$0
3ACFTWDSUT1130	Address Comments from Owner & TxDOT (round 3) - City of Fort Worth	10	11-Mar-13	22-Mar-13	269	$0
3ACFTWDSUT1140	Final Submittal to TxDOT - City of Fort Worth	15	15-Apr-13	03-May-13	254	$0
3ACFTWMSUT1150	MUAA Process Complete and Ready for Assembly Package - City of Fort Worth	0		03-May-13	366	$0
3ACFTWMSUT1160	TxDOT Final Approval - City of Fort Worth	0		03-May-13	249	$0
Utility Design		117	01-Oct-12	12-Mar-13	298	$0
3ACFTWMSUT1170	Start of Utility Design Process - City of Fort Worth	0	01-Oct-12		463	$0
3ACFTWDSUT1180	Utility Design Kick-Off Meeting - City of Fort Worth	2	01-Oct-12	02-Oct-12	322	$0
3ACFTWDSUT1190	Utility Design - 60% - City of Fort Worth	30	03-Oct-12	13-Nov-12	322	$0
3ACFTWDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - City of Fort Worth	20	14-Nov-12	12-Dec-12	322	$0
3ACFTWDSUT1200	Utility Design - 90% - City of Fort Worth	20	03-Dec-12	31-Dec-12	310	$0
3ACFTWDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - City of Fort Worth	10	03-Dec-12	14-Dec-12	310	$0
3ACFTWDSUT1230	Utility Design Final Comments Incorporated - City of Fort Worth	5	02-Jan-13	08-Jan-13	310	$0
3ACFTWDSUT1240	TxDOT and OTS Review of Final Plans - City of Fort Worth	10	04-Feb-13	15-Feb-13	292	$0
3ACFTWDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - City of Fort Worth	10	18-Feb-13	01-Mar-13	292	$0
3ACFTWDSUT1260	Final Plans to be Incorporated in the Assembly Package - City of Fort Worth	7	04-Mar-13	12-Mar-13	292	$0
3ACFTWMSUT1270	Final Utility Design Ready for Assembly Package - City of Fort Worth	0		12-Mar-13	418	$0

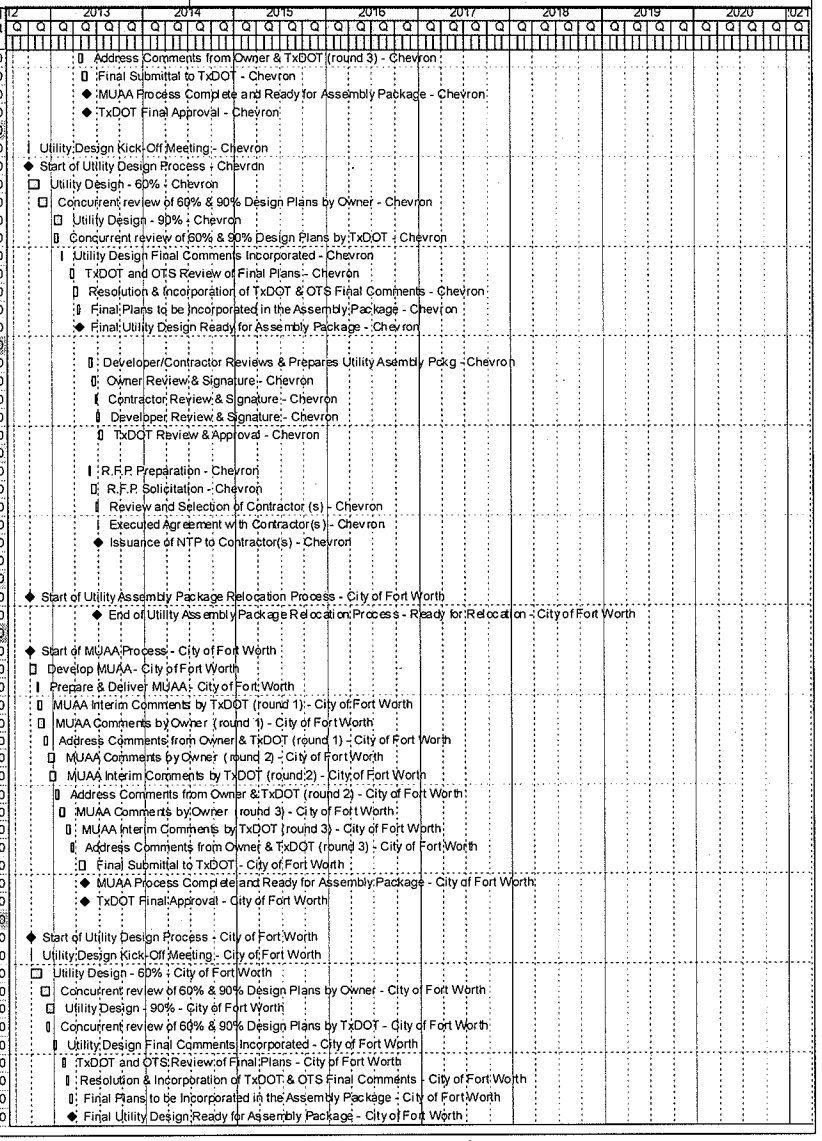

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Signature Process		38	06-May-13	27-Jun-13	254	$0
3ACFTWDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - City of Fort Worth	10	06-May-13	17-May-13	254	$0
3ACFTWDSUT1290	Owner Review & Signature - City of Fort Worth	10	20-May-13	03-Jun-13	254	$0
3ACFTWDSUT1300	Contractor Review & Signature - City of Fort Worth	3	04-Jun-13	06-Jun-13	254	$0
3ACFTWDSUT1310	Developer Review & Signature - City of Fort Worth	5	07-Jun-13	13-Jun-13	254	$0
3ACFTWDSUT1320	TxDOT Review & Approval - City of Fort Worth	10	14-Jun-13	27-Jun-13	254	$0
Procurement		28	06-May-13	12-Jun-13	271	$0
3ACFTWDSUT1330	R.F.P. Preparation - City of Fort Worth	5	06-May-13	10-May-13	265	$0
3ACFTWDSUT1340	R.F.P. Solicitation - City of Fort Worth	15	13-May-13	03-Jun-13	265	$0
3ACFTWDSUT1350	Review and Selection of Contractor (s) - City of Fort Worth	5	04-Jun-13	10-Jun-13	265	$0
3ACFTWDSUT1360	Executed Agreement with Contractor(s) - City of Fort Worth	2	11-Jun-13	12-Jun-13	265	$0
3ACFTWMSUT1370	Issuance of NTP to Contractor(s) - City of Fort Worth	0		12-Jun-13	379	$0
Energy Transfer		205	01-Oct-12	12-Jul-13	279	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	279	$0
3AENTRMSUT1000	Start of Utility Assembly Package Relocation Process - Energy Transfer	0	01-Oct-12		459	$0
3AENTRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Energy Transfer	0		12-Jul-13	391	$0
MUAA Process		165	01-Oct-12	17-May-13	280	$0
3AENTRMSUT1020	Start of MUAA Process - Energy Transfer	0	01-Oct-12		459	$0
3AENTRDSUT1030	Develop MUAA - Energy Transfer	20	01-Oct-12	26-Oct-12	320	$0
3AENTRDSUT1040	Prepare & Deliver MUAA - Energy Transfer	5	29-Oct-12	02-Nov-12	320	$0
3AENTRDSUT1060	MUAA Comments by Owner (round 1) - Energy Transfer	15	05-Nov-12	26-Nov-12	320	$0
3AENTRDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Energy Transfer	10	19-Nov-12	04-Dec-12	305	$0
3AENTRDSUT1070	Address Comments from Owner & TxDOT (round 1) - Energy Transfer	10	05-Dec-12	18-Dec-12	314	$0
3AENTRDSUT1080	MUAA Comments by Owner (round 2) - Energy Transfer	15	19-Dec-12	10-Jan-13	314	$0
3AENTRDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Energy Transfer	15	07-Jan-13	28-Jan-13	296	$0
3AENTRDSUT1100	Address Comments from Owner & TxDOT (round 2) - Energy Transfer	10	29-Jan-13	11-Feb-13	302	$0
3AENTRDSUT1110	MUAA Comments by Owner (round 3) - Energy Transfer	15	12-Feb-13	04-Mar-13	302	$0
3AENTRDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Energy Transfer	10	25-Mar-13	05-Apr-13	273	$0
3AENTRDSUT1130	Address Comments from Owner & TxDOT (round 3) - Energy Transfer	10	08-Apr-13	19-Apr-13	278	$0
3AENTRDSUT1140	Final Submittal to TxDOT - Energy Transfer	15	29-Apr-13	17-May-13	273	$0
3AENTRMSUT1150	MUAA Process Complete and Ready for Assembly Package - Energy Transfer	0		17-May-13	394	$0
3AENTRMSUT1160	TxDOT Final Approval - Energy Transfer	0		17-May-13	268	$0
Utility Design		197	01-Oct-12	09-Apr-13	308	$0
3AENTRMSUT1170	Start of Utility Design Process - Energy Transfer	0	01-Oct-12		504	$0
3AENTRDSUT1180	Utility Design Kick-Off Meeting - Energy Transfer	2	01-Oct-12	02-Oct-12	351	$0
3AENTRDSUT1190	Utility Design - 60% - Energy Transfer	30	03-Oct-12	13-Nov-12	351	$0
3AENTRDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Energy Transfer	20	14-Nov-12	12-Dec-12	351	$0
3AENTRDSUT1200	Utility Design - 90% - Energy Transfer	20	31-Dec-12	28-Jan-13	320	$0
3AENTRDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Energy Transfer	10	31-Dec-12	14-Jan-13	320	$0
3AENTRDSUT1230	Utility Design Final Comments Incorporated - Energy Transfer	5	29-Jan-13	04-Feb-13	320	$0
3AENTRDSUT1240	TxDOT and OTS Review of Final Plans - Energy Transfer	10	04-Mar-13	15-Mar-13	301	$0
3AENTRDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Energy Transfer	10	18-Mar-13	29-Mar-13	301	$0
3AENTRDSUT1260	Final Plans to be Incorporated in the Assembly Package - Energy Transfer	7	01-Apr-13	09-Apr-13	301	$0
3AENTRMSUT1270	Final Utility Design Ready for Assembly Package - Energy Transfer	0		09-Apr-13	432	$0
Signature Process		38	20-May-13	12-Jul-13	273	$0
3AENTRDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Energy Transfer	10	20-May-13	03-Jun-13	273	$0
3AENTRDSUT1290	Owner Review & Signature - Energy Transfer	10	04-Jun-13	17-Jun-13	273	$0
3AENTRDSUT1300	Contractor Review & Signature - Energy Transfer	3	18-Jun-13	20-Jun-13	273	$0
3AENTRDSUT1310	Developer Review & Signature - Energy Transfer	5	21-Jun-13	27-Jun-13	273	$0
3AENTRDSUT1320	TxDOT Review & Approval - Energy Transfer	10	28-Jun-13	12-Jul-13	273	$0
Procurement		28	20-May-13	26-Jun-13	291	$0
3AENTRDSUT1330	R.F.P. Preparation - Energy Transfer	5	20-May-13	24-May-13	284	$0
3AENTRDSUT1340	R.F.P. Solicitation - Energy Transfer	15	28-May-13	17-Jun-13	284	$0
3AENTRDSUT1350	Review and Selection of Contractor (s) - Energy Transfer	5	18-Jun-13	24-Jun-13	284	$0
3AENTRDSUT1360	Executed Agreement with Contractor(s) - Energy Transfer	2	25-Jun-13	26-Jun-13	284	$0
3AENTRMSUT1370	Issuance of NTP to Contractor(s) - Energy Transfer	0		26-Jun-13	407	$0
Magellan Pipeline		200	01-Oct-12	05-Jul-13	270	$0
Utility Assembly Package		200	01-Oct-12	05-Jul-13	270	$0
3AMAGEMSUT1000	Start of Utility Assembly Package Relocation Process - Magellan Pipeline	0	01-Oct-12		437	$0
3AMAGEMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Magellan Pipeline	0		05-Jul-13	380	$0

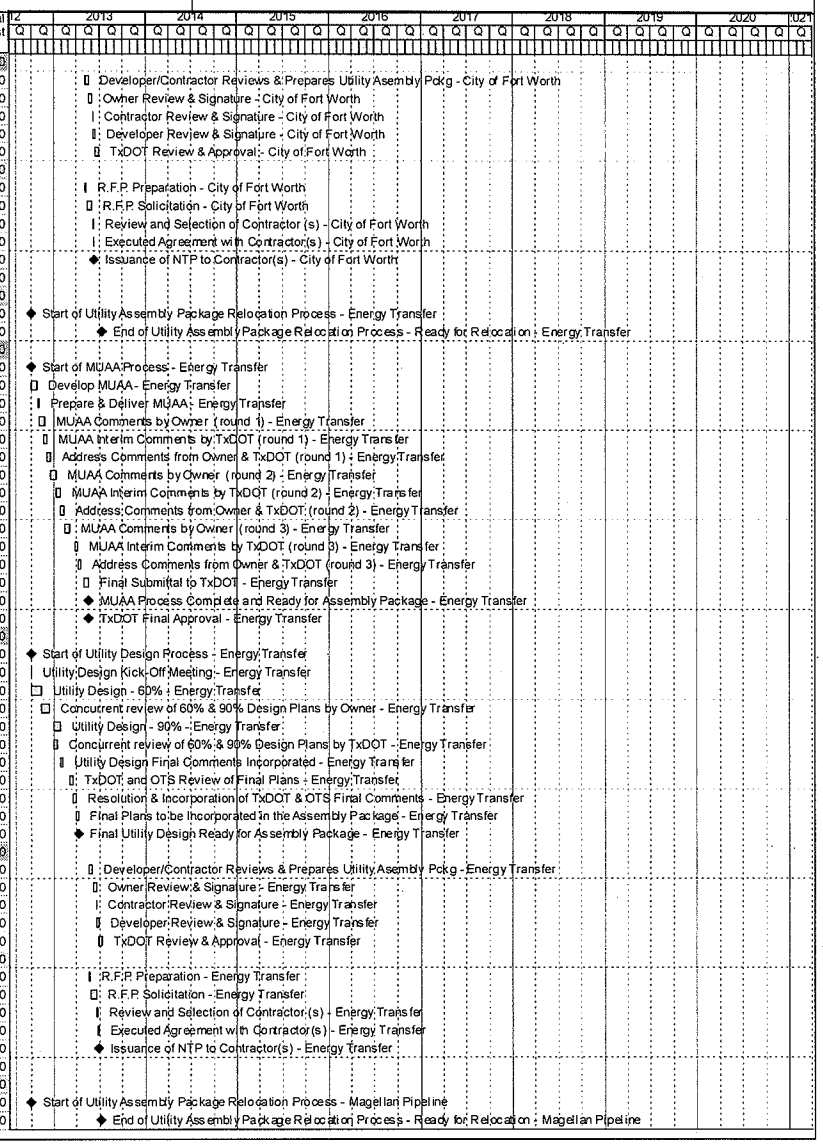

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
MUAA Process		160	01-Oct-12	10-May-13	271	$0
3AMAGEDSUT1020	Develop MUAA - Magellan Pipeline	20	01-Oct-12	26-Oct-12	306	$0
3AMAGEMSUT1020	Start of MUAA Process - Magellan Pipeline	0	01-Oct-12		437	$0
3AMAGEDSUT1040	Prepare & Deliver MUAA - Magellan Pipeline	5	29-Oct-12	02-Nov-12	305	$0
3AMAGEDSUT1050	MUAA Comments by Owner (round 1) - Magellan Pipeline	15	05-Nov-12	26-Nov-12	305	$0
3AMAGEDSUT1060	MUAA Interim Comments by TxDOT (round 1) - Magellan Pipeline	10	12-Nov-12	27-Nov-12	297	$0
3AMAGEDSUT1070	Address Comments from Owner & TxDOT (round 1) - Magellan Pipeline	10	28-Nov-12	11-Dec-12	305	$0
3AMAGEDSUT1080	MUAA Comments by Owner (round 2) - Magellan Pipeline	15	12-Dec-12	03-Jan-13	305	$0
3AMAGEDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Magellan Pipeline	15	27-Dec-12	17-Jan-13	288	$0
3AMAGEDSUT1100	Address Comments from Owner & TxDOT (round 2) - Magellan Pipeline	10	18-Jan-13	31-Jan-13	295	$0
3AMAGEDSUT1110	MUAA Comments by Owner (round 3) - Magellan Pipeline	15	01-Feb-13	21-Feb-13	295	$0
3AMAGEDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Magellan Pipeline	10	04-Mar-13	15-Mar-13	274	$0
3AMAGEDSUT1130	Address Comments from Owner & TxDOT (round 3) - Magellan Pipeline	10	18-Mar-13	29-Mar-13	279	$0
3AMAGEDSUT1140	Final Submittal to TxDOT - Magellan Pipeline	15	22-Apr-13	10-May-13	264	$0
3AMAGEMSUT1150	MUAA Process Complete and Ready for Assembly Package - Magellan Pipeline	0		10-May-13	381	$0
3AMAGEMSUT1160	TxDOT Final Approval - Magellan Pipeline	0		10-May-13	259	$0
Utility Design		122	01-Oct-12	19-Mar-13	309	$0
3AMAGEMSUT1170	Start of Utility Design Process - Magellan Pipeline	0	01-Oct-12		484	$0
3AMAGEDSUT1180	Utility Design Kick-Off Meeting - Magellan Pipeline	2	01-Oct-12	02-Oct-12	337	$0
3AMAGEDSUT1190	Utility Design - 60% - Magellan Pipeline	30	03-Oct-12	13-Nov-12	337	$0
3AMAGEDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Magellan Pipeline	20	14-Nov-12	12-Dec-12	337	$0
3AMAGEDSUT1200	Utility Design - 90% - Magellan Pipeline	20	10-Dec-12	08-Jan-13	320	$0
3AMAGEDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Magellan Pipeline	10	10-Dec-12	21-Dec-12	320	$0
3AMAGEDSUT1230	Utility Design Final Comments Incorporated - Magellan Pipeline	5	09-Jan-13	15-Jan-13	320	$0
3AMAGEDSUT1240	TxDOT and OTS Review of Final Plans - Magellan Pipeline	10	11-Feb-13	22-Feb-13	302	$0
3AMAGEDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Magellan Pipeline	10	25-Feb-13	08-Mar-13	302	$0
3AMAGEDSUT1260	Final Plans to be Incorporated in the Assembly Package - Magellan Pipeline	7	11-Mar-13	19-Mar-13	302	$0
3AMAGEMSUT1270	Final Utility Design Ready for Assembly Package - Magellan Pipeline	0		19-Mar-13	433	$0
Signature Process		36	13-May-13	05-Jul-13	264	$0
3AMAGEDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Magellan Pipeline	10	13-May-13	24-May-13	264	$0
3AMAGEDSUT1290	Owner Review & Signature - Magellan Pipeline	10	28-May-13	10-Jun-13	264	$0
3AMAGEDSUT1300	Contractor Review & Signature - Magellan Pipeline	3	11-Jun-13	13-Jun-13	264	$0
3AMAGEDSUT1310	Developer Review & Signature - Magellan Pipeline	5	14-Jun-13	20-Jun-13	264	$0
3AMAGEDSUT1320	TxDOT Review & Approval - Magellan Pipeline	10	21-Jun-13	05-Jul-13	264	$0
Procurement		28	13-May-13	19-Jun-13	282	$0
3AMAGEDSUT1330	R.F.P. Preparation - Magellan Pipeline	5	13-May-13	17-May-13	275	$0
3AMAGEDSUT1340	R.F.P. Solicitation - Magellan Pipeline	15	20-May-13	10-Jun-13	275	$0
3AMAGEDSUT1350	Review and Selection of Contractor (s) - Magellan Pipeline	5	11-Jun-13	17-Jun-13	275	$0
3AMAGEDSUT1360	Executed Agreement with Contractor(s) - Magellan Pipeline	2	18-Jun-13	19-Jun-13	275	$0
3AMAGEMSUT1370	Issuance of NTP to Contractor(s) - Magellan Pipeline	0		19-Jun-13	396	$0
Oncor		194	01-Oct-12	27-Jun-13	129	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	129	$0
3AONCRMSUT1000	Start of Utility Assembly Package Relocation Process - Oncor	0	01-Oct-12		178	$0
3AONCRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Oncor	0		27-Jun-13	181	$0
MUAA Process		155	01-Oct-12	03-May-13	128	$0
3AONCRMSUT1020	Start of MUAA Process - Oncor	0	01-Oct-12		178	$0
3AONCRDSUT1030	Develop MUAA - Oncor	20	01-Oct-12	26-Oct-12	125	$0
3AONCRDSUT1040	Prepare & Deliver MUAA - Oncor	5	29-Oct-12	02-Nov-12	125	$0
3AONCRDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Oncor	10	05-Nov-12	16-Nov-12	120	$0
3AONCRDSUT1060	MUAA Comments by Owner (round 1) - Oncor	15	05-Nov-12	26-Nov-12	162	$0
3AONCRDSUT1070	Address Comments from Owner & TxDOT (round 1) - Oncor	10	27-Nov-12	10-Dec-12	162	$0
3AONCRDSUT1080	MUAA Comments by Owner (round 2) - Oncor	15	11-Dec-12	02-Jan-13	162	$0
3AONCRDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Oncor	15	17-Dec-12	10-Jan-13	154	$0
3AONCRDSUT1100	Address Comments from Owner & TxDOT (round 2) - Oncor	10	11-Jan-13	24-Jan-13	156	$0
3AONCRDSUT1110	MUAA Comments by Owner (round 3) - Oncor	15	25-Jan-13	14-Feb-13	156	$0
3AONCRDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Oncor	10	19-Feb-13	04-Mar-13	144	$0
3AONCRDSUT1130	Address Comments from Owner & TxDOT (round 3) - Oncor	10	05-Mar-13	18-Mar-13	144	$0
3AONCRDSUT1140	Final Submittal to TxDOT - Oncor	15	15-Apr-13	03-May-13	125	$0
3AONCRMSUT1150	MUAA Process Complete and Ready for Assembly Package - Oncor	0		03-May-13	180	$0
3AONCRMSUT1160	TxDOT Final Approval - Oncor	0		03-May-13	125	$0

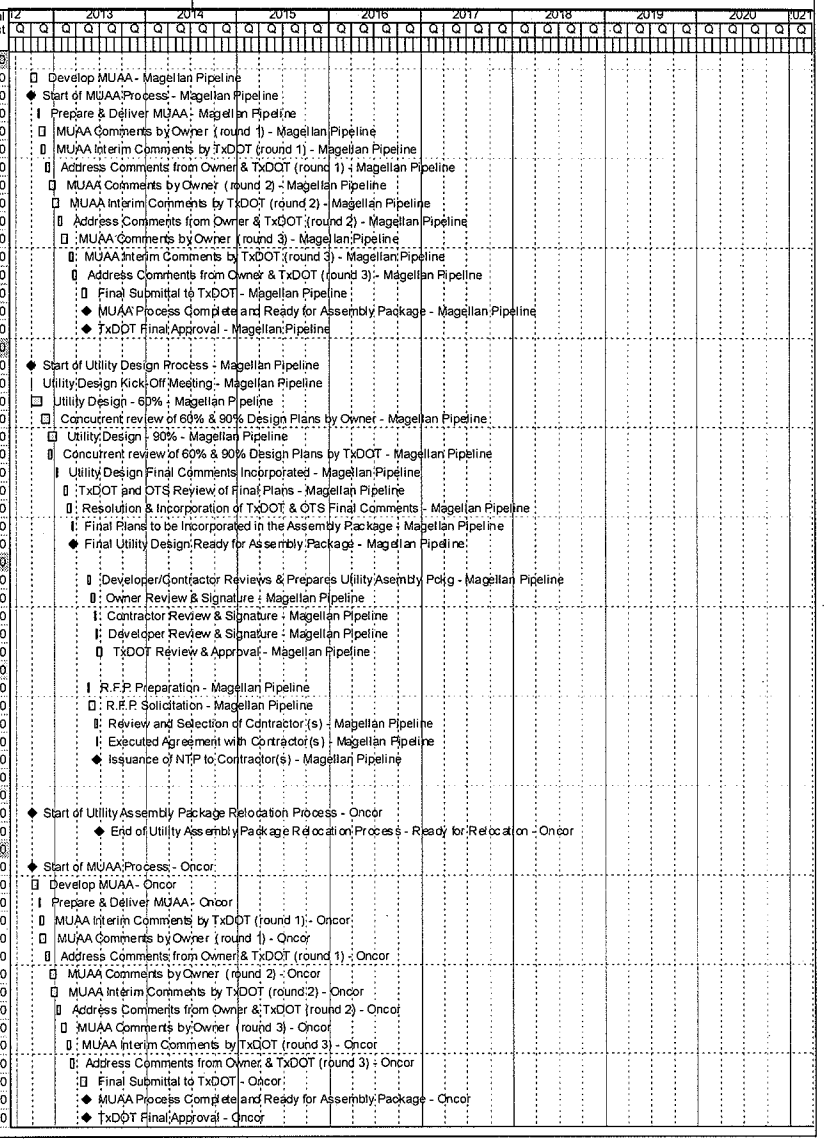

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Utility Design		117	01-Oct-12	12-Mar-13	166	$0
3AONCRDSUT1180	Utility Design Kick-Off Meeting - Oncor	2	01-Oct-12	02-Oct-12	193	$0
3AONCRMSUT1170	Start of Utility Design Process - Oncor	0	01-Oct-12		275	$0
3AONCRDSUT1190	Utility Design - 60% - Oncor	30	03-Oct-12	13-Nov-12	193	$0
3AONCRDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Oncor	20	14-Nov-12	12-Dec-12	193	$0
3AONCRDSUT1200	Utility Design - 90% - Oncor	20	03-Dec-12	31-Dec-12	181	$0
3AONCRDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Oncor	10	03-Dec-12	14-Dec-12	181	$0
3AONCRDSUT1230	Utility Design Final Comments Incorporated - Oncor	5	02-Jan-13	08-Jan-13	181	$0
3AONCRDSUT1240	TxDOT and OTS Review of Final Plans - Oncor	10	04-Feb-13	15-Feb-13	163	$0
3AONCRDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Oncor	10	18-Feb-13	01-Mar-13	163	$0
3AONCRDSUT1260	Final Plans to be Incorporated in the Assembly Package - Oncor	7	04-Mar-13	12-Mar-13	163	$0
3AONCRMSUT1270	Final Utility Design Ready for Assembly Package - Oncor	0		12-Mar-13	232	$0
Signature Process		38	06-May-13	27-Jun-13	125	$0
3AONCRDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Oncor	10	06-May-13	17-May-13	125	$0
3AONCRDSUT1290	Owner Review & Signature - Oncor	10	20-May-13	03-Jun-13	125	$0
3AONCRDSUT1300	Contractor Review & Signature - Oncor	3	04-Jun-13	06-Jun-13	125	$0
3AONCRDSUT1310	Developer Review & Signature - Oncor	5	07-Jun-13	13-Jun-13	125	$0
3AONCRDSUT1320	TxDOT Review & Approval - Oncor	10	14-Jun-13	27-Jun-13	125	$0
Procurement		28	06-May-13	12-Jun-13	140	$0
3AONCRDSUT1330	R.F.P. Preparation - Oncor	5	06-May-13	10-May-13	136	$0
3AONCRDSUT1340	R.F.P. Solicitation - Oncor	15	13-May-13	03-Jun-13	136	$0
3AONCRDSUT1350	Review and Selection of Contractor (s) - Oncor	5	04-Jun-13	10-Jun-13	136	$0
3AONCRDSUT1360	Executed Agreement with Contractor(s) - Oncor	2	11-Jun-13	12-Jun-13	136	$0
3AONCRMSUT1370	Issuance of NTP to Contractor(s) - Oncor	0		12-Jun-13	196	$0
Qwest		205	01-Oct-12	12-Jul-13	279	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	279	$0
3AQWSTMSUT1001	Start of Utility Assembly Package Relocation Process - Qwest	0	01-Oct-12		459	$0
3AQWSTMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Qwest	0		12-Jul-13	391	$0
MUAA Process		165	01-Oct-12	17-May-13	280	$0
3AQWSTMSUT1020	Start of MUAA Process - Qwest	0	01-Oct-12		459	$0
3AQWSTDSUT1030	Develop MUAA - Qwest	20	01-Oct-12	26-Oct-12	320	$0
3AQWSTDSUT1040	Prepare & Deliver MUAA - Qwest	5	29-Oct-12	02-Nov-12	320	$0
3AQWSTDSUT1060	MUAA Comments by Owner (round 1) - Qwest	15	05-Nov-12	26-Nov-12	320	$0
3AQWSTDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Qwest	10	19-Nov-12	04-Dec-12	305	$0
3AQWSTDSUT1070	Address Comments from Owner & TxDOT (round 1) - Qwest	10	05-Dec-12	18-Dec-12	314	$0
3AQWSTDSUT1080	MUAA Comments by Owner (round 2) - Qwest	15	19-Dec-12	10-Jan-13	314	$0
3AQWSTDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Qwest	15	07-Jan-13	28-Jan-13	296	$0
3AQWSTDSUT1100	Address Comments from Owner & TxDOT (round 2) - Qwest	10	29-Jan-13	11-Feb-13	302	$0
3AQWSTDSUT1110	MUAA Comments by Owner (round 3) - Qwest	15	12-Feb-13	04-Mar-13	302	$0
3AQWSTDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Qwest	10	11-Mar-13	22-Mar-13	283	$0
3AQWSTDSUT1130	Address Comments from Owner & TxDOT (round 3) - Qwest	10	25-Mar-13	05-Apr-13	288	$0
3AQWSTDSUT1140	Final Submittal to TxDOT - Qwest	15	29-Apr-13	17-May-13	273	$0
3AQWSTMSUT1150	MUAA Process Complete and Ready for Assembly Package - Qwest	0		17-May-13	394	$0
3AQWSTMSUT1160	TxDOT Final Approval - Qwest	0		17-May-13	268	$0
Utility Design		132	01-Oct-12	02-Apr-13	313	$0
3AQWSTMSUT1170	Start of Utility Design Process - Qwest	0	01-Oct-12		504	$0
3AQWSTDSUT1180	Utility Design Kick-Off Meeting - Qwest	2	01-Oct-12	02-Oct-12	351	$0
3AQWSTDSUT1190	Utility Design - 60% - Qwest	30	03-Oct-12	13-Nov-12	351	$0
3AQWSTDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Qwest	20	14-Nov-12	12-Dec-12	351	$0
3AQWSTDSUT1200	Utility Design - 90% - Qwest	20	31-Dec-12	28-Jan-13	320	$0
3AQWSTDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Qwest	10	31-Dec-12	14-Jan-13	320	$0
3AQWSTDSUT1230	Utility Design Final Comments Incorporated - Qwest	5	29-Jan-13	04-Feb-13	320	$0
3AQWSTDSUT1240	TxDOT and OTS Review of Final Plans - Qwest	10	25-Feb-13	08-Mar-13	306	$0
3AQWSTDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Qwest	10	11-Mar-13	22-Mar-13	306	$0
3AQWSTDSUT1260	Final Plans to be Incorporated in the Assembly Package - Qwest	7	25-Mar-13	02-Apr-13	306	$0
3AQWSTMSUT1270	Final Utility Design Ready for Assembly Package - Qwest	0		02-Apr-13	439	$0
Signature Process		38	20-May-13	12-Jul-13	273	$0
3AQWSTDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Qwest	10	20-May-13	03-Jun-13	273	$0
3AQWSTDSUT1290	Owner Review & Signature - Qwest	10	04-Jun-13	17-Jun-13	273	$0
3AQWSTDSUT1300	Contractor Review & Signature - Qwest	3	18-Jun-13	20-Jun-13	273	$0

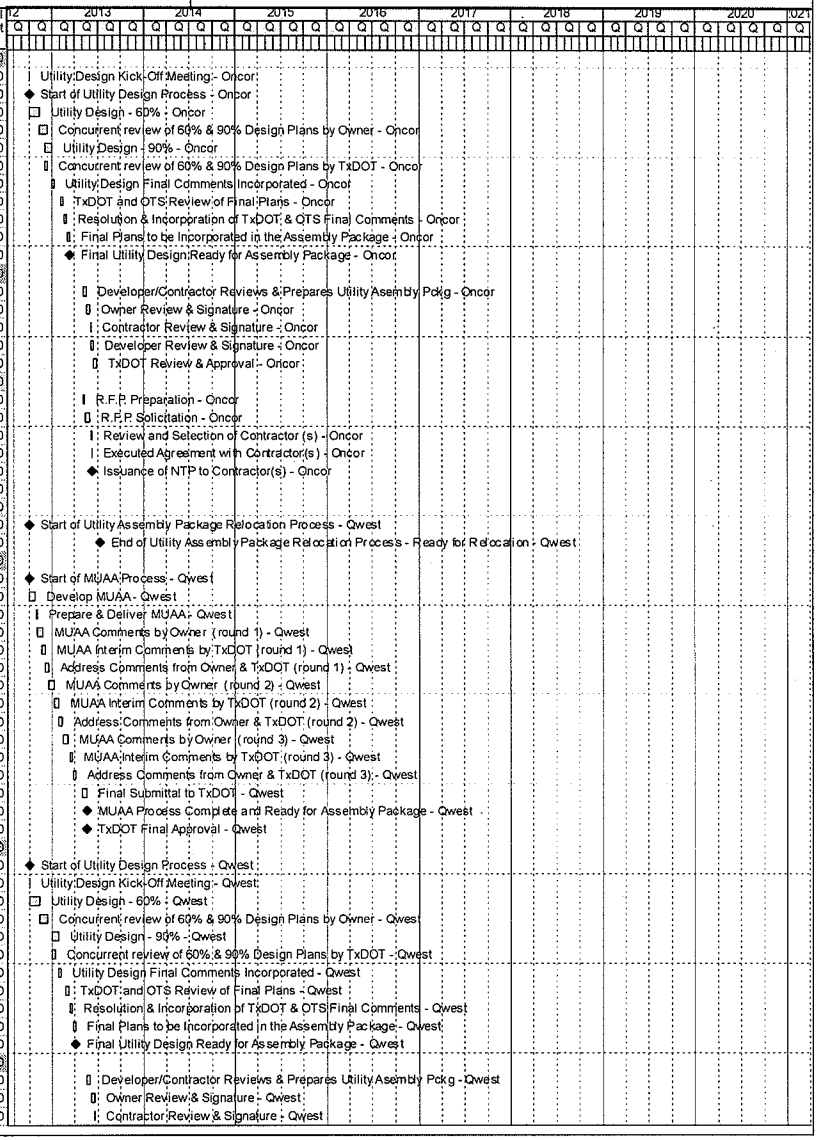

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AQWSTDSUT1310	Developer Review & Signature - Qwest	5	21-Jun-13	27-Jun-13	273	$0
3AQWSTDSUT1320	TxDOT Review & Approval - Qwest	10	28-Jun-13	12-Jul-13	273	$0
Procurement		28	20-May-13	26-Jun-13	291	$0
3AQWSTDSUT1330	R.F.P. Preparation - Qwest	5	20-May-13	24-May-13	284	$0
3AQWSTDSUT1340	R.F.P. Solicitation - Qwest	15	28-May-13	17-Jun-13	284	$0
3AQWSTDSUT1350	Review and Selection of Contractor (s) - Qwest	5	18-Jun-13	24-Jun-13	284	$0
3AQWSTDSUT1360	Executed Agreement with Contractor(s) - Qwest	2	25-Jun-13	26-Jun-13	284	$0
3AQWSTMSUT1370	Issuance of NTP to Contractor(s) - Qwest	0		26-Jun-13	407	$0
Sprint		215	01-Oct-12	26-Jul-13	514	$0
Utility Assembly Package		215	01-Oct-12	26-Jul-13	514	$0
3ASPRTMSUT1000	Start of Utility Assembly Package Relocation Process - Sprint	0	01-Oct-12		801	$0
3ASPRTMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Sprint	0		26-Jul-13	720	$0
MUAA Process		176	01-Oct-12	03-Jun-13	515	$0
3ASPRTMSUT1020	Start of MUAA Process - Sprint	0	01-Oct-12		801	$0
3ASPRTDSUT1030	Develop MUAA - Sprint	20	01-Oct-12	26-Oct-12	560	$0
3ASPRTDSUT1040	Prepare & Deliver MUAA - Sprint	5	29-Oct-12	02-Nov-12	560	$0
3ASPRTDSUT1060	MUAA Comments by Owner (round 1) - Sprint	15	05-Nov-12	26-Nov-12	560	$0
3ASPRTDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Sprint	10	03-Dec-12	14-Dec-12	533	$0
3ASPRTDSUT1070	Address Comments from Owner & TxDOT (round 1) - Sprint	10	17-Dec-12	31-Dec-12	546	$0
3ASPRTDSUT1080	MUAA Comments by Owner (round 2) - Sprint	15	02-Jan-13	22-Jan-13	546	$0
3ASPRTDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Sprint	15	28-Jan-13	15-Feb-13	517	$0
3ASPRTDSUT1100	Address Comments from Owner & TxDOT (round 2) - Sprint	10	18-Feb-13	01-Mar-13	528	$0
3ASPRTDSUT1110	MUAA Comments by Owner (round 3) - Sprint	15	04-Mar-13	22-Mar-13	528	$0
3ASPRTDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Sprint	10	08-Apr-13	19-Apr-13	498	$0
3ASPRTDSUT1130	Address Comments from Owner & TxDOT (round 3) - Sprint	10	22-Apr-13	03-May-13	508	$0
3ASPRTDSUT1140	Final Submittal to TxDOT - Sprint	15	13-May-13	03-Jun-13	503	$0
3ASPRTMSUT1150	MUAA Process Complete and Ready for Assembly Package - Sprint	0		03-Jun-13	721	$0
3ASPRTMSUT1160	TxDOT Final Approval - Sprint	0		03-Jun-13	493	$0
Utility Design		157	01-Oct-12	07-May-13	534	$0
3ASPRTMSUT1170	Start of Utility Design Process - Sprint	0	01-Oct-12		848	$0
3ASPRTDSUT1180	Utility Design Kick-Off Meeting - Sprint	2	01-Oct-12	02-Oct-12	591	$0
3ASPRTDSUT1190	Utility Design - 60% - Sprint	30	03-Oct-12	13-Nov-12	591	$0
3ASPRTDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Sprint	20	14-Nov-12	12-Dec-12	591	$0
3ASPRTDSUT1200	Utility Design - 90% - Sprint	20	28-Jan-13	22-Feb-13	541	$0
3ASPRTDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Sprint	10	28-Jan-13	08-Feb-13	541	$0
3ASPRTDSUT1230	Utility Design Final Comments Incorporated - Sprint	5	25-Feb-13	01-Mar-13	541	$0
3ASPRTDSUT1240	TxDOT and OTS Review of Final Plans - Sprint	10	01-Apr-13	12-Apr-13	521	$0
3ASPRTDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Sprint	10	15-Apr-13	26-Apr-13	521	$0
3ASPRTDSUT1260	Final Plans to be Incorporated in the Assembly Package - Sprint	7	29-Apr-13	07-May-13	521	$0
3ASPRTMSUT1270	Final Utility Design Ready for Assembly Package - Sprint	0		07-May-13	748	$0
Signature Process		38	04-Jun-13	26-Jul-13	503	$0
3ASPRTDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Sprint	10	04-Jun-13	17-Jun-13	503	$0
3ASPRTDSUT1290	Owner Review & Signature - Sprint	10	18-Jun-13	01-Jul-13	503	$0
3ASPRTDSUT1300	Contractor Review & Signature - Sprint	3	02-Jul-13	05-Jul-13	503	$0
3ASPRTDSUT1310	Developer Review & Signature - Sprint	5	08-Jul-13	12-Jul-13	503	$0
3ASPRTDSUT1320	TxDOT Review & Approval - Sprint	10	15-Jul-13	26-Jul-13	503	$0
Procurement		28	04-Jun-13	11-Jul-13	525	$0
3ASPRTDSUT1330	R.F.P. Preparation - Sprint	5	04-Jun-13	10-Jun-13	514	$0
3ASPRTDSUT1340	R.F.P. Solicitation - Sprint	15	11-Jun-13	01-Jul-13	514	$0
3ASPRTDSUT1350	Review and Selection of Contractor (s) - Sprint	5	02-Jul-13	09-Jul-13	514	$0
3ASPRTDSUT1360	Executed Agreement with Contractor(s) - Sprint	2	10-Jul-13	11-Jul-13	514	$0
3ASPRTMSUT1370	Issuance of NTP to Contractor(s) - Sprint	0		11-Jul-13	735	$0
Texas Midstream		205	01-Oct-12	12-Jul-13	273	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	273	$0
3ATEMIMSUT1000	Start of Utility Assembly Package Relocation Process - Texas Midstream	0	01-Oct-12		449	$0
3ATEMIMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Texas Midstream	0		12-Jul-13	383	$0
MUAA Process		165	01-Oct-12	17-May-13	274	$0
3ATEMIDSUT1030	Develop MUAA - Texas Midstream	20	01-Oct-12	26-Oct-12	314	$0
3ATEMIMSUT1020	Start of MUAA Process - Texas Midstream	0	01-Oct-12		449	$0
3ATEMIDSUT1040	Prepare & Deliver MUAA - Texas Midstream	5	29-Oct-12	02-Nov-12	314	$0

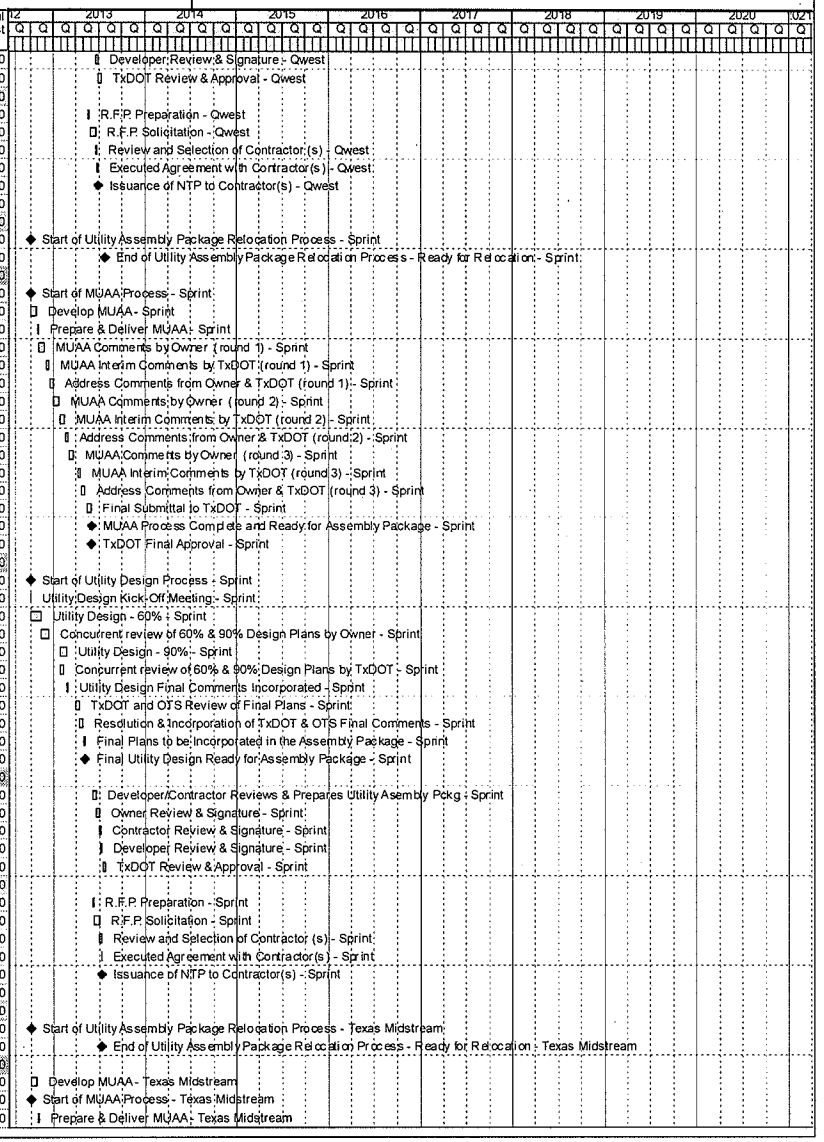

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ATEMIDSUT1060	MUAA Comments by Owner (round 1) - Texas Midstream	15	05-Nov-12	26-Nov-12	314	$0
3ATEMIDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Texas Midstream	10	19-Nov-12	04-Dec-12	299	$0
3ATEMIDSUT1070	Address Comments from Owner & TxDOT (round 1) - Texas Midstream	10	05-Dec-12	18-Dec-12	308	$0
3ATEMIDSUT1080	MUAA Comments by Owner (round 2) - Texas Midstream	15	19-Dec-12	10-Jan-13	308	$0
3ATEMIDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Texas Midstream	15	07-Jan-13	28-Jan-13	290	$0
3ATEMIDSUT1100	Address Comments from Owner & TxDOT (round 2) - Texas Midstream	10	29-Jan-13	11-Feb-13	296	$0
3ATEMIDSUT1110	MUAA Comments by Owner (round 3) - Texas Midstream	15	12-Feb-13	04-Mar-13	296	$0
3ATEMIDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Texas Midstream	10	11-Mar-13	22-Mar-13	277	$0
3ATEMIDSUT1130	Address Comments from Owner & TxDOT (round 3) - Texas Midstream	10	25-Mar-13	05-Apr-13	282	$0
3ATEMIDSUT1140	Final Submittal to TxDOT - Texas Midstream	15	29-Apr-13	17-May-13	267	$0
3ATEMIMSUT1150	TxDOT Final Approval - Texas Midstream	0		17-May-13	262	$0
3ATEMIMSUT1160	MUAA Process Complete and Ready for Assembly Package - Texas Midstream	0		17-May-13	384	$0
Utility Design		132	01-Oct-12	02-Apr-13	307	$0
3ATEMIMSUT1170	Start of Utility Design Process - Texas Midstream	0	01-Oct-12		494	$0
3ATEMIDSUT1180	Utility Design Kick-Off Meeting - Texas Midstream	2	01-Oct-12	02-Oct-12	345	$0
3ATEMIDSUT1190	Utility Design - 60% - Texas Midstream	30	03-Oct-12	13-Nov-12	345	$0
3ATEMIDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Texas Midstream	20	14-Nov-12	12-Dec-12	345	$0
3ATEMIDSUT1200	Utility Design - 90% - Texas Midstream	20	31-Dec-12	28-Jan-13	314	$0
3ATEMIDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Texas Midstream	10	31-Dec-12	14-Jan-13	314	$0
3ATEMIDSUT1230	Utility Design Final Comments Incorporated - Texas Midstream	5	29-Jan-13	04-Feb-13	314	$0
3ATEMIDSUT1240	TxDOT and OTS Review of Final Plans - Texas Midstream	10	25-Feb-13	08-Mar-13	300	$0
3ATEMIDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Texas Midstream	10	11-Mar-13	22-Mar-13	300	$0
3ATEMIDSUT1260	Final Plans to be Incorporated in the Assembly Package - Texas Midstream	7	25-Mar-13	02-Apr-13	300	$0
3ATEMIMSUT1270	Final Utility Design Ready for Assembly Package - Texas Midstream	0		02-Apr-13	429	$0
Signature Process		38	20-May-13	12-Jul-13	267	$0
3ATEMIDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Texas Midstream	10	20-May-13	03-Jun-13	267	$0
3ATEMIDSUT1290	Owner Review & Signature - Texas Midstream	10	04-Jun-13	17-Jun-13	267	$0
3ATEMIDSUT1300	Contractor Review & Signature - Texas Midstream	3	18-Jun-13	20-Jun-13	267	$0
3ATEMIDSUT1310	Developer Review & Signature - Texas Midstream	5	21-Jun-13	27-Jun-13	267	$0
3ATEMIDSUT1320	TxDOT Review & Approval - Texas Midstream	10	28-Jun-13	12-Jul-13	267	$0
Procurement		28	20-May-13	26-Jun-13	285	$0
3ATEMIDSUT1330	R.F.P. Preparation - Texas Midstream	5	20-May-13	24-May-13	278	$0
3ATEMIDSUT1340	R.F.P. Solicitation - Texas Midstream	15	28-May-13	17-Jun-13	278	$0
3ATEMIDSUT1350	Review and Selection of Contractor (s) - Texas Midstream	5	18-Jun-13	24-Jun-13	278	$0
3ATEMIDSUT1360	Executed Agreement with Contractor(s) - Texas Midstream	2	25-Jun-13	26-Jun-13	278	$0
3ATEMIMSUT1370	Issuance of NTP to Contractor(s) - Texas Midstream	0		26-Jun-13	399	$0
Time Warner / Fiber Light		194	01-Oct-12	27-Jun-13	258	$0
Utility Assembly Package		194	01-Oct-12	27-Jun-13	258	$0
3ATMWRMSUT1000	Start of Utility Assembly Package Relocation Process - Time Warner / Fiber Light	0	01-Oct-12		410	$0
3ATMWRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Time Warner / Fi	0		27-Jun-13	362	$0
MUAA Process		155	01-Oct-12	03-May-13	259	$0
3ATMWRMSUT1020	Start of MUAA Process - Time Warner / Fiber Light	0	01-Oct-12		410	$0
3ATMWRDSUT1030	Develop MUAA - Time Warner / Fiber Light	20	01-Oct-12	26-Oct-12	288	$0
3ATMWRDSUT1040	Prepare & Deliver MUAA - Time Warner / Fiber Light	5	29-Oct-12	02-Nov-12	288	$0
3ATMWRDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Time Warner / Fiber Light	10	05-Nov-12	16-Nov-12	285	$0
3ATMWRDSUT1060	MUAA Comments by Owner (round 1) - Time Warner / Fiber Light	15	05-Nov-12	26-Nov-12	288	$0
3ATMWRDSUT1070	Address Comments from Owner & TxDOT (round 1) - Time Warner / Fiber Light	10	27-Nov-12	10-Dec-12	288	$0
3ATMWRDSUT1080	MUAA Comments by Owner (round 2) - Time Warner / Fiber Light	15	11-Dec-12	02-Jan-13	289	$0
3ATMWRDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Time Warner / Fiber Light	15	17-Dec-12	10-Jan-13	276	$0
3ATMWRDSUT1100	Address Comments from Owner & TxDOT (round 2) - Time Warner / Fiber Light	10	11-Jan-13	24-Jan-13	283	$0
3ATMWRDSUT1110	MUAA Comments by Owner (round 3) - Time Warner / Fiber Light	15	25-Jan-13	14-Feb-13	283	$0
3ATMWRDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Time Warner / Fiber Light	10	19-Feb-13	04-Mar-13	266	$0
3ATMWRDSUT1130	Address Comments from Owner & TxDOT (round 3) - Time Warner / Fiber Light	10	05-Mar-13	18-Mar-13	271	$0
3ATMWRDSUT1140	Final Submittal to TxDOT - Time Warner / Fiber Light	15	15-Apr-13	03-May-13	252	$0
3ATMWRMSUT1150	MUAA Process Complete and Ready for Assembly Package - Time Warner / Fiber Light	0		03-May-13	362	$0
3ATMWRMSUT1160	TxDOT Final Approval - Time Warner / Fiber Light	0		03-May-13	247	$0
Utility Design		117	01-Oct-12	12-Mar-13	296	$0
3ATMWRDSUT1170	Utility Design Kick-Off Meeting - Time Warner / Fiber Light	2	01-Oct-12	02-Oct-12	320	$0
3ATMWRMSUT1180	Start of Utility Design Process - Time Warner / Fiber Light	0	01-Oct-12		459	$0
3ATMWRDSUT1190	Utility Design - 60% - Time Warner / Fiber Light	30	03-Oct-12	13-Nov-12	320	$0

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ATMWRDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Time Warner / Fiber Light	20	14-Nov-12	12-Dec-12	320	$0
3ATMWRDSUT1200	Utility Design - 90% - Time Warner / Fiber Light	20	03-Dec-12	31-Dec-12	308	$0
3ATMWRDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Time Warner / Fiber Light	10	03-Dec-12	14-Dec-12	308	$0
3ATMWRDSUT1230	Utility Design Final Comments Incorporated - Time Warner / Fiber Light	5	02-Jan-13	08-Jan-13	308	$0
3ATMWRDSUT1240	TxDOT and OTS Review of Final Plans - Time Warner / Fiber Light	10	04-Feb-13	15-Feb-13	290	$0
3ATMWRDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Time Warner / Fiber Light	10	18-Feb-13	01-Mar-13	290	$0
3ATMWRDSUT1260	Final Plans to be Incorporated in the Assembly Package - Time Warner / Fiber Light	7	04-Mar-13	12-Mar-13	290	$0
3ATMWRMSUT1270	Final Utility Design Ready for Assembly Package - Time Warner / Fiber Light	0		12-Mar-13	414	$0
Signature Process		38	06-May-13	27-Jun-13	252	$0
3ATMWRDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Time Warner / Fiber Light	10	06-May-13	17-May-13	252	$0
3ATMWRDSUT1290	Owner Review & Signature - Time Warner / Fiber Light	10	20-May-13	03-Jun-13	252	$0
3ATMWRDSUT1300	Contractor Review & Signature - Time Warner / Fiber Light	3	04-Jun-13	06-Jun-13	252	$0
3ATMWRDSUT1310	Developer Review & Signature - Time Warner / Fiber Light	5	07-Jun-13	13-Jun-13	252	$0
3ATMWRDSUT1320	TxDOT Review & Approval - Time Warner / Fiber Light	10	14-Jun-13	27-Jun-13	252	$0
Procurement		28	06-May-13	12-Jun-13	269	$0
3ATMWRDSUT1330	R.F.P. Preparation - Time Warner / Fiber Light	5	06-May-13	10-May-13	263	$0
3ATMWRDSUT1340	R.F.P. Solicitation - Time Warner / Fiber Light	15	13-May-13	03-Jun-13	263	$0
3ATMWRDSUT1350	Review and Selection of Contractor (s) - Time Warner / Fiber Light	5	04-Jun-13	10-Jun-13	263	$0
3ATMWRDSUT1360	Executed Agreement with Contractor(s) - Time Warner / Fiber Light	2	11-Jun-13	12-Jun-13	263	$0
3ATMWRMSUT1370	Issuance of NTP to Contractor(s) - Time Warner / Fiber Light	0		12-Jun-13	377	$0
Verizon		210	01-Oct-12	19-Jul-13	508	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	508	$0
3AVERZMSUT1000	Start of Utility Assembly Package Relocation Process - Verizon	0	01-Oct-12		785	$0
3AVERZMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Verizon	0		19-Jul-13	712	$0
MUAA Process		170	01-Oct-12	24-May-13	509	$0
3AVERZMSUT1020	Start of MUAA Process - Verizon	0	01-Oct-12		785	$0
3AVERZDSUT1030	Develop MUAA - Verizon	20	01-Oct-12	26-Oct-12	548	$0
3AVERZDSUT1040	Prepare & Deliver MUAA - Verizon	5	29-Oct-12	02-Nov-12	548	$0
3AVERZDSUT1060	MUAA Comments by Owner (round 1) - Verizon	15	05-Nov-12	26-Nov-12	548	$0
3AVERZDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Verizon	10	26-Nov-12	07-Dec-12	526	$0
3AVERZDSUT1070	Address Comments from Owner & TxDOT (round 1) - Verizon	10	10-Dec-12	21-Dec-12	539	$0
3AVERZDSUT1080	MUAA Comments by Owner (round 2) - Verizon	15	24-Dec-12	15-Jan-13	540	$0
3AVERZDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Verizon	15	22-Jan-13	11-Feb-13	510	$0
3AVERZDSUT1100	Address Comments from Owner & TxDOT (round 2) - Verizon	10	12-Feb-13	25-Feb-13	521	$0
3AVERZDSUT1110	MUAA Comments by Owner (round 3) - Verizon	15	26-Feb-13	18-Mar-13	521	$0
3AVERZDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Verizon	10	08-Apr-13	19-Apr-13	487	$0
3AVERZDSUT1130	Address Comments from Owner & TxDOT (round 3) - Verizon	10	22-Apr-13	03-May-13	497	$0
3AVERZDSUT1140	Final Submittal to TxDOT - Verizon	15	06-May-13	24-May-13	497	$0
3AVERZMSUT1150	MUAA Process Complete and Ready for Assembly Package - Verizon	0		24-May-13	713	$0
3AVERZMSUT1160	TxDOT Final Approval - Verizon	0		24-May-13	487	$0
Utility Design		157	01-Oct-12	07-May-13	522	$0
3AVERZMSUT1170	Start of Utility Design Process - Verizon	0	01-Oct-12		833	$0
3AVERZDSUT1180	Utility Design Kick-Off Meeting - Verizon	2	01-Oct-12	02-Oct-12	580	$0
3AVERZDSUT1190	Utility Design - 60% - Verizon	30	03-Oct-12	13-Nov-12	580	$0
3AVERZDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Verizon	20	14-Nov-12	12-Dec-12	580	$0
3AVERZDSUT1200	Utility Design - 90% - Verizon	20	28-Jan-13	22-Feb-13	530	$0
3AVERZDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Verizon	10	28-Jan-13	08-Feb-13	530	$0
3AVERZDSUT1230	Utility Design Final Comments Incorporated - Verizon	5	25-Feb-13	01-Mar-13	530	$0
3AVERZDSUT1240	TxDOT and OTS Review of Final Plans - Verizon	10	01-Apr-13	12-Apr-13	510	$0
3AVERZDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Verizon	10	15-Apr-13	26-Apr-13	510	$0
3AVERZDSUT1260	Final Plans to be Incorporated in the Assembly Package - Verizon	7	29-Apr-13	07-May-13	510	$0
3AVERZMSUT1270	Final Utility Design Ready for Assembly Package - Verizon	0		07-May-13	730	$0
Signature Process		38	28-May-13	19-Jul-13	497	$0
3AVERZDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Verizon	10	28-May-13	10-Jun-13	497	$0
3AVERZDSUT1290	Owner Review & Signature - Verizon	10	11-Jun-13	24-Jun-13	497	$0
3AVERZDSUT1300	Contractor Review & Signature - Verizon	3	25-Jun-13	27-Jun-13	497	$0
3AVERZDSUT1310	Developer Review & Signature - Verizon	5	28-Jun-13	05-Jul-13	497	$0
3AVERZDSUT1320	TxDOT Review & Approval - Verizon	10	08-Jul-13	19-Jul-13	497	$0
Procurement		27	28-May-13	03-Jul-13	520	$0
3AVERZDSUT1330	R.F.P. Preparation - Verizon	5	28-May-13	03-Jun-13	508	$0

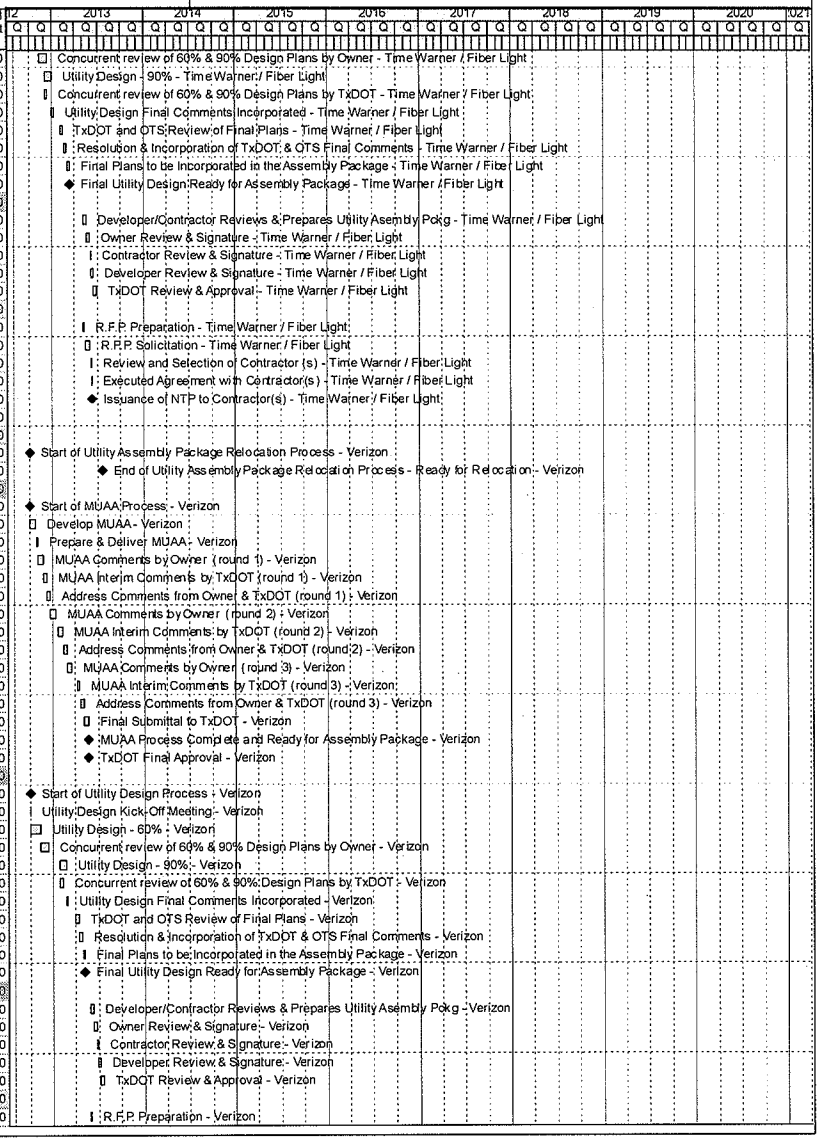

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AVERZDSUT1340	R.F.P. Solicitation - Verizon	15	04-Jun-13	24-Jun-13	508	$0
3AVERZDSUT1350	Review and Selection of Contractor (s) - Verizon	5	25-Jun-13	01-Jul-13	508	$0
3AVERZDSUT1360	Executed Agreement with Contractor(s) - Verizon	2	02-Jul-13	03-Jul-13	508	$0
3AVERZMSUT1370	Issuance of NTP to Contractor(s) - Verizon	0		03-Jul-13	728	$0
Crosstex Energy		205	01-Oct-12	12-Jul-13	329	$0
Utility Assembly Package		205	01-Oct-12	12-Jul-13	329	$0
ICCROSSMSUT1000	Start of Utility Assembly Package Relocation Process - Crosstex Energy	0	01-Oct-12		528	$0
ICCROSSMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Crosstex Energy	0		12-Jul-13	461	$0
MUAA Process		165	01-Oct-12	17-May-13	330	$0
ICCROSSMSUT1020	Start of MUAA Process - Crosstex Energy	0	01-Oct-12		528	$0
ICCROSSDSUT1030	Develop MUAA - Crosstex Energy	20	01-Oct-12	26-Oct-12	369	$0
ICCROSSDSUT1040	Prepare & Deliver MUAA - Crosstex Energy	5	29-Oct-12	02-Nov-12	369	$0
ICCROSSDSUT1060	MUAA Comments by Owner (round 1) - Crosstex Energy	15	05-Nov-12	26-Nov-12	369	$0
ICCROSSDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Crosstex Energy	10	19-Nov-12	04-Dec-12	354	$0
ICCROSSDSUT1070	Address Comments from Owner & TxDOT (round 1) - Crosstex Energy	10	05-Dec-12	18-Dec-12	363	$0
ICCROSSDSUT1080	MUAA Comments by Owner (round 2) - Crosstex Energy	15	19-Dec-12	10-Jan-13	363	$0
ICCROSSDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Crosstex Energy	15	07-Jan-13	28-Jan-13	345	$0
ICCROSSDSUT1100	Address Comments from Owner & TxDOT (round 2) - Crosstex Energy	10	29-Jan-13	11-Feb-13	351	$0
ICCROSSDSUT1110	MUAA Comments by Owner (round 3) - Crosstex Energy	15	12-Feb-13	04-Mar-13	351	$0
ICCROSSDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Crosstex Energy	10	25-Mar-13	05-Apr-13	322	$0
ICCROSSDSUT1130	Address Comments from Owner & TxDOT (round 3) - Crosstex Energy	10	08-Apr-13	19-Apr-13	327	$0
ICCROSSDSUT1140	Final Submittal to TxDOT - Crosstex Energy	15	29-Apr-13	17-May-13	322	$0
ICCROSSMSUT1150	MUAA Process Complete and Ready for Assembly Package - Crosstex Energy	0		17-May-13	464	$0
ICCROSSMSUT1160	TxDOT Final Approval - Crosstex Energy	0		17-May-13	317	$0
Utility Design		142	01-Oct-12	16-Apr-13	353	$0
ICCROSSMSUT1170	Start of Utility Design Process - Crosstex Energy	0	01-Oct-12		571	$0
ICCROSSDSUT1180	Utility Design Kick-Off Meeting - Crosstex Energy	2	01-Oct-12	02-Oct-12	400	$0
ICCROSSDSUT1190	Utility Design - 60% - Crosstex Energy	30	03-Oct-12	13-Nov-12	400	$0
ICCROSSDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Crosstex Energy	20	14-Nov-12	12-Dec-12	400	$0
ICCROSSDSUT1200	Utility Design - 90% - Crosstex Energy	20	14-Jan-13	08-Feb-13	360	$0
ICCROSSDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Crosstex Energy	10	14-Jan-13	25-Jan-13	360	$0
ICCROSSDSUT1230	Utility Design Final Comments Incorporated - Crosstex Energy	5	11-Feb-13	15-Feb-13	360	$0
ICCROSSDSUT1240	TxDOT and OTS Review of Final Plans - Crosstex Energy	10	11-Mar-13	22-Mar-13	345	$0
ICCROSSDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Crosstex Energy	10	25-Mar-13	05-Apr-13	345	$0
ICCROSSDSUT1260	Final Plans to be Incorporated in the Assembly Package - Crosstex Energy	7	08-Apr-13	16-Apr-13	345	$0
ICCROSSMSUT1270	Final Utility Design Ready for Assembly Package - Crosstex Energy	0		16-Apr-13	495	$0
Signature Process		38	20-May-13	12-Jul-13	322	$0
ICCROSSDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Crosstex Energy	10	20-May-13	03-Jun-13	322	$0
ICCROSSDSUT1290	Owner Review & Signature - Crosstex Energy	10	04-Jun-13	17-Jun-13	322	$0
ICCROSSDSUT1300	Contractor Review & Signature - Crosstex Energy	3	18-Jun-13	20-Jun-13	322	$0
ICCROSSDSUT1310	Developer Review & Signature - Crosstex Energy	5	21-Jun-13	27-Jun-13	322	$0
ICCROSSDSUT1320	TxDOT Review & Approval - Crosstex Energy	10	28-Jun-13	12-Jul-13	322	$0
Procurement		28	20-May-13	26-Jun-13	341	$0
ICCROSSDSUT1330	R.F.P. Preparation - Crosstex Energy	5	20-May-13	24-May-13	333	$0
ICCROSSDSUT1340	R.F.P. Solicitation - Crosstex Energy	15	28-May-13	17-Jun-13	333	$0
ICCROSSDSUT1350	Review and Selection of Contractor (s) - Crosstex Energy	5	18-Jun-13	24-Jun-13	333	$0
ICCROSSDSUT1360	Executed Agreement with Contractor(s) - Crosstex Energy	2	25-Jun-13	26-Jun-13	333	$0
ICCROSSMSUT1370	Issuance of NTP to Contractor(s) - Crosstex Energy	0		26-Jun-13	477	$0
Enterprisee Products		210	01-Oct-12	19-Jul-13	324	$0
Utility Assembly Package		210	01-Oct-12	19-Jul-13	324	$0
ICENTRMSUT1000	Start of Utility Assembly Package Relocation Process - Enterprise Products	0	01-Oct-12		528	$0
ICENTRMSUT1010	End of Utility Assembly Package Relocation Process - Ready for Relocation - Enterprise Products	0		19-Jul-13	454	$0
MUAA Process		170	01-Oct-12	24-May-13	325	$0
ICENTRMSUT1020	Start of MUAA Process - Enterprise Products	0	01-Oct-12		528	$0
ICENTRDSUT1030	Develop MUAA - Enterprise Products	20	01-Oct-12	26-Oct-12	369	$0
ICENTRDSUT1040	Prepare & Deliver MUAA - Enterprise Products	5	29-Oct-12	02-Nov-12	369	$0
ICENTRDSUT1060	MUAA Comments by Owner (round 1) - Enterprise Products	15	05-Nov-12	26-Nov-12	369	$0
ICENTRDSUT1050	MUAA Interim Comments by TxDOT (round 1) - Enterprise Products	10	26-Nov-12	07-Dec-12	351	$0
ICENTRDSUT1070	Address Comments from Owner & TxDOT (round 1) - Enterprise Products	10	10-Dec-12	21-Dec-12	360	$0
ICENTRDSUT1080	MUAA Comments by Owner (round 2) - Enterprise Products	15	24-Dec-12	15-Jan-13	360	$0

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
ICENTRDSUT1090	MUAA Interim Comments by TxDOT (round 2) - Enterprise Products	15	22-Jan-13	11-Feb-13	335	$0
ICENTRDSUT1100	Address Comments from Owner & TxDOT (round 2) - Enterprise Products	10	12-Feb-13	25-Feb-13	341	$0
ICENTRDSUT1110	MUAA Comments by Owner (round 3) - Enterprise Products	15	26-Feb-13	18-Mar-13	341	$0
ICENTRDSUT1120	MUAA Interim Comments by TxDOT (round 3) - Enterprise Products	10	25-Mar-13	05-Apr-13	322	$0
ICENTRDSUT1130	Address Comments from Owner & TxDOT (round 3) - Enterprise Products	10	08-Apr-13	19-Apr-13	327	$0
ICENTRDSUT1140	Final Submittal to TxDOT - Enterprise Products	15	06-May-13	24-May-13	317	$0
ICENTRMSUT1150	MUAA Process Complete and Ready for Assembly Package - Enterprise Products	0		24-May-13	457	$0
ICENTRMSUT1160	TxDOT Final Approval - Enterprise Products	0		24-May-13	312	$0
Utility Design		147	01-Oct-12	23-Apr-13	348	$0
ICENTRMSUT1170	Start of Utility Design Process - Enterprise Products	0	01-Oct-12		571	$0
ICENTRDSUT1180	Utility Design Kick-Off Meeting - Enterprise Products	2	01-Oct-12	02-Oct-12	400	$0
ICENTRDSUT1190	Utility Design - 60% - Enterprise Products	30	03-Oct-12	13-Nov-12	400	$0
ICENTRDSUT1220	Concurrent review of 60% & 90% Design Plans by Owner - Enterprise Products	20	14-Nov-12	12-Dec-12	400	$0
ICENTRDSUT1200	Utility Design - 90% - Enterprise Products	20	14-Jan-13	08-Feb-13	360	$0
ICENTRDSUT1210	Concurrent review of 60% & 90% Design Plans by TxDOT - Enterprise Products	10	14-Jan-13	25-Jan-13	360	$0
ICENTRDSUT1230	Utility Design Final Comments Incorporated - Enterprise Products	5	11-Feb-13	15-Feb-13	360	$0
ICENTRDSUT1240	TxDOT and OTS Review of Final Plans - Enterprise Products	10	18-Mar-13	29-Mar-13	340	$0
ICENTRDSUT1250	Resolution & Incorporation of TxDOT & OTS Final Comments - Enterprise Products	10	01-Apr-13	12-Apr-13	340	$0
ICENTRDSUT1260	Final Plans to be Incorporated in the Assembly Package - Enterprise Products	7	15-Apr-13	23-Apr-13	340	$0
ICENTRMSUT1270	Final Utility Design Ready for Assembly Package - Enterprise Products	0		23-Apr-13	488	$0
Signature Process		38	28-May-13	19-Jul-13	317	$0
ICENTRDSUT1280	Developer/Contractor Reviews & Prepares Utility Asembly Pckg - Enterprise Products	10	28-May-13	10-Jun-13	317	$0
ICENTRDSUT1290	Owner Review & Signature - Enterprise Products	10	11-Jun-13	24-Jun-13	317	$0
ICENTRDSUT1300	Contractor Review & Signature - Enterprise Products	3	25-Jun-13	27-Jun-13	317	$0
ICENTRDSUT1310	Developer Review & Signature - Enterprise Products	5	28-Jun-13	05-Jul-13	317	$0
ICENTRDSUT1320	TxDOT Review & Approval - Enterprise Products	10	08-Jul-13	19-Jul-13	317	$0
Procurement		27	28-May-13	03-Jul-13	336	$0
ICENTRDSUT1330	R.F.P. Preparation - Enterprise Products	5	28-May-13	03-Jun-13	328	$0
ICENTRDSUT1340	R.F.P. Solicitation - Enterprise Products	15	04-Jun-13	24-Jun-13	328	$0
ICENTRDSUT1350	Review and Selection of Contractor (s) - Enterprise Products	5	25-Jun-13	01-Jul-13	328	$0
ICENTRDSUT1360	Executed Agreement with Contractor(s) - Enterprise Products	2	02-Jul-13	03-Jul-13	328	$0
ICENTRMSUT1370	Issuance of NTP to Contractor(s) - Enterprise Products	0		03-Jul-13	470	$0
Utility Relocations		168	28-Jun-13	18-Feb-14	858	$20,469,314
AT&T		58	28-Jun-13	17-Sep-13	968	$2,139,494
3AAT&TMSUT1000	Start AT&T Utility Relocation	0	28-Jun-13		374	$0
OH - 52 (Fiber Optic) 111+45 to 112+05		37	01-Jul-13	20-Aug-13	988	$67,018
3AAT&TUTUTOH521(	Utility Construction / Relocation OH - 52 (Fiber Optic) 111+45 to 112+05	14	01-Jul-13	23-Jul-13	743	$67,018
3AAT&TUTUTOH521(	Owner Install and Testing OH - 52 (Fiber Optic) 111+45 to 112+05	20	24-Jul-13	20-Aug-13	948	$0
OH - 14 (Fiber Optic) 870+40 to 889+00		37	01-Jul-13	20-Aug-13	347	$102,399
3AAT&TUTUTOH141(	Utility Construction / Relocation OH - 14 (Fiber Optic) 870+40 to 889+00	14	01-Jul-13	23-Jul-13	265	$102,399
3AAT&TUTUTOH141(	Owner Install and Testing OH - 14 (Fiber Optic) 870+40 to 889+00	20	24-Jul-13	20-Aug-13	333	$0
OH - 31 (Fiber Optic) 766+60 to 771+40		35	01-Jul-13	16-Aug-13	435	$27,527
3AAT&TUTUTOH311(	Utility Construction / Relocation OH - 31 (Fiber Optic) 766+60 to 771+40	12	01-Jul-13	19-Jul-13	330	$27,527
3AAT&TUTUTOH311(	Owner Install and Testing OH - 31 (Fiber Optic) 766+60 to 771+40	20	22-Jul-13	16-Aug-13	415	$0
OH - 37 (Fiber Optic) 727+50 to 729+80		39	01-Jul-13	22-Aug-13	264	$66,064
3AAT&TUTUTOH371(	Utility Construction / Relocation OH - 37 (Fiber Optic) 727+50 to 729+80	15	01-Jul-13	25-Jul-13	200	$66,064
3AAT&TUTUTOH371(	Owner Install and Testing OH - 37 (Fiber Optic) 727+50 to 729+80	20	26-Jul-13	22-Aug-13	253	$0
OH - 10 (Fiber Optic) 908+00 to 915+00		35	01-Jul-13	16-Aug-13	349	$22,021
3AAT&TUTUTOH101(	Utility Construction / Relocation OH - 10 (Fiber Optic) 908+00 to 915+00	12	01-Jul-13	19-Jul-13	267	$22,021
3AAT&TUTUTOH101(	Owner Install and Testing OH - 10 (Fiber Optic) 908+00 to 915+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 14 (Fiber Optic) 884+00 to 889+00		35	01-Jul-13	16-Aug-13	349	$30,316
3AAT&TUTUTOH141(	Utility Construction / Relocation OH - 14 (Fiber Optic) 884+00 to 889+00	12	01-Jul-13	19-Jul-13	267	$30,316
3AAT&TUTUTOH141(	Owner Install and Testing OH - 14 (Fiber Optic) 884+00 to 889+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 17 (Fiber Optic) 868+20 to 869+20		35	01-Jul-13	16-Aug-13	295	$13,800
3AAT&TUTUTOH171(	Utility Construction / Relocation OH - 17 (Fiber Optic) 868+20 to 869+20	12	01-Jul-13	19-Jul-13	225	$13,800
3AAT&TUTUTOH171(	Owner Install and Testing OH - 17 (Fiber Optic) 868+20 to 869+20	20	22-Jul-13	16-Aug-13	283	$0
OH - 43 (Fiber Optic) 766+40 to 766+40		35	01-Jul-13	16-Aug-13	268	$34,427
3AAT&TUTUTOH431(	Utility Construction / Relocation OH - 43 (Fiber Optic) 766+40 to 766+40	12	01-Jul-13	19-Jul-13	203	$34,427
3AAT&TUTUTOH431(	Owner Install and Testing OH - 43 (Fiber Optic) 766+40 to 766+40	20	22-Jul-13	16-Aug-13	257	$0
FO1 - 01 (Fiber Optic) 869+20 to 869+37		39	01-Jul-13	22-Aug-13	291	$111,574

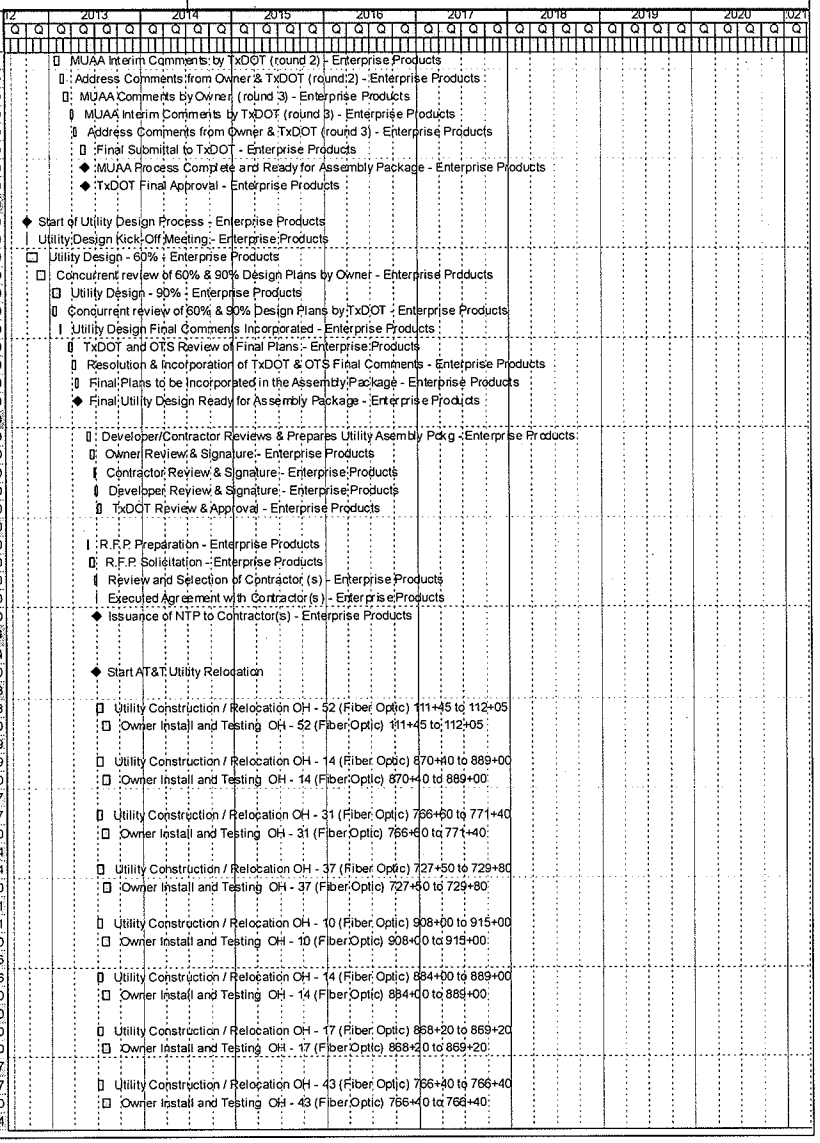

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AAT&TUTUTFO1110	Utility Construction / Relocation FO1 - 01 (Fiber Optic) 869+20 to 869+37	15	01-Jul-13	25-Jul-13	222	$111,574
3AAT&TUTUTFO1110	Owner Install and Testing FO1 - 01 (Fiber Optic) 869+20 to 869+37	20	26-Jul-13	22-Aug-13	279	$0
FO1 - 03 (Fiber Optic) 869+35 to 870+45		35	01-Jul-13	16-Aug-13	349	$16,149
3AAT&TUTUTFO1310	Utility Construction / Relocation FO1 - 03 (Fiber Optic) 869+35 to 870+45	12	01-Jul-13	19-Jul-13	267	$16,149
3AAT&TUTUTFO1310	Owner Install and Testing FO1 - 03 (Fiber Optic) 869+35 to 870+45	20	22-Jul-13	16-Aug-13	335	$0
OH - 10 (Telephone) 908+00 to 916+00		35	01-Jul-13	16-Aug-13	349	$8,295
3AAT&TUTUTOH1010	Utility Construction / Relocation OH - 10 (Telephone) 908+00 to 916+00	12	01-Jul-13	19-Jul-13	267	$8,295
3AAT&TUTUTOH1010	Owner Install and Testing OH - 10 (Telephone) 908+00 to 916+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 14 (Telephone) 884+00 to 889+00		35	01-Jul-13	16-Aug-13	349	$15,121
3AAT&TUTUTOH1410	Utility Construction / Relocation OH - 14 (Telephone) 884+00 to 889+00	12	01-Jul-13	19-Jul-13	267	$15,121
3AAT&TUTUTOH1410	Owner Install and Testing OH - 14 (Telephone) 884+00 to 889+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 25 (Telephone) 793+30 to 796+05		35	01-Jul-13	16-Aug-13	387	$7,194
3AAT&TUTUTOH2510	Utility Construction / Relocation OH - 25 (Telephone) 793+30 to 796+05	12	01-Jul-13	19-Jul-13	294	$7,194
3AAT&TUTUTOH2510	Owner Install and Testing OH - 25 (Telephone) 793+30 to 796+05	20	22-Jul-13	16-Aug-13	368	$0
OH - 27 (Telephone) 788+40 to 796+00		36	01-Jul-13	19-Aug-13	386	$26,132
3AAT&TUTUTOH2710	Utility Construction / Relocation OH - 27 (Telephone) 788+40 to 796+00	13	01-Jul-13	22-Jul-13	293	$26,132
3AAT&TUTUTOH2710	Owner Install and Testing OH - 27 (Telephone) 788+40 to 796+00	20	23-Jul-13	19-Aug-13	367	$0
OH - 31 (Telephone) 766+60 to 771+40		35	01-Jul-13	16-Aug-13	284	$13,800
3AAT&TUTUTOH3110	Utility Construction / Relocation OH - 31 (Telephone) 766+60 to 771+40	12	01-Jul-13	19-Jul-13	216	$13,800
3AAT&TUTUTOH3110	Owner Install and Testing OH - 31 (Telephone) 766+60 to 771+40	20	22-Jul-13	16-Aug-13	272	$0
OH - 32 (Telephone) 761+10 to 763+25		35	01-Jul-13	16-Aug-13	550	$6,313
3AAT&TUTUTOH3210	Utility Construction / Relocation OH - 32 (Telephone) 761+10 to 763+25	12	01-Jul-13	19-Jul-13	417	$6,313
3AAT&TUTUTOH3210	Owner Install and Testing OH - 32 (Telephone) 761+10 to 763+25	20	22-Jul-13	16-Aug-13	527	$0
OH - 37 (Telephone) 727+50 to 729+80		35	01-Jul-13	16-Aug-13	293	$17,727
3AAT&TUTUTOH3710	Utility Construction / Relocation OH - 37 (Telephone) 727+50 to 729+80	12	01-Jul-13	19-Jul-13	224	$17,727
3AAT&TUTUTOH3710	Owner Install and Testing OH - 37 (Telephone) 727+50 to 729+80	20	22-Jul-13	16-Aug-13	281	$0
OH - 40 (Telephone) 724+80 to 729+00		35	01-Jul-13	16-Aug-13	293	$18,204
3AAT&TUTUTOH4010	Utility Construction / Relocation OH - 40 (Telephone) 724+80 to 729+00	12	01-Jul-13	19-Jul-13	224	$18,204
3AAT&TUTUTOH4010	Owner Install and Testing OH - 40 (Telephone) 724+80 to 729+00	20	22-Jul-13	16-Aug-13	281	$0
OH - 43 (Telephone) 766+40 to 766+40		35	01-Jul-13	16-Aug-13	307	$17,213
3AAT&TUTUTOH4310	Utility Construction / Relocation OH - 43 (Telephone) 766+40 to 766+40	12	01-Jul-13	19-Jul-13	235	$17,213
3AAT&TUTUTOH4310	Owner Install and Testing OH - 43 (Telephone) 766+40 to 766+40	20	22-Jul-13	16-Aug-13	295	$0
OH - 13 (Telephone) 916+00 to 917+80		35	01-Jul-13	16-Aug-13	349	$8,809
3AAT&TUTUTOH1310	Utility Construction / Relocation OH - 13 (Telephone) 916+00 to 917+80	12	01-Jul-13	19-Jul-13	267	$8,809
3AAT&TUTUTOH1310	Owner Install and Testing OH - 13 (Telephone) 916+00 to 917+80	20	22-Jul-13	16-Aug-13	335	$0
T1 - 02 (Telephone) 915+00 to 915+70		35	01-Jul-13	16-Aug-13	349	$0
3AAT&TUTUTT121000	Utility Construction / Relocation T1 - 02 (Telephone) 915+00 to 915+70	12	01-Jul-13	19-Jul-13	267	$0
3AAT&TUTUTT121010	Owner Install and Testing T1 - 02 (Telephone) 915+00 to 915+70	20	22-Jul-13	16-Aug-13	335	$0
T1 - 03 (Telephone) 862+90 to 888+00		57	01-Jul-13	17-Sep-13	327	$658,362
3AAT&TUTUTT131000	Utility Construction / Relocation T1 - 03 (Telephone) 862+90 to 888+00	30	01-Jul-13	19-Aug-13	249	$658,362
3AAT&TUTUTT131010	Owner Install and Testing T1 - 03 (Telephone) 862+90 to 888+00	20	20-Aug-13	17-Sep-13	314	$0
T1 - 04 (Telephone) 886+00 to 888+00		42	01-Jul-13	27-Aug-13	342	$146,808
3AAT&TUTUTT141000	Utility Construction / Relocation T1 - 04 (Telephone) 886+00 to 888+00	18	01-Jul-13	30-Jul-13	261	$146,808
3AAT&TUTUTT141010	Owner Install and Testing T1 - 04 (Telephone) 886+00 to 888+00	20	31-Jul-13	27-Aug-13	328	$0
T1 - 05 (Telephone) 865+80 to 886+00		51	01-Jul-13	09-Sep-13	279	$217,937
3AAT&TUTUTT151000	Utility Construction / Relocation T1 - 05 (Telephone) 865+80 to 886+00	25	01-Jul-13	09-Aug-13	212	$217,937
3AAT&TUTUTT151010	Owner Install and Testing T1 - 05 (Telephone) 865+80 to 886+00	20	12-Aug-13	09-Sep-13	268	$0
T1 - 06 (Telephone) 872+10 to 873+00		35	01-Jul-13	16-Aug-13	349	$0
3AAT&TUTUTT161000	Utility Construction / Relocation T1 - 06 (Telephone) 872+10 to 873+00	12	01-Jul-13	19-Jul-13	267	$0
3AAT&TUTUTT161010	Owner Install and Testing T1 - 06 (Telephone) 872+10 to 873+00	20	22-Jul-13	16-Aug-13	335	$0
T1 - 07 (Telephone) 833+35 to 838+85		48	01-Jul-13	04-Sep-13	746	$250,657
3AAT&TUTUTT171000	Utility Construction / Relocation T1 - 07 (Telephone) 833+35 to 838+85	22	01-Jul-13	06-Aug-13	558	$250,657
3AAT&TUTUTT171010	Owner Install and Testing T1 - 07 (Telephone) 833+35 to 838+85	20	07-Aug-13	04-Sep-13	715	$0
T1 - 08 (Telephone) 763+00 to 766+50		37	01-Jul-13	20-Aug-13	433	$45,878
3AAT&TUTUTT181000	Utility Construction / Relocation T1 - 08 (Telephone) 763+00 to 766+50	14	01-Jul-13	23-Jul-13	328	$45,878
3AAT&TUTUTT181010	Owner Install and Testing T1 - 08 (Telephone) 763+00 to 766+50	20	24-Jul-13	20-Aug-13	413	$0
T1 - 09 (Telephone) 755+50 to 758+30		37	01-Jul-13	20-Aug-13	433	$45,878
3AAT&TUTUTT191000	Utility Construction / Relocation T1 - 09 (Telephone) 755+50 to 758+30	14	01-Jul-13	23-Jul-13	328	$45,878
3AAT&TUTUTT191010	Owner Install and Testing T1 - 09 (Telephone) 755+50 to 758+30	20	24-Jul-13	20-Aug-13	413	$0
T1 - 11 (Telephone) 727+20 to 729+60		41	01-Jul-13	26-Aug-13	689	$143,872

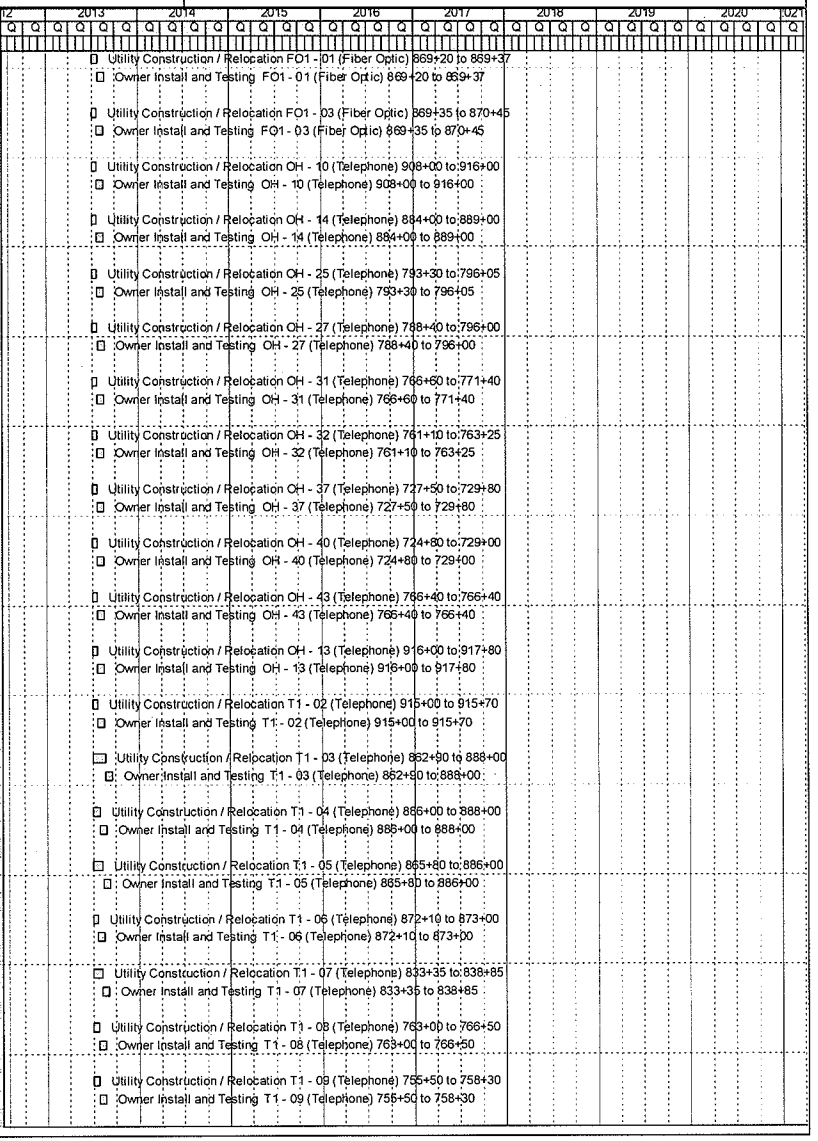

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AAT&TUTUTT11110(	Utility Construction / Relocation T1 - 11 (Telephone) 727+20 to 729+60	17	01-Jul-13	29-Jul-13	519	$143,872
3AAT&TUTUTT11110*	Owner Install and Testing T1 - 11 (Telephone) 727+20 to 729+60	20	30-Jul-13	26-Aug-13	659	$0
Atmos						
3AATMOMSUT1000	Start Atmos Utility Relocation	0	06-Jul-13		377	$0
G1 - 03 (Gas) 903+50 to 908+00		35	09-Jul-13	26-Aug-13	289	$0
3AATMOUTUTG1310(	Utility Construction / Relocation G1 - 03 (Gas) 903+50 to 908+00	13	09-Jul-13	29-Jul-13	220	$0
3AATMOUTUTG1310*	Owner Install and Testing G1 - 03 (Gas) 903+50 to 908+00	20	30-Jul-13	26-Aug-13	277	$0
G1 - 02 (Gas) 911+20 to 916+00		34	09-Jul-13	23-Aug-13	344	$49,401
3AATMOUTUTG1210(	Utility Construction / Relocation G1 - 02 (Gas) 911+20 to 916+00	12	09-Jul-13	26-Jul-13	263	$49,401
3AATMOUTUTG1210*	Owner Install and Testing G1 - 02 (Gas) 911+20 to 916+00	20	29-Jul-13	23-Aug-13	330	$0
G1 - 09 (Gas) 875+30 to 875+80		34	09-Jul-13	23-Aug-13	344	$0
3AATMOUTUTG1910(	Utility Construction / Relocation G1 - 09 (Gas) 875+30 to 875+80	12	09-Jul-13	26-Jul-13	263	$0
3AATMOUTUTG1910*	Owner Install and Testing G1 - 09 (Gas) 875+30 to 875+80	20	29-Jul-13	23-Aug-13	330	$0
G1 - 10 (Gas) 866+30 to 867+00		34	09-Jul-13	23-Aug-13	344	$0
3AATMOUTUTG1101(	Utility Construction / Relocation G1 - 10 (Gas) 866+30 to 867+00	12	09-Jul-13	26-Jul-13	263	$0
3AATMOUTUTG1101*	Owner Install and Testing G1 - 10 (Gas) 866+30 to 867+00	20	29-Jul-13	23-Aug-13	330	$0
G1 - 11 (Gas) 861+30 to 864+30		36	09-Jul-13	27-Aug-13	342	$47,272
3AATMOUTUTG1111(	Utility Construction / Relocation G1 - 11 (Gas) 861+30 to 864+30	14	09-Jul-13	30-Jul-13	261	$47,272
3AATMOUTUTG1111*	Owner Install and Testing G1 - 11 (Gas) 861+30 to 864+30	20	31-Jul-13	27-Aug-13	328	$0
G1 - 17 (Gas) 744+50 to 758+40		38	09-Jul-13	29-Aug-13	426	$114,694
3AATMOUTUTG1171(	Utility Construction / Relocation G1 - 17 (Gas) 744+50 to 758+40	16	09-Jul-13	01-Aug-13	322	$114,694
3AATMOUTUTG1171*	Owner Install and Testing G1 - 17 (Gas) 744+50 to 758+40	20	02-Aug-13	29-Aug-13	406	$0
G1 - 04 (Gas) 903+50 to 907+50		42	09-Jul-13	04-Sep-13	956	$147,763
3AATMOUTUTG1410(	Utility Construction / Relocation G1 - 04 (Gas) 903+50 to 907+50	18	09-Jul-13	06-Aug-13	720	$147,763
3AATMOUTUTG1410*	Owner Install and Testing G1 - 04 (Gas) 903+50 to 907+50	20	07-Aug-13	04-Sep-13	918	$0
G1 - 06 (Gas) 869+00 to 887+20		59	09-Jul-13	27-Sep-13	319	$428,387
3AATMOUTUTG1610(	Utility Construction / Relocation G1 - 06 (Gas) 869+00 to 887+20	33	09-Jul-13	29-Aug-13	242	$428,387
3AATMOUTUTG1610*	Owner Install and Testing G1 - 06 (Gas) 869+00 to 887+20	20	30-Aug-13	27-Sep-13	306	$0
G1 - 07 (Gas) 876+50 to 885+10		39	09-Jul-13	30-Aug-13	285	$135,945
3AATMOUTUTG1710(	Utility Construction / Relocation G1 - 07 (Gas) 876+50 to 885+10	17	09-Jul-13	02-Aug-13	216	$135,945
3AATMOUTUTG1710*	Owner Install and Testing G1 - 07 (Gas) 876+50 to 885+10	20	05-Aug-13	30-Aug-13	273	$0
G1 - 08 (Gas) 876+10 to 876+50		34	09-Jul-13	23-Aug-13	290	$0
3AATMOUTUTG1810(	Utility Construction / Relocation G1 - 08 (Gas) 876+10 to 876+50	12	09-Jul-13	26-Jul-13	221	$0
3AATMOUTUTG1810*	Owner Install and Testing G1 - 08 (Gas) 876+10 to 876+50	20	29-Jul-13	23-Aug-13	278	$0
G1 - 12 (Gas) 788+60 to 794+00		35	09-Jul-13	26-Aug-13	381	$48,961
3AATMOUTUTG1121(	Utility Construction / Relocation G1 - 12 (Gas) 788+60 to 794+00	13	09-Jul-13	29-Jul-13	289	$48,961
3AATMOUTUTG1121*	Owner Install and Testing G1 - 12 (Gas) 788+60 to 794+00	20	30-Jul-13	26-Aug-13	362	$0
G1 - 13 (Gas) 758+40 to 783+50		45	09-Jul-13	09-Sep-13	419	$242,381
3AATMOUTUTG1131(	Utility Construction / Relocation G1 - 13 (Gas) 758+40 to 783+50	21	09-Jul-13	09-Aug-13	317	$242,381
3AATMOUTUTG1131*	Owner Install and Testing G1 - 13 (Gas) 758+40 to 783+50	20	12-Aug-13	09-Sep-13	400	$0
G1 - 16 (Gas) 745+80 to 761+00		39	09-Jul-13	30-Aug-13	590	$141,156
3AATMOUTUTG1161(	Utility Construction / Relocation G1 - 16 (Gas) 745+80 to 761+00	17	09-Jul-13	02-Aug-13	444	$141,156
3AATMOUTUTG1161*	Owner Install and Testing G1 - 16 (Gas) 745+80 to 761+00	20	05-Aug-13	30-Aug-13	565	$0
G1 - 18 (Gas) 758+40 to 758+40		35	09-Jul-13	26-Aug-13	269	$42,721
3AATMOUTUTG1181(	Utility Construction / Relocation G1 - 18 (Gas) 758+40 to 758+40	13	09-Jul-13	29-Jul-13	203	$42,721
3AATMOUTUTG1181*	Owner Install and Testing G1 - 18 (Gas) 758+40 to 758+40	20	30-Jul-13	26-Aug-13	257	$0
G1 - 15 (Gas) 766+80 to 766+80		34	09-Jul-13	23-Aug-13	430	$0
3AATMOUTUTG1151(	Utility Construction / Relocation G1 - 15 (Gas) 766+80 to 766+80	12	09-Jul-13	26-Jul-13	326	$0
3AATMOUTUTG1151*	Owner Install and Testing G1 - 15 (Gas) 766+80 to 766+80	20	29-Jul-13	23-Aug-13	410	$0
G1 - 14 (Gas) 776+70 to 776+70		34	09-Jul-13	23-Aug-13	382	$0
3AATMOUTUTG1141(	Utility Construction / Relocation G1 - 14 (Gas) 776+70 to 776+70	12	09-Jul-13	26-Jul-13	290	$0
3AATMOUTUTG1141*	Owner Install and Testing G1 - 14 (Gas) 776+70 to 776+70	20	29-Jul-13	23-Aug-13	363	$0
Barnett Gathering		43	20-Jul-13	18-Sep-13	537	$222,415
ICMSUT1001	Start Barnett Gathering Utility Relocation	0	20-Jul-13		465	$0
G4 - 01 (Gas) 745+90 to 745+90		35	22-Jul-13	06-Sep-13	545	$12,185
ICUTUTG411000	Utility Construction / Relocation G4 - 01 (Gas) 745+90 to 745+90	12	22-Jul-13	08-Aug-13	413	$12,185
ICUTUTG411010	Owner Install and Testing G4 - 01 (Gas) 745+90 to 745+90	20	09-Aug-13	06-Sep-13	523	$0
G4 - 02 (Gas) 608+05/35W to 690+90/820		43	22-Jul-13	18-Sep-13	338	$210,230
ICUTUTG421000	Utility Construction / Relocation G4 - 02 (Gas) 608+05/35W to 690+90/820	19	22-Jul-13	20-Aug-13	254	$210,230
ICUTUTG421010	Owner Install and Testing G4 - 02 (Gas) 608+05/35W to 690+90/820	20	21-Aug-13	18-Sep-13	321	$0

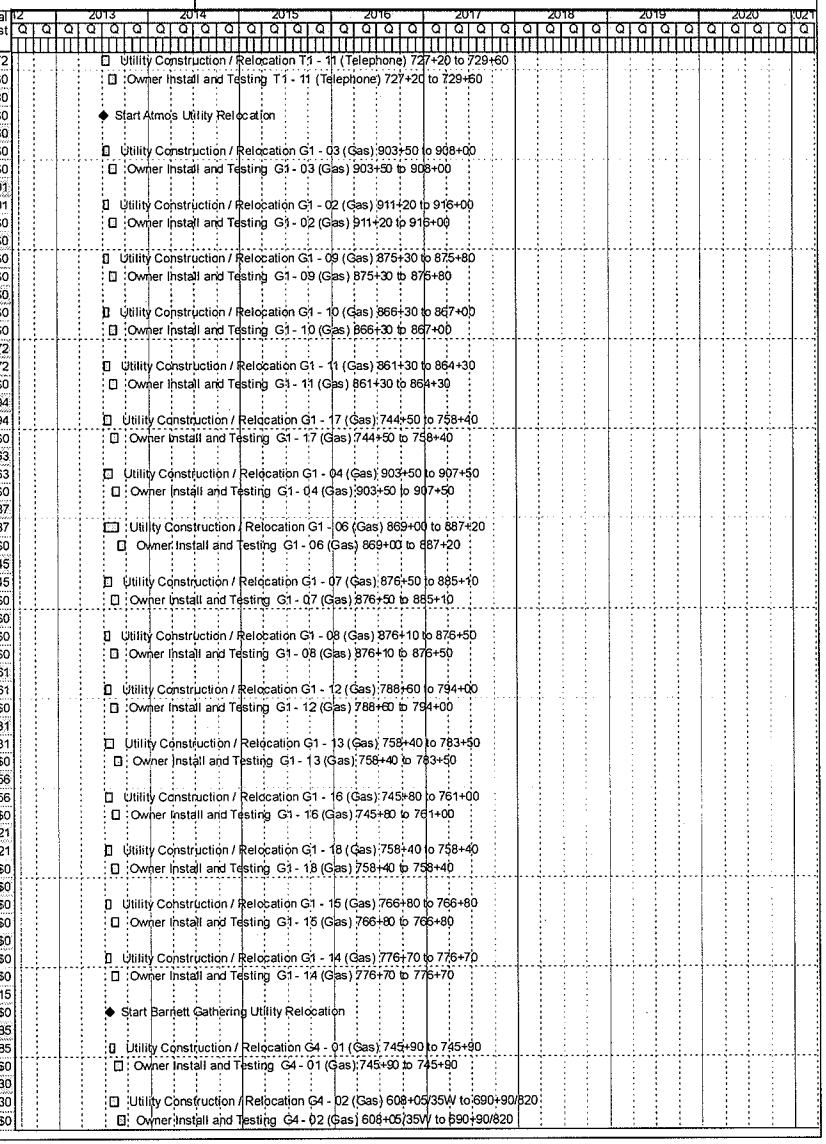

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Broadwing/Level 3		43	06-Jul-13	04-Sep-13	276	$135,064
3ALVL3MSUT100	Start Broadwing / Level 3 Utility Relocation	0	06-Jul-13		389	$0
FO3 - 01 (Fiber Optic) 809+00 to 815+50		42	09-Jul-13	04-Sep-13	276	$135,064
3AUTUTFO311000	Utility Construction / Relocation FO3 - 01 (Fiber Optic) 809+00 to 815+50	18	09-Jul-13	06-Aug-13	210	$135,064
3AUTUTFO311010	Owner Install and Testing FO3 - 01 (Fiber Optic) 809+00 to 815+50	20	07-Aug-13	04-Sep-13	265	$0
Charter Communication		37	06-Jul-13	27-Aug-13	983	$258,420
3ACHARMSUT100	Start Charter Communication Utility Relocation	0	06-Jul-13		380	$0
OH - 13 (Cable TV) 916+00 to 917+80		34	09-Jul-13	23-Aug-13	344	$8,074
3AUTUTOH131000	Utility Construction / Relocation OH - 13 (Cable TV) 916+00 to 917+80	12	09-Jul-13	26-Jul-13	263	$8,074
3AUTUTOH131010	Owner Install and Testing OH - 13 (Cable TV) 916+00 to 917+80	20	29-Jul-13	23-Aug-13	330	$0
OH - 14 (Cable TV) 870+40 to 889+00		36	09-Jul-13	27-Aug-13	342	$48,153
3AUTUTOH141005	Utility Construction / Relocation OH - 14 (Cable TV) 870+40 to 889+00	14	09-Jul-13	30-Jul-13	261	$48,153
3AUTUTOH141015	Owner Install and Testing OH - 14 (Cable TV) 870+40 to 889+00	20	31-Jul-13	27-Aug-13	328	$0
OH - 18 (Cable TV) 860+50 to 866+00		36	09-Jul-13	27-Aug-13	342	$55,714
3AUTUTOH181016	Utility Construction / Relocation OH - 18 (Cable TV) 860+50 to 866+00	14	09-Jul-13	30-Jul-13	261	$55,714
3AUTUTOH181015	Owner Install and Testing OH - 18 (Cable TV) 860+50 to 866+00	20	31-Jul-13	27-Aug-13	328	$0
OH - 52 (Cable TV) 111+45 to 112+05		35	09-Jul-13	26-Aug-13	984	$44,887
3AUTUTOH521005	Utility Construction / Relocation OH - 52 (Cable TV) 111+45 to 112+05	13	09-Jul-13	29-Jul-13	740	$44,887
3AUTUTOH521015	Owner Install and Testing OH - 52 (Cable TV) 111+45 to 112+05	20	30-Jul-13	26-Aug-13	944	$0
OH - 31 (Fiber Optic) 766+30 to 771+00		34	09-Jul-13	23-Aug-13	430	$26,866
3AUTUTOH311005	Utility Construction / Relocation OH - 31 (Fiber Optic) 766+30 to 771+00	12	09-Jul-13	26-Jul-13	326	$26,866
3AUTUTOH311015	Owner Install and Testing OH - 31 (Fiber Optic) 766+30 to 771+00	20	29-Jul-13	23-Aug-13	410	$0
OH - 43 (Fiber Optic) 766+30 to 766+30		34	09-Jul-13	23-Aug-13	270	$31,637
3AUTUTOH431000	Utility Construction / Relocation OH - 43 (Fiber Optic) 766+30 to 766+30	12	09-Jul-13	26-Jul-13	204	$31,637
3AUTUTOH431010	Owner Install and Testing OH - 43 (Fiber Optic) 766+30 to 766+30	20	29-Jul-13	23-Aug-13	258	$0
OH - 9 (Cable TV) 902+50 to 913+00		35	09-Jul-13	26-Aug-13	289	$30,389
3AUTUTOH91006	Utility Construction / Relocation OH - 9 (Cable TV) 902+50 to 913+00	13	09-Jul-13	29-Jul-13	220	$30,389
3AUTUTOH91005	Owner Install and Testing OH - 9 (Cable TV) 902+50 to 913+00	20	30-Jul-13	26-Aug-13	277	$0
OH - 10 (Cable TV) 908+00 to 916+00		34	09-Jul-13	23-Aug-13	344	$12,699
3AUTUTOH101005	Utility Construction / Relocation OH - 10 (Cable TV) 908+00 to 916+00	12	09-Jul-13	26-Jul-13	263	$12,699
3AUTUTOH101015	Owner Install and Testing OH - 10 (Cable TV) 908+00 to 916+00	20	29-Jul-13	23-Aug-13	330	$0
Chevron		42	20-Jul-13	17-Sep-13	365	$168,830
3ACHEVMSUT1000	Start Chevron Utility Relocation	0	20-Jul-13		507	$0
PL5 - 01 (Gas) 784+00 to 810+00		42	22-Jul-13	17-Sep-13	365	$168,830
3AUTUTPL511000	Utility Construction / Relocation PL5 - 01 (Gas) 784+00 to 810+00	18	22-Jul-13	19-Aug-13	276	$168,830
3AUTUTPL511010	Owner Install and Testing PL5 - 01 (Gas) 784+00 to 810+00	20	20-Aug-13	17-Sep-13	347	$0
City of Fort Worth		73	28-Jun-13	08-Oct-13	953	$2,761,925
3ACFTWMSUT1000	Start City of Fort Worth Utility Relocation	0	28-Jun-13		364	$0
W1 - 22 (Water) 771+10 to 771+10		35	01-Jul-13	16-Aug-13	268	$0
3AUTUTW1221000	Utility Construction / Relocation W1 - 22 (Water) 771+10 to 771+10	12	01-Jul-13	19-Jul-13	203	$0
3AUTUTW1221010	Owner Install and Testing W1 - 22 (Water) 771+10 to 771+10	20	22-Jul-13	16-Aug-13	257	$0
W1 - 23 (Water) 766+80 to 766+80		35	01-Jul-13	16-Aug-13	268	$0
3AUTUTW1231000	Utility Construction / Relocation W1 - 23 (Water) 766+80 to 766+80	12	01-Jul-13	19-Jul-13	203	$0
3AUTUTW1231010	Owner Install and Testing W1 - 23 (Water) 766+80 to 766+80	20	22-Jul-13	16-Aug-13	257	$0
W1 - 25 (Water) 758+40 to 758+40		35	01-Jul-13	16-Aug-13	268	$0
3AUTUTW1251000	Utility Construction / Relocation W1 - 25 (Water) 758+40 to 758+40	12	01-Jul-13	19-Jul-13	203	$0
3AUTUTW1251010	Owner Install and Testing W1 - 25 (Water) 758+40 to 758+40	20	22-Jul-13	16-Aug-13	257	$0
W1 - 05 (Water) 875+00 to 887+30		48	01-Jul-13	04-Sep-13	336	$74,102
3AUTUTW151000	Utility Construction / Relocation W1 - 05 (Water) 875+00 to 887+30	22	01-Jul-13	06-Aug-13	257	$74,102
3AUTUTW151010	Owner Install and Testing W1 - 05 (Water) 875+00 to 887+30	20	07-Aug-13	04-Sep-13	323	$0
W1 - 13 (Water) 866+30 to 866+90		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTW1131000	Utility Construction / Relocation W1 - 13 (Water) 866+30 to 866+90	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTW1131010	Owner Install and Testing W1 - 13 (Water) 866+30 to 866+90	20	22-Jul-13	16-Aug-13	335	$0
W1 - 14 (Water) 863+80 to 864+30		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTW1141000	Utility Construction / Relocation W1 - 14 (Water) 863+80 to 864+30	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTW1141010	Owner Install and Testing W1 - 14 (Water) 863+80 to 864+30	20	22-Jul-13	16-Aug-13	335	$0
W1 - 20 (Water) 741+00 to 783+50		72	01-Jul-13	08-Oct-13	398	$233,168
3AUTUTW1201000	Utility Construction / Relocation W1 - 20 (Water) 741+00 to 783+50	43	01-Jul-13	10-Sep-13	299	$233,168
3AUTUTW1201010	Owner Install and Testing W1 - 20 (Water) 741+00 to 783+50	20	11-Sep-13	08-Oct-13	379	$0
W1 - 21 (Water) 776+30 to 776+30		35	01-Jul-13	16-Aug-13	387	$0

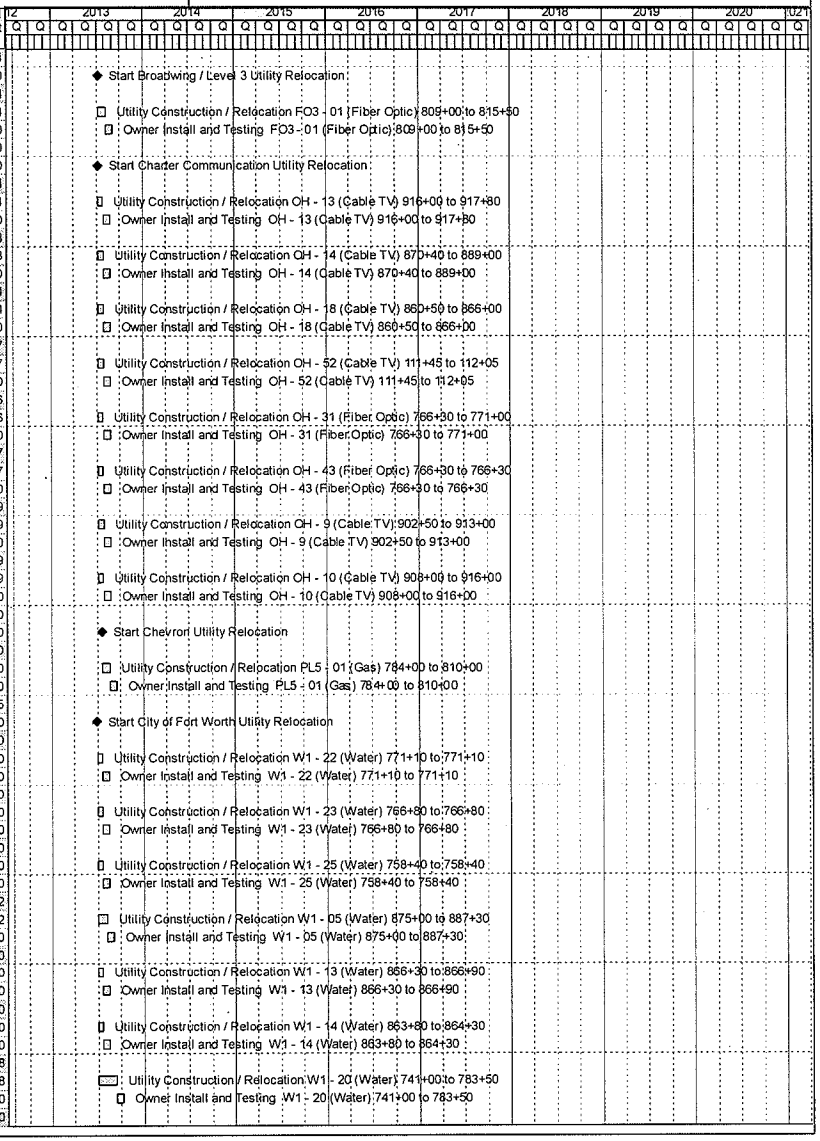

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AUTUTW1211000	Utility Construction / Relocation W1 - 21 (Water) 776+30 to 776+30	12	01-Jul-13	19-Jul-13	294	$0
3AUTUTW1211010	Owner Install and Testing W1 - 21 (Water) 776+30 to 776+30	20	22-Jul-13	16-Aug-13	368	$0
W1 - 27 (Water) 742+00 to 743+00		35	01-Jul-13	16-Aug-13	600	$5,505
3AUTUTW1271000	Utility Construction / Relocation W1 - 27 (Water) 742+00 to 743+00	12	01-Jul-13	19-Jul-13	453	$5,505
3AUTUTW1271010	Owner Install and Testing W1 - 27 (Water) 742+00 to 743+00	20	22-Jul-13	16-Aug-13	575	$0
W1 - 28 (Water) 730+00 to 731+80		40	01-Jul-13	23-Aug-13	288	$53,842
3AUTUTW1281000	Utility Construction / Relocation W1 - 28 (Water) 730+00 to 731+80	16	01-Jul-13	26-Jul-13	220	$53,842
3AUTUTW1281010	Owner Install and Testing W1 - 28 (Water) 730+00 to 731+80	20	29-Jul-13	23-Aug-13	276	$0
W1 - 31 (Water) 680+50 to 681+40		35	01-Jul-13	16-Aug-13	268	$9,506
3AUTUTW1311000	Utility Construction / Relocation W1 - 31 (Water) 680+50 to 681+40	12	01-Jul-13	19-Jul-13	203	$9,506
3AUTUTW1311010	Owner Install and Testing W1 - 31 (Water) 680+50 to 681+40	20	22-Jul-13	16-Aug-13	257	$0
W1 - 07 (Water) 883+90 to 884+30		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTW171000	Utility Construction / Relocation W1 - 07 (Water) 883+90 to 884+30	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTW171010	Owner Install and Testing W1 - 07 (Water) 883+90 to 884+30	20	22-Jul-13	16-Aug-13	335	$0
W1 - 08 (Water) 881+10 to 881+50		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTW181000	Utility Construction / Relocation W1 - 08 (Water) 881+10 to 881+50	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTW181010	Owner Install and Testing W1 - 08 (Water) 881+10 to 881+50	20	22-Jul-13	16-Aug-13	335	$0
W1 - 09 (Water) 876+00 to 876+80		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTW191000	Utility Construction / Relocation W1 - 09 (Water) 876+00 to 876+80	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTW191010	Owner Install and Testing W1 - 09 (Water) 876+00 to 876+80	20	22-Jul-13	16-Aug-13	335	$0
W1 - 04 (Water) 885+10 to 888+00		41	01-Jul-13	26-Aug-13	259	$109,299
3AUTUTW141000	Utility Construction / Relocation W1 - 04 (Water) 885+10 to 888+00	17	01-Jul-13	29-Jul-13	195	$109,299
3AUTUTW141010	Owner Install and Testing W1 - 04 (Water) 885+10 to 888+00	20	30-Jul-13	26-Aug-13	248	$0
W1 - 06 (Water) 863+50 to 885+10		52	01-Jul-13	10-Sep-13	278	$177,271
3AUTUTW161000	Utility Construction / Relocation W1 - 06 (Water) 863+50 to 885+10	26	01-Jul-13	12-Aug-13	211	$177,271
3AUTUTW161010	Owner Install and Testing W1 - 06 (Water) 863+50 to 885+10	20	13-Aug-13	10-Sep-13	267	$0
W1 - 10 (Water) 860+40 to 875+00		48	01-Jul-13	04-Sep-13	336	$118,181
3AUTUTW1101000	Utility Construction / Relocation W1 - 10 (Water) 860+40 to 875+00	22	01-Jul-13	06-Aug-13	257	$118,181
3AUTUTW1101010	Owner Install and Testing W1 - 10 (Water) 860+40 to 875+00	20	07-Aug-13	04-Sep-13	323	$0
W1 - 11 (Water) 874+40 to 874+80		35	01-Jul-13	16-Aug-13	295	$0
3AUTUTW1111000	Utility Construction / Relocation W1 - 11 (Water) 874+40 to 874+80	12	01-Jul-13	19-Jul-13	225	$0
3AUTUTW1111010	Owner Install and Testing W1 - 11 (Water) 874+40 to 874+80	20	22-Jul-13	16-Aug-13	283	$0
W1 - 12 (Water) 869+50 to 868+00		36	01-Jul-13	19-Aug-13	294	$23,453
3AUTUTW1121000	Utility Construction / Relocation W1 - 12 (Water) 869+50 to 868+00	13	01-Jul-13	22-Jul-13	224	$23,453
3AUTUTW1121010	Owner Install and Testing W1 - 12 (Water) 869+50 to 868+00	20	23-Jul-13	19-Aug-13	282	$0
W1 - 26 (Water) 755+60 to 755+60		40	01-Jul-13	23-Aug-13	270	$78,102
3AUTUTW1261000	Utility Construction / Relocation W1 - 26 (Water) 755+60 to 755+60	16	01-Jul-13	26-Jul-13	204	$78,102
3AUTUTW1261010	Owner Install and Testing W1 - 26 (Water) 755+60 to 755+60	20	29-Jul-13	23-Aug-13	258	$0
W1 - 30 (Water) 681+40 to 686+40		39	01-Jul-13	22-Aug-13	596	$42,207
3AUTUTW1301000	Utility Construction / Relocation W1 - 30 (Water) 681+40 to 686+40	15	01-Jul-13	25-Jul-13	450	$42,207
3AUTUTW1301010	Owner Install and Testing W1 - 30 (Water) 681+40 to 686+40	20	26-Jul-13	22-Aug-13	571	$0
W1 - 56 (Water) 107+80 to 109+95		36	01-Jul-13	19-Aug-13	989	$18,571
3AUTUTW1561000	Utility Construction / Relocation W1 - 56 (Water) 107+80 to 109+95	13	01-Jul-13	22-Jul-13	744	$18,571
3AUTUTW1561010	Owner Install and Testing W1 - 56 (Water) 107+80 to 109+95	20	23-Jul-13	19-Aug-13	949	$0
W1 - 18 (Water) 785+70 to 796+40		42	01-Jul-13	27-Aug-13	380	$105,335
3AUTUTW1181000	Utility Construction / Relocation W1 - 18 (Water) 785+70 to 796+40	18	01-Jul-13	30-Jul-13	288	$105,335
3AUTUTW1181010	Owner Install and Testing W1 - 18 (Water) 785+70 to 796+40	20	31-Jul-13	27-Aug-13	361	$0
W1 - 19 (Water) 785+70 to 785+70		37	01-Jul-13	20-Aug-13	385	$63,348
3AUTUTW1191000	Utility Construction / Relocation W1 - 19 (Water) 785+70 to 785+70	14	01-Jul-13	23-Jul-13	292	$63,348
3AUTUTW1191010	Owner Install and Testing W1 - 19 (Water) 785+70 to 785+70	20	24-Jul-13	20-Aug-13	366	$0
W1 - 17 (Water) 801+40 to 801+40		37	01-Jul-13	20-Aug-13	350	$69,220
3AUTUTW1171000	Utility Construction / Relocation W1 - 17 (Water) 801+40 to 801+40	14	01-Jul-13	23-Jul-13	269	$69,220
3AUTUTW1171010	Owner Install and Testing W1 - 17 (Water) 801+40 to 801+40	20	24-Jul-13	20-Aug-13	336	$0
WW1 - 04 (Wastewater) 925+00 to 926+10		36	01-Jul-13	19-Aug-13	534	$107,831
3AUTUTWW141000	Utility Construction / Relocation WW1 - 04 (Wastewater) 925+00 to 926+10	13	01-Jul-13	22-Jul-13	404	$107,831
3AUTUTWW141010	Owner Install and Testing WW1 - 04 (Wastewater) 925+00 to 926+10	20	23-Jul-13	19-Aug-13	512	$0
WW1 - 28 (Wastewater) 756+30 to 759+00		36	01-Jul-13	19-Aug-13	599	$18,204
3AUTUTWW1281000	Utility Construction / Relocation WW1 - 28 (Wastewater) 756+30 to 759+00	13	01-Jul-13	22-Jul-13	452	$18,204
3AUTUTWW1281010	Owner Install and Testing WW1 - 28 (Wastewater) 756+30 to 759+00	20	23-Jul-13	19-Aug-13	574	$0
WW1 - 06 (Wastewater) 911+20 to 921+00		41	01-Jul-13	26-Aug-13	343	$64,596

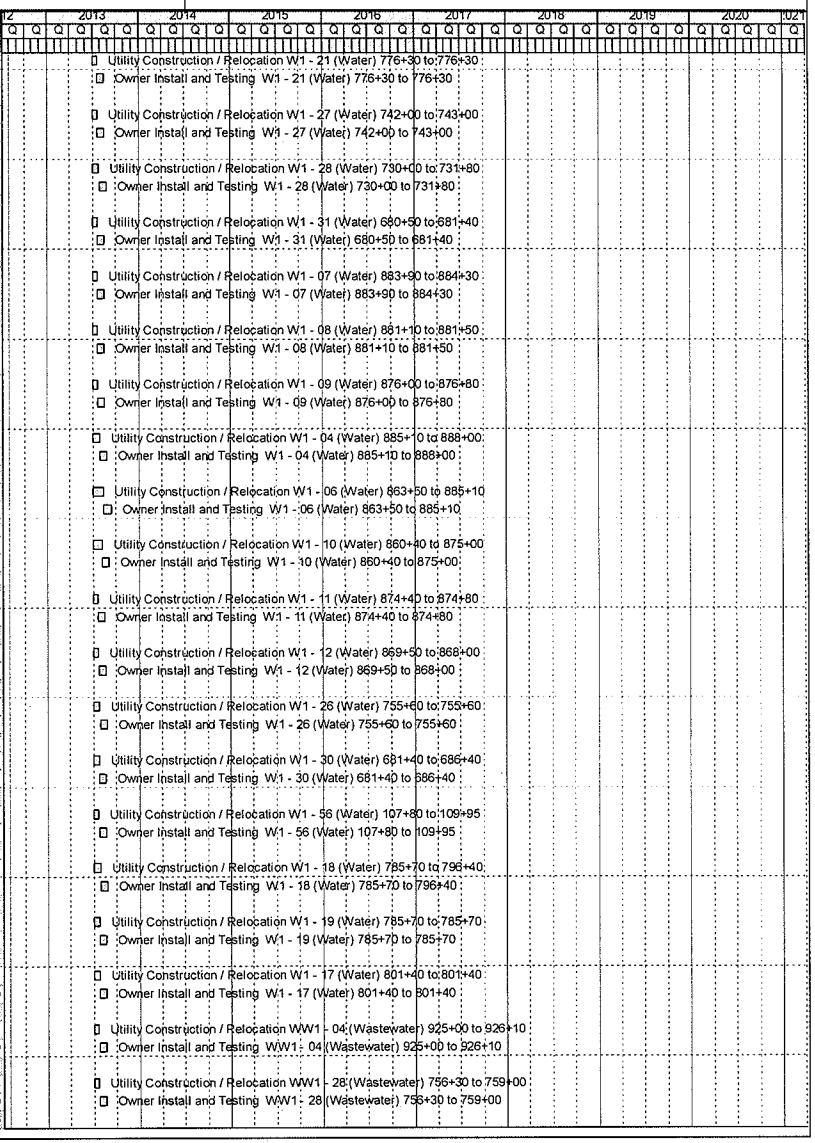

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AUTUTWW161000	Utility Construction / Relocation WW1 - 06 (Wastewater) 911+20 to 921+00	17	01-Jul-13	29-Jul-13	262	$64,596
3AUTUTWW161010	Owner Install and Testing WW1 - 06 (Wastewater) 911+20 to 921+00	20	30-Jul-13	26-Aug-13	329	$0
WW1 - 08 (Wastewater) 914+80 to 914+80		41	01-Jul-13	26-Aug-13	259	$91,608
3AUTUTWW181000	Utility Construction / Relocation WW1 - 08 (Wastewater) 914+80 to 914+80	17	01-Jul-13	29-Jul-13	195	$91,608
3AUTUTWW181010	Owner Install and Testing WW1 - 08 (Wastewater) 914+80 to 914+80	20	30-Jul-13	26-Aug-13	248	$0
WW1 - 11 (Wastewater) 862+00 to 889+70		57	01-Jul-13	17-Sep-13	327	$186,593
3AUTUTWW1111000	Utility Construction / Relocation WW1 - 11 (Wastewater) 862+00 to 889+70	30	01-Jul-13	19-Aug-13	249	$186,593
3AUTUTWW1111010	Owner Install and Testing WW1 - 11 (Wastewater) 862+00 to 889+70	20	20-Aug-13	17-Sep-13	314	$0
WW1 - 12 (Wastewater) 887+90 to 888+60		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTWW1121000	Utility Construction / Relocation WW1 - 12 (Wastewater) 887+90 to 888+60	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTWW1121010	Owner Install and Testing WW1 - 12 (Wastewater) 887+90 to 888+60	20	22-Jul-13	16-Aug-13	335	$0
WW1 - 13 (Wastewater) 875+50 to 875+80		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTWW1131000	Utility Construction / Relocation WW1 - 13 (Wastewater) 875+50 to 875+80	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTWW1131010	Owner Install and Testing WW1 - 13 (Wastewater) 875+50 to 875+80	20	22-Jul-13	16-Aug-13	335	$0
WW1 - 14 (Wastewater) 869+60 to 869+60		35	01-Jul-13	16-Aug-13	295	$7,854
3AUTUTWW1141000	Utility Construction / Relocation WW1 - 14 (Wastewater) 869+60 to 869+60	12	01-Jul-13	19-Jul-13	225	$7,854
3AUTUTWW1141010	Owner Install and Testing WW1 - 14 (Wastewater) 869+60 to 869+60	20	22-Jul-13	16-Aug-13	283	$0
WW1 - 16 (Wastewater) 867+60 to 868+10		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTWW1161000	Utility Construction / Relocation WW1 - 16 (Wastewater) 867+60 to 868+10	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTWW1161010	Owner Install and Testing WW1 - 16 (Wastewater) 867+60 to 868+10	20	22-Jul-13	16-Aug-13	335	$0
WW1 - 18 (Wastewater) 865+10 to 865+50		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTWW1181000	Utility Construction / Relocation WW1 - 18 (Wastewater) 865+10 to 865+50	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTWW1181010	Owner Install and Testing WW1 - 18 (Wastewater) 865+10 to 865+50	20	22-Jul-13	16-Aug-13	335	$0
WW1 - 20 (Wastewater) 805+00 to 806+20		41	01-Jul-13	26-Aug-13	283	$78,543
3AUTUTWW1201000	Utility Construction / Relocation WW1 - 20 (Wastewater) 805+00 to 806+20	17	01-Jul-13	29-Jul-13	215	$78,543
3AUTUTWW1201010	Owner Install and Testing WW1 - 20 (Wastewater) 805+00 to 806+20	20	30-Jul-13	26-Aug-13	271	$0
WW1 - 25 (Wastewater) 758+60 to 777+00		52	01-Jul-13	10-Sep-13	418	$143,505
3AUTUTWW1251000	Utility Construction / Relocation WW1 - 25 (Wastewater) 758+60 to 777+00	26	01-Jul-13	12-Aug-13	316	$143,505
3AUTUTWW1251010	Owner Install and Testing WW1 - 25 (Wastewater) 758+60 to 777+00	20	13-Aug-13	10-Sep-13	399	$0
WW1 - 26 (Wastewater) 776+60 to 776+60		35	01-Jul-13	16-Aug-13	387	$0
3AUTUTWW1261000	Utility Construction / Relocation WW1 - 26 (Wastewater) 776+60 to 776+60	12	01-Jul-13	19-Jul-13	294	$0
3AUTUTWW1261010	Owner Install and Testing WW1 - 26 (Wastewater) 776+60 to 776+60	20	22-Jul-13	16-Aug-13	368	$0
WW1 - 27 (Wastewater) 771+20 to 771+20		35	01-Jul-13	16-Aug-13	435	$0
3AUTUTWW1271000	Utility Construction / Relocation WW1 - 27 (Wastewater) 771+20 to 771+20	12	01-Jul-13	19-Jul-13	330	$0
3AUTUTWW1271010	Owner Install and Testing WW1 - 27 (Wastewater) 771+20 to 771+20	20	22-Jul-13	16-Aug-13	415	$0
WW1 - 29 (Wastewater) 744+50 to 753+50		44	01-Jul-13	29-Aug-13	541	$117,740
3AUTUTWW1291000	Utility Construction / Relocation WW1 - 29 (Wastewater) 744+50 to 753+50	20	01-Jul-13	01-Aug-13	409	$117,740
3AUTUTWW1291010	Owner Install and Testing WW1 - 29 (Wastewater) 744+50 to 753+50	20	02-Aug-13	29-Aug-13	518	$0
WW1 - 32 (Wastewater) 732+50 to 736+50		37	01-Jul-13	20-Aug-13	433	$28,701
3AUTUTWW1321000	Utility Construction / Relocation WW1 - 32 (Wastewater) 732+50 to 736+50	14	01-Jul-13	23-Jul-13	328	$28,701
3AUTUTWW1321010	Owner Install and Testing WW1 - 32 (Wastewater) 732+50 to 736+50	20	24-Jul-13	20-Aug-13	413	$0
WW1 - 21 (Wastewater) 794+00 to 795+10		35	01-Jul-13	16-Aug-13	387	$0
3AUTUTWW1211000	Utility Construction / Relocation WW1 - 21 (Wastewater) 794+00 to 795+10	12	01-Jul-13	19-Jul-13	294	$0
3AUTUTWW1211010	Owner Install and Testing WW1 - 21 (Wastewater) 794+00 to 795+10	20	22-Jul-13	16-Aug-13	368	$0
WW1 - 22 (Wastewater) 794+20 to 794+20		35	01-Jul-13	16-Aug-13	387	$0
3AUTUTWW1221000	Utility Construction / Relocation WW1 - 22 (Wastewater) 794+20 to 794+20	12	01-Jul-13	19-Jul-13	294	$0
3AUTUTWW1221010	Owner Install and Testing WW1 - 22 (Wastewater) 794+20 to 794+20	20	22-Jul-13	16-Aug-13	368	$0
WW1 - 35 (Wastewater) 674+55 to 695+00		40	01-Jul-13	23-Aug-13	568	$62,027
3AUTUTWW1351000	Utility Construction / Relocation WW1 - 35 (Wastewater) 674+55 to 695+00	16	01-Jul-13	26-Jul-13	430	$62,027
3AUTUTWW1351010	Owner Install and Testing WW1 - 35 (Wastewater) 674+55 to 695+00	20	29-Jul-13	23-Aug-13	545	$0
WW1 - 61 (Wastewater) 107+80 to 109+95		36	01-Jul-13	19-Aug-13	572	$19,526
3AUTUTWW1611000	Utility Construction / Relocation WW1 - 61 (Wastewater) 107+80 to 109+95	13	01-Jul-13	22-Jul-13	433	$19,526
3AUTUTWW1611010	Owner Install and Testing WW1 - 61 (Wastewater) 107+80 to 109+95	20	23-Jul-13	19-Aug-13	549	$0
WW1 - 03 (Wastewater) 924+80 to 926+30		41	01-Jul-13	26-Aug-13	529	$88,672
3AUTUTWW131000	Utility Construction / Relocation WW1 - 03 (Wastewater) 924+80 to 926+30	17	01-Jul-13	29-Jul-13	400	$88,672
3AUTUTWW131010	Owner Install and Testing WW1 - 03 (Wastewater) 924+80 to 926+30	20	30-Jul-13	26-Aug-13	507	$0
W1 - 33 (Water) 673+80 to 673+80		39	01-Jul-13	22-Aug-13	569	$123,466
3AUTUTW1331000	Utility Construction / Relocation W1 - 33 (Water) 673+80 to 673+80	15	01-Jul-13	25-Jul-13	431	$123,466
3AUTUTW1331010	Owner Install and Testing W1 - 33 (Water) 673+80 to 673+80	20	26-Jul-13	22-Aug-13	546	$0
W1 - 35 (Water) 107+90 to 110+90		36	01-Jul-13	19-Aug-13	572	$37,198

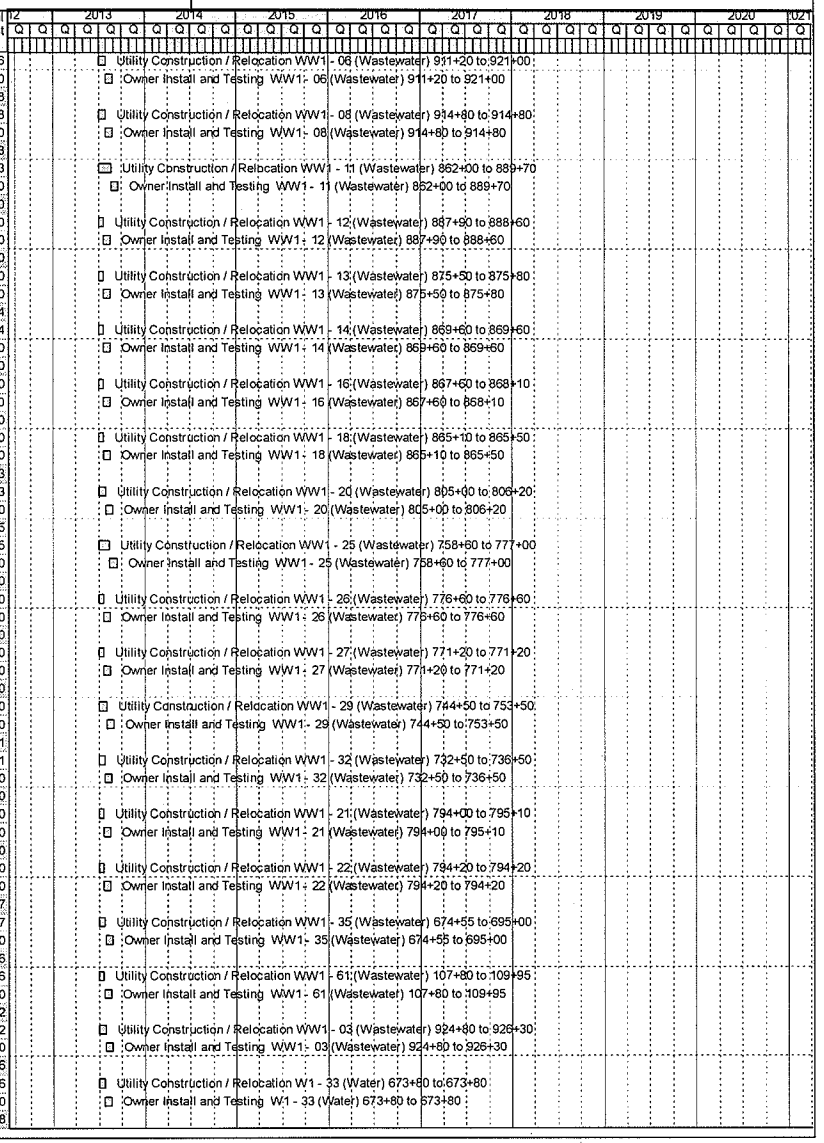

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AUTUTW1351000	Utility Construction / Relocation W1 - 35 (Water) 107+90 to 110+90	13	01-Jul-13	22-Jul-13	433	$37,198
3AUTUTW1351010	Owner Install and Testing W1 - 35 (Water) 107+90 to 110+90	20	23-Jul-13	19-Aug-13	549	$0
WW1 - 10 (Wastewater) 903+10 to 904+00		39	01-Jul-13	22-Aug-13	291	$35,895
3AUTUTWW1101000	Utility Construction / Relocation WW1 - 10 (Wastewater) 903+10 to 904+00	15	01-Jul-13	25-Jul-13	222	$35,895
3AUTUTWW1101010	Owner Install and Testing WW1 - 10 (Wastewater) 903+10 to 904+00	20	26-Jul-13	22-Aug-13	279	$0
WW1 - 31 (Wastewater) 740+50 to 742+40		40	01-Jul-13	23-Aug-13	555	$80,433
3AUTUTWW1311000	Utility Construction / Relocation WW1 - 31 (Wastewater) 740+50 to 742+40	16	01-Jul-13	26-Jul-13	421	$80,433
3AUTUTWW1311010	Owner Install and Testing WW1 - 31 (Wastewater) 740+50 to 742+40	20	29-Jul-13	23-Aug-13	532	$0
WW1 - 30 (Wastewater) 741+00 to 751+25		42	01-Jul-13	27-Aug-13	261	$73,569
3AUTUTWW1301000	Utility Construction / Relocation WW1 - 30 (Wastewater) 741+00 to 751+25	18	01-Jul-13	30-Jul-13	197	$73,569
3AUTUTWW1301010	Owner Install and Testing WW1 - 30 (Wastewater) 741+00 to 751+25	20	31-Jul-13	27-Aug-13	250	$0
WW1 - 24 (Wastewater) 786+80 to 786+80		48	01-Jul-13	04-Sep-13	460	$125,374
3AUTUTWW1241000	Utility Construction / Relocation WW1 - 24 (Wastewater) 786+80 to 786+80	22	01-Jul-13	06-Aug-13	346	$125,374
3AUTUTWW1241010	Owner Install and Testing WW1 - 24 (Wastewater) 786+80 to 786+80	20	07-Aug-13	04-Sep-13	440	$0
WW1 - 23 (Wastewater) 794+00 to 794+00		35	01-Jul-13	16-Aug-13	387	$0
3AUTUTWW1231000	Utility Construction / Relocation WW1 - 23 (Wastewater) 794+00 to 794+00	12	01-Jul-13	19-Jul-13	294	$0
3AUTUTWW1231010	Owner Install and Testing WW1 - 23 (Wastewater) 794+00 to 794+00	20	22-Jul-13	16-Aug-13	368	$0
WW1 - 07 (Wastewater) 914+30 to 916+00		36	01-Jul-13	19-Aug-13	294	$24,077
3AUTUTWW171000	Utility Construction / Relocation WW1 - 07 (Wastewater) 914+30 to 916+00	13	01-Jul-13	22-Jul-13	224	$24,077
3AUTUTWW171010	Owner Install and Testing WW1 - 07 (Wastewater) 914+30 to 916+00	20	23-Jul-13	19-Aug-13	282	$0
WW1 - 34 (Wastewater) 730+50 to 732+60		40	01-Jul-13	23-Aug-13	288	$65,403
3AUTUTWW1341000	Utility Construction / Relocation WW1 - 34 (Wastewater) 730+50 to 732+60	16	01-Jul-13	26-Jul-13	220	$65,403
3AUTUTWW1341010	Owner Install and Testing WW1 - 34 (Wastewater) 730+50 to 732+60	20	29-Jul-13	23-Aug-13	276	$0
Energy Transfer		42	13-Jul-13	10-Sep-13	370	$389,483
3AENTRMSUT1003	Start Energy Transfer Utility Relocation	0	13-Jul-13		391	$0
PL3 - 03 (Gas) 784+00 to 810+00		42	15-Jul-13	10-Sep-13	370	$244,803
3AUTUTPL331000	Utility Construction / Relocation PL3 - 03 (Gas) 784+00 to 810+00	18	15-Jul-13	12-Aug-13	280	$244,803
3AUTUTPL331010	Owner Install and Testing PL3 - 03 (Gas) 784+00 to 810+00	20	13-Aug-13	10-Sep-13	352	$0
PL3 - 01 (Gas) 860+00 to 866+00		41	15-Jul-13	09-Sep-13	279	$144,680
3AUTUTPL311000	Utility Construction / Relocation PL3 - 01 (Gas) 860+00 to 866+00	17	15-Jul-13	09-Aug-13	212	$144,680
3AUTUTPL311010	Owner Install and Testing PL3 - 01 (Gas) 860+00 to 866+00	20	12-Aug-13	09-Sep-13	268	$0
Magellan Pipeline		35	06-Jul-13	23-Aug-13	270	$23,269
3AMAGEMSUT1004	Start Magellan Pipeline Utility Relocation	0	06-Jul-13		380	$0
PL11 - 01 (Gas) 758+45 to 768+00		34	09-Jul-13	23-Aug-13	270	$23,269
3AUTUTPL1111000	Utility Construction / Relocation PL11 - 01 (Gas) 758+45 to 768+00	12	09-Jul-13	26-Jul-13	204	$23,269
3AUTUTPL1111010	Owner Install and Testing PL11 - 01 (Gas) 758+45 to 768+00	20	29-Jul-13	23-Aug-13	258	$0
Oncor		168	28-Jun-13	18-Feb-14	858	$11,203,060
3AMSUT1003	Start Oncor Utility Relocation	0	28-Jun-13		181	$0
OH - 10 (Electric) 911+00 to 916+00		35	01-Jul-13	16-Aug-13	349	$27,894
3AUTUTOH101000	Utility Construction / Relocation OH - 10 (Electric) 911+00 to 916+00	12	01-Jul-13	19-Jul-13	267	$27,894
3AUTUTOH101010	Owner Install and Testing OH - 10 (Electric) 911+00 to 916+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 12 (Electric) 911+00 to 914+00		41	01-Jul-13	26-Aug-13	343	$249,427
3AUTUTOH121000	Utility Construction / Relocation OH - 12 (Electric) 911+00 to 914+00	17	01-Jul-13	29-Jul-13	262	$249,427
3AUTUTOH121010	Owner Install and Testing OH - 12 (Electric) 911+00 to 914+00	20	30-Jul-13	26-Aug-13	329	$0
OH - 14 (Electric) 867+50 to 889+00		37	01-Jul-13	20-Aug-13	347	$93,333
3AUTUTOH141000	Utility Construction / Relocation OH - 14 (Electric) 867+50 to 889+00	14	01-Jul-13	23-Jul-13	265	$93,333
3AUTUTOH141010	Owner Install and Testing OH - 14 (Electric) 867+50 to 889+00	20	24-Jul-13	20-Aug-13	333	$0
OH - 17 (Electric) 868+55 to 870+70		40	01-Jul-13	23-Aug-13	290	$169,711
3AUTUTOH171000	Utility Construction / Relocation OH - 17 (Electric) 868+55 to 870+70	16	01-Jul-13	26-Jul-13	221	$169,711
3AUTUTOH171010	Owner Install and Testing OH - 17 (Electric) 868+55 to 870+70	20	29-Jul-13	23-Aug-13	278	$0
OH - 19 (Electric) 862+05 to 862+70		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTOH191000	Utility Construction / Relocation OH - 19 (Electric) 862+05 to 862+70	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTOH191010	Owner Install and Testing OH - 19 (Electric) 862+05 to 862+70	20	22-Jul-13	16-Aug-13	335	$0
OH - 20 (Electric) 857+50 to 862+00		35	01-Jul-13	16-Aug-13	349	$27,416
3AUTUTOH201000	Utility Construction / Relocation OH - 20 (Electric) 857+50 to 862+00	12	01-Jul-13	19-Jul-13	267	$27,416
3AUTUTOH201010	Owner Install and Testing OH - 20 (Electric) 857+50 to 862+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 21 (Electric) 860+00 to 861+15		35	01-Jul-13	16-Aug-13	349	$13,470
3AUTUTOH211000	Utility Construction / Relocation OH - 21 (Electric) 860+00 to 861+15	12	01-Jul-13	19-Jul-13	267	$13,470
3AUTUTOH211010	Owner Install and Testing OH - 21 (Electric) 860+00 to 861+15	20	22-Jul-13	16-Aug-13	335	$0
OH - 22 (Electric) 832+50 to 839+85		36	01-Jul-13	19-Aug-13	758	$34,830

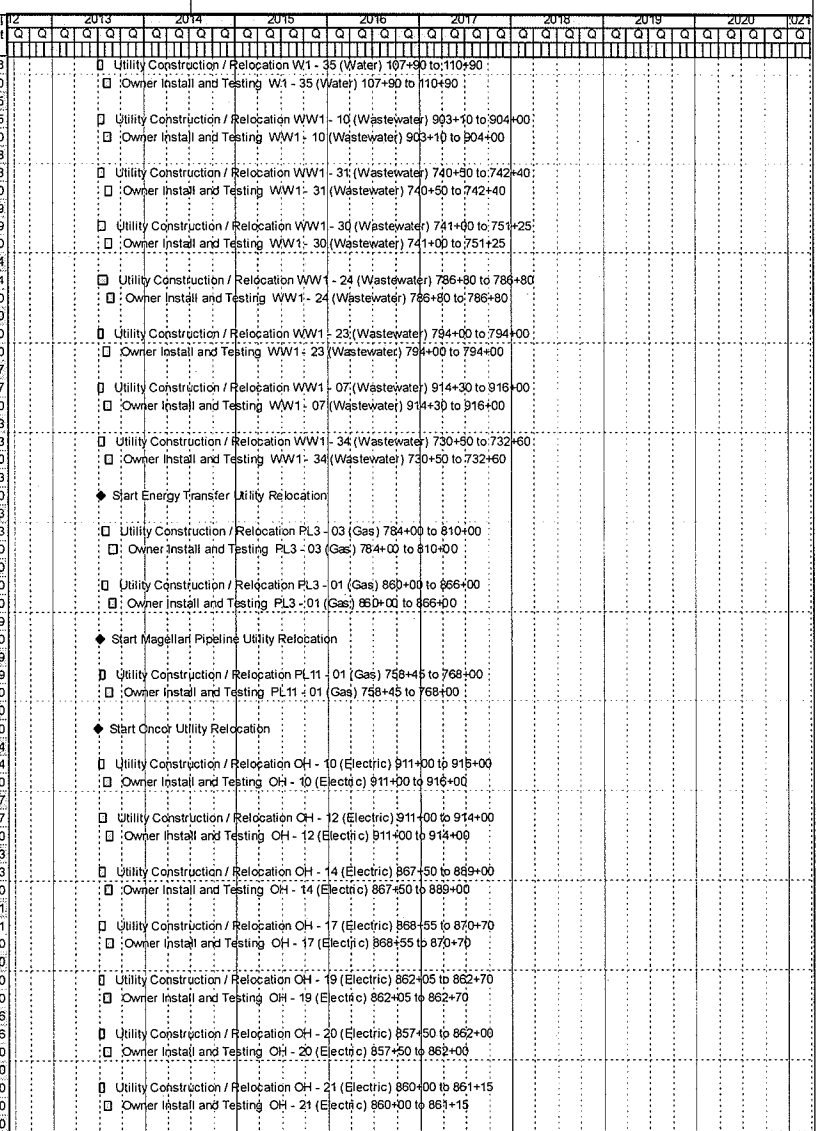

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AUTUTOH221000	Utility Construction / Relocation OH - 22 (Electric) 832+50 to 839+85	13	01-Jul-13	22-Jul-13	567	$34,830
3AUTUTOH221010	Owner Install and Testing OH - 22 (Electric) 832+50 to 839+85	20	23-Jul-13	19-Aug-13	726	$0
OH - 24 (Electric) 806+80 to 807+00		35	01-Jul-13	16-Aug-13	289	$0
3AUTUTOH241000	Utility Construction / Relocation OH - 24 (Electric) 806+80 to 807+00	12	01-Jul-13	19-Jul-13	220	$0
3AUTUTOH241010	Owner Install and Testing OH - 24 (Electric) 806+80 to 807+00	20	22-Jul-13	16-Aug-13	277	$0
OH - 26 (Electric) 794+50 to 794+50		35	01-Jul-13	16-Aug-13	352	$30,206
3AUTUTOH261000	Utility Construction / Relocation OH - 26 (Electric) 794+50 to 794+50	12	01-Jul-13	19-Jul-13	271	$30,206
3AUTUTOH261010	Owner Install and Testing OH - 26 (Electric) 794+50 to 794+50	20	22-Jul-13	16-Aug-13	338	$0
OH - 28 (Electric) 778+20 to 779+35		35	01-Jul-13	16-Aug-13	387	$10,478
3AUTUTOH281000	Utility Construction / Relocation OH - 28 (Electric) 778+20 to 779+35	12	01-Jul-13	19-Jul-13	294	$10,478
3AUTUTOH281010	Owner Install and Testing OH - 28 (Electric) 778+20 to 779+35	20	22-Jul-13	16-Aug-13	368	$0
OH - 29 (Electric) 776+20 to 778+20		35	01-Jul-13	16-Aug-13	352	$24,352
3AUTUTOH291000	Utility Construction / Relocation OH - 29 (Electric) 776+20 to 778+20	12	01-Jul-13	19-Jul-13	271	$24,352
3AUTUTOH291010	Owner Install and Testing OH - 29 (Electric) 776+20 to 778+20	20	22-Jul-13	16-Aug-13	338	$0
OH - 30 (Electric) 775+50 to 776+30		35	01-Jul-13	16-Aug-13	352	$24,352
3AUTUTOH301000	Utility Construction / Relocation OH - 30 (Electric) 775+50 to 776+30	12	01-Jul-13	19-Jul-13	271	$24,352
3AUTUTOH301010	Owner Install and Testing OH - 30 (Electric) 775+50 to 776+30	20	22-Jul-13	16-Aug-13	338	$0
OH - 31 (Electric) 762+90 to 776+35		36	01-Jul-13	19-Aug-13	434	$67,348
3AUTUTOH311000	Utility Construction / Relocation OH - 31 (Electric) 762+90 to 776+35	13	01-Jul-13	22-Jul-13	329	$67,348
3AUTUTOH311010	Owner Install and Testing OH - 31 (Electric) 762+90 to 776+35	20	23-Jul-13	19-Aug-13	414	$0
OH - 34 (Electric) 762+90 to 762+90		35	01-Jul-13	16-Aug-13	435	$0
3AUTUTOH341000	Utility Construction / Relocation OH - 34 (Electric) 762+90 to 762+90	12	01-Jul-13	19-Jul-13	330	$0
3AUTUTOH341010	Owner Install and Testing OH - 34 (Electric) 762+90 to 762+90	20	22-Jul-13	16-Aug-13	415	$0
OH - 35 (Electric) 755+60 to 758+35		35	01-Jul-13	16-Aug-13	435	$12,993
3AUTUTOH351000	Utility Construction / Relocation OH - 35 (Electric) 755+60 to 758+35	12	01-Jul-13	19-Jul-13	330	$12,993
3AUTUTOH351010	Owner Install and Testing OH - 35 (Electric) 755+60 to 758+35	20	22-Jul-13	16-Aug-13	415	$0
OH - 36 (Electric) 740+70 to 745+00		35	01-Jul-13	16-Aug-13	435	$20,205
3AUTUTOH361000	Utility Construction / Relocation OH - 36 (Electric) 740+70 to 745+00	12	01-Jul-13	19-Jul-13	330	$20,205
3AUTUTOH361010	Owner Install and Testing OH - 36 (Electric) 740+70 to 745+00	20	22-Jul-13	16-Aug-13	415	$0
OH - 37 (Electric) 727+20 to 729+65		39	01-Jul-13	22-Aug-13	289	$132,898
3AUTUTOH371000	Utility Construction / Relocation OH - 37 (Electric) 727+20 to 729+65	15	01-Jul-13	25-Jul-13	221	$132,898
3AUTUTOH371010	Owner Install and Testing OH - 37 (Electric) 727+20 to 729+65	20	26-Jul-13	22-Aug-13	277	$0
OH - 38 (Electric) 728+60 to 729+65		35	01-Jul-13	16-Aug-13	293	$0
3AUTUTOH381000	Utility Construction / Relocation OH - 38 (Electric) 728+60 to 729+65	12	01-Jul-13	19-Jul-13	224	$0
3AUTUTOH381010	Owner Install and Testing OH - 38 (Electric) 728+60 to 729+65	20	22-Jul-13	16-Aug-13	281	$0
OH - 7 (Electric) 913+00 to 921+00		36	01-Jul-13	19-Aug-13	294	$46,465
3AUTUTOH71000	Utility Construction / Relocation OH - 7 (Electric) 913+00 to 921+00	13	01-Jul-13	22-Jul-13	224	$46,465
3AUTUTOH71010	Owner Install and Testing OH - 7 (Electric) 913+00 to 921+00	20	23-Jul-13	19-Aug-13	282	$0
OH - 8 (Electric) 895+00 to 903+50		36	01-Jul-13	19-Aug-13	294	$55,916
3AUTUTOH81000	Utility Construction / Relocation OH - 8 (Electric) 895+00 to 903+50	13	01-Jul-13	22-Jul-13	224	$55,916
3AUTUTOH81010	Owner Install and Testing OH - 8 (Electric) 895+00 to 903+50	20	23-Jul-13	19-Aug-13	282	$0
OH - 27 (Electric) 788+25 to 794+00		35	01-Jul-13	16-Aug-13	387	$25,508
3AUTUTOH271000	Utility Construction / Relocation OH - 27 (Electric) 788+25 to 794+00	12	01-Jul-13	19-Jul-13	294	$25,508
3AUTUTOH271010	Owner Install and Testing OH - 27 (Electric) 788+25 to 794+00	20	22-Jul-13	16-Aug-13	368	$0
OH - 52 (Electric) 111+45 to 112+05		37	01-Jul-13	20-Aug-13	988	$104,858
3AUTUTOH521000	Utility Construction / Relocation OH - 52 (Electric) 111+45 to 112+05	14	01-Jul-13	23-Jul-13	743	$104,858
3AUTUTOH521010	Owner Install and Testing OH - 52 (Electric) 111+45 to 112+05	20	24-Jul-13	20-Aug-13	948	$0
OH - 103 (Electric) 784+00 to 810+00 - Complex Relocation		167	01-Jul-13	18-Feb-14	255	$1,519,467
3AUTUTOH1031000	Utility Construction / Relocation OH - 103 (Electric) 784+00 to 810+00	114	01-Jul-13	20-Jan-14	192	$1,519,467
3AUTUTOH1031010	Owner Install and Testing OH - 103 (Electric) 784+00 to 810+00	20	21-Jan-14	18-Feb-14	245	$0
OH - 104 (Electric) 688+30 to 688+30		35	01-Jul-13	16-Aug-13	297	$84,415
3AUTUTOH1041000	Utility Construction / Relocation OH - 104 (Electric) 688+30 to 688+30	12	01-Jul-13	19-Jul-13	226	$84,415
3AUTUTOH1041010	Owner Install and Testing OH - 104 (Electric) 688+30 to 688+30	20	22-Jul-13	16-Aug-13	285	$0
OH - 33 (Electric) 758+35 to 763+00		36	01-Jul-13	19-Aug-13	274	$823,081
3AUTUTOH331000	Utility Construction / Relocation OH - 33 (Electric) 758+35 to 763+00	13	01-Jul-13	22-Jul-13	207	$823,081
3AUTUTOH331010	Owner Install and Testing OH - 33 (Electric) 758+35 to 763+00	20	23-Jul-13	19-Aug-13	262	$0
OH - 100 (Electric) 755+25 to 757+00 - Complex Relocation		164	01-Jul-13	13-Feb-14	306	$1,266,223
3AUTUTOH1001000	Utility Construction / Relocation OH - 100 (Electric) 755+25 to 757+00	112	01-Jul-13	15-Jan-14	230	$1,266,223
3AUTUTOH1001010	Owner Install and Testing OH - 100 (Electric) 755+25 to 757+00	20	16-Jan-14	13-Feb-14	294	$0
E1 - 5 (Electric) 106+05 to 109+00		36	01-Jul-13	19-Aug-13	989	$45,768

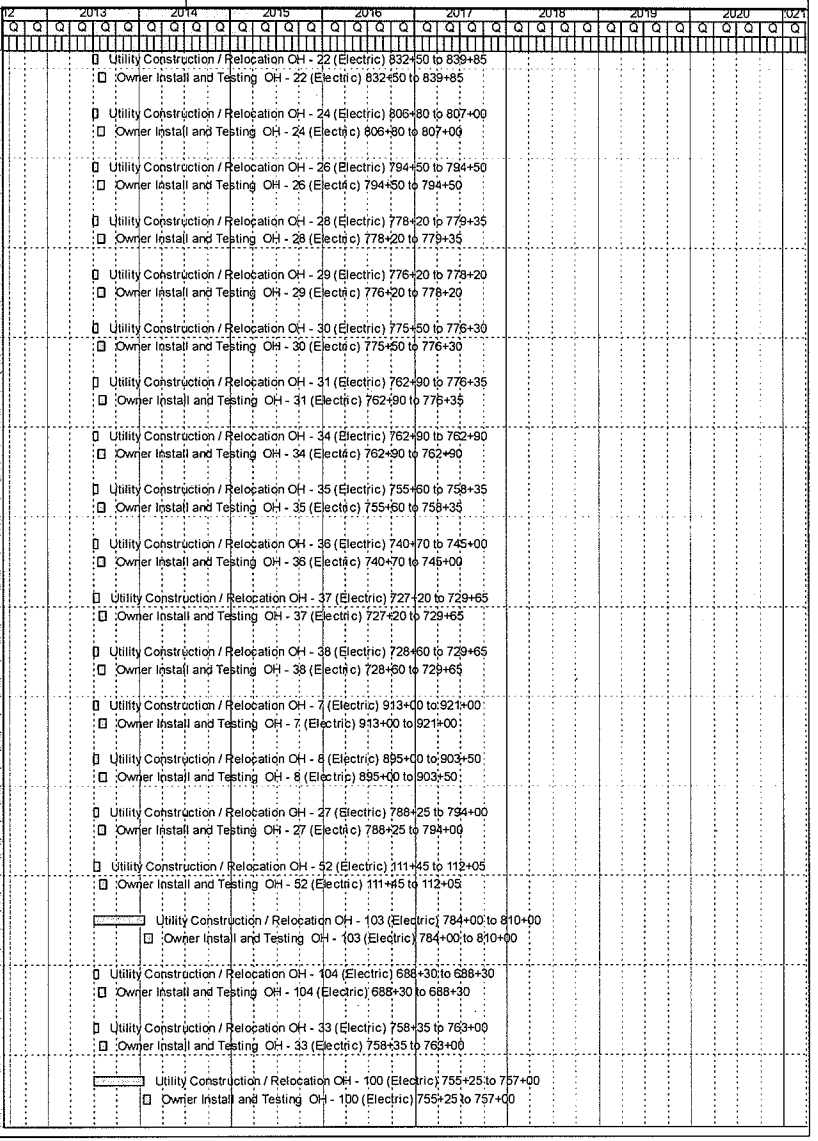

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AUTUTE151000	Utility Construction / Relocation E1 - 5 (Electric) 106+05 to 109+00	13	01-Jul-13	22-Jul-13	744	$45,768
3AUTUTE151010	Owner Install and Testing E1 - 5 (Electric) 106+05 to 109+00	20	23-Jul-13	19-Aug-13	949	$0
OH - 15 (Electric) 861+80 to 884+25		39	01-Jul-13	22-Aug-13	291	$104,895
3AUTUTOH151000	Utility Construction / Relocation OH - 15 (Electric) 861+80 to 884+25	15	01-Jul-13	25-Jul-13	222	$104,895
3AUTUTOH151010	Owner Install and Testing OH - 15 (Electric) 861+80 to 884+25	20	26-Jul-13	22-Aug-13	279	$0
OH - 16 (Electric) 874+90 to 875+10		35	01-Jul-13	16-Aug-13	349	$0
3AUTUTOH161000	Utility Construction / Relocation OH - 16 (Electric) 874+90 to 875+10	12	01-Jul-13	19-Jul-13	267	$0
3AUTUTOH161010	Owner Install and Testing OH - 16 (Electric) 874+90 to 875+10	20	22-Jul-13	16-Aug-13	335	$0
E1 - 3 (Electric) 696+55 to 700+20		36	01-Jul-13	19-Aug-13	434	$53,622
3AUTUTE131000	Utility Construction / Relocation E1 - 3 (Electric) 696+55 to 700+20	13	01-Jul-13	22-Jul-13	329	$53,622
3AUTUTE131010	Owner Install and Testing E1 - 3 (Electric) 696+55 to 700+20	20	23-Jul-13	19-Aug-13	414	$0
OH - 105 (Electric) 687+60 to 687+60		35	01-Jul-13	16-Aug-13	297	$84,415
3AUTUTOH1051000	Utility Construction / Relocation OH - 105 (Electric) 687+60 to 687+60	12	01-Jul-13	19-Jul-13	226	$84,415
3AUTUTOH1051010	Owner Install and Testing OH - 105 (Electric) 687+60 to 687+60	20	22-Jul-13	16-Aug-13	285	$0
OH - 9 (Electric) 902+50 to 913+00		36	01-Jul-13	19-Aug-13	348	$53,402
3AUTUTOH91000	Utility Construction / Relocation OH - 9 (Electric) 902+50 to 913+00	13	01-Jul-13	22-Jul-13	266	$53,402
3AUTUTOH91010	Owner Install and Testing OH - 9 (Electric) 902+50 to 913+00	20	23-Jul-13	19-Aug-13	334	$0
OH - 11 (Electric) 913+80 to 915+30		35	01-Jul-13	16-Aug-13	295	$9,322
3AUTUTOH111000	Utility Construction / Relocation OH - 11 (Electric) 913+80 to 915+30	12	01-Jul-13	19-Jul-13	225	$9,322
3AUTUTOH111010	Owner Install and Testing OH - 11 (Electric) 913+80 to 915+30	20	22-Jul-13	16-Aug-13	283	$0
OH - 18 (Electric) 860+50 to 866+00		35	01-Jul-13	16-Aug-13	349	$18,571
3AUTUTOH181000	Utility Construction / Relocation OH - 18 (Electric) 860+50 to 866+00	12	01-Jul-13	19-Jul-13	267	$18,571
3AUTUTOH181010	Owner Install and Testing OH - 18 (Electric) 860+50 to 866+00	20	22-Jul-13	16-Aug-13	335	$0
OH - 25 (Electric) 793+30 to 796+05		35	01-Jul-13	16-Aug-13	387	$12,038
3AUTUTOH251000	Utility Construction / Relocation OH - 25 (Electric) 793+30 to 796+05	12	01-Jul-13	19-Jul-13	294	$12,038
3AUTUTOH251010	Owner Install and Testing OH - 25 (Electric) 793+30 to 796+05	20	22-Jul-13	16-Aug-13	368	$0
OH - 32 (Electric) 761+10 to 763+25		35	01-Jul-13	16-Aug-13	550	$9,322
3AUTUTOH321000	Utility Construction / Relocation OH - 32 (Electric) 761+10 to 763+25	12	01-Jul-13	19-Jul-13	417	$9,322
3AUTUTOH321010	Owner Install and Testing OH - 32 (Electric) 761+10 to 763+25	20	22-Jul-13	16-Aug-13	527	$0
OH - 42 (Electric) 678+65 to 696+55		36	01-Jul-13	19-Aug-13	434	$37,822
3AUTUTOH421000	Utility Construction / Relocation OH - 42 (Electric) 678+65 to 696+55	13	01-Jul-13	22-Jul-13	329	$37,822
3AUTUTOH421010	Owner Install and Testing OH - 42 (Electric) 678+65 to 696+55	20	23-Jul-13	19-Aug-13	414	$0
OH - 102 (Electric) 830+00 to 834+55 - Complex Relocation		164	01-Jul-13	13-Feb-14	630	$1,688,297
3AUTUTOH1021000	Utility Construction / Relocation OH - 102 (Electric) 830+00 to 834+55	112	01-Jul-13	15-Jan-14	468	$1,688,297
3AUTUTOH1021010	Owner Install and Testing OH - 102 (Electric) 830+00 to 834+55	20	16-Jan-14	13-Feb-14	606	$0
OH - 101 (Electric) 912+00 to 919+50 - Complex Relocation		164	01-Jul-13	13-Feb-14	136	$4,220,742
3AUTUTOH1011000	Utility Construction / Relocation OH - 101 (Electric) 912+00 to 919+50	112	01-Jul-13	15-Jan-14	100	$4,220,742
3AUTUTOH1011010	Owner Install and Testing OH - 101 (Electric) 912+00 to 919+50	20	16-Jan-14	13-Feb-14	133	$0
Qwest		40	13-Jul-13	06-Sep-13	278	$141,817
3AQWSTMSUT1000	Start Qwest Utility Relocation	0	13-Jul-13		391	$0
FO10 - 01 (Fiber Optic) 723+00 to 726+00		40	15-Jul-13	06-Sep-13	278	$141,817
3AUTUTFO1011000	Utility Construction / Relocation FO10 - 01 (Fiber Optic) 723+00 to 726+00	16	15-Jul-13	08-Aug-13	212	$141,817
3AUTUTFO1011010	Owner Install and Testing FO10 - 01 (Fiber Optic) 723+00 to 726+00	20	09-Aug-13	06-Sep-13	267	$0
Sprint		37	27-Jul-13	17-Sep-13	513	$81,038
3AMSUT1002	Start Sprint Utility Relocation	0	27-Jul-13		720	$0
FO14 - 01 (Fiber Optic) 921+00 to 921+00		37	29-Jul-13	17-Sep-13	513	$81,038
3AUTUTFO1411000	Utility Construction / Relocation FO14 - 01 (Fiber Optic) 921+00 to 921+00	14	29-Jul-13	19-Aug-13	387	$81,038
3AUTUTFO1411010	Owner Install and Testing FO14 - 01 (Fiber Optic) 921+00 to 921+00	20	20-Aug-13	17-Sep-13	492	$0
Texas Midstream		41	13-Jul-13	09-Sep-13	273	$156,351
3AMSUT1001	Start Texas Midstream Utility Relocation	0	13-Jul-13		383	$0
PL12 - 01 (Gas) 809+00 to 815+00		41	15-Jul-13	09-Sep-13	273	$156,351
3AUTUTPL1211000	Utility Construction / Relocation PL12 - 01 (Gas) 809+00 to 815+00	17	15-Jul-13	09-Aug-13	207	$156,351
3AUTUTPL1211010	Owner Install and Testing PL12 - 01 (Gas) 809+00 to 815+00	20	12-Aug-13	09-Sep-13	262	$0
Time Warner/Fiber Light		43	28-Jun-13	27-Aug-13	258	$202,596
3AMSUT1005	Start Time Warner / Fiber Light Utility Relocation	0	28-Jun-13		362	$0
FO9 - 01 (Fiber Optic) 912+30 to 916+70		42	01-Jul-13	27-Aug-13	258	$202,596
3AUTUTFO911000	Utility Construction / Relocation FO9 - 01 (Fiber Optic) 912+30 to 916+70	18	01-Jul-13	30-Jul-13	194	$202,596
3AUTUTFO911010	Owner Install and Testing FO9 - 01 (Fiber Optic) 912+30 to 916+70	20	31-Jul-13	27-Aug-13	247	$0
Verizon		47	20-Jul-13	24-Sep-13	508	$270,127
3AMSUT1000	Start Verizon Utility Relocation	0	20-Jul-13		712	$0

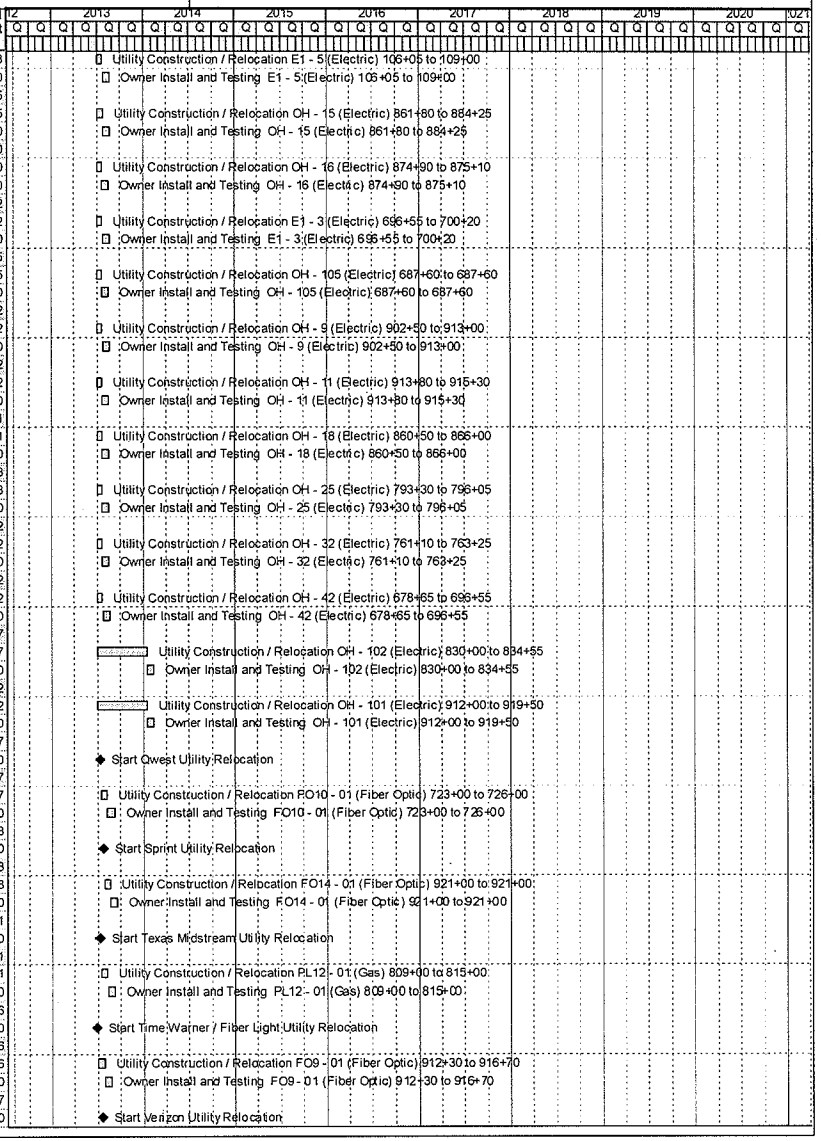

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
FO7 - 01 (Fiber Optic) 920+00 to 923+50		47	22-Jul-13	24-Sep-13	508	$270,127
3AUTUTFO711000	Utility Construction / Relocation FO7 - 01 (Fiber Optic) 920+00 to 923+50	22	22-Jul-13	26-Aug-13	383	$270,127
3AUTUTFO711010	Owner Install and Testing FO7 - 01 (Fiber Optic) 920+00 to 923+50	20	27-Aug-13	24-Sep-13	487	$0
Crosstex Energy		50	13-Jul-13	20-Sep-13	336	$376,490
ICMSUT1005	Start Crosstex Energy Utility Relocation	0	13-Jul-13		461	$0
G3 - 01 (Gas) 590+40/35W to 680+05/820		50	15-Jul-13	20-Sep-13	336	$376,490
ICUTUTG311000	Utility Construction / Relocation G3 - 01 (Gas) 590+40/35W to 680+05/820	24	15-Jul-13	22-Aug-13	253	$376,490
ICUTUTG311010	Owner Install and Testing G3 - 01 (Gas) 590+40/35W to 680+05/820	20	23-Aug-13	20-Sep-13	319	$0
Enterprisee Products		49	20-Jul-13	26-Sep-13	332	$540,255
ICMSUT1000	Start Enterprisee Products Utility Relocation	0	20-Jul-13		454	$0
G14 - 01 (Gas) 590+70/35W to 679+70/820		49	22-Jul-13	26-Sep-13	332	$540,255
ICUTUTG1411000	Utility Construction / Relocation G14 - 01 (Gas) 590+70/35W to 679+70/820	24	22-Jul-13	28-Aug-13	249	$540,255
ICUTUTG1411010	Owner Install and Testing G14 - 01 (Gas) 590+70/35W to 679+70/820	20	29-Aug-13	26-Sep-13	315	$0
Design		475	01-Oct-12	25-Jul-14	935	$71,355,000
NTE-3AIC-DSGN	Total Design Cost	475	01-Oct-12	25-Jul-14	935	$71,355,000
Preliminary Design		100	01-Oct-12	15-Feb-13	617	$0
Preliminary Design - Segment 3A		100	01-Oct-12	15-Feb-13	617	$0
3A1000	Archeological Investigation Parcel 852 and 853 - Segment 3A	100	01-Oct-12	15-Feb-13	617	$0
3A1001	Conduct Design Survey - Segment 3A	100	01-Oct-12	15-Feb-13	251	$0
3A1005	Conduct Geotechnical Investigation - Segment 3A	100	01-Oct-12	15-Feb-13	251	$0
Preliminary Design - Interchange		100	01-Oct-12	15-Feb-13	39	$0
ICDS1001	Conduct Design Survey - Interchange	100	01-Oct-12	15-Feb-13	39	$0
ICDS1000	Conduct Geotechnical Investigation - Interchange	100	01-Oct-12	15-Feb-13	39	$0
Roadway Design		300	20-Oct-12	13-Dec-13	1075	$0
NTEIC-RDW	Start Roadway Design - Interchange	0	20-Oct-12		55	$0
NTE3A-RDW	Start Roadway Design - Segment 3A	0	20-Oct-12		410	$0
Roadway Design - Segment 3A		300	22-Oct-12	13-Dec-13	1061	$0
3ANBFRDTDSRD1000	NBFR - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	573	$0
3ANBFRSIDSRD1000	NBFR - S. of Trinity River to IH-30	130	22-Oct-12	19-Apr-13	350	$0
3ASBFRMDDSRD1000	SBFR - Meacham to Dewey	130	22-Oct-12	19-Apr-13	353	$0
3ASBFRDTDSRD1000	SBFR - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	412	$0
3ASBFRSIDSRD1000	SBFR - S. of Trinity River to IH-30	130	22-Oct-12	19-Apr-13	399	$0
3ANBGPDTDSRD1000	NBGP - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	505	$0
3ASBGPMDDSRD1000	SBGP - Meacham to Dewey	130	22-Oct-12	19-Apr-13	352	$0
3ASBGPDTDSRD1000	SBGP - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	353	$0
3ANSMLDTDSRD1000	NSML - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	292	$0
3ANBRPMDDSRD1000	NBRP - Meacham to Dewey	130	22-Oct-12	19-Apr-13	560	$0
3ANBRPDTDSRD1000	NBRP - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	561	$0
3ASBRPMDDSRD1000	SBRP - Meacham to Dewey	130	22-Oct-12	19-Apr-13	353	$0
3ASBRPDTDSRD1000	SBRP - Dewey to S. of Trinity River	130	22-Oct-12	19-Apr-13	444	$0
3AXRDS18DSRD1000	XRDS - SH 183/NE 28th St.	130	22-Oct-12	19-Apr-13	525	$0
3AXRDSYCDSRD1000	XRDS - Yucca Av./Northside Dr.	130	22-Oct-12	19-Apr-13	470	$0
3AXRDS28DSRD1000	XRDS - Spur 280	130	22-Oct-12	19-Apr-13	318	$0
3ANBFRMDDSRD1000	NBFR - Meacham to Dewey	130	22-Oct-12	19-Apr-13	369	$0
3ANBGPMDDSRD1000	NBGP - Meacham to Dewey	130	18-Feb-13	16-Aug-13	649	$0
3ANBGPSIDSRD1000	NBGP - S. of Trinity River to IH-30	130	18-Feb-13	16-Aug-13	624	$0
3ASBGPSIDSRD1000	SBGP - S. of Trinity River to IH-30	130	18-Feb-13	16-Aug-13	657	$0
3ASBRPSIDSRD1000	SBRP - S. of Trinity River to IH-30	130	18-Feb-13	16-Aug-13	583	$0
3ANSMLMDDSRD1000	NSML - Meacham to Dewey	130	17-Jun-13	13-Dec-13	818	$0
3ANSMLSIDSRD1000	NSML - S. of Trinity River to IH-30	130	17-Jun-13	13-Dec-13	998	$0
3ANBRPSIDSRD1000	NBRP - S. of Trinity River to IH-30	130	17-Jun-13	13-Dec-13	800	$0
3ANBLAMDDSRD1000	NBLA - Meacham to Dewey	130	17-Jun-13	13-Dec-13	783	$0
3ANBLADTDSRD1000	NBLA - Dewey to S. of Trinity River	130	17-Jun-13	13-Dec-13	783	$0
3ANBLASIDSRD1000	NBLA - S. of Trinity River to IH-30	130	17-Jun-13	13-Dec-13	783	$0
3ASBLAMDDSRD1000	SBLA - Meacham to Dewey	130	17-Jun-13	13-Dec-13	783	$0
3ASBLADTDSRD1000	SBLA - Dewey to S. of Trinity River	130	17-Jun-13	13-Dec-13	783	$0
3ASBLASIDSRD1000	SBLA - S. of Trinity River to IH-30	130	17-Jun-13	13-Dec-13	783	$0
3AXRDSMIDSRD1000	XRDS - Meacham Blvd.	130	17-Jun-13	13-Dec-13	1061	$0
3AXRDSE4DSRD1000	XRDS - E. 4th St.	130	17-Jun-13	13-Dec-13	893	$0

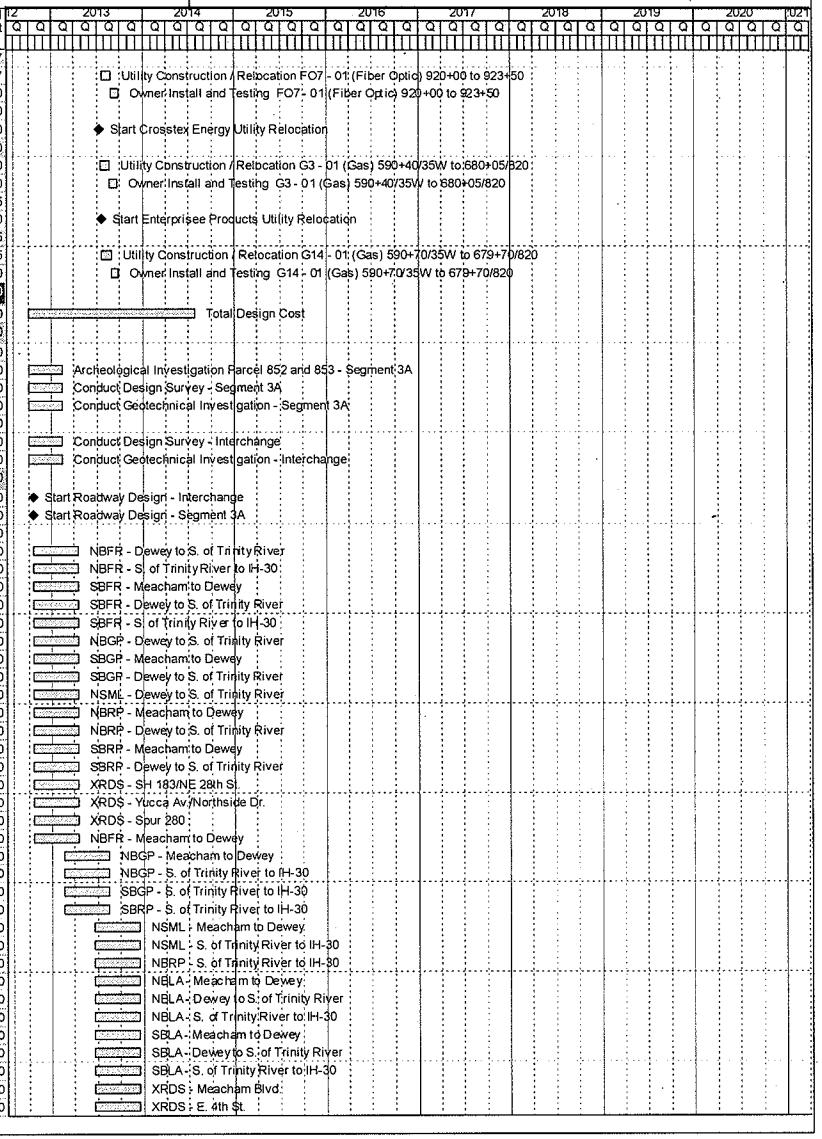

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3AXRDSCYDSRD1000	XRDS - Cypress St.	130	17-Jun-13	13-Dec-13	1030	$0
Roadway Design - Interchange		300	22-Oct-12	13-Dec-13	1075	$0
ICSBFRIMDSRD1000	SBFR - Interchange to Meacham	130	22-Oct-12	19-Apr-13	92	$0
ICNBGPIMDSRD1000	NBGP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	352	$0
ICSBGPIMDSRD1000	SBGP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	326	$0
ICEBGPIMDSRD1000	EBGP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	292	$0
ICWBGPIMDSRD1000	WBGP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	479	$0
ICNSMLIMDSRD1000	NSML - Interchange to Meacham	130	22-Oct-12	19-Apr-13	128	$0
ICEWMLIMDSRD1000	EWML - Interchange to Meacham	130	22-Oct-12	19-Apr-13	309	$0
ICNBRPIMDSRD1000	NBRP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	93	$0
ICSBRPIMDSRD1000	SBRP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	62	$0
ICEBRPIMDSRD1000	EBRP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	118	$0
ICWBRPIMDSRD1000	WBRP - Interchange to Meacham	130	22-Oct-12	19-Apr-13	207	$0
ICNBFRIMDSRD1000	NBFR - Interchange to Meacham	130	22-Oct-12	19-Apr-13	39	$0
ICNBLAIMDSRD1000	NBLA - Interchange to Meacham	130	17-Jun-13	13-Dec-13	1075	$0
ICSBLAIMDSRD1000	SBLA - Interchange to Meacham	130	17-Jun-13	13-Dec-13	1075	$0
ICEBLAIMDSRD1000	EBLA - Interchange to Meacham	130	17-Jun-13	13-Dec-13	1075	$0
ICWBLAIMDSRD1000	WBLA - Interchange to Meacham	130	17-Jun-13	13-Dec-13	1075	$0
Bridge Design		460	20-Oct-12	25-Jul-14	887	$0
NTE3A-BRD	Start Bridge Design - Segment 3A	0	20-Oct-12		353	$0
IC1005	Start Bridge Design - Interchange	0	09-Mar-13		152	$0
Bridge Design - Segment 3A		460	22-Oct-12	25-Jul-14	887	$0
3AXRDS18DS2141000	Design Bridge - B214 - SH 183/NE 28th Street over 35W	130	22-Oct-12	19-Apr-13	558	$0
3ANSMLDTDS2181000	Design Bridge - B218 - 35W ML over UPRR	130	22-Oct-12	19-Apr-13	305	$0
3ANBGPDTDS2241000	Design Bridge - B224 - NB 35W GP over Trinity River (TRWD and USACE Reviews Included)	460	22-Oct-12	25-Jul-14	449	$0
3ANSMLDTDS2251000	Design Bridge - B225 - 35W ML over Trinity River & Elevated Section (TRWD and USACE Revi	460	22-Oct-12	25-Jul-14	750	$0
3ANSMLDTDS2421000	Design Bridge - B242 - 35W ML over Trinity River & Elevated Section (TRWD and USACE Revi	460	22-Oct-12	25-Jul-14	750	$0
3ANSMLDTDS2431000	Design Bridge - B243 - 35W ML over Trinity River & Elevated Section (TRWD and USACE Revi	460	22-Oct-12	25-Jul-14	750	$0
3ASBRPSIDS2321000	Design Bridge - B232 - 35W ML over Trinity River & Elevated Section (TRWD and USACE Revi	460	22-Oct-12	25-Jul-14	490	$0
3ASBGPDTDS2261000	Design Bridge - B226 - SB 35W GP over Trinity River (TRWD and USACE Reviews Included)	460	22-Oct-12	25-Jul-14	252	$0
3AXRDS28DS2371000	Design Bridge - B237 - Spur 280 over 35W	130	22-Oct-12	19-Apr-13	304	$0
3ASBGPMDDS2401000	Design Bridge - B240 - SB 35W GP over Meacham	130	18-Feb-13	16-Aug-13	576	$0
3ASBGPMDDS2051000	Design Bridge - B205 - SB 35W GP over FWWR	130	18-Feb-13	16-Aug-13	265	$0
3ASBGPMDDS2081000	Design Bridge - B208 - SB 35W GP over BNSF	130	18-Feb-13	16-Aug-13	562	$0
3ASBGPDTDS2171000	Design Bridge - B217 - SB 35W GP over UPRR	130	18-Feb-13	16-Aug-13	252	$0
3ASBGPDTDS2211000	Design Bridge - B221 - SB 35W GP over Northside Dr/Yucca Ave	130	18-Feb-13	16-Aug-13	531	$0
3ASBGPSIDS2301000	Design Bridge - B230 - SB 35W GP over Pharr/TX121	130	18-Feb-13	16-Aug-13	603	$0
3ASBGPSIDS2341000	Design Bridge - B234 - SB 35W GP over 4th St	130	18-Feb-13	16-Aug-13	564	$0
3ASBGPSIDS2361000	Design Bridge - B236 - SB 35W GP over RR (922+00)	130	18-Feb-13	16-Aug-13	540	$0
3ASBRPMDDS2021000	Design Bridge - B202 - SB 35W GP Ramp to SB 35W ML	130	18-Feb-13	16-Aug-13	291	$0
3ANSMLMDDS2041000	Design Bridge - B204 - 35W ML Transition (713+00)	130	17-Jun-13	13-Dec-13	985	$0
3ANSMLMDDS2061000	Design Bridge - B206 - 35W ML over FWWR	130	17-Jun-13	13-Dec-13	907	$0
3ANBGPMDDS2071000	Design Bridge - B207 - NB 35W GP over FWWR	130	17-Jun-13	13-Dec-13	610	$0
3ANSMLMDFO2091000	Design Bridge - B209 - 35W ML over BNSF	130	17-Jun-13	13-Dec-13	972	$0
3ANBGPMDDS2101000	Design Bridge - B210 - NB 35W GP over BNSF	130	17-Jun-13	13-Dec-13	635	$0
3ASBRPMDDS2111000	Design Bridge - B211 - SB 35W ML Exit Ramp to SH 183	130	17-Jun-13	13-Dec-13	972	$0
3ANBRPMDDS2121000	Design Bridge - B212 - SH183 Entrance Ramp to NB 35W ML	130	17-Jun-13	13-Dec-13	678	$0
3ANSMLMDDS2131000	Design Bridge - B213 - 35W ML Transition (755+00)	130	17-Jun-13	13-Dec-13	989	$0
3ANBGPDTDS2191000	Design Bridge - B219 - NB 35W GP over UPRR	130	17-Jun-13	13-Dec-13	604	$0
3ANSMLDTDS2221000	Design Bridge - B222 - 35W ML over Northside Dr/Yucca Ave	130	17-Jun-13	13-Dec-13	944	$0
3ANBGPDTDS2231000	Design Bridge - B223 - NB 35W GP over Northside Dr/Yucca Ave	130	17-Jun-13	13-Dec-13	681	$0
3ANBRPSIDS2311000	Design Bridge - B231 - Spur 280 Entrance Ramp to NB 35W ML	130	17-Jun-13	13-Dec-13	650	$0
3ANBGPSIDS2331000	Design Bridge - B233 - NB 35W GP over 4th St	130	17-Jun-13	13-Dec-13	684	$0
3ANBGPSIDS2351000	Design Bridge - B235 - NB 35W GP over RR (922+00)	130	17-Jun-13	13-Dec-13	687	$0
3AXRDSE4DS2391000	Design Bridge - B239 - Pedestrian Bridge over US 287	130	17-Jun-13	13-Dec-13	921	$0
3ANBGPMDDS2411000	Design Bridge - B241 - NB 35W GP over Meacham	130	17-Jun-13	13-Dec-13	718	$0
3AXRDSCYDS2451000	Design Bridge - B245 - Cypress St. over 280	130	17-Jun-13	13-Dec-13	1047	$0
3ANSMLMDDS2011000	Design Bridge - B201 - 35W ML over Meacham	130	17-Jun-13	13-Dec-13	1005	$0
3ANBRPMDDS2031000	Design Bridge - B203 - NB 35W ML Ramp to NB 35W GP	130	17-Jun-13	13-Dec-13	678	$0
Bridge Design - Interchange		215	11-Mar-13	03-Jan-14	515	$0

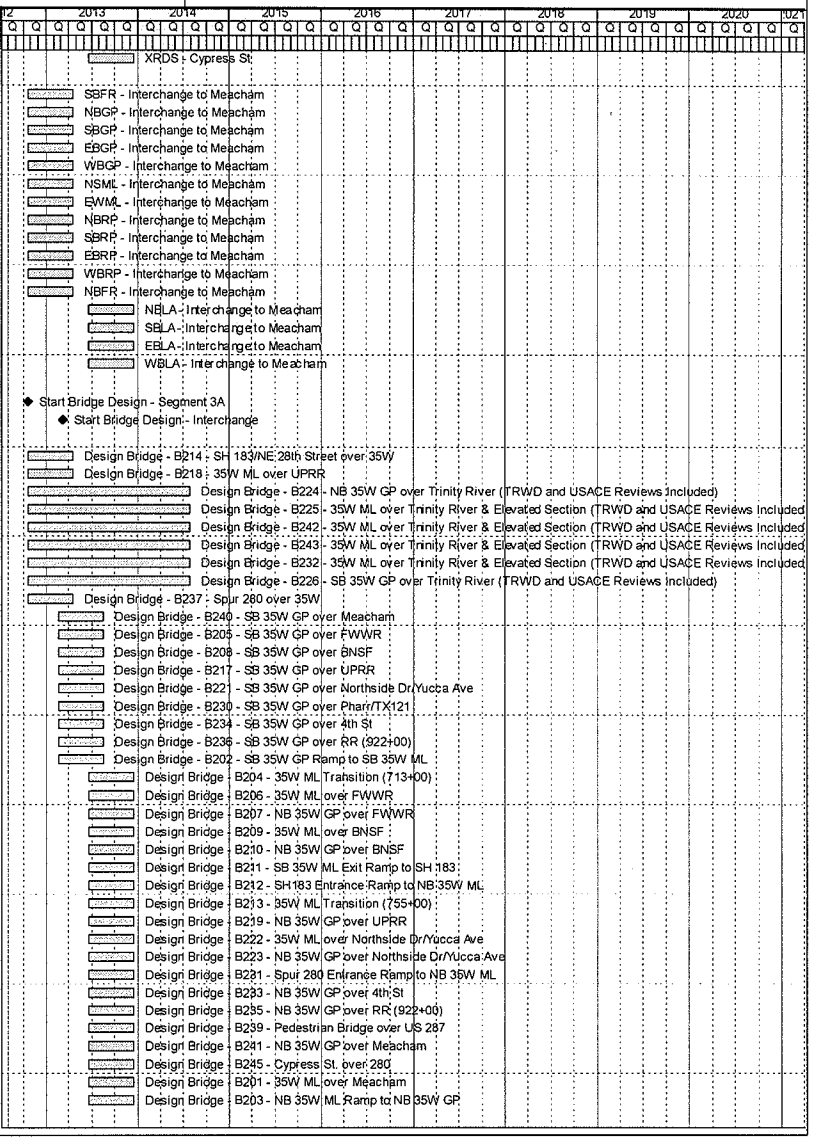

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
ICNBGPIMDS11000	Design Bridge - B2 - 35W NB GP over 820	130	11-Mar-13	06-Sep-13	235	$0
ICSBRPIMDS101000	Design Bridge - B20 - 35W SB - 820 WB GP DC	130	11-Mar-13	06-Sep-13	200	$0
ICSBRPIMDS111000	Design Bridge - B21 - 35W SB - 820 EB GP DC	130	11-Mar-13	06-Sep-13	108	$0
ICWBRPIMDS121000	Design Bridge - B22 - 820 WB - 35W NB GP DC	130	11-Mar-13	06-Sep-13	235	$0
ICEBRPIMDS131000	Design Bridge - B23 - 820 EB - 35W NB GP DC	130	11-Mar-13	06-Sep-13	189	$0
ICEBRPIMDS141000	Design Bridge - B24 - 820 EB - 35W SB GP DC	130	11-Mar-13	06-Sep-13	108	$0
ICWBRPIMDS151000	Design Bridge - B25 - 820 WB - 35W SB GP DC	130	11-Mar-13	06-Sep-13	180	$0
ICNBRPIMDS161000	Design Bridge - B26 - 35W NB - 820 EB GP DC	130	11-Mar-13	06-Sep-13	140	$0
ICWBRPIMDS211000	Design Bridge - B21 - 820 WB - 35W SB ML DC	130	11-Mar-13	06-Sep-13	246	$0
ICNBFRIMDS331000	Design Bridge - B23 - NB 35W FR over Little Fossil Creek	130	11-Mar-13	06-Sep-13	158	$0
ICNBRPIMDS351000	Design Bridge - B25 - 35W NB GP Exit Ramp to Melody Hills	130	11-Mar-13	06-Sep-13	252	$0
ICNSMLIMDS41000	Design Bridge - B4 - 35W ML over 820	130	11-Mar-13	06-Sep-13	222	$0
ICSBGPIMDS71000	Design Bridge - B7 - 35W SB GP over 820	130	11-Mar-13	06-Sep-13	241	$0
ICSBFRIMDS341000	Design Bridge - B24 - SB 35W FR over Little Fossil Creek	130	11-Mar-13	06-Sep-13	242	$0
ICSBGPIMDS32G1000	Design Bridge - B22GPL - 35W over Little Fossil Creek	130	08-Jul-13	03-Jan-14	499	$0
ICNSMLIMDS32M1000	Design Bridge - B22ML - 35W over Little Fossil Creek	130	08-Jul-13	03-Jan-14	515	$0
ICNBRPIMDS171000	Design Bridge - B27 - 35W NB - 820 WB GP DC	130	08-Jul-13	03-Jan-14	352	$0
ICWBRPIMDS181000	Design Bridge - B28 - 820 WB - 35W NB ML DC	130	08-Jul-13	03-Jan-14	343	$0
Retaining Wall Design		315	20-Oct-12	03-Jan-14	1080	$0
NTE3AIC-RW1010	Start Retaining Wall Design - Segment 3A	0	20-Oct-12		554	$0
IC1000	Start Retaining Wall Design - Interchange	0	09-Mar-13		444	$0
Retaining Wall Design - Segment 3A		300	22-Oct-12	13-Dec-13	1095	$0
3AXRDS28DSRW.N27	Retaining Wall RWN27	130	22-Oct-12	19-Apr-13	529	$0
3AXRDS18DSRW.07A	Retaining Wall RW07A	130	22-Oct-12	19-Apr-13	551	$0
3AXRDS18DSRW.08A	Retaining Wall RW08A	130	22-Oct-12	19-Apr-13	553	$0
3AXRDS18DSRW.08B	Retaining Wall RW08B	130	22-Oct-12	19-Apr-13	553	$0
3AXRDS18DSRW.20A	Retaining Wall RW20A	130	22-Oct-12	19-Apr-13	554	$0
3ANSMLDTDSRW.S15	Retaining Wall RWS15	130	22-Oct-12	19-Apr-13	486	$0
3AXRDS28DSRW.S28	Retaining Wall RWS28	130	22-Oct-12	19-Apr-13	525	$0
3AXRDS28DSRW.280S	Retaining Wall RW280S1	130	22-Oct-12	19-Apr-13	553	$0
3AXRDS28DSRW.280N	Retaining Wall RW280N1	130	22-Oct-12	19-Apr-13	553	$0
3AXRDS28DSRW.280N	Retaining Wall RW280N2	130	22-Oct-12	19-Apr-13	505	$0
3ASBRPMDDSRW.02B	Retaining Wall RW02B	130	18-Feb-13	16-Aug-13	481	$0
3ASBRPMDDSRW.02A	Retaining Wall RW02A	130	18-Feb-13	16-Aug-13	648	$0
3ANBFRDTDSRW.N32	Retaining Wall RWN32	130	18-Feb-13	16-Aug-13	550	$0
3ASBGPMDDSRW.S01	Retaining Wall RWS01A	130	18-Feb-13	16-Aug-13	608	$0
3ASBGPMDDSRW.S02	Retaining Wall RWS02	130	18-Feb-13	16-Aug-13	577	$0
3ADSRW.S02A1000	Retaining Wall RWS02A	130	18-Feb-13	16-Aug-13	474	$0
3AXRDSMIDSRW.10A	Retaining Wall RW10A	130	18-Feb-13	16-Aug-13	645	$0
3ASBRPMDDSRW.13A	Retaining Wall RW13A	130	18-Feb-13	16-Aug-13	653	$0
3AXRDS18DSRW.21A	Retaining Wall RW21A	130	18-Feb-13	16-Aug-13	648	$0
3AXRDS18DSRW.21B	Retaining Wall RW21B	130	18-Feb-13	16-Aug-13	645	$0
3ANBFRMDDSRW.N13	Retaining Wall RWN13	130	18-Feb-13	16-Aug-13	446	$0
3ANSMLDTDSRW.N15	Retaining Wall RWN15	130	18-Feb-13	16-Aug-13	560	$0
3ASBRPMDDSRW.S04	Retaining Wall RWS04	130	18-Feb-13	16-Aug-13	469	$0
3ASBRPMDDSRW.S07	Retaining Wall RWS07	130	18-Feb-13	16-Aug-13	395	$0
3ASBGPMDDSRW.S08	Retaining Wall RWS08	130	18-Feb-13	16-Aug-13	424	$0
3ASBRPMDDSRW.S10	Retaining Wall RWS10	130	18-Feb-13	16-Aug-13	625	$0
3ASBFRMDDSRW.S12	Retaining Wall RWS12	130	18-Feb-13	16-Aug-13	396	$0
3ASBRPMDDSRW.S13	Retaining Wall RWS13	130	18-Feb-13	16-Aug-13	637	$0
3ASBFRDTDSRW.S14	Retaining Wall RWS14	130	18-Feb-13	16-Aug-13	478	$0
3ASBFRDTDSRW.S16	Retaining Wall RWS16A	130	18-Feb-13	16-Aug-13	476	$0
3ASBRPDTDSRW.S17	Retaining Wall RWS17A	130	18-Feb-13	16-Aug-13	480	$0
3ASBFRDTDSRW.S20	Retaining Wall RWS20	130	18-Feb-13	16-Aug-13	438	$0
3ASBRPSIDSRW.S251	Retaining Wall RWS25	130	18-Feb-13	16-Aug-13	608	$0
3ASBRPSIDSRW.S271	Retaining Wall RWS27	130	18-Feb-13	16-Aug-13	648	$0
3ASBRPSIDSRW.S291	Retaining Wall RWS29	130	18-Feb-13	16-Aug-13	649	$0
3ASBGPSIDSRW.S301	Retaining Wall RWS30	130	18-Feb-13	16-Aug-13	655	$0
3ASBGPSIDSRW.S311	Retaining Wall RWS31	130	18-Feb-13	16-Aug-13	609	$0
3ASBFRMDDSRW.S32	Retaining Wall RWS32	130	18-Feb-13	16-Aug-13	470	$0

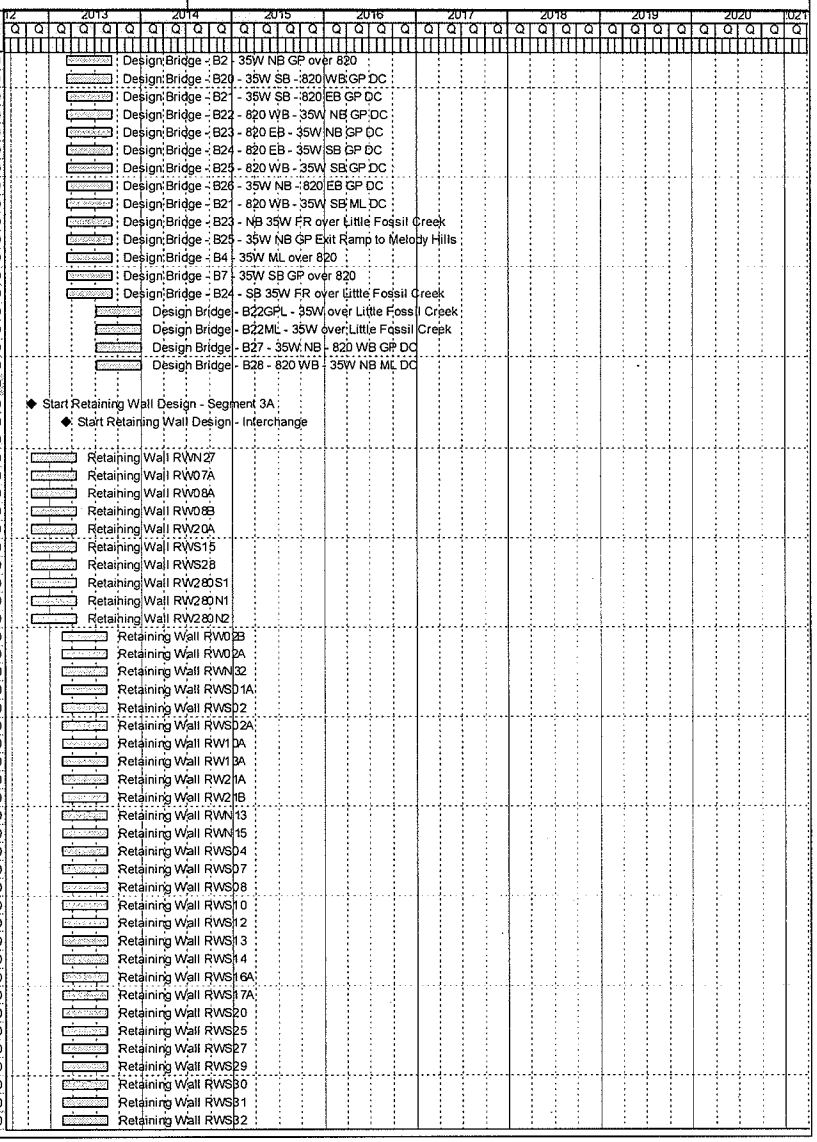

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3ASBRPDTDSRW.S18	Retaining Wall RWS18	130	18-Feb-13	16-Aug-13	472	$0
3ANSMLMDDSRW.03A	Retaining Wall RW03A	130	17-Jun-13	13-Dec-13	1095	$0
3ANBRPMDDSRW.04A	Retaining Wall RW04A	130	17-Jun-13	13-Dec-13	800	$0
3ANSMLMDDSRW.06A	Retaining Wall RW06A	130	17-Jun-13	13-Dec-13	1095	$0
3ANBGPDTDSRW.N20	Retaining Wall RWN20	130	17-Jun-13	13-Dec-13	729	$0
3ANBGPDTDSRW.N21	Retaining Wall RWN21	130	17-Jun-13	13-Dec-13	761	$0
3ANBGPSIDSRW.N23	Retaining Wall RWN23	130	17-Jun-13	13-Dec-13	775	$0
3ANBGPSIDSRW.N25	Retaining Wall RWN25	130	17-Jun-13	13-Dec-13	772	$0
3ANBGPSIDSRW.N26	Retaining Wall RWN26	130	17-Jun-13	13-Dec-13	770	$0
3ANBRPSIDSRW.N31	Retaining Wall RWN31	130	17-Jun-13	13-Dec-13	788	$0
3ANSMLMDDSRW.S03	Retaining Wall RWS03	130	17-Jun-13	13-Dec-13	984	$0
3ANSMLMDDSRW.09A	Retaining Wall RW09A	130	17-Jun-13	13-Dec-13	1091	$0
3ANSMLMDDSRW.11A	Retaining Wall RW11A	130	17-Jun-13	13-Dec-13	1093	$0
3ANBRPMDDSRW.13B	Retaining Wall RW13B	130	17-Jun-13	13-Dec-13	802	$0
3ANBGPMDDSRW.N01	Retaining Wall RWN01	130	17-Jun-13	13-Dec-13	748	$0
3ANBGPMDDSRW.N02	Retaining Wall RWN02	130	17-Jun-13	13-Dec-13	731	$0
3ANBRPMDDSRW.N02A	Retaining Wall RWN02A	130	17-Jun-13	13-Dec-13	733	$0
3ANSMLMDDSRW.N03	Retaining Wall RWN03	130	17-Jun-13	13-Dec-13	984	$0
3ANBRPMDDSRW.N04	Retaining Wall RWN04	130	17-Jun-13	13-Dec-13	732	$0
3ANBGPMDDSRW.N05	Retaining Wall RWN05	130	17-Jun-13	13-Dec-13	804	$0
3ANSMLMDDSRW.N06	Retaining Wall RWN06	130	17-Jun-13	13-Dec-13	1066	$0
3ANBRPMDDSRW.N07	Retaining Wall RWN07	130	17-Jun-13	13-Dec-13	752	$0
3ANBGPMDDSRW.N08	Retaining Wall RWN08	130	17-Jun-13	13-Dec-13	633	$0
3ANSMLMDDSRW.N09	Retaining Wall RWN09	130	17-Jun-13	13-Dec-13	1004	$0
3ANBGPMDDSRW.N10	Retaining Wall RWN10	130	17-Jun-13	13-Dec-13	739	$0
3ANSMLMDDSRW.N11	Retaining Wall RWN11	130	17-Jun-13	13-Dec-13	1004	$0
3ANBRPMDDSRW.N12	Retaining Wall RWN12	130	17-Jun-13	13-Dec-13	791	$0
3ANSMLMDDSRW.S06	Retaining Wall RWS06	130	17-Jun-13	13-Dec-13	1066	$0
3ANSMLMDDSRW.S09	Retaining Wall RWS09	130	17-Jun-13	13-Dec-13	1005	$0
3ANSMLMDDSRW.S11	Retaining Wall RWS11	130	17-Jun-13	13-Dec-13	978	$0
Retaining Wall Design - Interchange		215	11-Mar-13	03-Jan-14	712	$0
ICSBRPIMDSRW.WB04	Retaining Wall WBRW04	130	11-Mar-13	06-Sep-13	351	$0
ICSBRPIMDSRW.WB03	Retaining Wall WBRW03	130	11-Mar-13	06-Sep-13	370	$0
ICSBRPIMDSRW.EB06	Retaining Wall EBRW06	130	11-Mar-13	06-Sep-13	375	$0
ICSBRPIMDSRW.EB05	Retaining Wall EBRW-05	130	11-Mar-13	06-Sep-13	376	$0
ICSBRPIMDSRW.EB02	Retaining Wall EBRW-02	130	11-Mar-13	06-Sep-13	342	$0
ICSBRPIMDSRW.EB01	Retaining Wall EBRW-01	130	11-Mar-13	06-Sep-13	364	$0
ICEBRPIMDSRW.EB12	Retaining Wall EBRW-12	130	11-Mar-13	06-Sep-13	341	$0
ICEBRPIMDSRW.EB11	Retaining Wall EBRW11	130	11-Mar-13	06-Sep-13	341	$0
ICWBRPIMDSRW.WB09	Retaining Wall WBRW-09	130	11-Mar-13	06-Sep-13	320	$0
ICWBRPIMDSRW.WB10	Retaining Wall WBRW 10	130	11-Mar-13	06-Sep-13	316	$0
ICNBRPIMDSRW.WB06	Retaining Wall WBR06	130	08-Jul-13	03-Jan-14	537	$0
ICNBRPIMDSRW.WB05	Retaining Wall WBR05	130	08-Jul-13	03-Jan-14	529	$0
ICNBRPIMDSRW.W04D	Retaining Wall WBRW-04D	130	08-Jul-13	03-Jan-14	564	$0
ICNBRPIMDSRW.W04E	Retaining Wall WBRW-04E	130	08-Jul-13	03-Jan-14	564	$0
ICSBRPIMDSRW.EB03	Retaining Wall EBRW-03	130	08-Jul-13	03-Jan-14	655	$0
ICSBRPIMDSRW.EB04	Retaining Wall EBRW-04	130	08-Jul-13	03-Jan-14	618	$0
ICNBRPIMDSRW.EB09	Retaining Wall EBRW-09	130	08-Jul-13	03-Jan-14	711	$0
ICNBRPIMDSRW.EB10	Retaining Wall EBRW-10	130	08-Jul-13	03-Jan-14	712	$0
ICNBRPIMDSRW.W01A	Retaining Wall WBRW-01A	130	08-Jul-13	03-Jan-14	517	$0
ICWBRPIMDSRW.WB02	Retaining Wall WBRW02	130	08-Jul-13	03-Jan-14	520	$0
ICWBRPIMDSRW.WB01	Retaining Wall WBRW01	130	08-Jul-13	03-Jan-14	504	$0
Procurement		210	22-Apr-13	07-Feb-14	276	$0
Segment 3A		210	22-Apr-13	07-Feb-14	276	$0
Shop Drawings		120	22-Apr-13	04-Oct-13	276	$0
3APCSDB218-1100	Prepare Shop Drawings for Beams - Bridge B218	20	22-Apr-13	17-May-13	305	$0
3APCSDB237-1110	Prepare Shop Drawings for Beams - Bridge B237	20	22-Apr-13	17-May-13	304	$0
3APCSDB205-1070	Prepare Shop Drawings for Beams - Bridge B205	20	19-Aug-13	13-Sep-13	265	$0
3APCSDB202-1080	Prepare Shop Drawings for Beams - Bridge B202	20	19-Aug-13	13-Sep-13	291	$0
3APCSDB217-1120	Prepare Shop Drawings for Beams - Bridge B217	20	19-Aug-13	13-Sep-13	252	$0

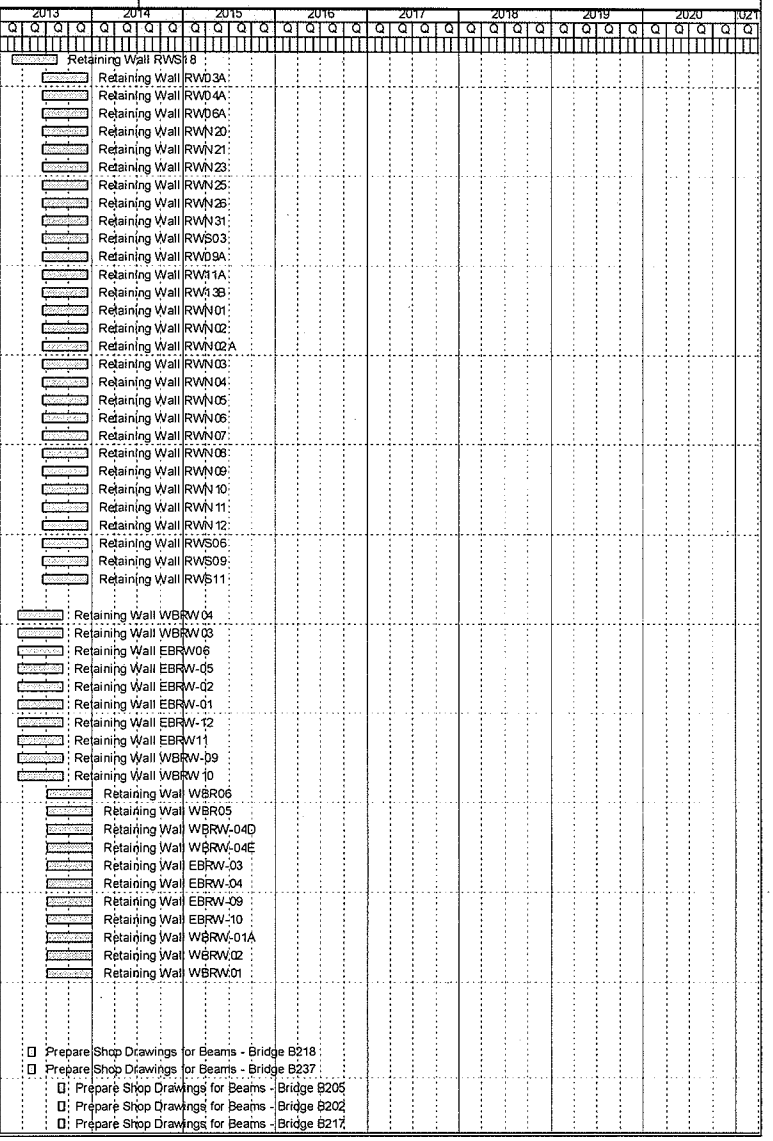

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
3APCSDBXXX-1090	Prepare Shop Drawings for Beams - Bridge BXXX	20	09-Sep-13	04-Oct-13	276	$0
Manufacture & Deliver		190	20-May-13	07-Feb-14	276	$0
3APCMDB218-1030	Manufacture & Deliver Beams for Bridge B218	90	20-May-13	20-Sep-13	305	$0
3APCMDB237-1040	Manufacture & Deliver Beams for Bridge B237	90	20-May-13	20-Sep-13	304	$0
3APCMDB205-1000	Manufacture & Deliver Beams for Bridge B205	90	16-Sep-13	17-Jan-14	265	$0
3APCMDB202-1010	Manufacture & Deliver Beams for Bridge B202	90	16-Sep-13	17-Jan-14	291	$0
3APCMDB217-1050	Manufacture & Deliver Beams for Bridge B217	90	16-Sep-13	17-Jan-14	252	$0
3APCMDBXXX-1020	Manufacture & Deliver Beams for Bridge BXXX	90	07-Oct-13	07-Feb-14	276	$0
Interchange		110	09-Sep-13	07-Feb-14	252	$0
Shop Drawings		20	09-Sep-13	04-Oct-13	252	$0
ICPCSDB33-1070	Prepare Shop Drawings for Beams - B33	20	09-Sep-13	04-Oct-13	158	$0
ICPCSDB34-1080	Prepare Shop Drawings for Beams - B34	20	09-Sep-13	04-Oct-13	242	$0
ICPCSDB1-1090	Prepare Shop Drawings for Beams - B1	20	09-Sep-13	04-Oct-13	235	$0
ICPCSDB7-1100	Prepare Shop Drawings for Beams - B7	20	09-Sep-13	04-Oct-13	241	$0
ICPCSDB4-1110	Prepare Shop Drawings for Beams - B4	20	09-Sep-13	04-Oct-13	222	$0
ICPCSDB35-1120	Prepare Shop Drawings for Beams - B35	20	09-Sep-13	04-Oct-13	252	$0
ICPCSDB16-1130	Prepare Shop Drawings for Beams - B16	20	09-Sep-13	04-Oct-13	165	$0
ICPCSDB11-1140	Prepare Shop Drawings for Beams - B11	20	09-Sep-13	04-Oct-13	188	$0
ICPCSDB10-1150	Prepare Shop Drawings for Beams - B10	20	09-Sep-13	04-Oct-13	200	$0
ICPCSDB14-1160	Prepare Shop Drawings for Beams - B14	20	09-Sep-13	04-Oct-13	125	$0
ICPCSDB13-1170	Prepare Shop Drawings for Beams - B13	20	09-Sep-13	04-Oct-13	189	$0
ICPCSDB12-1180	Prepare Shop Drawings for Beams - B12	20	09-Sep-13	04-Oct-13	235	$0
ICPCSDB15-1190	Prepare Shop Drawings for Beams - B15	20	09-Sep-13	04-Oct-13	194	$0
ICPCSDB21-1200	Prepare Shop Drawings for Beams - B21	20	09-Sep-13	04-Oct-13	246	$0
Manufacture & Deliver		90	07-Oct-13	07-Feb-14	252	$0
ICPCMDB33-1210	Manufacture & Deliver Beams for Bridge B33	90	07-Oct-13	07-Feb-14	158	$0
ICPCMDB34-1220	Manufacture & Deliver Beams for Bridge B34	90	07-Oct-13	07-Feb-14	242	$0
ICPCMDB1-1230	Manufacture & Deliver Beams for Bridge B1	90	07-Oct-13	07-Feb-14	235	$0
ICPCMDB7-1240	Manufacture & Deliver Beams for Bridge B7	90	07-Oct-13	07-Feb-14	241	$0
ICPCMDB4-1250	Manufacture & Deliver Beams for Bridge B4	90	07-Oct-13	07-Feb-14	222	$0
ICPCMDB35-1260	Manufacture & Deliver Beams for Bridge B35	90	07-Oct-13	07-Feb-14	252	$0
ICPCMDB16-1270	Manufacture & Deliver Beams for Bridge B16	90	07-Oct-13	07-Feb-14	165	$0
ICPCMDB11-1280	Manufacture & Deliver Beams for Bridge B11	90	07-Oct-13	07-Feb-14	188	$0
ICPCMDB10-1290	Manufacture & Deliver Beams for Bridge B10	90	07-Oct-13	07-Feb-14	200	$0
ICPCMDB14-1300	Manufacture & Deliver Beams for Bridge B14	90	07-Oct-13	07-Feb-14	125	$0
ICPCMDB13-1310	Manufacture & Deliver Beams for Bridge B13	90	07-Oct-13	07-Feb-14	189	$0
ICPCMDB12-1320	Manufacture & Deliver Beams for Bridge B12	90	07-Oct-13	07-Feb-14	235	$0
ICPCMDB15-1330	Manufacture & Deliver Beams for Bridge B15	90	07-Oct-13	07-Feb-14	194	$0
ICPCMDB21-1340	Manufacture & Deliver Beams for Bridge B21	90	07-Oct-13	07-Feb-14	246	$0
Permits		386	01-Oct-12	24-Mar-14	893	$0
Rail Road Permit		248	01-Oct-12	11-Sep-13	1031	$0
Rail Road Permit for Brige 205		248	01-Oct-12	11-Sep-13	256	$0
3ASBGPMD2051000	Prepare Rail Road Permit for Bridge 205	120	01-Oct-12	15-Mar-13	255	$0
3ASBGPMD2051010	Review and Approval of Rail Road Permit for Bridge 205	180	16-Mar-13	11-Sep-13	358	$0
Rail Road Permit for Brige 206		248	01-Oct-12	11-Sep-13	948	$0
3ANSMLMD2061000	Prepare Rail Road Permit for Bridge 206	120	01-Oct-12	15-Mar-13	948	$0
3ANSMLMD2061010	Review and Approval of Rail Road Permit for Bridge 206	180	16-Mar-13	11-Sep-13	1328	$0
Rail Road Permit for Brige 207		248	01-Oct-12	11-Sep-13	654	$0
3ANBGPMD2071000	Prepare Rail Road Permit for Bridge 207	120	01-Oct-12	15-Mar-13	654	$0
3ANBGPMD2071010	Review and Approval of Rail Road Permit for Bridge 207	180	16-Mar-13	11-Sep-13	916	$0
Rail Road Permit for Brige 208		248	01-Oct-12	11-Sep-13	533	$0
3ASBGPMD2081000	Prepare Rail Road Permit for Bridge 208	120	01-Oct-12	15-Mar-13	533	$0
3ASBGPMD2081010	Receive Rail Road Permit for Bridge 208	180	16-Mar-13	11-Sep-13	747	$0
Rail Road Permit for Brige 209		248	01-Oct-12	11-Sep-13	1031	$0
3ANSMLMD2091000	Prepare Rail Road Permit for Bridge 209	120	01-Oct-12	15-Mar-13	1030	$0
3ANSMLMD2091010	Receive Rail Road Permit for Bridge 209	180	16-Mar-13	11-Sep-13	1443	$0
Rail Road Permit for Brige 210		248	01-Oct-12	11-Sep-13	684	$0
3ANBGPMD2101000	Prepare Rail Road Permit for Bridge 210	120	01-Oct-12	15-Mar-13	684	$0
3ANBGPMD2101010	Receive Rail Road Permit for Bridge 210	180	16-Mar-13	11-Sep-13	958	$0

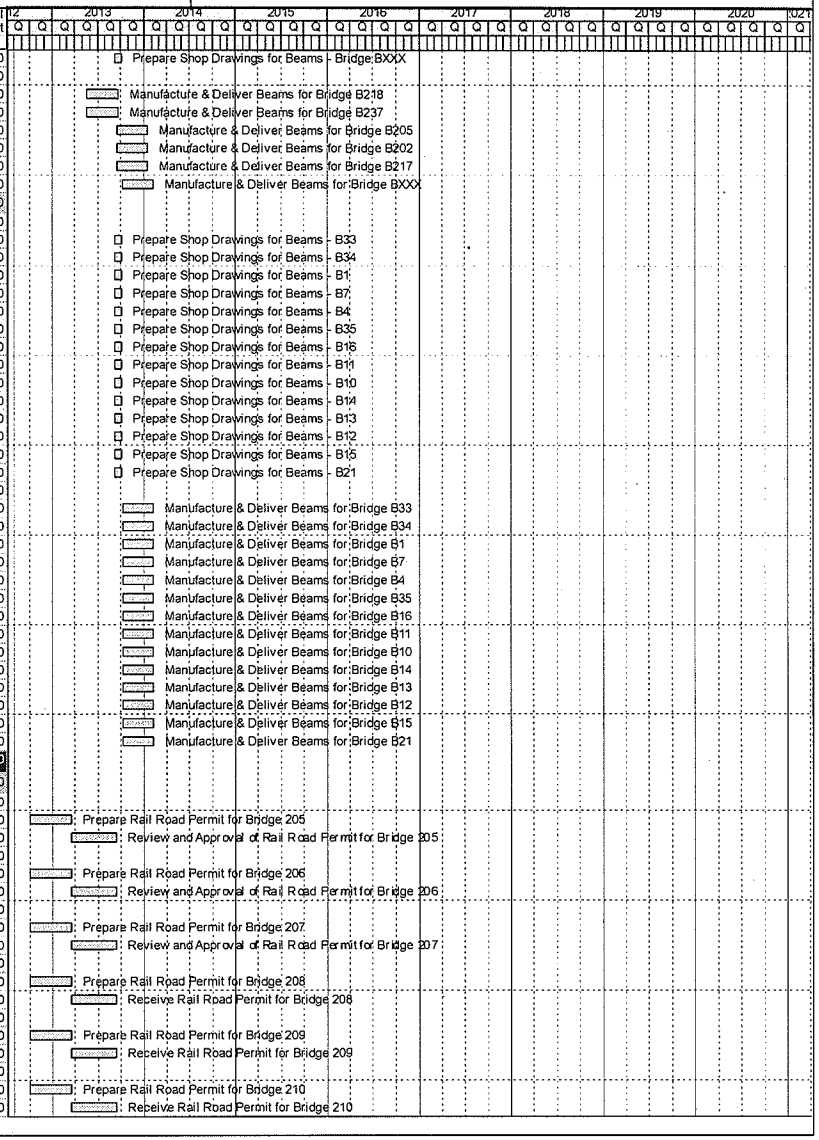

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Rail Road Permit for Brige 217		248	01-Oct-12	11-Sep-13	266	$0
3ASBGPDT2171000	Prepare Rail Road Permit for Bridge 217	120	01-Oct-12	15-Mar-13	265	$0
3ASBGPDT2171010	Receive Rail Road Permit for Bridge 217	180	16-Mar-13	11-Sep-13	372	$0
Rail Road Permit for Brige 218		248	01-Oct-12	11-Sep-13	207	$0
3ANSMLDT2181000	Prepare Rail Road Permit for Bridge 218	120	01-Oct-12	15-Mar-13	207	$0
3ANSMLDT2181010	Receive Rail Road Permit for Bridge 218	180	16-Mar-13	11-Sep-13	291	$0
Rail Road Permit for Brige 219		248	01-Oct-12	11-Sep-13	659	$0
3ANBGPDT2191000	Prepare Rail Road Permit for Bridge 219	120	01-Oct-12	15-Mar-13	659	$0
3ANBGPDT2191010	Receive Rail Road Permit for Bridge 219	180	16-Mar-13	11-Sep-13	923	$0
Rail Road Permit for Brige 235		248	01-Oct-12	11-Sep-13	747	$0
3ANBGPSI2351000	Prepare Rail Road Permit for Bridge 235	120	01-Oct-12	15-Mar-13	747	$0
3ANBGPSI2351010	Receive Rail Road Permit for Bridge 235	180	16-Mar-13	11-Sep-13	1047	$0
Rail Road Permit for Brige 236		248	01-Oct-12	11-Sep-13	507	$0
3ASBGPSI2361000	Prepare Rail Road Permit for Bridge 236	120	01-Oct-12	15-Mar-13	507	$0
3ASBGPSI2361010	Receive Rail Road Permit for Bridge 236	180	16-Mar-13	11-Sep-13	711	$0
US Army Corp Permit		540	01-Oct-12	24-Mar-14	463	$0
3ANBGPDT2241000	Preparation and application of Permit 404 and 408	180	01-Oct-12	29-Mar-13	463	$0
3ANBGPDT2241010	Review and Approval of US Army Corp Permit 404 and 408 (Bridge 224, 225 and 226)	360	30-Mar-13	24-Mar-14	463	$0
Construction		1248	20-Apr-13	31-Jan-18	37	$892,775,686
Segment 3A Construction		1248	20-Apr-13	31-Jan-18	37	$595,392,400
A132900	Base Construction Cost Over / Under	1248	22-Apr-13	31-Jan-18	37	$0
Phase 1		760	20-Apr-13	18-Mar-16	525	$170,844,858
3AMSMS11005	Segment 3A- Phase 1 Finish	0		03-Mar-16	4	$0
Stage 1		640	20-Apr-13	02-Oct-15	645	$137,910,617
3AMSMS111000	Segment 3A- Phase 1 Stage 1 Finish	0		08-Jul-15	4	$0
3AMSMS11000	Segment 3A- Phase 1 Stage 1 Misc Roadway Items Finish	0		02-Oct-15	905	$0
NBFR - Mecham to Dewey		215	22-Aug-14	18-Jun-15	721	$7,684,765
TCP & Temp Work		211	22-Aug-14	12-Jun-15	20	$172,818
Drainage		63	24-Sep-14	19-Jan-15	16	$868,095
Roadworks		142	16-Sep-14	12-Jun-15	16	$5,195,473
ITS / Signs / Stripes / Electrical / MISC.		58	31-Mar-15	18-Jun-15	721	$482,243
Noise Wall		2	26-Aug-14	27-Aug-14	227	$24,346
Retaining Wall RWN13-M1		0			0	$0
Retaining Wall RWN13-M2		0			0	$0
Retaining Wall RWN13-S		40	24-Sep-14	01-Dec-14	131	$940,809
NBFR - Dewey to S. of Trinity River		8	14-May-14	23-May-14	295	$195,286
TCP & Temp Work		8	14-May-14	23-May-14	295	$195,286
NBFR - S. of Trinity River to IH-30		236	22-Aug-14	17-Jul-15	700	$7,327,196
TCP & Temp Work		229	22-Aug-14	08-Jul-15	2	$270,747
Drainage		65	03-Oct-14	09-Feb-15	1	$979,735
Roadworks		166	29-Aug-14	08-Jul-15	1	$5,899,104
ITS / Signs / Stripes / Electrical / MISC.		62	23-Apr-15	17-Jul-15	700	$650,146
Noise Wall		2	27-Aug-14	28-Aug-14	226	$27,458
SBFR - Meacham to Dewey		291	22-Aug-14	02-Oct-15	645	$21,511,564
TCP & Temp Work		226	22-Aug-14	02-Jul-15	8	$818,349
Drainage		76	02-Oct-14	20-Feb-15	4	$2,077,698
Roadworks		183	29-Aug-14	02-Jul-15	4	$12,007,811
ITS / Signs / Stripes / Electrical / MISC.		116	24-Apr-15	02-Oct-15	645	$2,036,560
Noise Wall		3	29-Aug-14	02-Sep-14	228	$58,273
Retaining Wall RWS12		81	16-Sep-14	30-Jan-15	95	$4,158,187
Retaining Wall RWS32		20	19-Nov-14	23-Dec-14	118	$354,705
SBFR - Dewey to S. of Trinity River		185	22-Aug-14	07-May-15	751	$6,029,851
TCP & Temp Work		159	22-Aug-14	01-Apr-15	72	$498,082
Drainage		38	03-Nov-14	08-Jan-15	51	$431,611
Roadworks		101	26-Sep-14	01-Apr-15	51	$2,749,707
ITS / Signs / Stripes / Electrical / MISC.		58	17-Feb-15	07-May-15	751	$889,978
Noise Wall		2	26-Aug-14	27-Aug-14	227	$12,097
Retaining Wall RWS13B		0			0	$0
Retaining Wall RWS14		14	24-Dec-14	14-Jan-15	104	$106,409

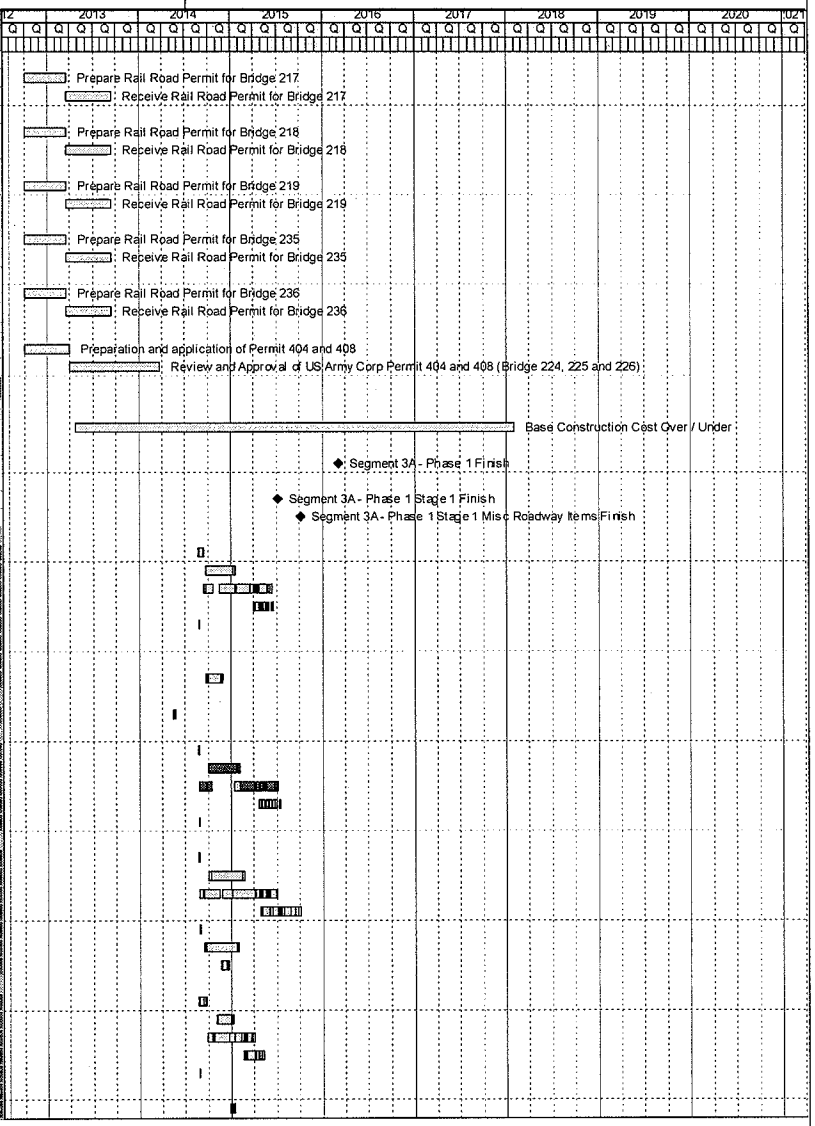

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Retaining Wall RWS16A	15	24-Dec-14	16-Jan-15	109	$218,013
	Retaining Wall RWS20	47	24-Dec-14	11-Mar-15	71	$1,123,959
	Retaining Wall RWS38	0			0	$0
	SBFR - S. of Trinity River to IH-30	182	06-Sep-14	19-May-15	743	$4,624,007
	TCP & Temp Work	176	06-Sep-14	11-May-15	44	$106,874
	Drainage	48	20-Oct-14	19-Jan-15	32	$632,987
	Roadworks	118	30-Sep-14	11-May-15	32	$3,479,119
	ITS / Signs / Stripes / Electrical / MISC.	48	13-Mar-15	19-May-15	743	$387,282
	Noise Wall	2	11-Sep-14	12-Sep-14	215	$17,745
	NBGP - Dewey to S. of Trinity River	76	06-Sep-14	22-Dec-14	849	$0
	TCP & Temp Work	70	06-Sep-14	12-Dec-14	150	$0
	Drainage	8	29-Sep-14	08-Oct-14	109	$0
	Roadworks	46	22-Sep-14	12-Dec-14	109	$0
	ITS / Signs / Stripes / Electrical / MISC.	42	24-Oct-14	22-Dec-14	849	$0
	Noise Wall	5	16-Sep-14	22-Sep-14	209	$0
	NBRP - Meacham to Dewey	23	20-Apr-13	22-May-13	557	$639,616
	TCP & Temp Work	23	20-Apr-13	22-May-13	557	$639,616
	NBRP - Dewey to S. of Trinity River	21	20-Apr-13	20-May-13	559	$597,669
	TCP & Temp Work	21	20-Apr-13	20-May-13	559	$597,669
	SBGP - Meacham to Dewey	225	22-Aug-14	02-Jul-15	711	$13,671,275
	TCP & Temp Work	225	22-Aug-14	02-Jul-15	6	$393,814
	Drainage	24	18-Sep-14	28-Oct-14	39	$528,046
	Roadworks	128	29-Aug-14	23-Apr-15	39	$5,141,971
	ITS / Signs / Stripes / Electrical / MISC.	81	02-Mar-15	22-Jun-15	719	$1,021,431
	Noise Wall	3	28-Aug-14	01-Sep-14	224	$42,539
	B205 - SB 35W GP over FWWR	220	29-Aug-14	02-Jul-15	6	$4,879,185
	Retaining Wall RWS05	0			0	$0
	Retaining Wall RWS06	58	24-Oct-14	30-Jan-15	95	$1,663,289
	SBRP - Meacham to Dewey	224	22-Aug-14	01-Jul-15	712	$17,021,965
	TCP & Temp Work	224	22-Aug-14	01-Jul-15	7	$428,955
	Drainage	24	30-Sep-14	07-Nov-14	91	$428,691
	Roadworks	65	19-Sep-14	16-Jan-15	91	$2,554,210
	ITS / Signs / Stripes / Electrical / MISC.	38	05-Dec-14	23-Jan-15	823	$243,273
	Noise Wall	2	26-Aug-14	27-Aug-14	227	$8,201
	B202 - SB 35W GP Ramp to SB 35W ML	204	19-Sep-14	01-Jul-15	7	$8,376,364
	B-XXX - FR to GPL Entrance (TBD)	203	19-Sep-14	30-Jun-15	8	$1,998,571
	Retaining Wall RWS33	0			0	$0
	Retaining Wall RWS04	21	08-Oct-14	11-Nov-14	141	$418,316
	Retaining Wall RWS05	21	08-Oct-14	11-Nov-14	141	$0
	Retaining Wall RWMB01	21	08-Oct-14	11-Nov-14	141	$0
	Retaining Wall RWMB02	21	08-Oct-14	11-Nov-14	141	$0
	Retaining Wall RWS02A	17	08-Oct-14	04-Nov-14	145	$318,676
	Retaining Wall RW02B	11	08-Oct-14	27-Oct-14	151	$42,628
	Retaining Wall RWS07	82	08-Oct-14	24-Feb-15	80	$2,209,076
	NSML - Dewey to S. of Trinity River	375	20-Apr-13	26-Sep-14	910	$21,617,973
	TCP & Temp Work	375	20-Apr-13	26-Sep-14	205	$304,591
	Drainage	30	11-Jun-13	31-Jul-13	299	$597,249
	Roadworks	146	20-May-13	10-Feb-14	275	$5,194,037
	ITS / Signs / Stripes / Electrical / MISC.	62	13-Dec-13	10-Mar-14	1054	$740,619
	Noise Wall	2	26-Apr-13	29-Apr-13	574	$33,572
	B218 - 35W ML over UPRR	271	13-Sep-13	26-Sep-14	205	$12,783,485
	Retaining Wall RWN18A-S	0			0	$0
	Retaining Wall RWS15-S	77	31-May-13	02-Oct-13	382	$2,024,424
	SBRP - Dewey to S. of Trinity River	133	22-Aug-14	24-Feb-15	803	$2,673,569
	TCP & Temp Work	130	22-Aug-14	19-Feb-15	101	$728,696
	Drainage	20	31-Oct-14	09-Dec-14	73	$223,463
	Roadworks	75	02-Oct-14	19-Feb-15	73	$1,116,785
	ITS / Signs / Stripes / Electrical / MISC.	34	08-Jan-15	24-Feb-15	803	$91,293
	Noise Wall	2	26-Aug-14	27-Aug-14	227	$6,477
	Retaining Wall RWS16	0			0	$0

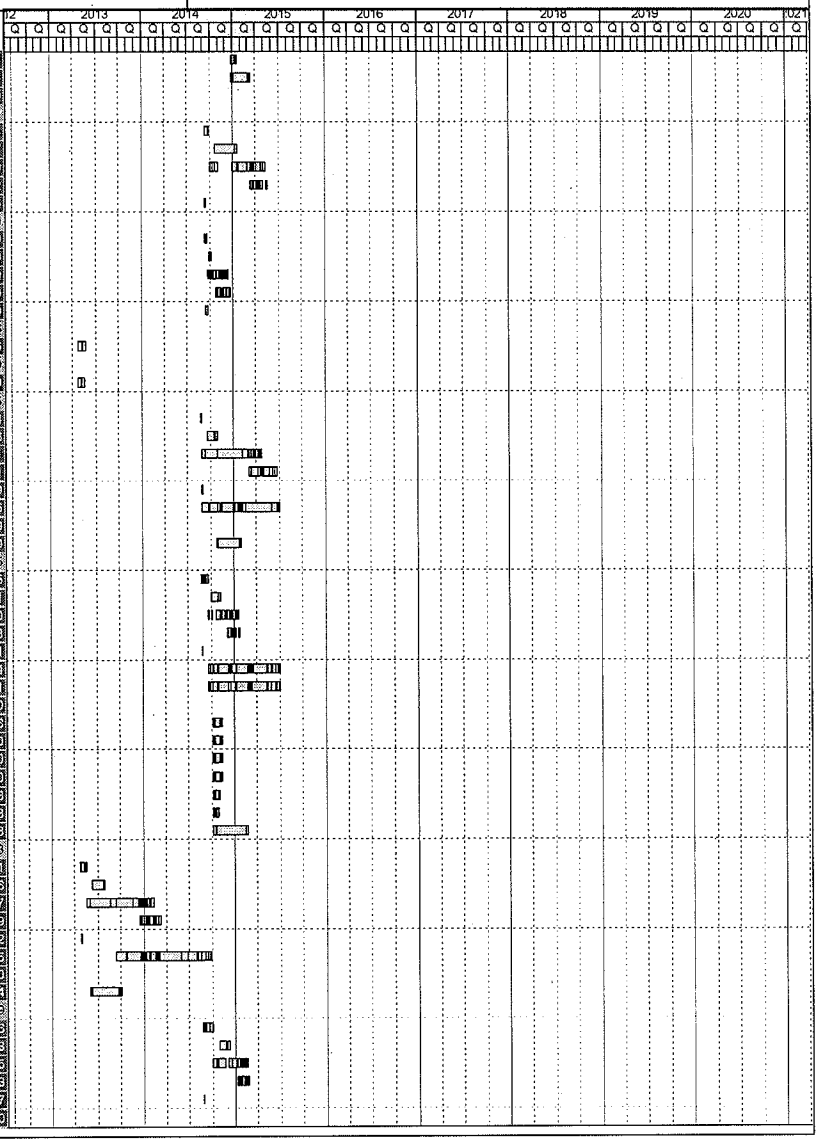

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Retaining Wall RWS17A	12	24-Nov-14	15-Dec-14	123	$145,801
	Retaining Wall RW17B	0			0	$0
	Retaining Wall RWS18	19	24-Nov-14	26-Dec-14	116	$361,054
	XRDS - SH 183/NE 28th St.	47	20-Apr-13	25-Jun-13	533	$1,358,033
	TCP & Temp Work	47	20-Apr-13	25-Jun-13	533	$441,157
	Retaining Wall RW07A	24	16-May-13	25-Jun-13	444	$405,799
	Retaining Wall RW08A-S	22	16-May-13	21-Jun-13	446	$249,493
	Retaining Wall RW08B-S	22	16-May-13	21-Jun-13	446	$261,584
	XRDS - Spur 280	275	20-Apr-13	09-May-14	1010	$17,514,240
	TCP & Temp Work	275	20-Apr-13	09-May-14	305	$135,374
	Drainage	63	11-Jun-13	28-Sep-13	272	$865,615
	Roadworks	149	20-May-13	14-Feb-14	272	$2,463,096
	ITS / Signs / Stripes / Electrical / MISC.	59	03-Dec-13	21-Feb-14	1065	$471,331
	Noise Wall	2	24-Apr-13	25-Apr-13	576	$24,265
	B237 - Spur 280 over 35W	255	20-May-13	09-May-14	305	$8,802,733
	Retaining Wall RW280S1	22	24-Jun-13	26-Jul-13	424	$468,436
	Retaining Wall RW280N1	22	24-Jun-13	26-Jul-13	424	$447,477
	Retaining Wall RW280N2-M	24	24-Jun-13	30-Jul-13	422	$484,737
	Retaining Wall RW280N2-S	62	31-May-13	09-Sep-13	397	$1,581,925
	Retaining Wall RWN27	42	31-May-13	06-Aug-13	417	$835,200
	Retaining Wall RWS28	45	31-May-13	09-Aug-13	414	$954,052
	SBGP - Dewey to S. of Trinity River	210	22-Aug-14	11-Jun-15	726	$13,399,042
	TCP & Temp Work	210	22-Aug-14	11-Jun-15	5	$220,609
	Drainage	16	30-Sep-14	24-Oct-14	61	$296,607
	Roadworks	110	12-Sep-14	02-Apr-15	37	$3,476,827
	ITS / Signs / Stripes / Electrical / MISC.	50	26-Feb-15	30-Apr-15	755	$592,687
	Noise Wall	2	26-Aug-14	27-Aug-14	211	$23,864
	Retaining Wall RWS21	0			0	$0
	B217 - SB 35W GP over UPRR	195	12-Sep-14	11-Jun-15	5	$8,789,447
	XRDS - Yucca Av./Northside Dr.	110	20-Apr-13	20-Sep-13	1175	$2,044,533
	TCP & Temp Work	105	20-Apr-13	13-Sep-13	475	$135,392
	Drainage	23	28-May-13	09-Jul-13	355	$269,007
	Roadworks	72	09-May-13	13-Sep-13	355	$1,155,909
	ITS / Signs / Stripes / Electrical / MISC.	33	07-Aug-13	20-Sep-13	1175	$97,361
	Noise Wall	4	26-Apr-13	01-May-13	572	$7,541
	Retaining Wall RW20A	26	25-Jun-13	30-Jul-13	506	$378,326
	Stage 2	760	20-Apr-13	18-Mar-16	525	$32,934,241
3AMSMS121000	Segment 3A- Phase 1 Stage 2 Finish	0		03-Mar-16	4	$0
3AMS21000	Segment 3A- Phase 1 Stage 2 Misc Roadway Items Finish	0		18-Mar-16	737	$0
	SBGP - S. of Trinity River to IH-30	10	09-Jul-15	22-Jul-15	163	$277,725
	TCP & Temp Work	10	09-Jul-15	22-Jul-15	163	$277,725
	NBGP - S. of Trinity River to IH-30	38	09-Jul-15	31-Aug-15	135	$1,246,646
	TCP & Temp Work	38	09-Jul-15	31-Aug-15	135	$1,246,646
	NBFR - Meacham to Dewey	182	09-Jul-15	18-Mar-16	525	$7,684,765
	TCP & Temp Work	171	09-Jul-15	03-Mar-16	2	$172,818
	Drainage	45	05-Aug-15	23-Oct-15	2	$868,095
	Roadworks	123	20-Jul-15	03-Mar-16	2	$5,196,479
	ITS / Signs / Stripes / Electrical / MISC.	53	06-Jan-16	18-Mar-16	525	$482,243
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$24,346
	Retaining Wall RWN13-M1	0			0	$0
	Retaining Wall RWN13-M2	0			0	$0
	Retaining Wall RWN13-S	40	28-Jul-15	29-Sep-15	92	$940,809
	SBFR - Dewey to S. of Trinity River	81	09-Jul-15	29-Oct-15	626	$911,258
	TCP & Temp Work	71	09-Jul-15	15-Oct-15	102	$22,962
	Drainage	11	05-Aug-15	24-Aug-15	75	$86,322
	Roadworks	45	28-Jul-15	15-Oct-15	75	$549,941
	ITS / Signs / Stripes / Electrical / MISC.	38	08-Sep-15	29-Oct-15	626	$143,604
	Noise Wall	5	20-Jul-15	24-Jul-15	161	$2,419
	Retaining Wall RWS14	13	18-Aug-15	04-Sep-15	105	$106,409
	NBFR - Dewey to S. of Trinity River	140	09-Jul-15	20-Jan-16	567	$5,552,590

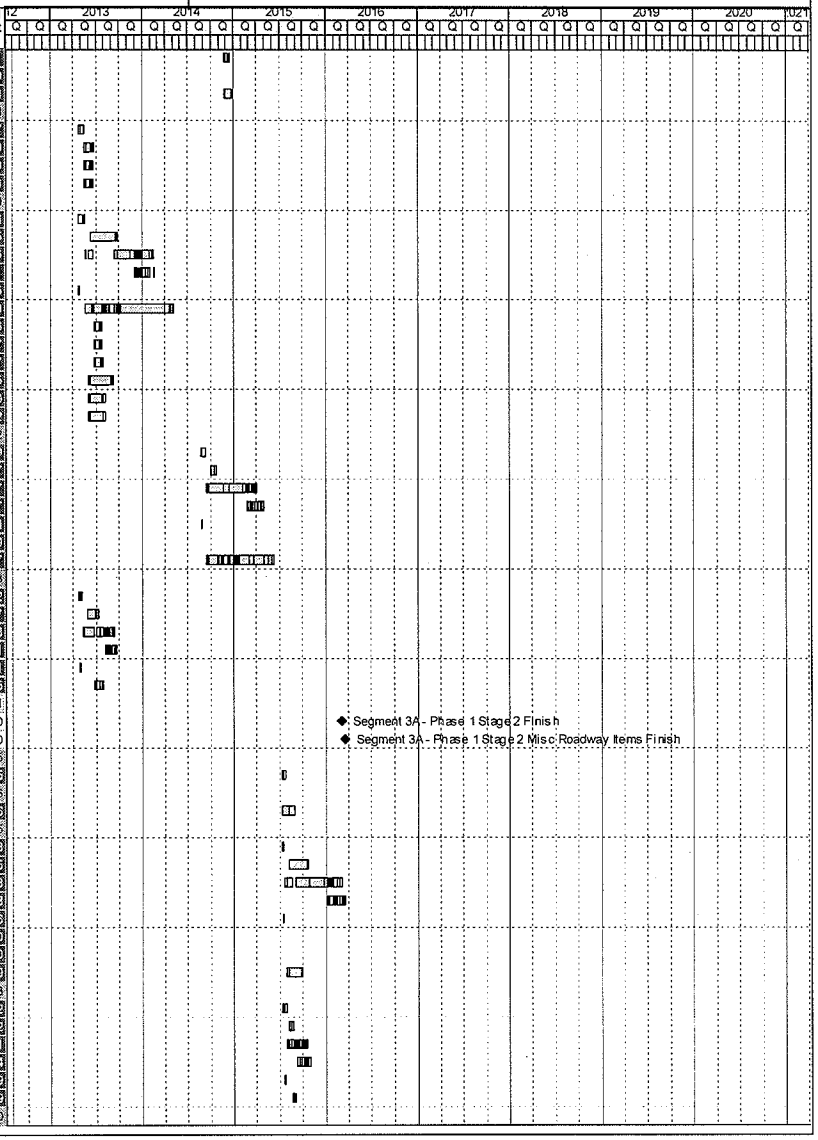

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	TCP & Temp Work	140	09-Jul-15	20-Jan-16	33	$69,165
	Drainage	16	19-Aug-15	16-Sep-15	57	$162,498
	Roadworks	62	29-Jul-15	18-Nov-15	57	$1,173,376
	ITS / Signs / Stripes / Electrical / MISC.	32	13-Oct-15	25-Nov-15	607	$54,509
	Noise Wall	2	15-Jul-15	16-Jul-15	167	$4,560
	Retaining Wall RWN32	94	11-Aug-15	20-Jan-16	29	$4,097,481
	SBFR - Meacham to Dewey	148	09-Jul-15	01-Feb-16	25	$4,158,187
	Retaining Wall RWS12	148	09-Jul-15	01-Feb-16	25	$4,158,187
	SBFR - S. of Trinity River to IH-30	65	06-Sep-14	02-Jan-15	840	$1,198,193
	TCP & Temp Work	76	06-Sep-14	22-Dec-14	148	$28,500
	Drainage	10	06-Oct-14	22-Oct-14	107	$168,797
	Roadworks	50	23-Sep-14	22-Dec-14	107	$927,765
	ITS / Signs / Stripes / Electrical / MISC.	39	11-Nov-14	02-Jan-15	840	$68,399
	Noise Wall	5	16-Sep-14	22-Sep-14	213	$4,732
	NBRP - Meacham to Dewey	58	09-Jul-15	28-Sep-15	649	$244,273
	TCP & Temp Work	54	09-Jul-15	22-Sep-15	119	$9,025
	Drainage	9	27-Jul-15	07-Aug-15	88	$45,909
	Roadworks	37	20-Jul-15	22-Sep-15	88	$170,570
	ITS / Signs / Stripes / Electrical / MISC.	31	17-Aug-15	28-Sep-15	649	$17,430
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$1,331
	XRDS - SH 183/NE 28th St	295	29-Apr-13	06-Jun-14	990	$8,470,810
	TCP & Temp Work	295	29-Apr-13	06-Jun-14	456	$135,374
	Drainage	55	07-Jun-13	09-Sep-13	421	$747,965
	Roadworks	131	16-May-13	08-Jan-14	421	$3,197,426
	ITS / Signs / Stripes / Electrical / MISC.	52	04-Nov-13	14-Jan-14	1093	$404,974
	Noise Wall	2	24-Apr-13	25-Apr-13	747	$20,944
	B214 - SH 183/NE 28th Street over 35W	277	16-May-13	06-Jun-14	456	$3,964,127
	XRDS - Yucca Av./Northside Dr	164	09-Jul-15	23-Feb-16	543	$3,189,775
	TCP & Temp Work	161	09-Jul-15	18-Feb-16	12	$89,347
	Drainage	40	17-Aug-15	28-Oct-15	10	$522,190
	Roadworks	103	07-Aug-15	18-Feb-16	10	$2,243,821
	ITS / Signs / Stripes / Electrical / MISC.	52	14-Dec-15	23-Feb-16	543	$319,780
	Noise Wall	2	20-Jul-15	21-Jul-15	164	$14,638
	Phase 2	214	12-Jun-15	06-Apr-16	512	$81,182,862
3AMSMS21000	Segment 3A - Phase 2 Finish	0		07-Mar-16	0	$0
	Stage 1	214	12-Jun-15	06-Apr-16	512	$40,554,527
3AMSMS211000	Segment 3A - Phase 2 Stage 1 Finish	0		29-Feb-16	7	$0
3AMS1003	Segment 3A - Phase 2 Stage 1 Misc Roadway Items Finish	0		06-Apr-16	718	$0
	SBRP - Meacham to Dewey	62	09-Jul-15	02-Oct-15	111	$1,500,285
	TCP & Temp Work	62	09-Jul-15	02-Oct-15	111	$508,730
	Retaining Wall RWS10	35	06-Aug-15	02-Oct-15	91	$891,556
	SBGP - Meacham to Dewey	169	09-Jul-15	28-Mar-16	519	$8,604,152
	TCP & Temp Work	153	09-Jul-15	08-Feb-16	20	$1,475,704
	Drainage	18	28-Aug-15	02-Oct-15	15	$363,719
	Roadworks	95	13-Aug-15	08-Feb-16	15	$3,535,105
	ITS / Signs / Stripes / Electrical / MISC.	64	30-Dec-15	28-Mar-16	519	$694,059
	Noise Wall	2	15-Jul-15	16-Jul-15	167	$29,246
	B208 - SB 35W GP over BNSF	116	13-Aug-15	21-Jan-16	32	$2,503,319
	SBGP - S. of Trinity River to IH-30	196	09-Jul-15	06-Apr-16	512	$13,147,446
	TCP & Temp Work	168	09-Jul-15	29-Feb-16	5	$619,722
	Drainage	17	03-Aug-15	28-Aug-15	4	$528,120
	Roadworks	117	27-Jul-15	29-Feb-16	4	$4,950,449
	ITS / Signs / Stripes / Electrical / MISC.	73	28-Dec-15	06-Apr-16	512	$991,015
	Noise Wall	3	17-Jul-15	21-Jul-15	164	$42,453
	B234 - SB 35W GP over 4th St	111	27-Jul-15	28-Dec-15	50	$1,593,121
	B238 - SB 35W GP over RR (922+00)	138	27-Jul-15	03-Feb-16	23	$2,420,991
	B230 - SB 35W GP over Pharr/TX121	78	11-Sep-15	29-Dec-15	49	$669,468
	Retaining Wall RWS26-M	0			0	$0
	Retaining Wall RWS30	9	27-Aug-15	09-Sep-15	103	$76,792
	Retaining Wall RWS31	46	27-Aug-15	18-Nov-15	64	$1,255,416

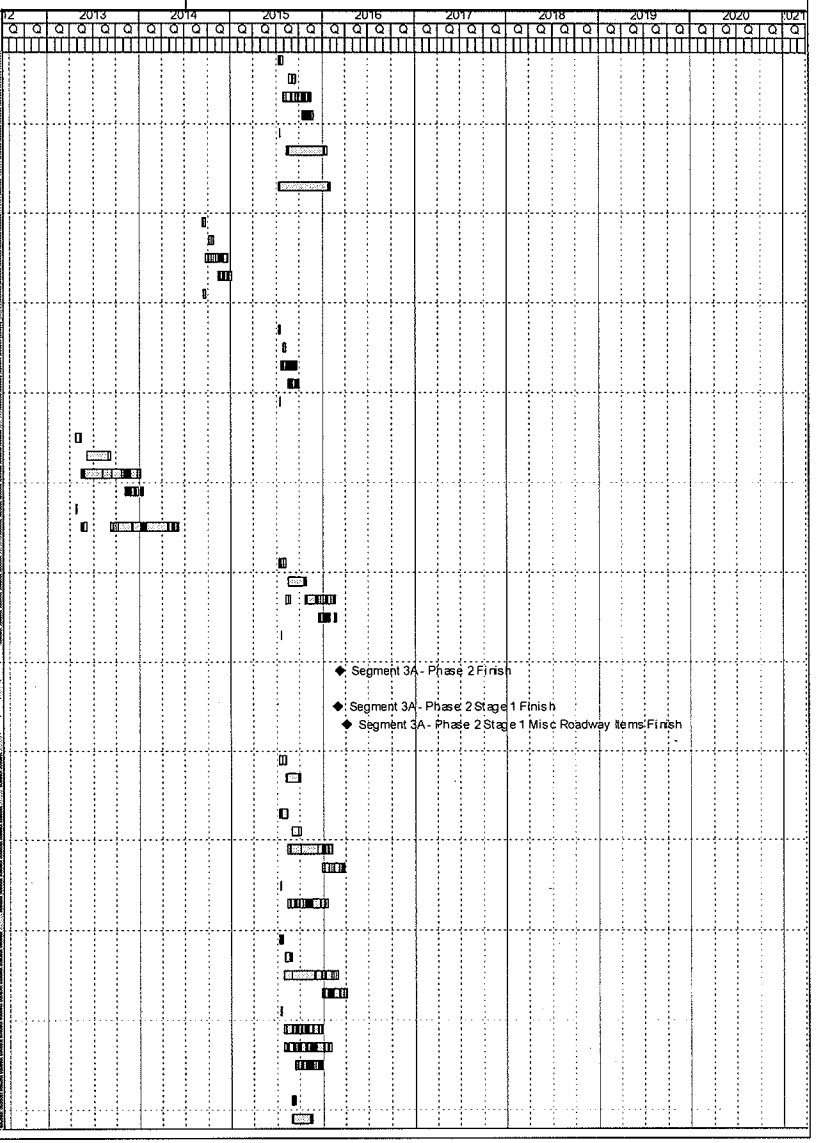

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
SBRP - Dewey to S. of Trinity River		80	09-Jul-15	28-Oct-15	627	$876,749
TCP & Temp Work		74	09-Jul-15	20-Oct-15	99	$37,905
Drainage		14	07-Aug-15	28-Aug-15	72	$130,353
Roadworks		50	24-Jul-15	20-Oct-15	72	$651,458
ITS / Signs / Stripes / Electrical / MISC.		33	14-Sep-15	28-Oct-15	627	$53,254
Noise Wall		2	14-Jul-15	15-Jul-15	168	$3,779
NBRP - Dewey to S. of Trinity River		0			0	$0
Retaining Wall RWN16-M		0			0	$0
Retaining Wall RWN16-S		0			0	$0
SBGP - Dewey to S. of Trinity River		186	12-Jun-15	26-Feb-16	540	$11,837,743
TCP & Temp Work		186	12-Jun-15	26-Feb-16	6	$747,380
Drainage		14	13-Jul-15	03-Aug-15	60	$242,676
Roadworks		98	24-Jun-15	22-Dec-15	41	$2,843,859
ITS / Signs / Stripes / Electrical / MISC.		45	04-Nov-15	05-Jan-16	578	$401,700
Noise Wall		2	16-Jun-15	17-Jun-15	186	$19,525
B226 - SB 35W GP over Trinity River		176	24-Jun-15	26-Feb-16	6	$7,582,601
SBRP - S. of Trinity River to IH-30		144	09-Jul-15	26-Jan-16	563	$4,270,610
TCP & Temp Work		137	09-Jul-15	15-Jan-16	36	$1,177,530
Drainage		25	22-Sep-15	04-Nov-15	27	$291,347
Roadworks		66	11-Sep-15	15-Jan-16	27	$808,062
ITS / Signs / Stripes / Electrical / MISC.		38	04-Dec-15	26-Jan-16	563	$253,496
Noise Wall		2	15-Jul-15	16-Jul-15	167	$8,457
Retaining Wall RWS25		49	28-Sep-15	22-Dec-15	45	$1,180,441
Retaining Wall RWS27		15	28-Sep-15	21-Oct-15	79	$270,296
Retaining Wall RWS29		14	28-Sep-15	20-Oct-15	80	$180,961
XRDS - Meacham Blvd		17	10-Jul-15	05-Aug-15	126	$317,541
Retaining Wall RW10A		17	10-Jul-15	05-Aug-15	126	$317,541
Stage 2		214	12-Jun-15	06-Apr-16	512	$9,747,839
3AMSMS221000	Segment 3A - Phase 2 Stage 2 Finish	0		22-Jan-16	45	$0
3AMSRD1001	Segment 3A - Phase 2 Stage 2 Misc Roadway Items Finish	0		06-Apr-16	718	$0
SBGP - Meacham to Dewey		63	09-Jul-15	05-Oct-15	644	$421,028
TCP & Temp Work		57	09-Jul-15	25-Sep-15	116	$24,613
Drainage		7	31-Jul-15	11-Aug-15	85	$33,055
Roadworks		34	29-Jul-15	25-Sep-15	85	$321,378
ITS / Signs / Stripes / Electrical / MISC.		31	24-Aug-15	05-Oct-15	644	$39,317
Noise Wall		2	14-Jul-15	15-Jul-15	168	$2,659
SBGP - Dewey to S. of Trinity River		161	12-Jun-15	22-Jan-16	565	$5,214,423
TCP & Temp Work		161	12-Jun-15	22-Jan-16	31	$140,388
Drainage		12	24-Jul-15	11-Aug-15	67	$188,750
Roadworks		81	07-Jul-15	01-Dec-15	51	$2,211,890
ITS / Signs / Stripes / Electrical / MISC.		35	23-Oct-15	10-Dec-15	596	$341,496
Noise Wall		2	16-Jun-15	17-Jun-15	186	$16,166
B221 - SB 35W GP over Northside Dr/Yucca Ave		144	07-Jul-15	22-Jan-16	31	$2,316,713
Retaining Wall RWS23		0			0	$0
SBRP - S. of Trinity River to IH-30		83	09-Jul-15	02-Nov-15	624	$710,423
TCP & Temp Work		78	09-Jul-15	26-Oct-15	95	$45,125
Drainage		15	07-Aug-15	31-Aug-15	69	$145,673
Roadworks		48	31-Jul-15	26-Oct-15	69	$454,041
ITS / Signs / Stripes / Electrical / MISC.		32	18-Sep-15	02-Nov-15	624	$61,356
Noise Wall		2	14-Jul-15	15-Jul-15	168	$4,228
SBGP - S. of Trinity River to IH-30		72	09-Jul-15	16-Oct-15	635	$1,076,947
TCP & Temp Work		67	09-Jul-15	09-Oct-15	1	$56,999
Drainage		4	05-Aug-15	10-Aug-15	3	$88,020
Roadworks		40	30-Jul-15	09-Oct-15	1	$825,075
ITS / Signs / Stripes / Electrical / MISC.		33	02-Sep-15	16-Oct-15	635	$99,777
Noise Wall		2	14-Jul-15	15-Jul-15	63	$7,076
SBRP - Meacham to Dewey		71	09-Jul-15	13-Oct-15	636	$1,727,092
TCP & Temp Work		65	09-Jul-15	07-Oct-15	108	$18,802
Drainage		10	03-Aug-15	18-Aug-15	80	$112,314
Roadworks		40	28-Jul-15	07-Oct-15	80	$672,161

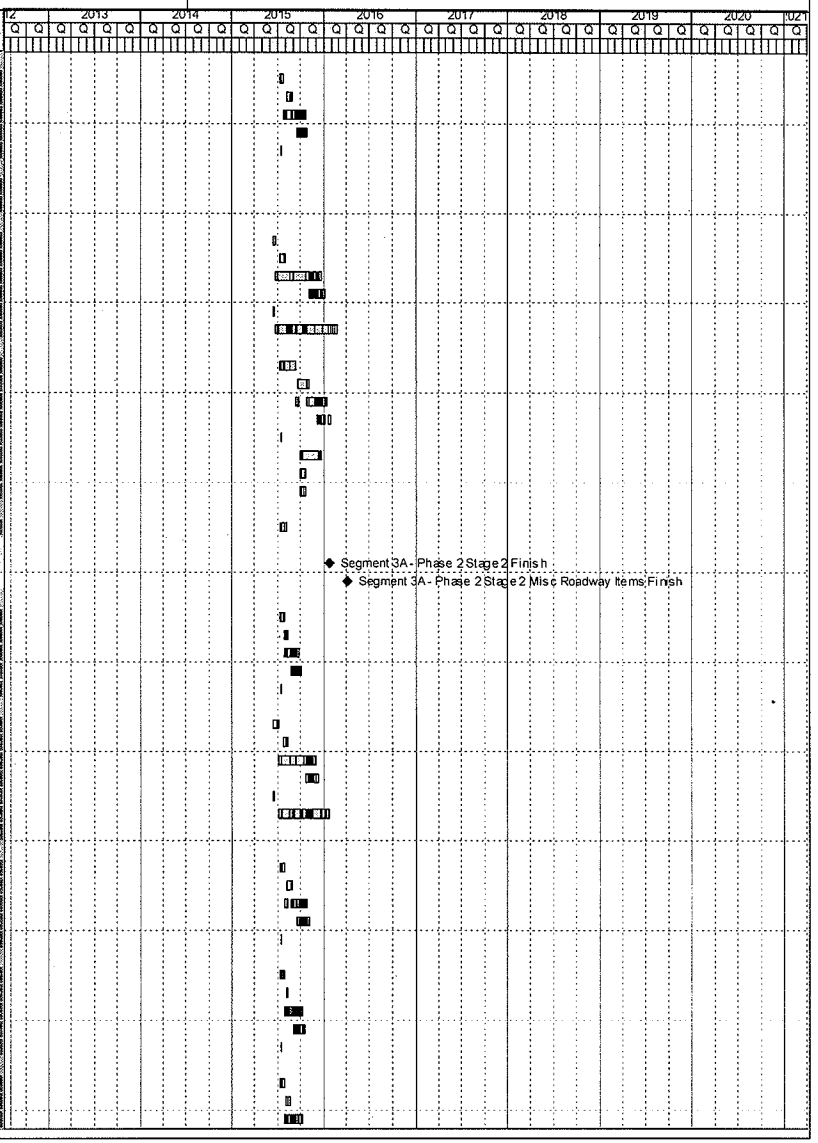

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	ITS / Signs / Stripes / Electrical / MISC.	96	27-Aug-15	15-Oct-15	636	$29,602
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$2,158
	Retaining Wall RWS10	35	03-Aug-15	28-Sep-15	93	$891,566
	NBRP - Dewey to S. of Trinity River	0			0	$0
	Retaining Wall RWN16-M	0			0	$0
	SBRP - Dewey to S. of Trinity River	13	10-Jul-15	28-Jul-15	159	$146,801
	Retaining Wall RWS16	0			0	$0
	Retaining Wall RWS17A	12	10-Jul-15	28-Jul-15	131	$145,801
	XRDS - SH 183/NE 28th St.	17	10-Jul-15	05-Aug-15	126	$452,125
	Retaining Wall RW21A	15	10-Jul-15	31-Jul-15	128	$175,637
	Retaining Wall RW21B	17	10-Jul-15	05-Aug-15	126	$276,289
	Stage 3	195	09-Jul-15	06-Apr-16	512	$30,880,497
3AMSMS231000	Segment 3A- Phase 2 Stage 3 Finish	0		07-Mar-16	0	$0
3AMSRD1000	Segment 3A- Phase 2 Stage 3 Misc Roadway Items Finish	0		06-Apr-16	718	$0
	NBRP - Meacham to Dewey	17	09-Jul-15	31-Jul-15	156	$544,858
	TCP & Temp Work	17	09-Jul-15	31-Jul-15	156	$544,858
	NBRP - Dewey to S. of Trinity River	0			0	$0
	Retaining Wall RWN16-S	0			0	$0
	NBGP - Meacham to Dewey	22	09-Jul-15	07-Aug-15	151	$701,664
	TCP & Temp Work	22	09-Jul-15	07-Aug-15	151	$701,664
	NBFR - Dewey to S. of Trinity River	46	09-Jul-15	10-Sep-15	127	$1,475,492
	TCP & Temp Work	46	09-Jul-15	10-Sep-15	127	$1,475,492
	NBGP - Dewey to S of Trinity River	54	09-Jul-15	22-Sep-15	119	$1,658,125
	TCP & Temp Work	54	09-Jul-15	22-Sep-15	119	$1,658,125
	SBGP - Meacham to Dewey	140	09-Jul-15	20-Jan-16	567	$9,257,340
	TCP & Temp Work	140	09-Jul-15	20-Jan-16	33	$2,699,976
	Drainage	11	27-Aug-15	16-Sep-15	48	$165,327
	Roadworks	59	21-Aug-15	10-Dec-15	46	$1,606,866
	ITS / Signs / Stripes / Electrical / MISC.	38	30-Oct-15	22-Dec-15	586	$327,371
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$13,293
	B240 - SB 35W GP over Meacham	101	21-Aug-15	08-Jan-16	41	$1,492,075
	Retaining Wall RWS01A	49	14-Sep-15	10-Dec-15	52	$1,212,420
	Retaining Wall RWS02	72	14-Sep-15	20-Jan-16	29	$1,760,011
	SBFR - Meacham to Dewey	112	10-Jul-15	15-Jan-16	31	$4,284,037
	Retaining Wall RWS12	112	10-Jul-15	15-Jan-16	31	$4,284,037
	SBGP - S. of Trinity River to IH-30	106	10-Oct-15	07-Mar-16	534	$3,053,997
	TCP & Temp Work	106	10-Oct-15	07-Mar-16	0	$56,999
	Drainage	9	10-Nov-15	25-Nov-15	24	$88,020
	Roadworks	42	03-Nov-15	22-Jan-16	24	$825,075
	ITS / Signs / Stripes / Electrical / MISC.	29	23-Dec-15	01-Feb-16	559	$99,777
	Noise Wall	2	14-Oct-15	15-Oct-15	102	$7,076
	B236 - SB 35W GP over RR (922+00)	90	03-Nov-15	07-Mar-16	0	$1,192,379
	B234 - SB 35W GP over 4th St	78	03-Nov-15	18-Feb-16	12	$784,671
	SBRP - Meacham to Dewey	73	09-Jul-15	19-Oct-15	634	$1,598,622
	TCP & Temp Work	68	09-Jul-15	12-Oct-15	105	$22,562
	Drainage	11	05-Aug-15	21-Aug-15	77	$135,376
	Roadworks	42	29-Jul-15	12-Oct-15	77	$806,593
	ITS / Signs / Stripes / Electrical / MISC.	35	01-Sep-15	19-Oct-15	634	$35,523
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$2,590
	Retaining Wall RW13A	11	07-Aug-15	24-Aug-15	114	$93,476
	Retaining Wall RWS13	25	07-Aug-15	14-Sep-15	100	$542,502
	NSML - Dewey to S. of Trinity River	153	09-Jul-15	08-Feb-16	554	$8,133,625
	TCP & Temp Work	147	09-Jul-15	29-Jan-16	26	$169,217
	Drainage	19	24-Aug-15	25-Sep-15	33	$298,470
	Roadworks	93	07-Aug-15	29-Jan-16	20	$2,885,576
	ITS / Signs / Stripes / Electrical / MISC.	38	17-Dec-15	08-Feb-16	554	$396,923
	Noise Wall	2	14-Jul-15	15-Jul-15	168	$18,651
	Retaining Wall RWN15	87	14-Aug-15	12-Jan-16	33	$2,340,984
	Retaining Wall RWS15-S	77	14-Aug-15	24-Dec-15	43	$2,024,424
	XRDS - Meacham Blvd.	15	10-Jul-15	31-Jul-15	128	$172,737

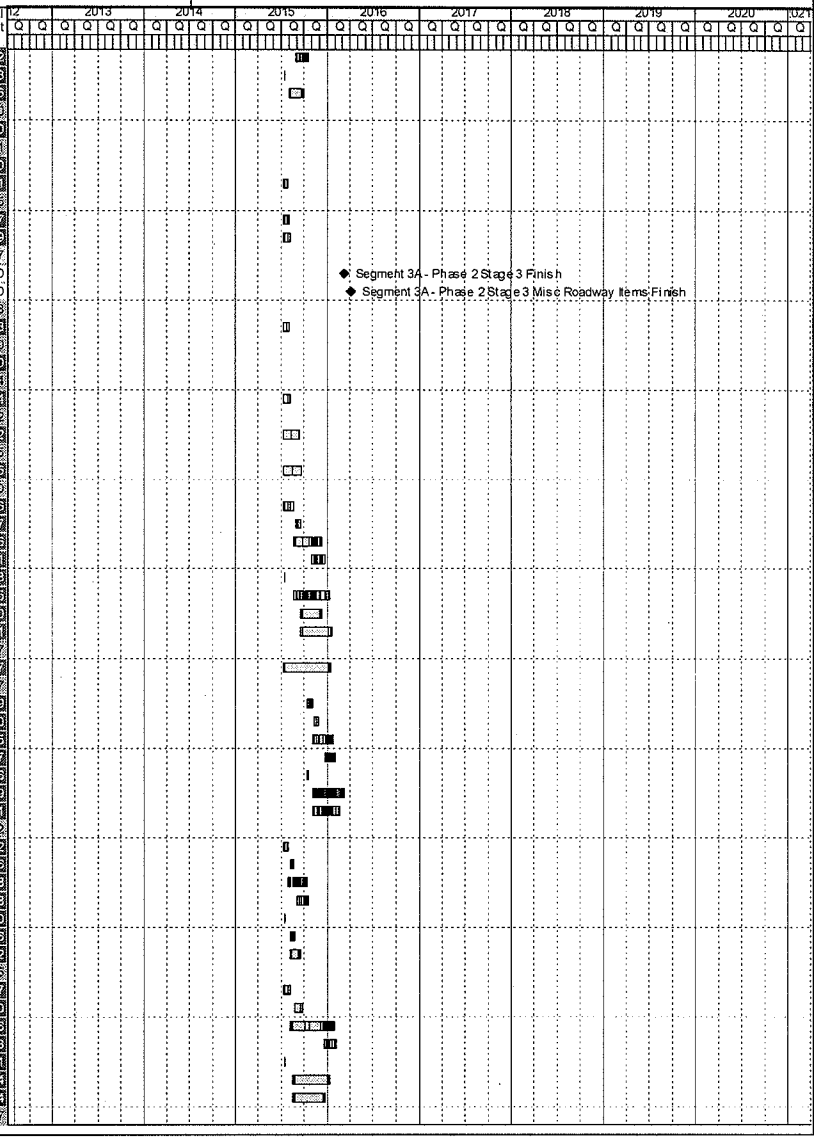

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
Retaining Wall RW02A		15	10-Jul-15	31-Jul-15	128	$172,737
Phase 3		336	08-Mar-16	20-Jun-17	198	$145,242,545
3AMSMS31000	Segment 3A - Phase 3 Finish	0		27-Jan-17	2	$0
Stage 1		336	08-Mar-16	20-Jun-17	198	$52,217,688
3AMSMS311000	Segment 3A - Phase 3 Stage 1 Finish	0		27-Jan-17	2	$0
3AMS1001	Segment 3A - Phase 3 Stage 1 Misc Roadway Items Finish	0		20-Jun-17	278	$0
NBRP - S. of Trinity River to IH-30		15	08-Mar-16	28-Mar-16	219	$420,323
TCP & Temp Work		15	08-Mar-16	28-Mar-16	219	$420,323
NBRP - Dewey to S. of Trinity River		13	08-Mar-16	24-Mar-16	221	$398,446
TCP & Temp Work		13	08-Mar-16	24-Mar-16	221	$398,446
NBFR - Dewey to S. of Trinity River		35	08-Mar-16	18-Jul-16	439	$1,590,295
TCP & Temp Work		91	08-Mar-16	12-Jul-16	143	$544,188
Drainage		14	25-Apr-16	24-May-16	111	$121,874
Roadworks		49	12-Apr-16	12-Jul-16	111	$880,032
ITS / Signs / Stripes / Electrical / MISC.		29	08-Jun-16	18-Jul-16	439	$40,882
Noise Wall		2	11-Mar-16	14-Mar-16	229	$3,420
NBGP - S. of Trinity River to IH-30		28	08-Mar-16	14-Apr-16	9	$2,359,723
TCP & Temp Work		28	08-Mar-16	14-Apr-16	9	$2,359,723
NBFR - Meacham to Dewey		119	08-Mar-16	19-Aug-16	415	$3,255,426
TCP & Temp Work		114	08-Mar-16	12-Aug-16	120	$60,486
Drainage		26	20-Apr-16	10-Jun-16	91	$303,833
Roadworks		76	28-Mar-16	12-Aug-16	91	$1,818,766
ITS / Signs / Stripes / Electrical / MISC.		31	08-Jul-16	19-Aug-16	415	$123,010
Noise Wall		2	11-Mar-16	14-Mar-16	229	$8,521
Retaining Wall RWN13-M1		0			0	$0
Retaining Wall RWN13-M2		0			0	$0
Retaining Wall RWN13-S		56	20-Apr-16	06-Jul-16	147	$840,809
SBFR - Meacham to Dewey		61	08-Mar-16	31-May-16	473	$238,101
TCP & Temp Work		56	08-Mar-16	24-May-16	178	$7,849
Drainage		8	21-Mar-16	04-Apr-16	138	$30,554
Roadworks		34	16-Mar-16	24-May-16	138	$176,585
ITS / Signs / Stripes / Electrical / MISC.		34	14-Apr-16	31-May-16	473	$22,256
Noise Wall		2	11-Mar-16	14-Mar-16	229	$857
NBGP - Meacham to Dewey		336	08-Mar-16	20-Jun-17	198	$31,747,483
TCP & Temp Work		234	08-Mar-16	27-Jan-17	0	$1,864,235
Drainage		30	06-Apr-16	03-Jun-16	2	$956,730
Roadworks		170	16-Mar-16	24-Jan-17	2	$9,457,712
ITS / Signs / Stripes / Electrical / MISC.		147	28-Nov-16	20-Jun-17	198	$1,830,622
Noise Wall		4	16-Mar-16	21-Mar-16	224	$76,956
B241 - NB 35W GP over Meacham		103	16-Mar-16	05-Aug-16	125	$1,551,910
B210 - NB 35W GP over BNSF		196	16-Mar-16	14-Dec-16	32	$2,444,298
B207 - NB 35W GP over FWWR		226	16-Mar-16	27-Jan-17	0	$4,437,905
Retaining Wall RWN01		54	30-Jun-16	23-Sep-16	73	$1,460,342
Retaining Wall RWN02		68	30-Jun-16	17-Oct-16	59	$1,692,150
Retaining Wall RWN05		10	30-Jun-16	15-Jul-16	117	$152,542
Retaining Wall RWN10-M		0			0	$0
Retaining Wall RWN10-S		61	28-Mar-16	08-Jul-16	122	$1,577,643
Retaining Wall RWN08		152	28-Mar-16	06-Dec-16	31	$4,244,537
NBRP - Meacham to Dewey		156	08-Mar-16	11-Oct-16	378	$10,800,637
TCP & Temp Work		156	08-Mar-16	11-Oct-16	78	$112,611
Drainage		43	12-Apr-16	01-Jul-16	65	$573,957
Roadworks		98	04-Apr-16	27-Sep-16	65	$2,132,226
ITS / Signs / Stripes / Electrical / MISC.		38	16-Aug-16	06-Oct-16	381	$348,663
Noise Wall		2	11-Mar-16	14-Mar-16	229	$16,638
B212 - SH183 Entrance Ramp to NB 35W ML		137	04-Apr-16	11-Oct-16	78	$2,386,255
Retaining Wall RWN02A		66	05-May-16	19-Aug-16	94	$1,686,605
Retaining Wall RWN04		67	05-May-16	22-Aug-16	93	$1,694,269
Retaining Wall RW04A		13	05-May-16	25-May-16	147	$101,174
Retaining Wall RWN07-M		51	05-May-16	28-Jul-16	109	$1,267,952
Retaining Wall RWN07-S		0			0	$0

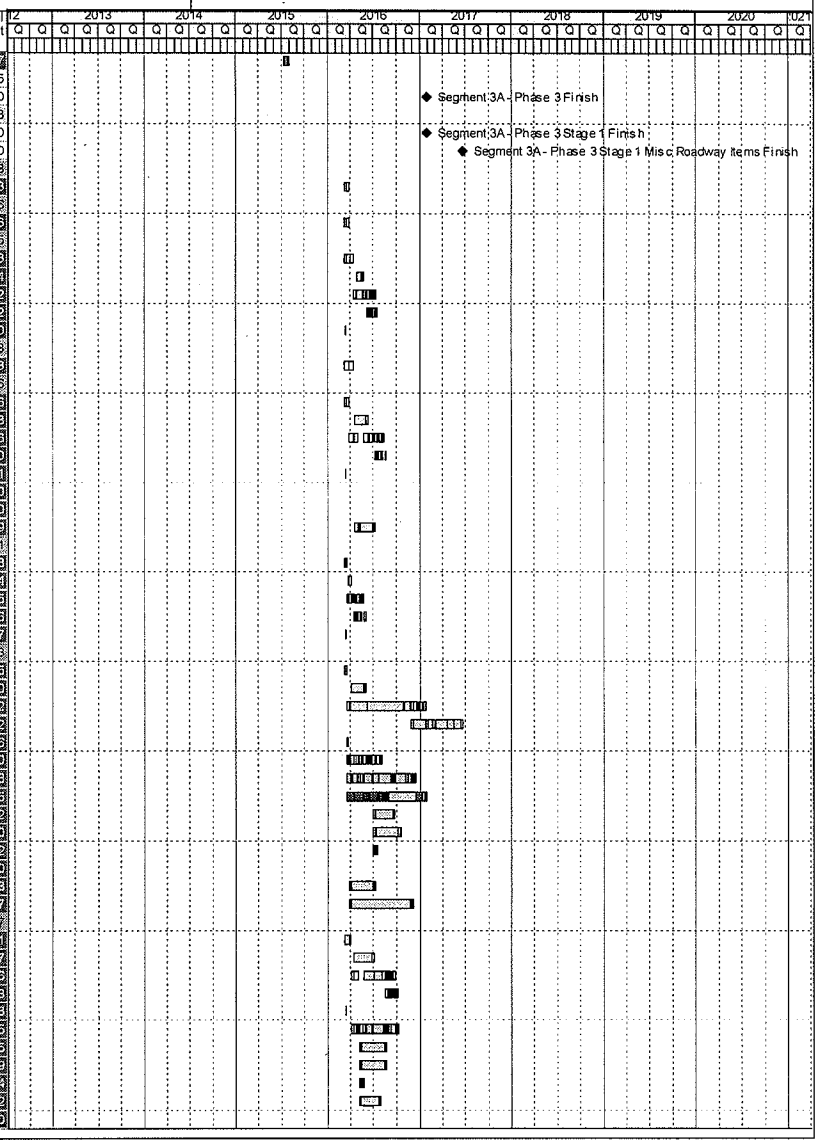

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Retaining Wall RWN12	20	05-May-16	08-Jun-16	140	$429,076
	Retaining Wall RW13B	11	05-May-16	23-May-16	149	$51,211
	XRDS - Meacham Blvd.	21	08-Mar-16	11-Apr-16	173	$1,407,154
	Retaining Wall RW02A	16	08-Mar-16	01-Apr-16	178	$172,737
	Retaining Wall RW07A	21	08-Mar-16	11-Apr-16	173	$405,799
	Retaining Wall RW10A	19	08-Mar-16	06-Apr-16	175	$317,541
	Retaining Wall RW08A-S	21	08-Mar-16	11-Apr-16	173	$249,493
	Retaining Wall RW08B-S	21	08-Mar-16	11-Apr-16	173	$261,584
	Stage 2	336	08-Mar-16	20-Jun-17	198	$75,441,658
3AMSMS321000	Segment 3A - Phase 3 Stage 2 Finish	0		20-Jan-17	9	$0
3AMS	Segment 3A - Phase 3 Stage 2 Misc Roadway Items Finish	0		20-Jun-17	278	$0
	SBRP - S. of Trinity River to IH-30	208	08-Mar-16	22-Dec-16	326	$9,761,309
	TCP & Temp Work	208	08-Mar-16	22-Dec-16	26	$0
	Drainage	9	29-Mar-16	14-Apr-16	124	$0
	Roadworks	46	21-Mar-16	17-Jun-16	124	$0
	ITS / Signs / Stripes / Electrical / MISC.	38	29-Apr-16	21-Jun-16	458	$0
	Noise Wall	5	11-Mar-16	17-Mar-16	226	$0
	B232 - SB 35W ML Exit Ramp to Spur 280	199	21-Mar-16	22-Dec-16	26	$9,761,309
	NBFR - Dewey to S. of Trinity River	62	08-Mar-16	01-Jun-16	472	$363,777
	TCP & Temp Work	56	08-Mar-16	24-May-16	178	$15,042
	Drainage	8	24-Mar-16	08-Apr-16	138	$40,625
	Roadworks	33	18-Mar-16	24-May-16	138	$293,344
	ITS / Signs / Stripes / Electrical / MISC.	33	18-Apr-16	01-Jun-16	472	$13,627
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$1,140
	NBFR - Meacham to Dewey	49	08-Mar-16	13-May-16	185	$940,809
	Retaining Wall RWN13-M1	0			0	$0
	Retaining Wall RWN13-M2	0			0	$0
	Retaining Wall RWN13-S	40	08-Mar-16	13-May-16	154	$940,809
	NBGP - Meacham to Dewey	69	08-Mar-16	10-Jun-16	485	$951,736
	TCP & Temp Work	64	08-Mar-16	02-Jun-16	170	$46,414
	Drainage	8	23-Mar-16	06-Apr-16	132	$61,725
	Roadworks	40	16-Mar-16	03-Jun-16	132	$610,175
	ITS / Signs / Stripes / Electrical / MISC.	36	22-Apr-16	10-Jun-16	465	$75,916
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$4,955
	Retaining Wall RWN05	10	30-Mar-16	14-Apr-16	171	$152,542
	NBGP - Dewey to S. of Trinity River	253	08-Mar-16	23-Feb-17	281	$24,084,672
	TCP & Temp Work	228	08-Mar-16	19-Jan-17	3	$368,216
	Drainage	23	06-Apr-16	23-May-16	52	$495,084
	Roadworks	160	16-Mar-16	06-Jan-17	12	$6,054,927
	ITS / Signs / Stripes / Electrical / MISC.	73	15-Nov-16	23-Feb-17	281	$944,997
	Noise Wall	3	15-Mar-16	17-Mar-16	226	$39,832
	B219 - NB 35W GP over UPRR	222	16-Mar-16	19-Jan-17	6	$10,087,432
	B224 - NB 35W GP over Trinity River	218	16-Mar-16	13-Jan-17	10	$6,094,204
	NBGP - S. of Trinity River to IH-30	247	15-Apr-16	27-Mar-17	259	$18,261,247
	TCP & Temp Work	196	15-Apr-16	13-Jan-17	10	$1,487,162
	Drainage	20	20-May-16	22-Jun-16	7	$762,141
	Roadworks	144	27-Apr-16	13-Jan-17	7	$7,039,344
	ITS / Signs / Stripes / Electrical / MISC.	104	02-Nov-16	27-Mar-17	259	$1,533,454
	Noise Wall	4	25-Apr-16	28-Apr-16	196	$61,301
	B235 - NB 35W GP over RR (922+00)	136	27-Apr-16	02-Nov-16	62	$2,446,180
	B233 - NB 35W GP over 4th St	148	27-Apr-16	18-Nov-16	50	$2,602,356
	Retaining Wall RWN23	33	30-Jun-16	19-Aug-16	94	$656,420
	Retaining Wall RWN25	35	30-Jun-16	24-Aug-16	92	$727,209
	Retaining Wall RWN26	37	30-Jun-16	26-Aug-16	90	$945,659
	NBRP - Meacham to Dewey	155	08-Mar-16	10-Oct-16	379	$4,191,229
	TCP & Temp Work	155	08-Mar-16	10-Oct-16	79	$13,537
	Drainage	10	29-Mar-16	15-Apr-16	131	$68,363
	Roadworks	40	18-Mar-16	06-Jun-16	131	$265,867
	ITS / Signs / Stripes / Electrical / MISC.	34	27-Apr-16	13-Jun-16	464	$26,145
	Noise Wall	2	11-Mar-16	14-Mar-16	229	$1,997

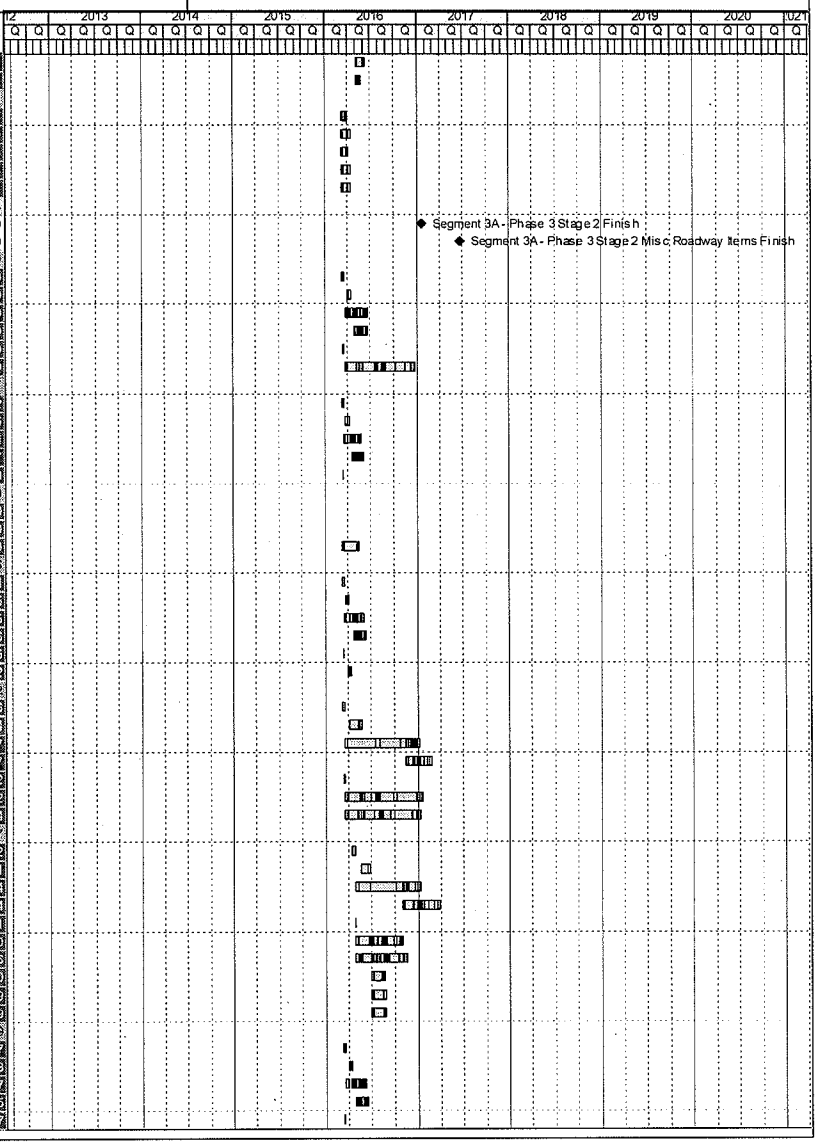

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
B203 - NB 35W ML Ramp to NB 35W GP		147	18-Mar-16	10-Oct-16	79	$3,824,820
NBRP - Dewey to S. of Trinity River		164	08-Mar-16	21-Oct-16	370	$3,247,280
TCP & Temp Work		160	08-Mar-16	17-Oct-16	74	$97,770
Drainage		37	17-May-16	21-Jul-16	54	$481,395
Roadworks		109	04-Apr-16	17-Oct-16	54	$2,340,554
ITS / Signs / Stripes / Electrical / MISC.		36	02-Sep-16	21-Oct-16	370	$313,662
Noise Wall		2	11-Mar-16	14-Mar-16	229	$13,958
Retaining Wall RWN19-M1		0			0	$0
NBRP - S. of Trinity River to IH-30		229	08-Mar-16	20-Jan-17	305	$13,260,274
TCP & Temp Work		229	08-Mar-16	20-Jan-17	5	$258,441
Drainage		48	12-Apr-16	12-Jul-16	54	$635,822
Roadworks		109	04-Apr-16	17-Oct-16	54	$1,980,738
ITS / Signs / Stripes / Electrical / MISC.		41	29-Aug-16	24-Oct-16	369	$525,611
Noise Wall		2	14-Mar-16	15-Mar-16	228	$18,448
B231 - Spur 280 Entrance Ramp to NB 35W ML		210	04-Apr-16	20-Jan-17	5	$9,489,264
Retaining Wall RWN31		22	28-Apr-16	03-Jun-16	142	$351,958
Retaining Wall RW31A		0			0	$0
XRDS - SH 183/NE 28th St		25	08-Mar-16	18-Apr-16	169	$379,325
Retaining Wall RW20A		25	08-Mar-16	18-Apr-16	169	$379,325
Stage 3		336	08-Mar-16	20-Jun-17	198	$17,583,199
3AMSMS331000	Segment 3A - Phase 3 Stage 3 Finish	0		08-Nov-16	82	$0
3AMS1000	Segment 3A - Phase 3 Stage 3 Misc Roadway Items Finish	0		20-Jun-17	278	$0
NBFR - Dewey to S. of Trinity River		69	08-Mar-16	10-Jun-16	465	$363,777
TCP & Temp Work		64	08-Mar-16	03-Jun-16	170	$15,042
Drainage		8	28-Mar-16	11-Apr-16	132	$40,625
Roadworks		38	21-Mar-16	03-Jun-16	132	$293,344
ITS / Signs / Stripes / Electrical / MISC.		38	20-Apr-16	10-Jun-16	465	$13,627
Noise Wall		2	14-Mar-16	15-Mar-16	228	$1,140
NBGP - Meacham to Dewey		79	08-Mar-16	24-Jun-16	455	$799,194
TCP & Temp Work		74	08-Mar-16	17-Jun-16	160	$46,414
Drainage		8	01-Apr-16	15-Apr-16	124	$91,725
Roadworks		43	28-Mar-16	17-Jun-16	124	$610,175
ITS / Signs / Stripes / Electrical / MISC.		37	05-May-16	24-Jun-16	455	$75,916
Noise Wall		2	14-Mar-16	15-Mar-16	228	$4,965
NBGP - Dewey to S. of Trinity River		176	08-Mar-16	08-Nov-16	358	$10,799,554
TCP & Temp Work		175	08-Mar-16	08-Nov-16	58	$174,278
Drainage		14	22-Apr-16	23-May-16	87	$232,971
Roadworks		94	04-Apr-16	21-Sep-16	69	$2,849,377
ITS / Signs / Stripes / Electrical / MISC.		36	12-Aug-16	04-Oct-16	383	$390,852
Noise Wall		2	11-Mar-16	14-Mar-16	229	$18,744
B223 - NB 35W GP over Northside Dr/Yucca Ave		145	28-Mar-16	14-Oct-16	75	$2,532,599
Retaining Wall RWN20		70	20-Jul-16	08-Nov-16	46	$3,475,527
Retaining Wall RWN21		43	20-Jul-16	23-Sep-16	73	$1,126,205
NBGP - S. of Trinity River to IH-30		111	14-Jun-16	15-Nov-16	353	$2,633,068
TCP & Temp Work		99	14-Jun-16	28-Oct-16	65	$170,998
Drainage		13	21-Jul-16	08-Aug-16	47	$209,239
Roadworks		66	11-Jul-16	28-Oct-16	47	$1,877,159
ITS / Signs / Stripes / Electrical / MISC.		38	23-Sep-16	15-Nov-16	353	$365,326
Noise Wall		4	17-Jun-16	22-Jun-16	157	$10,347
NBRP - Dewey to S. of Trinity River		105	08-Mar-16	01-Aug-16	429	$1,198,652
TCP & Temp Work		101	08-Mar-16	26-Jul-16	133	$37,604
Drainage		18	15-Apr-16	23-May-16	103	$185,129
Roadworks		66	23-Mar-16	26-Jul-16	103	$900,213
ITS / Signs / Stripes / Electrical / MISC.		32	17-Jun-16	01-Aug-16	429	$70,337
Noise Wall		2	14-Mar-16	15-Mar-16	228	$5,369
Retaining Wall RWN19-M1		0			0	$0
NBRP - S. of Trinity River to IH-30		67	07-May-16	09-Aug-16	423	$150,357
TCP & Temp Work		62	07-May-16	02-Aug-16	128	$12,507
Drainage		3	01-Jun-16	13-Jun-16	98	$30,277
Roadworks		41	24-May-16	02-Aug-16	98	$94,321

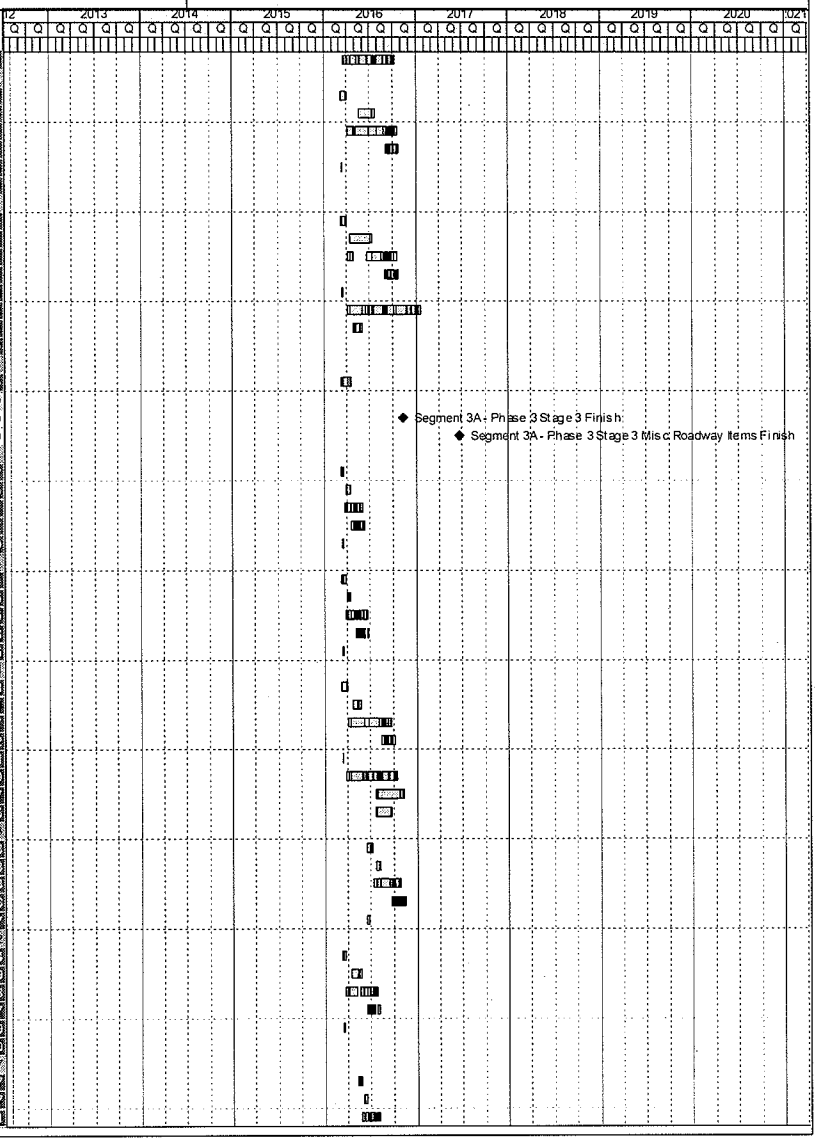

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	ITS / Signs / Stripes / Electrical / MISC.	35	22-Jun-16	09-Aug-16	423	$12,573
	Noise Wall	4	16-May-16	19-May-16	181	$878
	NBLA - Meacham to Dewey	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	NBLA - Dewey to S. of Trinity River	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	NBLA - S. of Trinity River to IH-30	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	SBLA - Meacham to Dewey	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	SBLA - Dewey to S. of Trinity River	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	SBLA - S. of Trinity River to IH-30	31	08-Mar-16	19-Apr-16	203	$197,745
	TCP & Temp Work	43	08-Mar-16	19-Apr-16	285	$0
	Drainage	0			0	$0
	Roadworks	17	08-Mar-16	08-Apr-16	154	$157,782
	ITS / Signs / Stripes / Electrical / MISC.	6	11-Apr-16	19-Apr-16	154	$39,963
	Noise Wall	0			0	$0
	XRDS - SH 183/NE 28th St	23	08-Mar-16	14-Apr-16	171	$452,125
	Retaining Wall RW21A	20	08-Mar-16	08-Apr-16	174	$175,837
	Retaining Wall RW21B	23	08-Mar-16	14-Apr-16	171	$276,289
Phase 4		263	28-Jan-17	31-Jan-18	37	$198,122,135
3AMSMS41000	Segment 3A - Phase 4 Finish	0		31-Jan-18	53	$0
Stage 1		263	28-Jan-17	31-Jan-18	37	$198,122,135
3AMSMS411000	Segment 3A - Phase 4 Stage 1 Finish	0		31-Jan-18	53	$0
	SBRP - S. of Trinity River to IH-30	260	28-Jan-17	26-Jan-18	40	$9,761,309
	TCP & Temp Work	260	28-Jan-17	26-Jan-18	40	$0
	Drainage	8	20-Feb-17	03-Mar-17	188	$0
	Roadworks	44	10-Feb-17	04-May-17	188	$0
	ITS / Signs / Stripes / Electrical / MISC.	40	16-Mar-17	10-May-17	227	$0
	Noise Wall	5	03-Feb-17	09-Feb-17	291	$0
	B232 - SB 35W ML Exit Ramp to Spur 280	251	10-Feb-17	26-Jan-18	40	$9,761,309
	NBGP - Interchange to Meacham	144	28-Jan-17	17-Aug-17	156	$4,508,239
	TCP & Temp Work	144	28-Jan-17	17-Aug-17	156	$206,284
	Drainage	16	13-Mar-17	12-Apr-17	132	$662,628
	Roadworks	90	23-Feb-17	08-Aug-17	134	$3,098,024
	ITS / Signs / Stripes / Electrical / MISC.	39	26-Jun-17	17-Aug-17	156	$541,304
	Noise Wall	5	01-Feb-17	07-Feb-17	293	$0
	SBGP - S. of Trinity River to IH-30	96	28-Jan-17	12-Jun-17	204	$1,746,204
	TCP & Temp Work	96	28-Jan-17	12-Jun-17	204	$85,499

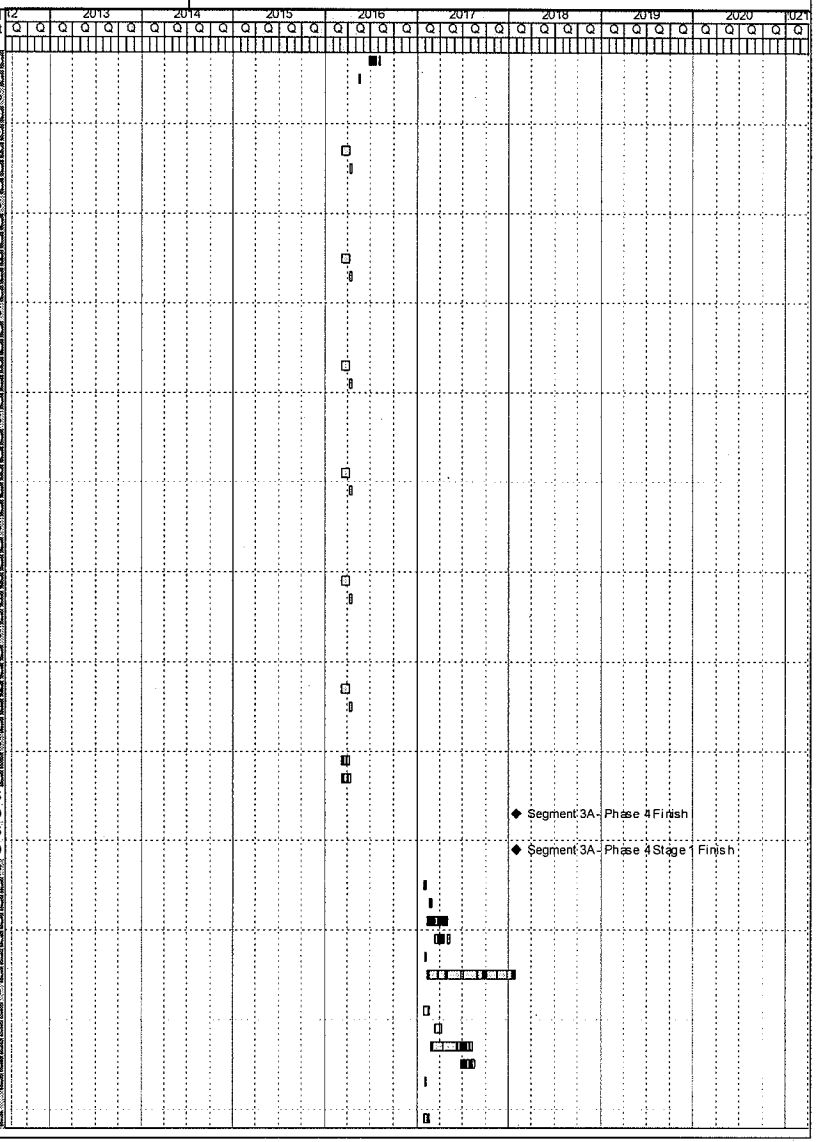

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Drainage	10	01-Mar-17	20-Mar-17	176	$132,030
	Roadworks	53	23-Feb-17	07-Jun-17	178	$1,237,612
	ITS / Signs / Stripes / Electrical / MISC.	36	24-Apr-17	12-Jun-17	204	$280,450
	Noise Wall	3	06-Feb-17	08-Feb-17	292	$10,613
	NSML - Meacham to Dewey	255	28-Jan-17	19-Jan-18	45	$72,429,188
	TCP & Temp Work	255	28-Jan-17	19-Jan-18	45	$1,489,111
	Drainage	60	27-Feb-17	21-Jun-17	23	$2,524,478
	Roadworks	179	08-Feb-17	02-Jan-18	54	$20,229,945
	ITS / Signs / Stripes / Electrical / MISC.	93	31-Aug-17	08-Jan-18	54	$3,741,374
	Noise Wall	9	08-Feb-17	20-Feb-17	284	$157,650
	B213 - 35W ML Transition (755+00)	146	08-Feb-17	30-Aug-17	147	$2,303,535
	B209 - 35W ML over BNSF	162	08-Feb-17	21-Sep-17	131	$2,882,439
	B208 - 35W ML over FWWR	243	08-Feb-17	12-Jan-18	50	$5,570,026
	B204 - 35W ML Transition (713+00)	148	08-Feb-17	01-Sep-17	145	$2,035,195
	B201 - 35W ML over Meacham	129	08-Feb-17	07-Aug-17	164	$2,103,586
	Retaining Wall RWN03	118	03-Jul-17	12-Jan-18	50	$6,522,407
	Retaining Wall RWS03	118	03-Jul-17	12-Jan-18	50	$6,622,372
	Retaining Wall RW03A	20	03-Jul-17	02-Aug-17	148	$271,713
	Retaining Wall RWN06	49	03-Jul-17	20-Sep-17	119	$1,182,211
	Retaining Wall RW06A	20	03-Jul-17	02-Aug-17	148	$236,548
	Retaining Wall RWS06	49	03-Jul-17	20-Sep-17	119	$1,194,896
	Retaining Wall RWN09	101	03-Jul-17	15-Dec-17	67	$2,932,664
	Retaining Wall RWS09	96	03-Jul-17	07-Dec-17	72	$2,702,799
	Retaining Wall RW09A	24	03-Jul-17	08-Aug-17	144	$411,387
	Retaining Wall RWN11	101	03-Jul-17	15-Dec-17	67	$2,784,705
	Retaining Wall RW11A	22	03-Jul-17	04-Aug-17	146	$313,488
	Retaining Wall RWS11	123	03-Jul-17	19-Jan-18	45	$3,616,357
	NSML - Dewey to S. of Trinity River	263	28-Jan-17	31-Jan-18	37	$93,863,796
	TCP & Temp Work	263	28-Jan-17	31-Jan-18	37	$338,434
	Drainage	33	08-Mar-17	08-May-17	25	$586,940
	Roadworks	159	13-Feb-17	30-Nov-17	70	$5,771,152
	ITS / Signs / Stripes / Electrical / MISC.	68	14-Sep-17	18-Dec-17	69	$924,631
	Noise Wall	2	06-Feb-17	07-Feb-17	293	$37,302
	Bridge 225 - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	Bridge 243 - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	Bridge 242 - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	Bridge 232M - 35W ML over Trinity River & Elevated Section	253	13-Feb-17	31-Jan-18	37	$20,001,662
	B222 - 35W ML over Northside Dr/Yucca Ave	199	13-Feb-17	16-Nov-17	91	$3,848,325
	Retaining Wall RWN19A	0			0	$0
	Retaining Wall RWN15	88	27-Feb-17	25-Jul-17	154	$2,340,364
	NSML - S. of Trinity River to IH-30	136	28-Jan-17	07-Aug-17	164	$1,967,366
	TCP & Temp Work	136	28-Jan-17	07-Aug-17	164	$135,374
	Drainage	13	26-Apr-17	19-May-17	139	$163,886
	Roadworks	86	28-Feb-17	02-Aug-17	140	$1,424,494
	ITS / Signs / Stripes / Electrical / MISC.	31	26-Jun-17	07-Aug-17	164	$253,396
	Noise Wall	3	01-Feb-17	03-Feb-17	295	$10,217
	Retaining Wall RWN29	0			0	$0
	NBRP - S. of Trinity River to IH-30	123	28-Jan-17	19-Jul-17	177	$1,764,709
	TCP & Temp Work	123	28-Jan-17	19-Jul-17	177	$135,374
	Drainage	28	01-Mar-17	24-Apr-17	152	$333,050
	Roadworks	73	23-Feb-17	11-Jul-17	162	$1,097,530
	ITS / Signs / Stripes / Electrical / MISC.	40	26-May-17	19-Jul-17	177	$269,092
	Noise Wall	3	01-Feb-17	03-Feb-17	295	$9,663
	SBRP - Meacham to Dewey	172	28-Jan-17	26-Sep-17	128	$4,106,327
	TCP & Temp Work	172	28-Jan-17	26-Sep-17	128	$22,562
	Drainage	11	17-Feb-17	08-Mar-17	189	$135,376
	Roadworks	43	09-Feb-17	02-May-17	190	$806,593
	ITS / Signs / Stripes / Electrical / MISC.	31	24-Mar-17	05-May-17	230	$36,523
	Noise Wall	3	03-Feb-17	07-Feb-17	293	$2,590
	B211 - SB 35W ML Exit Ramp to SH 183	164	09-Feb-17	26-Sep-17	128	$3,103,684

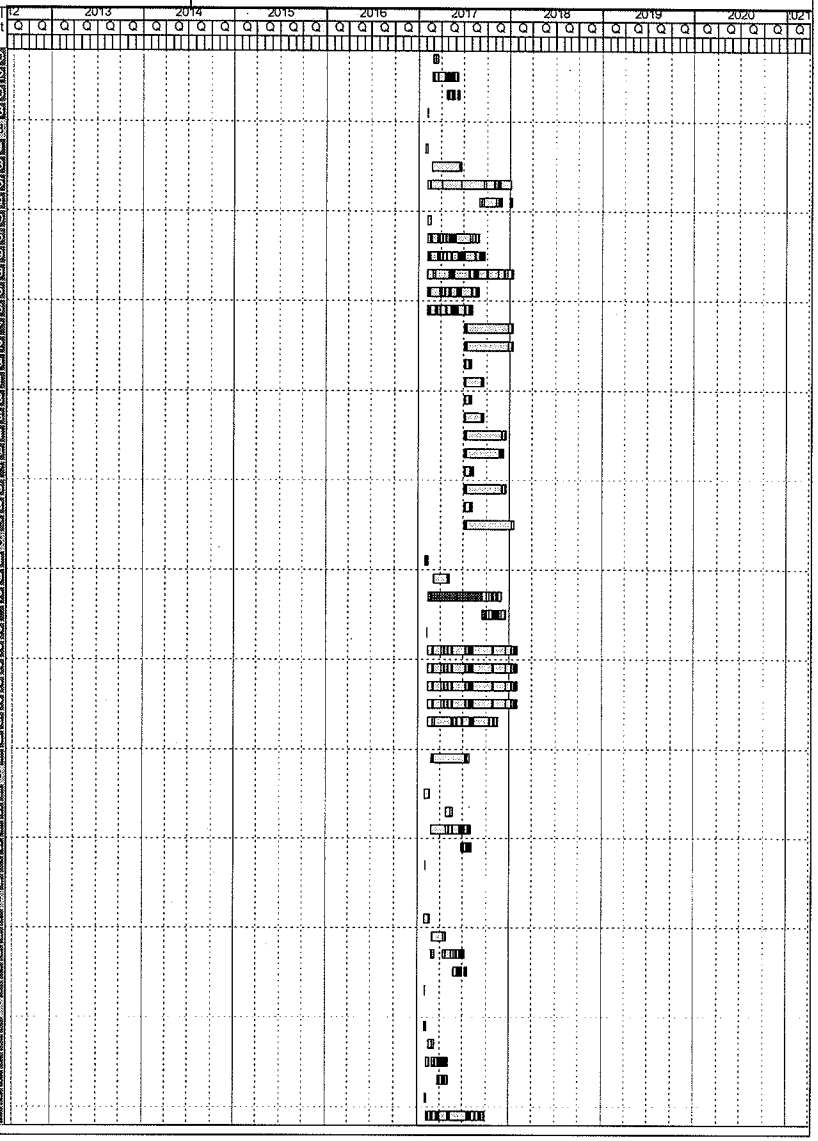

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
SBRP - Dewey to S. of Trinity River		83	28-Jan-17	24-May-17	217	$751,499
TCP & Temp Work		83	28-Jan-17	24-May-17	217	$92,490
Drainage		13	24-Feb-17	20-Mar-17	181	$111,731
Roadworks		49	13-Feb-17	16-May-17	181	$556,393
ITS / Signs / Stripes / Electrical / MISC.		39	31-Mar-17	24-May-17	217	$45,647
Noise Wall		3	06-Feb-17	08-Feb-17	292	$3,239
XRDS - Meacham Blvd.		73	28-Jan-17	10-May-17	227	$1,449,630
TCP & Temp Work		73	28-Jan-17	10-May-17	227	$0
Drainage		8	20-Feb-17	03-Mar-17	188	$0
Roadworks		44	10-Feb-17	04-May-17	188	$0
ITS / Signs / Stripes / Electrical / MISC.		40	16-Mar-17	10-May-17	227	$0
Noise Wall		5	03-Feb-17	09-Feb-17	291	$0
Retaining Wall RW02A		16	28-Feb-17	24-Mar-17	225	$177,817
Retaining Wall RW07A		22	28-Feb-17	04-Apr-17	219	$417,962
Retaining Wall RW10A		19	28-Feb-17	29-Mar-17	222	$327,175
Retaining Wall RW08A-S		20	20-Feb-17	23-Mar-17	226	$257,019
Retaining Wall RW08B-S		20	20-Feb-17	23-Mar-17	226	$269,556
XRDS - E 4th St.		232	28-Jan-17	19-Dec-17	68	$3,998,488
TCP & Temp Work		232	28-Jan-17	19-Dec-17	68	$0
Drainage		8	20-Feb-17	03-Mar-17	188	$0
Roadworks		44	10-Feb-17	04-May-17	188	$0
ITS / Signs / Stripes / Electrical / MISC.		40	16-Mar-17	10-May-17	227	$0
Noise Wall		5	03-Feb-17	09-Feb-17	291	$0
B239 - Pedestrian Bridge over US 287		223	10-Feb-17	19-Dec-17	68	$3,422,964
Retaining Wall RW21A		16	28-Feb-17	24-Mar-17	225	$180,965
Retaining Wall RW21B		18	28-Feb-17	28-Mar-17	223	$284,559
XRDS - Cypress St.		96	28-Jan-17	12-Jun-17	204	$1,845,481
TCP & Temp Work		96	28-Jan-17	12-Jun-17	204	$0
Drainage		17	20-Feb-17	21-Mar-17	178	$178,874
Roadworks		53	10-Feb-17	22-May-17	178	$524,496
ITS / Signs / Stripes / Electrical / MISC.		41	07-Apr-17	02-Jun-17	210	$51,801
Noise Wall		2	03-Feb-17	06-Feb-17	294	$5,023
B245 - Cypress St. over 280		87	10-Feb-17	12-Jun-17	204	$1,085,287
Interchange Construction		1130	20-Apr-13	18-Aug-17	155	$297,383,286
Phase 1		491	20-Apr-13	09-Mar-15	794	$158,465,857
ICMSMS1000	Interchange Phase 1 Finish	0		03-Feb-15	49	$0
ICMS1001	Interchange Phase 1 Misc Roadway Items Finish	0		09-Mar-15	1112	$0
Stage 1		491	20-Apr-13	09-Mar-15	794	$158,465,857
WBGP - Interchange to Meacham		25	20-Apr-13	24-May-13	477	$1,693,723
TCP & Temp Work		25	20-Apr-13	24-May-13	477	$1,693,723
NBFR - Interchange to Meacham		491	20-Apr-13	09-Mar-15	794	$10,845,939
TCP & Temp Work		467	20-Apr-13	03-Feb-15	35	$270,747
Drainage		224	27-Jun-13	12-Aug-14	26	$3,321,690
Roadworks		339	20-May-13	03-Feb-15	26	$4,475,922
ITS / Signs / Stripes / Electrical / MISC.		89	05-Nov-14	09-Mar-15	794	$1,518,288
Noise Wall		5	26-Apr-13	02-May-13	493	$0
Bridge (B33 - NB 35W FR over Little Fossil Creek)		323	20-May-13	13-Aug-14	159	$1,259,292
SBFR - Interchange to Meacham		438	20-Apr-13	24-Dec-14	847	$9,722,314
TCP & Temp Work		405	20-Apr-13	07-Nov-14	97	$270,747
Drainage		192	27-Jun-13	19-Jun-14	70	$2,693,002
Roadworks		295	20-May-13	07-Nov-14	70	$3,926,991
ITS / Signs / Stripes / Electrical / MISC.		84	29-Aug-14	24-Dec-14	847	$1,457,606
Noise Wall		5	26-Apr-13	02-May-13	493	$0
Bridge (B34 - SB 35W FR over Little Fossil Creek)		238	20-May-13	16-Apr-14	244	$1,234,033
NBGP - Interchange to Meacham		268	20-Apr-13	30-Apr-14	1017	$3,191,717
TCP & Temp Work		268	20-Apr-13	30-Apr-14	234	$847,642
Drainage		8	19-Jun-13	01-Jul-13	314	$82,626
Roadworks		40	13-Jun-13	19-Aug-13	314	$387,253
ITS / Signs / Stripes / Electrical / MISC.		30	15-Jul-13	23-Aug-13	1195	$34,997
Noise Wall		5	24-Apr-13	30-Apr-13	495	$0

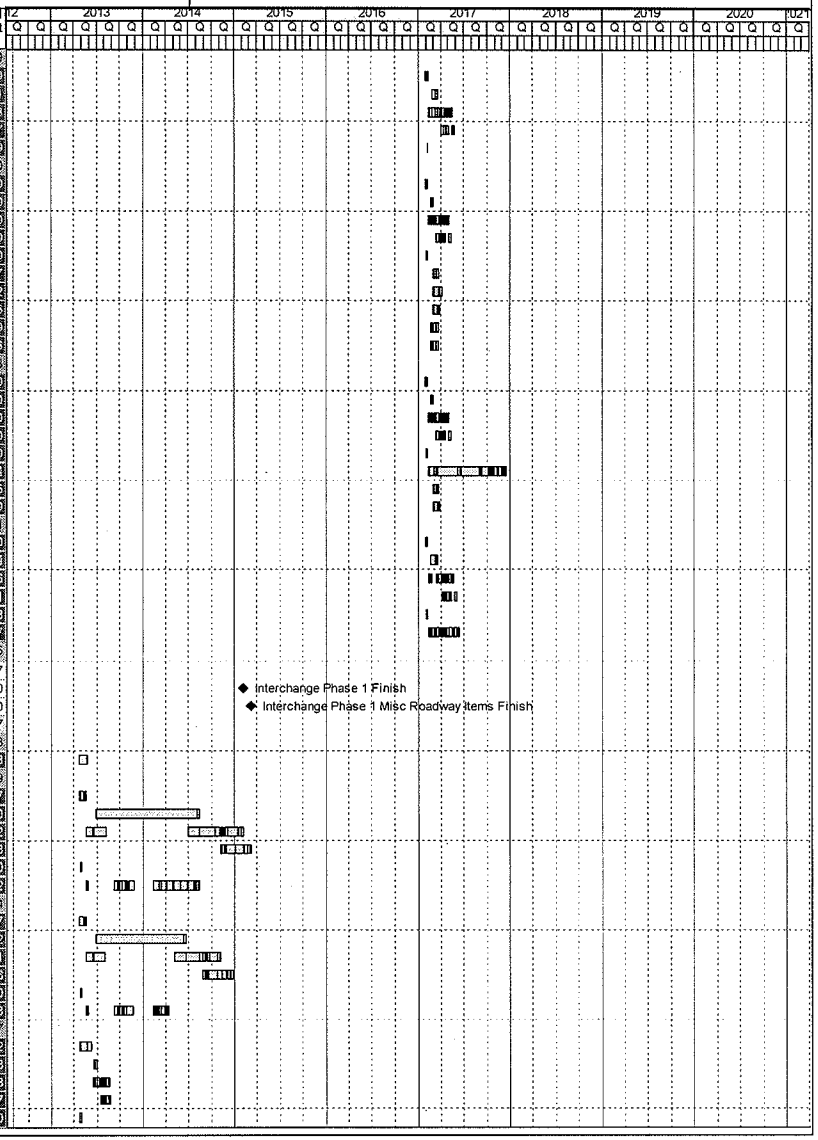

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Bridge (B1 - 35W NB GP over 820)	230	13-Jun-13	30-Apr-14	234	$1,839,025
	SBGP - Interchange to Meacham	260	20-Apr-13	18-Apr-14	1025	$5,588,301
	TCP & Temp Work	260	20-Apr-13	18-Apr-14	242	$1,560,410
	Drainage	11	22-Aug-13	09-Sep-13	252	$352,621
	Roadworks	76	25-Jul-13	09-Dec-13	252	$1,639,922
	ITS / Signs / Stripes / Electrical / MISC.	39	25-Oct-13	18-Dec-13	1112	$318,600
	Noise Wall	5	24-Apr-13	30-Apr-13	495	$0
	Bridge (B7 - 35W SB GP over 820	192	25-Jul-13	18-Apr-14	242	$1,696,748
	EBGP - Interchange to Meacham	228	20-Apr-13	05-Mar-14	1057	$7,486,364
	TCP & Temp Work	213	20-Apr-13	12-Feb-14	289	$1,873,208
	Drainage	19	19-Aug-13	19-Sep-13	217	$877,917
	Roadworks	108	01-Aug-13	12-Feb-14	217	$4,047,274
	ITS / Signs / Stripes / Electrical / MISC.	55	19-Dec-13	05-Mar-14	1057	$687,986
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	NSML - Interchange to Meacham	473	20-Apr-13	11-Feb-15	812	$19,527,318
	TCP & Temp Work	371	20-Apr-13	22-Sep-14	131	$741,612
	Drainage	61	11-Jun-13	23-Sep-13	98	$2,722,510
	Roadworks	287	20-May-13	22-Sep-14	98	$11,252,524
	ITS / Signs / Stripes / Electrical / MISC.	173	16-Jun-14	11-Feb-15	812	$2,247,472
	Noise Wall	5	03-May-13	09-May-13	488	$0
	Bridge (B4 - 35W ML over 820	261	20-May-13	19-May-14	221	$2,563,200
	EWML - Interchange to Meacham	210	20-Apr-13	07-Feb-14	1075	$7,129,497
	TCP & Temp Work	196	20-Apr-13	20-Jan-14	305	$369,932
	Drainage	29	11-Jun-13	30-Jul-13	230	$1,147,291
	Roadworks	135	20-May-13	20-Jan-14	230	$4,743,287
	ITS / Signs / Stripes / Electrical / MISC.	66	08-Nov-13	07-Feb-14	1075	$868,988
	Noise Wall	5	29-Apr-13	03-May-13	492	$0
	NBRP - Interchange to Meacham	406	20-Apr-13	10-Nov-14	879	$14,752,237
	TCP & Temp Work	405	20-Apr-13	10-Nov-14	86	$3,702,071
	Drainage	13	30-Oct-13	20-Nov-13	232	$173,465
	Roadworks	46	23-Oct-13	15-Jan-14	232	$483,419
	ITS / Signs / Stripes / Electrical / MISC.	34	09-Dec-13	23-Jan-14	1086	$72,938
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	Bridge (B35 - 35W NB GP Exit Ramp to Melody Hills)	119	23-Oct-13	07-Apr-14	251	$856,488
	Bridge (B16 - 35W NB - 820 EB GP DC)	274	23-Oct-13	10-Nov-14	86	$9,463,854
	SBRP - Interchange to Meacham	445	20-Apr-13	02-Jan-15	840	$26,529,491
	TCP & Temp Work	445	20-Apr-13	02-Jan-15	57	$3,615,374
	Drainage	35	31-Oct-13	06-Jan-14	183	$670,806
	Roadworks	93	25-Oct-13	18-Apr-14	183	$1,668,367
	ITS / Signs / Stripes / Electrical / MISC.	48	19-Feb-14	25-Apr-14	1020	$323,266
	Noise Wall	5	26-Apr-13	02-May-13	493	$0
	Bridge (B11 - 35W SB - 820 EB GP DC)	311	25-Oct-13	02-Jan-15	57	$9,198,148
	Bridge (B10 - 35W SB - 820 WB GP DC)	191	25-Oct-13	16-Jul-14	177	$6,005,897
	Retaining Wall EBRW-01	32	26-Nov-13	21-Jan-14	254	$791,577
	Retaining Wall EBRW-02	50	26-Nov-13	19-Feb-14	236	$1,595,365
	Retaining Wall EBRW-05	21	26-Nov-13	02-Jan-14	265	$450,715
	Retaining Wall EBRW-06	22	26-Nov-13	03-Jan-14	264	$461,926
	Retaining Wall WBRW-03	26	26-Nov-13	10-Jan-14	260	$579,799
	Retaining Wall WBRW-04	42	26-Nov-13	06-Feb-14	244	$1,028,250
	EBRP - Interchange to Meacham	393	20-Apr-13	22-Oct-14	892	$23,991,418
	TCP & Temp Work	393	20-Apr-13	22-Oct-14	109	$1,908,450
	Drainage	26	14-Aug-13	26-Sep-13	249	$479,896
	Roadworks	72	08-Aug-13	13-Dec-13	249	$1,337,659
	ITS / Signs / Stripes / Electrical / MISC.	42	28-Oct-13	24-Dec-13	1108	$182,973
	Noise Wall	5	24-Apr-13	30-Apr-13	495	$0
	Bridge (B14 - 820 EB - 35W SB GP DC)	315	08-Aug-13	22-Oct-14	109	$12,275,522
	Bridge (B13 - 820 EB - 35W NB GP DC)	234	08-Aug-13	01-Jul-14	190	$5,488,514
	Retaining Wall EBRW-11	51	09-Sep-13	02-Dec-13	283	$1,321,116
	Retaining Wall EBRW-12	51	09-Sep-13	02-Dec-13	283	$997,287
	WBRP - Interchange to Meacham	324	20-Apr-13	17-Jul-14	961	$28,027,518

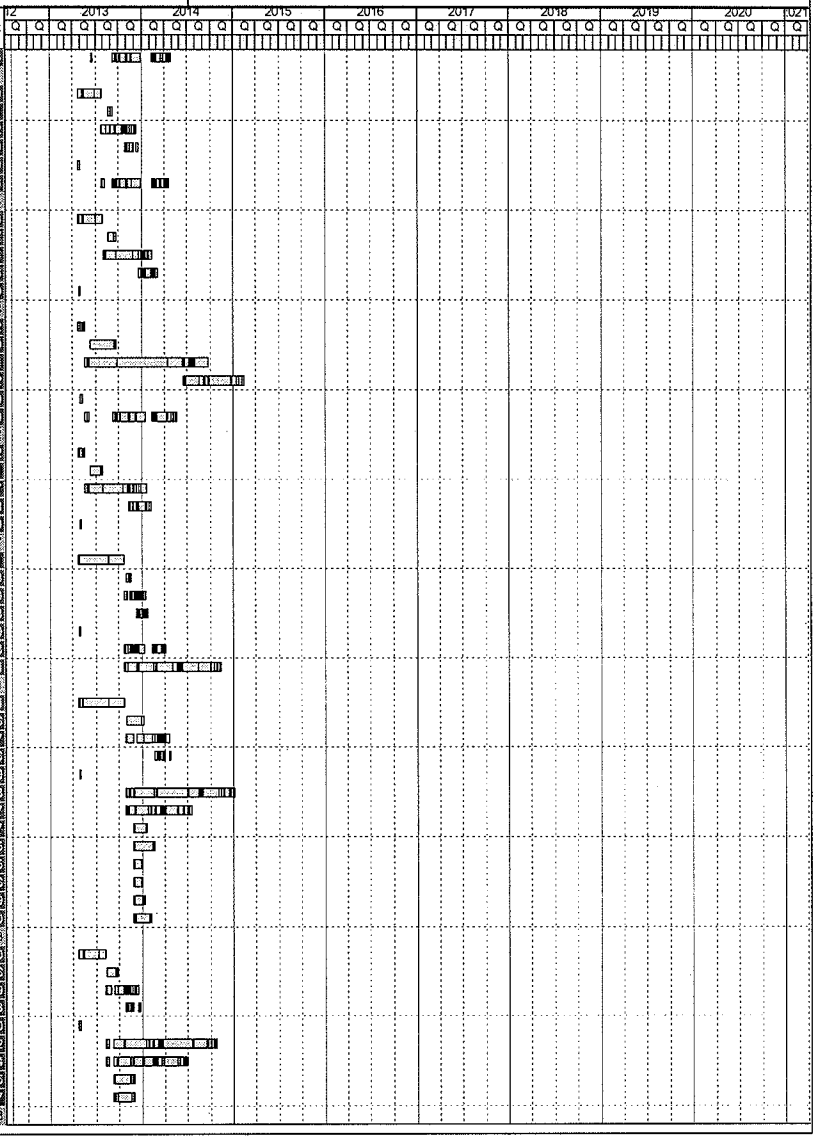

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
TCP & Temp Work		324	29-Apr-13	17-Jul-14	178	$8,576,907
Drainage		10	31-Jul-13	15-Aug-13	276	$410,409
Roadworks		77	18-Jul-13	26-Nov-13	257	$1,143,252
ITS / Signs / Stripes / Electrical / MISC.		39	15-Oct-13	06-Dec-13	1120	$117,897
Noise Wall		5	29-Apr-13	03-May-13	492	$0
Bridge (B12 - 820 WB - 35W NB GP DC)		205	18-Jul-13	30-Apr-14	234	$9,671,429
Bridge (B15 - 820 WB - 35W SB GP DC)		261	18-Jul-13	17-Jul-14	178	$7,162,606
Bridge (B21 - 820 WB - 35W SB ML DC)		192	18-Jul-13	11-Apr-14	247	$2,022,770
Retaining Wall WBRW-09		68	27-Sep-13	21-Jan-14	254	$1,917,920
Retaining Wall WBRW-10		70	27-Sep-13	23-Jan-14	252	$2,004,690
Phase 2		281	04-Feb-15	02-Mar-16	537	$98,596,108
ICMS1005	Interchange Phase 2 Misc Roadway Items Finish	0		01-Dec-15	845	$0
ICMS11001	Interchange Phase 2 Finish	0		02-Mar-16	46	$0
Stage 1		281	04-Feb-15	02-Mar-16	537	$98,596,108
NBGP - Interchange to Meacham		170	04-Feb-15	29-Sep-15	649	$5,569,907
TCP & Temp Work		153	04-Feb-15	04-Sep-15	160	$257,855
Drainage		18	20-Mar-15	20-Apr-15	116	$828,285
Roadworks		103	27-Feb-15	04-Sep-15	116	$3,672,530
ITS / Signs / Stripes / Electrical / MISC.		50	22-Jul-15	29-Sep-15	648	$611,238
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
SBGP - Interchange to Meacham		215	04-Feb-15	01-Dec-15	603	$8,495,663
TCP & Temp Work		180	04-Feb-15	13-Oct-15	133	$309,426
Drainage		22	20-Mar-15	27-Apr-15	97	$1,057,862
Roadworks		122	27-Feb-15	13-Oct-15	97	$4,918,766
ITS / Signs / Stripes / Electrical / MISC.		76	18-Aug-15	01-Dec-15	603	$825,017
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
Bridge (B32GPL - 35W over Little Fossil Creek)		105	27-Feb-15	24-Jul-15	190	$1,393,593
EBGP - Interchange to Meacham		189	04-Feb-15	26-Oct-15	629	$6,239,107
TCP & Temp Work		168	04-Feb-15	25-Sep-15	145	$243,673
Drainage		20	20-Mar-15	23-Apr-15	108	$940,625
Roadworks		113	27-Feb-15	25-Sep-15	106	$4,336,366
ITS / Signs / Stripes / Electrical / MISC.		61	03-Aug-15	26-Oct-15	629	$718,444
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
WBGP - Interchange to Meacham		181	04-Feb-15	14-Oct-15	637	$6,118,217
TCP & Temp Work		157	04-Feb-15	10-Sep-15	156	$232,843
Drainage		20	11-Mar-15	15-Apr-15	114	$825,104
Roadworks		105	27-Feb-15	10-Sep-15	114	$4,256,102
ITS / Signs / Stripes / Electrical / MISC.		59	24-Jul-15	14-Oct-15	637	$704,168
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
NSML - Interchange to Meacham		189	04-Feb-15	28-Sep-15	649	$5,754,701
TCP & Temp Work		145	04-Feb-15	25-Aug-15	168	$206,008
Drainage		21	13-Mar-15	17-Apr-15	123	$756,253
Roadworks		96	27-Feb-15	25-Aug-15	123	$3,125,701
ITS / Signs / Stripes / Electrical / MISC.		59	08-Jul-15	28-Sep-15	649	$704,222
Noise Wall		5	10-Feb-15	12-Feb-15	306	$0
Bridge (B32ML - 35W over Little Fossil Creek)		90	27-Feb-15	02-Jul-15	206	$962,522
EWML - Interchange to Meacham		215	04-Feb-15	01-Dec-15	603	$7,422,417
TCP & Temp Work		199	04-Feb-15	09-Nov-15	114	$386,016
Drainage		30	20-Mar-15	18-May-15	83	$1,197,173
Roadworks		136	27-Feb-15	09-Nov-15	83	$4,949,516
ITS / Signs / Stripes / Electrical / MISC.		65	02-Sep-15	01-Dec-15	603	$889,711
Noise Wall		5	12-Feb-15	18-Feb-15	302	$0
NBRP - Interchange to Meacham		274	04-Feb-15	22-Feb-16	544	$19,918,629
TCP & Temp Work		274	04-Feb-15	22-Feb-16	39	$64,124
Drainage		28	04-Mar-15	23-Apr-15	143	$520,404
Roadworks		78	24-Feb-15	23-Jul-15	143	$1,450,257
ITS / Signs / Stripes / Electrical / MISC.		40	04-Jun-15	29-Jul-15	682	$218,813
Noise Wall		5	10-Feb-15	16-Feb-15	304	$0
Bridge (B16 - 35W NB - 820 EB GP DC)		137	24-Feb-15	02-Sep-15	162	$3,154,618
Bridge (B17 - 35W NB - 820 WB GP DC)		260	24-Feb-15	22-Feb-16	39	$10,550,820

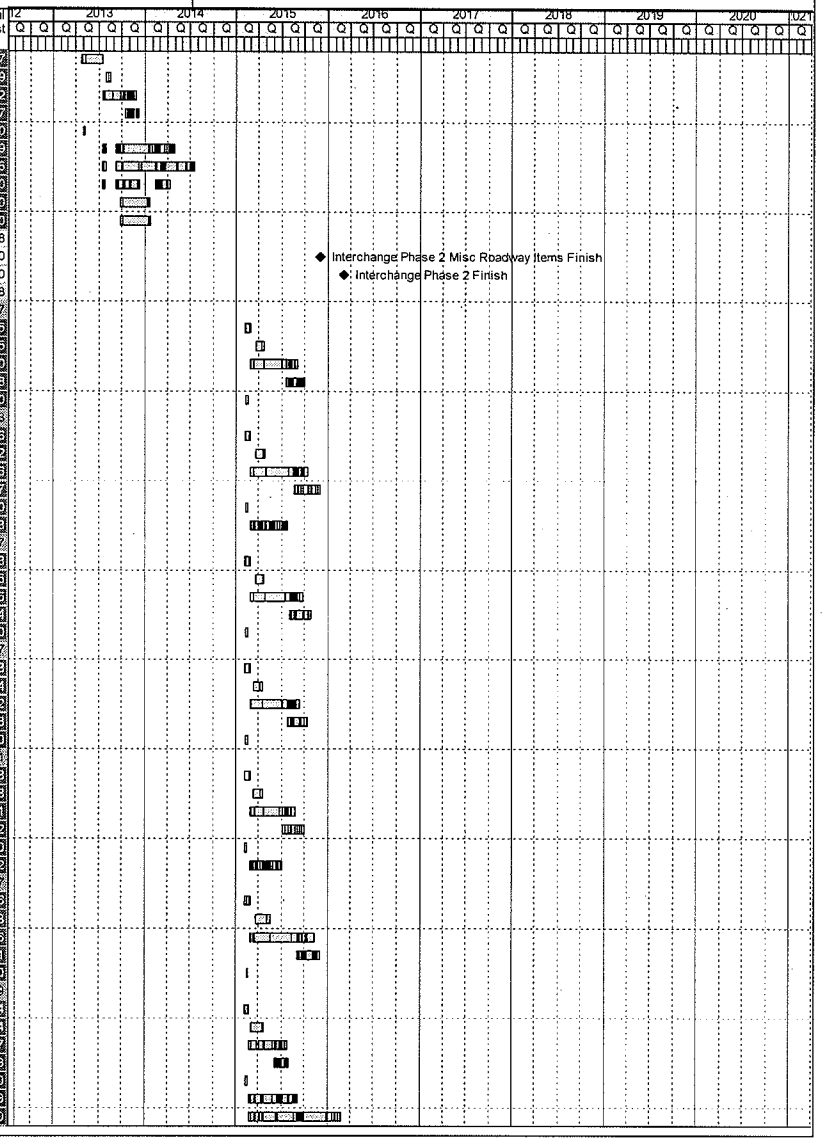

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Retaining Wall WBRW-05	56	25-Mar-15	26-Jun-15	174	$1,528,482
	Retaining Wall WBRW-06	49	25-Mar-15	15-Jun-15	181	$1,272,437
	Retaining Wall WBRW-04D	26	25-Mar-15	07-May-15	204	$579,287
	Retaining Wall WBRW-04E	26	25-Mar-15	07-May-15	204	$579,287
	SBRP - Interchange to Meacham	122	04-Feb-15	23-Jul-15	696	$3,383,408
	TCP & Temp Work	122	04-Feb-15	23-Jul-15	191	$92,818
	Drainage	17	25-Feb-15	30-Mar-15	169	$255,545
	Roadworks	55	19-Feb-15	05-Jun-15	169	$711,759
	ITS / Signs / Stripes / Electrical / MISC.	45	13-Apr-15	12-Jun-15	725	$73,326
	Noise Wall	3	12-Feb-15	16-Feb-15	304	$0
	Bridge (B10 - 35W SB - 820 WB GP DC)	111	19-Feb-15	23-Jul-15	191	$2,309,961
	EBRP - Interchange to Meacham	61	04-Feb-15	29-Apr-15	757	$221,287
	TCP & Temp Work	57	04-Feb-15	23-Apr-15	256	$13,537
	Drainage	8	23-Feb-15	09-Mar-15	189	$83,322
	Roadworks	37	16-Feb-15	23-Apr-15	189	$148,629
	ITS / Signs / Stripes / Electrical / MISC.	30	19-Mar-15	29-Apr-15	757	$5,799
	Noise Wall	5	06-Feb-15	12-Feb-15	906	$0
	WBRP - Interchange to Meacham	281	04-Feb-15	02-Mar-16	537	$35,472,872
	TCP & Temp Work	281	04-Feb-15	02-Mar-16	32	$93,843
	Drainage	10	24-Feb-15	16-Mar-15	174	$263,083
	Roadworks	51	17-Feb-15	27-May-15	174	$732,854
	ITS / Signs / Stripes / Electrical / MISC.	47	01-Apr-15	04-Jun-15	731	$75,601
	Noise Wall	3	10-Feb-15	12-Feb-15	906	$0
	Bridge (B12 - 820 WB - 35W NB GP DC)	156	17-Feb-15	22-Sep-15	148	$6,447,736
	Bridge (B18 - 820 WB - 35W NB ML DC)	272	17-Feb-15	02-Mar-16	32	$12,083,218
	Bridge (B21 - 820 WB - 35W SB ML DC)	247	17-Feb-15	27-Jan-16	57	$11,462,361
	Retaining Wall WBRW-01	76	02-Mar-15	07-Jul-15	168	$2,357,414
	Retaining Wall WBRW-01A	65	02-Mar-15	18-Jun-15	179	$247,581
	Retaining Wall WBRW-02	63	02-Mar-15	15-Jun-15	181	$1,769,182
	Phase 3	154	03-Mar-16	04-Oct-16	383	$25,276,793
ICMS1000	Interchange Phase 3 Misc Roadway Items Finish	0		18-Aug-16	584	$0
ICMS11005	Interchange Phase 3 Finish	0		04-Oct-16	54	$0
	Stage 1	154	03-Mar-16	04-Oct-16	383	$25,276,793
	NBGP - Interchange to Meacham	93	03-Mar-16	11-Jul-16	444	$1,609,572
	TCP & Temp Work	89	03-Mar-16	05-Jul-16	103	$599,475
	Drainage	9	20-Apr-16	05-May-16	83	$185,657
	Roadworks	45	11-Apr-16	05-Jul-16	83	$774,506
	ITS / Signs / Stripes / Electrical / MISC.	30	31-May-16	11-Jul-16	444	$69,934
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	SBGP - Interchange to Meacham	121	03-Mar-16	18-Aug-16	416	$2,414,285
	TCP & Temp Work	114	03-Mar-16	09-Aug-16	78	$103,142
	Drainage	11	28-Apr-16	23-May-16	61	$382,621
	Roadworks	74	28-Mar-16	09-Aug-16	61	$1,639,922
	ITS / Signs / Stripes / Electrical / MISC.	29	11-Jul-16	18-Aug-16	416	$318,600
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	EBGP - Interchange to Meacham	76	03-Mar-16	16-Jun-16	461	$797,005
	TCP & Temp Work	70	03-Mar-16	08-Jun-16	122	$332,490
	Drainage	7	23-Mar-16	04-Apr-16	98	$125,417
	Roadworks	43	16-Mar-16	08-Jun-16	98	$578,182
	ITS / Signs / Stripes / Electrical / MISC.	42	20-Apr-16	16-Jun-16	461	$60,917
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	NBRP - Interchange to Meacham	147	03-Mar-16	23-Sep-16	390	$10,157,450
	TCP & Temp Work	147	03-Mar-16	23-Sep-16	45	$49,875
	Drainage	23	29-Mar-16	13-May-16	74	$404,759
	Roadworks	65	18-Mar-16	21-Jul-16	74	$1,127,978
	ITS / Signs / Stripes / Electrical / MISC.	35	10-Jun-16	28-Jul-16	431	$170,188
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	Bridge (B16 - 35W NB - 820 EB GP DC)	136	18-Mar-16	23-Sep-16	43	$3,154,618
	Bridge (B17 - 35W NB - 820 WB GP DC)	134	18-Mar-16	21-Sep-16	45	$3,768,150
	Retaining Wall EBRW-09	35	15-Apr-16	14-Jun-16	99	$748,556

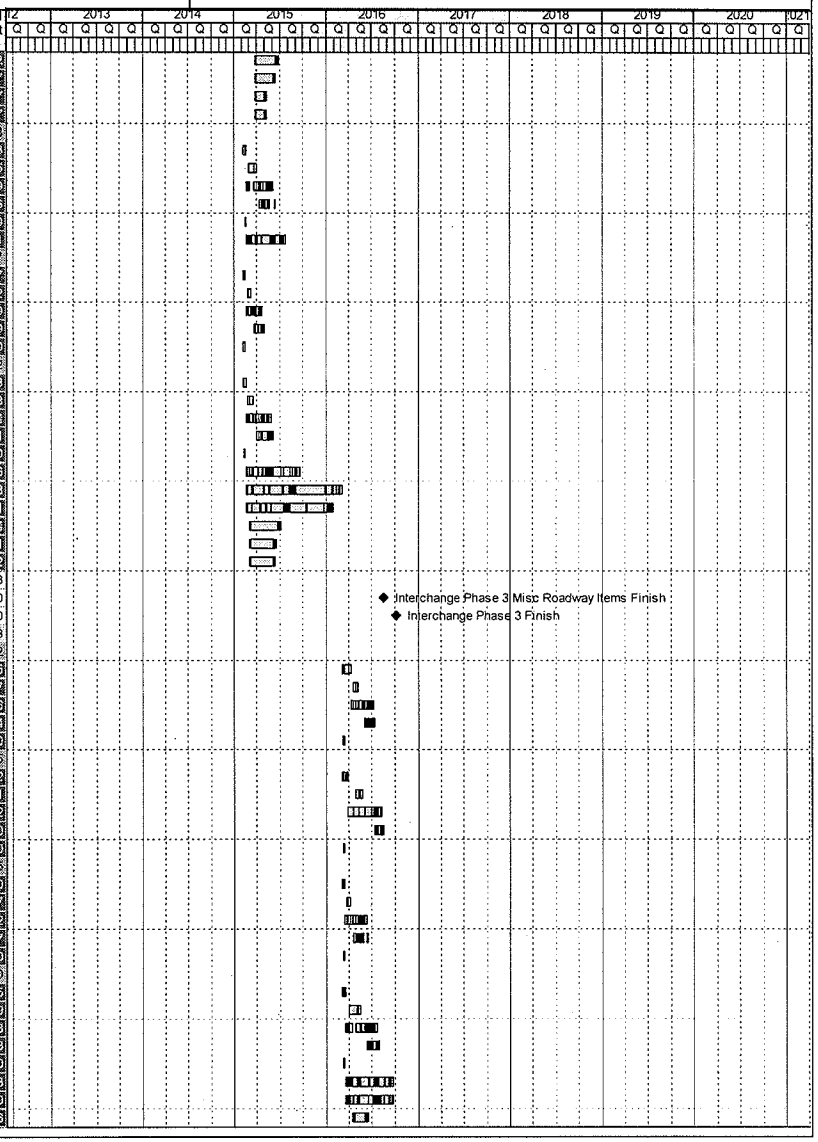

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Retaining Wall EBRW-10	34	15-Apr-16	13-Jun-16	100	$733,927
	SBRP - Interchange to Meacham	154	03-Mar-16	04-Oct-16	383	$6,331,193
	TCP & Temp Work	154	03-Mar-16	04-Oct-16	38	$16,409
	Drainage	11	23-Mar-16	12-Apr-16	97	$127,773
	Roadworks	44	15-Mar-16	09-Jun-16	97	$355,879
	ITS / Signs / Stripes / Electrical / MISC.	37	27-Apr-16	16-Jun-16	461	$36,663
	Noise Wall	5	08-Mar-16	14-Mar-16	184	$0
	Retaining Wall EBRW-03	85	29-Mar-16	16-Aug-16	60	$2,362,956
	Retaining Wall EBRW-04	115	29-Mar-16	04-Oct-16	30	$3,431,513
	EBRP - Interchange to Meacham	138	03-Mar-16	12-Sep-16	54	$2,703,298
	Bridge (B13 - 820 EB - 35W NB GP DC)	138	03-Mar-16	12-Sep-16	54	$2,703,298
	WBRP - Interchange to Meacham	100	03-Mar-16	20-Jul-16	92	$1,263,989
	Bridge (B15 - 820 WB - 35W SB GP DC)	100	03-Mar-16	20-Jul-16	92	$1,263,989
	Phase 4	228	05-Oct-16	18-Aug-17	155	$15,044,528
ICMS11000	Interchange Phase 4 Finish	0		18-Aug-17	219	$0
	Stage 1	228	05-Oct-16	18-Aug-17	155	$15,044,528
	SBGP - Interchange to Meacham	61	05-Oct-16	28-Dec-16	322	$570,875
	TCP & Temp Work	61	05-Oct-16	28-Dec-16	322	$25,785
	Drainage	7	24-Oct-16	03-Nov-16	257	$86,155
	Roadworks	37	17-Oct-16	22-Dec-16	257	$409,990
	ITS / Signs / Stripes / Electrical / MISC.	32	15-Nov-16	28-Dec-16	322	$46,954
	Noise Wall	5	07-Oct-16	13-Oct-16	376	$0
	EBGP - Interchange to Meacham	70	05-Oct-16	10-Jan-17	313	$929,839
	TCP & Temp Work	70	05-Oct-16	10-Jan-17	313	$37,905
	Drainage	8	27-Oct-16	08-Nov-16	251	$146,319
	Roadworks	41	18-Oct-16	03-Jan-17	251	$674,546
	ITS / Signs / Stripes / Electrical / MISC.	32	28-Nov-16	10-Jan-17	313	$71,069
	Noise Wall	5	07-Oct-16	13-Oct-16	376	$0
	WBGP - Interchange to Meacham	228	05-Oct-16	18-Aug-17	155	$8,025,032
	TCP & Temp Work	228	05-Oct-16	18-Aug-17	155	$308,652
	Drainage	25	14-Nov-16	30-Dec-16	30	$1,226,300
	Roadworks	136	27-Oct-16	13-Jul-17	151	$5,641,610
	ITS / Signs / Stripes / Electrical / MISC.	72	11-May-17	18-Aug-17	155	$848,270
	Noise Wall	5	10-Oct-16	14-Oct-16	375	$0
	EWML - Interchange to Meacham	74	05-Oct-16	16-Jan-17	309	$1,025,218
	TCP & Temp Work	74	05-Oct-16	16-Jan-17	309	$56,294
	Drainage	9	28-Oct-16	11-Nov-16	248	$174,588
	Roadworks	43	21-Oct-16	10-Jan-17	248	$721,804
	ITS / Signs / Stripes / Electrical / MISC.	32	02-Dec-16	16-Jan-17	309	$72,531
	Noise Wall	5	07-Oct-16	13-Oct-16	376	$0
	WBRP - Interchange to Meacham	100	05-Oct-16	21-Feb-17	283	$1,591,748
	TCP & Temp Work	100	05-Oct-16	21-Feb-17	283	$48,735
	Drainage	22	27-Oct-16	06-Dec-16	229	$378,839
	Roadworks	63	19-Oct-16	15-Feb-17	229	$1,055,310
	ITS / Signs / Stripes / Electrical / MISC.	36	03-Jan-17	21-Feb-17	283	$108,865
	Noise Wall	5	07-Oct-16	13-Oct-16	376	$0
	SBRP - Interchange to Meacham	87	05-Oct-16	02-Feb-17	296	$923,984
	Bridge (B10 - 35W SB - 820 WB GP DC)	87	05-Oct-16	02-Feb-17	296	$923,984
	NBRP - Interchange to Meacham	78	05-Oct-16	20-Jan-17	305	$753,630
	Bridge (B17 - 35W NB - 820 WB GP DC)	78	05-Oct-16	20-Jan-17	305	$753,630
	NBLA - Interchange to Meacham	47	05-Oct-16	08-Dec-16	336	$306,050
	TCP & Temp Work	65	05-Oct-16	08-Dec-16	472	$0
	Roadworks	26	05-Oct-16	16-Nov-16	268	$241,665
	ITS / Signs / Stripes / Electrical / MISC.	10	18-Nov-16	08-Dec-16	268	$64,385
	SBLA - Interchange to Meacham	47	05-Oct-16	08-Dec-16	336	$306,052
	TCP & Temp Work	65	05-Oct-16	08-Dec-16	472	$0
	Roadworks	26	05-Oct-16	16-Nov-16	268	$241,666
	ITS / Signs / Stripes / Electrical / MISC.	10	18-Nov-16	08-Dec-16	268	$64,385
	EBLA - Interchange to Meacham	47	05-Oct-16	08-Dec-16	336	$306,050
	TCP & Temp Work	65	05-Oct-16	08-Dec-16	472	$0

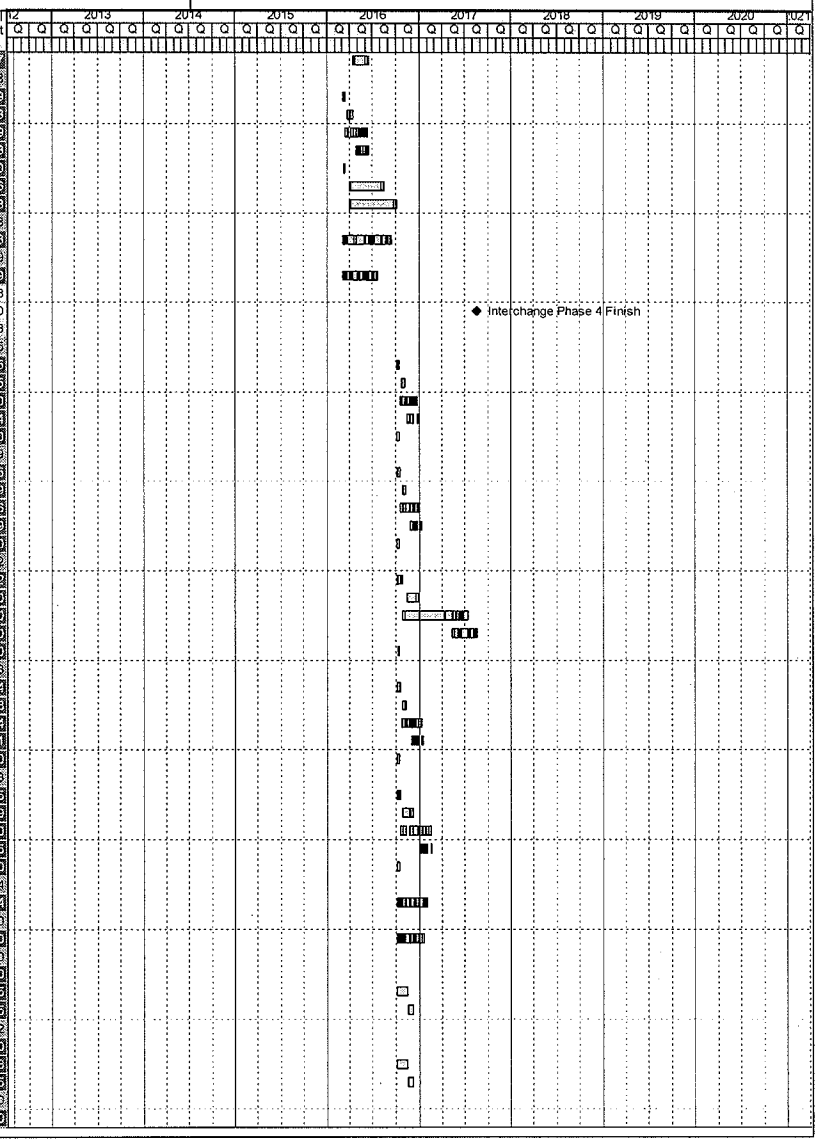

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	Budgeted Total Cost
	Roadworks	26	05-Oct-16	16-Nov-16	268	$241,665
	ITS / Signs / Stripes / Electrical / MISC.	10	16-Nov-16	08-Dec-16	268	$64,385
	WBLA - Interchange to Meacham	47	05-Oct-16	08-Dec-16	336	$306,050
	TCP & Temp Work	65	05-Oct-16	08-Dec-16	472	$0
	Roadworks	26	05-Oct-16	16-Nov-16	268	$241,665
	ITS / Signs / Stripes / Electrical / MISC.	10	16-Nov-16	08-Dec-16	268	$64,385



TAB B
Segment 3C Facility Segment Preliminary Baseline Schedule

[Attached]

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
NTE-3C 35W Schedule MASTER			1234	0	07-Mar-19	28-Nov-23
Project Administration			1234	0	07-Mar-19	28-Nov-23
3C Summary Schedule			1234	0	07-Mar-19	28-Nov-23
3C Contract Milestones			1234	0	07-Mar-19	28-Nov-23
COA3C	TX-3CD	3C COA EFFECTIVE DATE	0	0	07-Mar-19	
NTP13	TX-3CD	3C NOTICE TO PROCEED 1	0	32	17-Mar-19	
FC3C	TX-3CD	3C COMMERICIAL CLOSE	0	40		24-Jul-19
CCF3C	TX-3CD	3C FINANCIAL CLOSE	0	32		31-Jul-19
NTP2 :	TX-3CD	3C NOTICE TO PROCEED 2	0	374		31-Aug-19
COC3C	TX-3CD	3C COMMENCEMENT OF CONSTRUCTION	0	141	21-Apr-20	
PSUB(	TX-3CD	3C PREPARATION FOR SUBSTANTIAL COMPLETION	31	12	19-Jul-23	18-Aug-23
NSUB(	TX-3CD	3C NOTICE OF SUBSTANTIAL COMPLETION TO TXDOT	0	12	19-Jul-23	19-Jul-23
SRVC(	TX-3CD	3C SERVICE COMMENCEMENT\SUBSTANCIAL COMPLETION DEADLINE (NTP 2 + 1460 DAYS)	0	0		31-Aug-23*
PRPF/	TX-3CD	3C PREPARATION FOR FINAL ACCEPTANCE	90	0	31-Aug-23	28-Nov-23
FNLA3	TX-3CD	3C FINAL ACCEPTANCE DEADLINE (SC + 90 DAYS)	0	0		28-Nov-23*
3C Work Areas			528	0	19-Nov-21	28-Nov-23
C3(	TX-3CD	Segment 3C Completion of Punchlist	64	0	31-Aug-23	28-Nov-23
C3(	TX-3CD	Segment 3C Completed	0	0	31-Aug-23	31-Aug-23
3C Northbound Lanes			449	0	10-Dec-21	31-Aug-23
(	TX-3CD	Segment 3C Northbound Entry Ramps Complete	0	449	10-Dec-21	10-Dec-21
(	TX-3CD	Segment 3C Northbound Frontage Road Complete	0	349	29-Apr-22	29-Apr-22
(	TX-3CD	Segment 3C Northbound General Purpose Lanes Complete	0	288	25-Jul-22	25-Jul-22
(	TX-3CD	Segment 3C Northbound Exit Ramps Complete	0	140	16-Feb-23	16-Feb-23
(	TX-3CD	Segment 3C Northbound Managed Lanes Complete	0	0	31-Aug-23	31-Aug-23
3C Southbound Lanes			332	132	19-Nov-21	28-Feb-23
(	TX-3CD	Segment 3C Southbound Exit Ramps Complete	0	464	19-Nov-21	19-Nov-21
(	TX-3CD	Segment 3C Southbound General Purpose Complete	0	402	15-Feb-22	15-Feb-22
(	TX-3CD	Segment 3C Southbound Frontage Road Complete	0	330	26-May-22	26-May-22
(	TX-3CD	Segment 3C Southbound Entry Ramps Complete	0	197	29-Nov-22	29-Nov-22
(	TX-3CD	Segment 3C Southbound Managed Lanes Complete	0	132	28-Feb-23	28-Feb-23
3C Cross Streets			0	298	11-Jul-22	11-Jul-22
(	TX-3CD	Segment 3C Cross Roads Complete	0	298	11-Jul-22	11-Jul-22
IH 820 Contract Milestones			657	34	07-Jan-20	24-Oct-21
COC8:	TX-3CD	IH 820 COMMENCEMENT OF CONSTRUCTION	0	127	07-Jan-20	
PSUB(	TX-3CD	IH 820 PREPARATION FOR SUBSTANTIAL COMPLETION	30	44	17-Jun-21	16-Jul-21
NSUB(	TX-3CD	IH 820 NOTICE OF SUBSTANTIAL COMPLETION TO TXDOT	0	44	17-Jun-21	17-Jun-21
SRVC(	TX-3CD	IH 820 SERVICE COMMENCEMENT\SUBSTANCIAL COMPLETION DEADLINE (NTP 2 + 730 DAYS	0	34		27-Jul-21*
PRPF/	TX-3CD	IH 820 PREPARATION FOR FINAL ACCEPTANCE	90	34	27-Jul-21	24-Oct-21
FNLA8	TX-3CD	IH 820 FINAL ACCEPTANCE DEADLINE (SC + 90 DAYS)	0	34		24-Oct-21*
Work Area			60	29	27-Jul-21	18-Oct-21
IH 820 Direct Connector Ramps			60	29	27-Jul-21	18-Oct-21
C82	TX-3CD	IH 820 Direct Connector Completed	0	24	27-Jul-21	27-Jul-21
C82	TX-3CD	IH 820 Direct Connector Completion of Punchlist	60	29	27-Jul-21	18-Oct-21
Mobilization			37	334	07-Mar-19	26-Apr-19
Developer			20	351	07-Mar-19	03-Apr-19
ADMC	TX-3CD	Developer Mobilization	20	351	07-Mar-19	03-Apr-19
ADMC	TX-3CD	Mobilize ROW Staff	20	351	07-Mar-19	03-Apr-19
DB Contractor			37	0	07-Mar-19	26-Apr-19
ADMC	TX-3CD	D & B Contractor Mobilization	37	0	07-Mar-19	26-Apr-19
Segment 3C Documentation Requirements			54	73	07-Mar-19	21-May-19
Conditions to Closing			54	73	07-Mar-19	21-May-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
ADCC	TX-3CD	Conditions for Closing Completed	0	73		21-May-19
7a USDOT Build America Bureau			27	100	07-Mar-19	12-Apr-19
AD(	TX-3CD	19-Feb-20	9	100	07-Mar-19	19-Mar-19
AD(	TX-3CD	Submit TIFIA Letter of Interest to USDOT Build America Bureau and TxDOT	1	100	20-Mar-19	20-Mar-19
AD(	TX-3CD	USDOT Build America Bureau and TxDOT Review & Comments TIFIA Letter of Interest for TIFIA	10	100	21-Mar-19	03-Apr-19
AD(	TX-3CD	Incorporate & Resolve USDOT Build America Bureau and TxDOT Comments TIFIA Letter of Interest fo	5	100	04-Apr-19	10-Apr-19
AD(	TX-3CD	TIFIA Letter of Interest for TIFIA in Place	1	100	12-Apr-19	12-Apr-19
7b USDOT Build America Bureau			27	100	07-Mar-19	12-Apr-19
AD(	TX-3CD	Develop Produces Complete Application for Allocation of PAB's	9	100	07-Mar-19	19-Mar-19
AD(	TX-3CD	Submit Application for Allocation of PAB's to USDOT Build America Bureau and TxDOT	1	100	20-Mar-19	20-Mar-19
AD(	TX-3CD	USDOT Build America Bureau and TxDOT Review & Comments Application for Allocation of PAB's	10	100	21-Mar-19	03-Apr-19
AD(	TX-3CD	Incorporate & Resolve USDOT Build America Bureau and TxDOT Comments Application for Allocation	5	100	04-Apr-19	10-Apr-19
AD(	TX-3CD	Application for Allocation of PAB's in Place	1	100	12-Apr-19	12-Apr-19
7c Rating Agencies			38	89	07-Mar-19	29-Apr-19
AD(	TX-3CD	Rating Agencies Reports	20	89	07-Mar-19	03-Apr-19
AD(	TX-3CD	Submit Rating Agencies Reports	1	89	04-Apr-19	04-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Rating Agencies Reports	10	89	05-Apr-19	18-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Rating Agencies Reports	5	89	19-Apr-19	25-Apr-19
AD(	TX-3CD	Rating Agencies Reports in Place	1	89	29-Apr-19	29-Apr-19
7d Amendments to Design-Build Contract Incorporating 3C			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Develop Amendments to Design-Build Contract Incorporating 3C	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Amendments to Design-Build Contract Incorporating 3C	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Amendments to Design-Build Contract Incorporating 3C	15	124	11-Apr-19	25-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Amendments to Design-Build Contract Incorporating 3C	1	88	26-Apr-19	26-Apr-19
AD(	TX-3CD	Amendments to Design-Build Contract Incorporating 3C in Place	1	88	30-Apr-19	30-Apr-19
7e Key Personnel			36	91	07-Mar-19	25-Apr-19
AD(	TX-3CD	Develop Key Personnel Document	20	91	07-Mar-19	03-Apr-19
AD(	TX-3CD	Submit Key Personnel Document	1	91	04-Apr-19	04-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Key Personnel Document	15	129	05-Apr-19	19-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Key Personnel Document	2	91	22-Apr-19	23-Apr-19
AD(	TX-3CD	Key Personnel Document in Place	1	91	25-Apr-19	25-Apr-19
7f Key Contractors & New Key Contracts			36	91	07-Mar-19	25-Apr-19
AD(	TX-3CD	Develop Key Contractors & New Sucontractors Document	20	91	07-Mar-19	03-Apr-19
AD(	TX-3CD	Submit Key Contractors & New Sucontractors Document	1	91	04-Apr-19	04-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Key Contractors & New Sucontractors Document	15	129	05-Apr-19	19-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Key Contractors & New Sucontractors Document	2	91	22-Apr-19	23-Apr-19
AD(	TX-3CD	Key Contractors & New Sucontractors Document in Place	1	91	25-Apr-19	25-Apr-19
7g Developer/NTTA Amended Tolling Services Agreement			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Develop Amended Tolling Services Agrement	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Amended Tolling Services Agrement	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Amended Tolling Services Agrement	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Amended Tolling Services Agrement	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Amended Tolling Services Agrement in Place	1	88	30-Apr-19	30-Apr-19
7h Developer/NTTA Amended Joinder Agreement			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Developer/NTTA Amended Joinder Agreement	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Developer/NTTA Amended Joinder Agreement	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Developer/NTTA Amended Joinder Agreement	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Developer/NTTA Amended Joinder Agreement	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Developer/NTTA Amended Joinder Agreement in Place	1	88	30-Apr-19	30-Apr-19
7i Amended Facility Trust Agreement			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Amended Facility Trust Agreement	24	88	07-Mar-19	09-Apr-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
AD(	TX-3CD	Submit Amended Facility Trust Agreement	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Amended Facility Trust Agreement	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Amended Facility Trust Agreement	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Amended Facility Trust Agreement in Place	1	88	30-Apr-19	30-Apr-19
7j Amended Joint Work Authorization (IE)			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Develop Amended Joint Work Authorization (IE)	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Amended Joint Work Authorization (IE)	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT/IE Review & Comments Amended Joint Work Authorization (IE)	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT/IE Comments Amended Joint Work Authorization (IE)	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Amended Joint Work Authorization (IE) in Place	1	88	30-Apr-19	30-Apr-19
7k Preliminary Base Case Financial Model Update (3C)			39	73	07-Mar-19	30-Apr-19
AD(	TX-3CD	Develop Preliminary Base Case Financial Model Update (3C)	24	73	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Preliminary Base Case Financial Model Update (3C)	1	73	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Preliminary Base Case Financial Model Update (3C)	10	73	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Preliminary Base Case Financial Model Update (3C)	2	73	25-Apr-19	26-Apr-19
AD(	TX-3CD	Preliminary Base Case Financial Model Update (3C) in Place	1	73	30-Apr-19	30-Apr-19
7l Base Case Financial Model Update (3C)			15	73	01-May-19	21-May-19
AD(	TX-3CD	Develop Base Case Financial Model Update (3C)	1	73	01-May-19	01-May-19
AD(	TX-3CD	Submit Base Case Financial Model Update (3C)	1	73	02-May-19	02-May-19
AD(	TX-3CD	TxDOT Review & Comments Base Case Financial Model Update (3C)	10	73	03-May-19	16-May-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Base Case Financial Model Update (3C)	2	73	17-May-19	20-May-19
AD(	TX-3CD	Base Case Financial Model Update (3C) in Place	1	73	21-May-19	21-May-19
7m Drafts of Funding Agreements and Security Documents (3c)			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Develop Drafts of Funding Agreements and Security Documents (3c)	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Drafts of Funding Agreements and Security Documents (3c)	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Drafts of Funding Agreements and Security Documents (3c)	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Drafts of Funding Agreements and Security Documents (3c)	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Drafts of Funding Agreements and Security Documents (3c) in Place	1	88	30-Apr-19	30-Apr-19
7n Developer Current Documentation and Evidence of Ownership			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Developer Current Documentation and Evidence of Ownership	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Developer Current Documentation and Evidence of Ownership	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Developer Current Documentation and Evidence of Ownership	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Developer Current Documentation and Evidence of Ownersl	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Developer Current Documentation and Evidence of Ownership in Place	1	88	30-Apr-19	30-Apr-19
7o Opinions of Legal Counsol of Developer			39	88	07-Mar-19	30-Apr-19
AD(	TX-3CD	Develop Opinions of Legal Counsol of Developer	24	88	07-Mar-19	09-Apr-19
AD(	TX-3CD	Submit Opinions of Legal Counsol of Developer	1	88	10-Apr-19	10-Apr-19
AD(	TX-3CD	TxDOT Review & Comments Opinions of Legal Counsol of Developer	10	88	11-Apr-19	24-Apr-19
AD(	TX-3CD	Incorporate & Resolve TxDOT Comments Opinions of Legal Counsol of Developer	2	88	25-Apr-19	26-Apr-19
AD(	TX-3CD	Opinions of Legal Counsol of Developer in Place	1	88	30-Apr-19	30-Apr-19
7p Opinions of Legal Counsol of TxDOT			44	83	07-Mar-19	07-May-19
AD(	TX-3CD	Opinions of Legal Counsol of TxDOT	20	83	07-Mar-19	03-Apr-19
AD(	TX-3CD	Developer Review Opinions of Legal Counsol of TxDOT	10	83	04-Apr-19	17-Apr-19
AD(	TX-3CD	TxDOT Clears Comments Opinions of Legal Counsol of TxDOT	10	83	18-Apr-19	01-May-19
AD(	TX-3CD	Resolved TxDOT Comments Opinions of Legal Counsol of TxDOT	2	83	02-May-19	03-May-19
AD(	TX-3CD	Opinions of Legal Counsol of TxDOT in Place	1	83	07-May-19	07-May-19
7q Final Drafts of Funding Agreements and Security Documents			43	84	07-Mar-19	06-May-19
AD(	TX-3CD	Develop Final Drafts of Funding Agreements and Security Documents	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit Final Drafts of Funding Agreements and Security Documents	1	84	02-May-19	02-May-19
AD(	TX-3CD	Final Drafts of Funding Agreements and Security Documents in Place	1	84	06-May-19	06-May-19
7r Market Interest Rate Changes			43	84	07-Mar-19	06-May-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
AD(	TX-3CD	Develop Market Interest Rate Changes	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit Market Interest Rate Changes	1	84	02-May-19	02-May-19
AD(	TX-3CD	Market Interest Rate Changes in Place	1	84	06-May-19	06-May-19
7s TIFIA Financing Terms Fictitious Adjustment			43	84	07-Mar-19	06-May-19
AD(	TX-3CD	TIFIA Financing Terms Fictitious Adjustment	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit TIFIA Financing Terms Fictitious Adjustment	1	84	02-May-19	02-May-19
AD(	TX-3CD	TIFIA Financing Terms Fictitious Adjustment in Place	1	84	06-May-19	06-May-19
7t Conformation of No Temp Restaining Orders or Injuctions			43	84	07-Mar-19	06-May-19
AD(	TX-3CD	Conformation of No Temp Restaining Orders or Injuctions	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit Conformation of No Temp Restaining Orders or Injuctions	1	84	02-May-19	02-May-19
AD(	TX-3CD	Conformation of No Temp Restaining Orders or Injuctions in Place	1	84	06-May-19	06-May-19
7u Conformation of No Incurable or Uncured Developer Default or TxDOT Warning Notices			43	84	07-Mar-19	06-May-19
AD(	TX-3CD	Conformation of No Incurable or Uncured Developer Default or TxDOT Warning Notices	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit Conformation of No Incurable or Uncured Developer Default or TxDOT Warning Notices	1	84	02-May-19	02-May-19
AD(	TX-3CD	Conformation of No Incurable or Uncured Developer Default or TxDOT Warning Notices in Place	1	84	06-May-19	06-May-19
7v Conformation of No Material TxDOT Default Under Section 17.5.1.1 of the Facility Agreement			43	84	07-Mar-19	06-May-19
AD(	TX-3CD	Conformation of No Material TxDOT Default Under Section 17.5.1.1 of the Facility Agreement	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit Conformation of No Material TxDOT Default Under Section 17.5.1.1 of the Facility Agreement	1	84	02-May-19	02-May-19
AD(	TX-3CD	Conformation of No Material TxDOT Default Under Section 17.5.1.1 of the Facility Agreement in Place	1	84	06-May-19	06-May-19
7w FWHA Approval of Amended & Restated Facility Agreement, Technical Provisions and Change Order			43	84	07-Mar-19	06-May-19
AD(	TX-3CD	FWHA Approval of Amended & Restated Facility Agreement, Technical Provisions and Change Order	40	84	07-Mar-19	01-May-19
AD(	TX-3CD	Submit FWHA Approval of Amended & Restated Facility Agreement, Technical Provisions and Change	1	84	02-May-19	02-May-19
AD(	TX-3CD	FWHA Approval of Amended & Restated Facility Agreement, Technical Provisions and Change Order ir	1	84	06-May-19	06-May-19
Submittals and Permitting			293	101	07-Mar-19	20-Apr-20
Permitting Governmental Agency			293	101	07-Mar-19	20-Apr-20
Federal			205	189	07-Mar-19	18-Dec-19
TIFIA Approvals			14	113	07-Mar-19	26-Mar-19
A	TX-3CD	C3 Developer Prepares TIFIA Documents	5	111	07-Mar-19	13-Mar-19
A	TX-3CD	Submit to TXDOT District C3 TIFIA Documents	1	111	14-Mar-19	14-Mar-19
A	TX-3CD	TXDOT District Review C3 TIFIA Documents	10	157	15-Mar-19	24-Mar-19
A	TX-3CD	C3 TIFIA Documents - Clear Comments	1	113	25-Mar-19	25-Mar-19
A	TX-3CD	TXDOT District Forwards C3 to TIFIA	1	113	26-Mar-19	26-Mar-19
FAA Notification			17	189	26-Nov-19	18-Dec-19
A	TX-3CD	C3 Developer Prepares FAA Notifications	5	189	26-Nov-19	02-Dec-19
A	TX-3CD	Submit to TXDOT District C3 FAA Notifications	1	189	03-Dec-19	03-Dec-19
A	TX-3CD	TXDOT District Review C3 FAA Notifications	10	265	04-Dec-19	13-Dec-19
A	TX-3CD	C3 FAA Notifications - Clear Comments	2	189	16-Dec-19	17-Dec-19
A	TX-3CD	Forward C3 FAA Notifications to FAA	1	189	18-Dec-19	18-Dec-19
FEMA Application			17	189	26-Nov-19	18-Dec-19
A	TX-3CD	C3 Developer Prepares FEMA Application	5	189	26-Nov-19	02-Dec-19
A	TX-3CD	Submit to TXDOT District C3 FEMA Application	1	189	03-Dec-19	03-Dec-19
A	TX-3CD	TXDOT District Review C3 FEMA Application	10	265	04-Dec-19	13-Dec-19
A	TX-3CD	C3 FEMA Applications - Clear Comments	2	189	16-Dec-19	17-Dec-19
A	TX-3CD	Forward C3 FEMA Applications to FEMA	1	189	18-Dec-19	18-Dec-19
NEPA Re-evaluation C3			96	298	07-Mar-19	18-Jul-19
[	TX-3CD	C3 Traffic Analysis info provided by Cintra	1	296	07-Mar-19	07-Mar-19
[	TX-3CD	C3 Developer Prepares Final IAJR and DRC	40	296	08-Mar-19	02-May-19
[	TX-3CD	Submit to TXDOT District C3 Final IAJR and DRC	0	296	03-May-19	03-May-19
[	TX-3CD	TXDOT District Review C3 Final IAJR and DRC	10	414	03-May-19	12-May-19
[	TX-3CD	C3 Final IAJR and DRC - Clear Comments	10	296	13-May-19	24-May-19
[	TX-3CD	TXDOT District Forwards C3 Final IAJR and DRC to TXDOT Austin	0	296	27-May-19	27-May-19

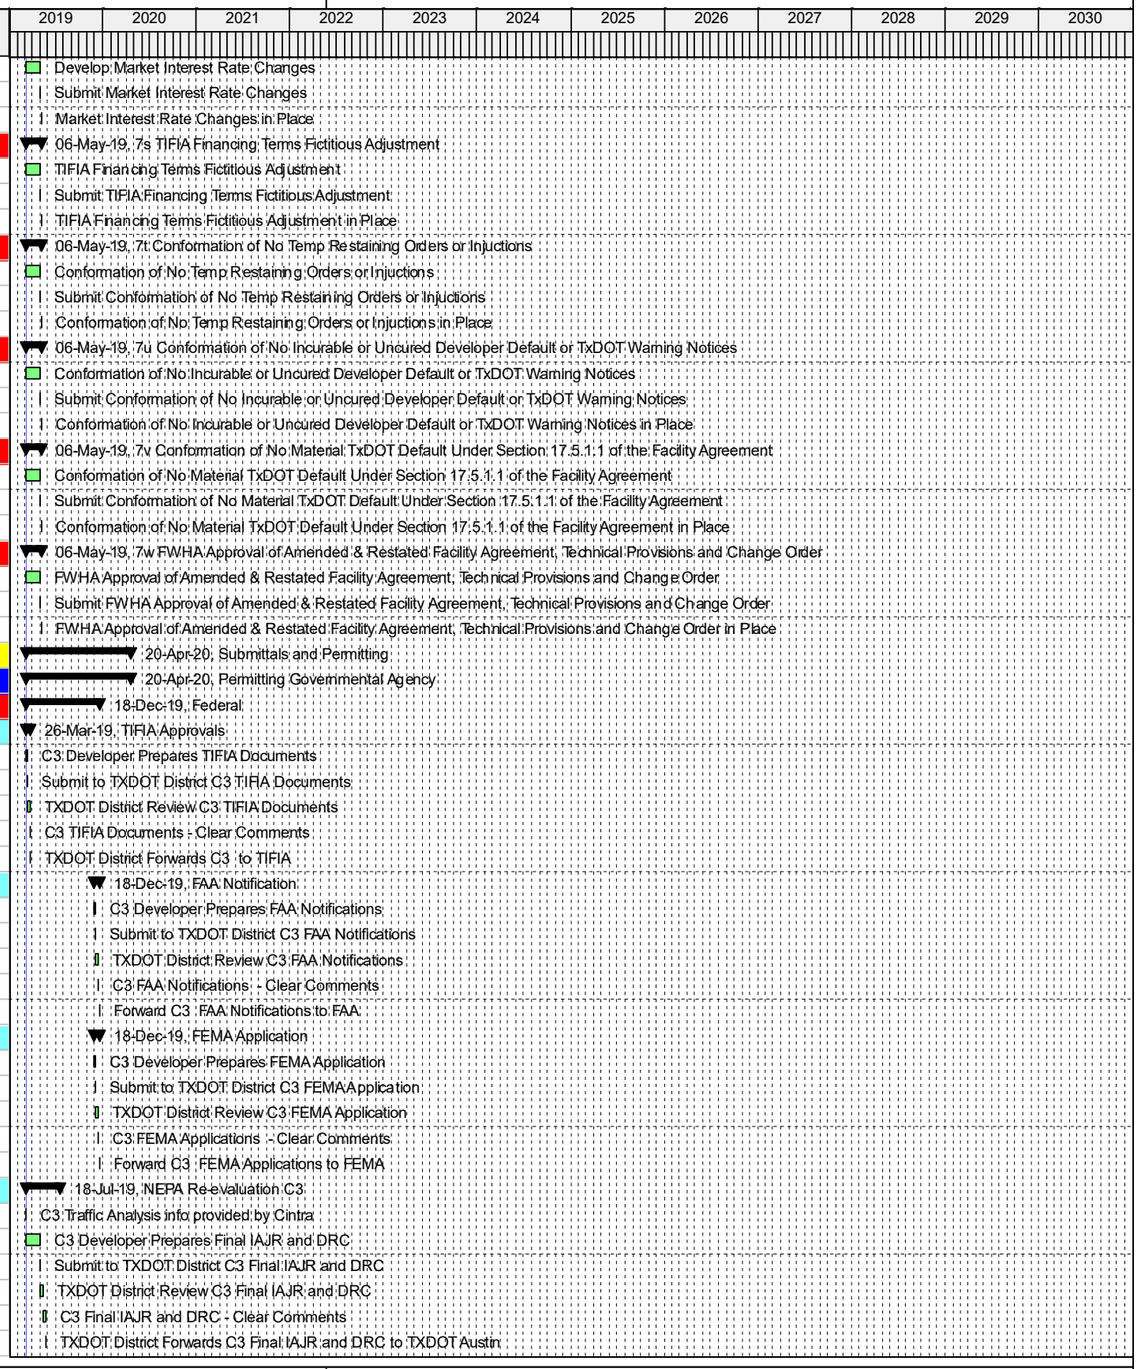

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	TXDOT Austin Review C3 Final IAJR and DRC	10	414	27-May-19	05-Jun-19
[	TX-3CD	C3 Final IAJR and DRC - 1st Round TXDOT Austin Comments	1	296	06-Jun-19	06-Jun-19
[	TX-3CD	NTI Clears the1st Round Clears Comments C3 Final IAJR and DRC	10	296	07-Jun-19	20-Jun-19
[	TX-3CD	Submit to TXDOT Austin 1st Round cleared comments of C3 Final IAJR and DRC	1	296	21-Jun-19	21-Jun-19
[	TX-3CD	TXDOT Austin Review 2nd Round of C3 Final IAJR and DRC	10	416	22-Jun-19	01-Jul-19
[	TX-3CD	NTI Clears the 2nd Round Clears Comments C3 Final IAJR and DRC - Clear Comments	10	298	02-Jul-19	15-Jul-19
[	TX-3CD	TXDOT Austin Closes Comments and Signs C3 DRC	2	298	16-Jul-19	17-Jul-19
[	TX-3CD	Recieve Approved C3 DRC Documentation in Place	1	298	18-Jul-19	18-Jul-19
NEPA Re-evaluation IH 820			83	219	18-Mar-19	10-Jul-19
[	TX-3CD	IH 820 DC ML RampsTraffic Analysis info provided by Cintra	1	217	18-Mar-19	18-Mar-19
[	TX-3CD	IH 820 DC ML RampsTraffic Analysis & IAJR	20	217	19-Mar-19	15-Apr-19
[	TX-3CD	IH 820 DC ML RampsDeveloper Prepares Traffic Analysis & IAJR and DRC	2	217	16-Apr-19	17-Apr-19
[	TX-3CD	Submit to TXDOT IH 820 DC ML RampsTraffic Analysis & IAJR and DRC	1	217	18-Apr-19	18-Apr-19
[	TX-3CD	TXDOT Review IH 820 DC ML RampsTraffic Analysis & IAJR and DRC	10	305	19-Apr-19	28-Apr-19
[	TX-3CD	IH 820 DC ML RampsFinal IAJR and DRC - Clear Comments	6	219	29-Apr-19	06-May-19
[	TX-3CD	TXDOT District Forwards IH 820 DC ML RampsFinal IAJR and DRC to TXDOT Austin	1	219	07-May-19	07-May-19
[	TX-3CD	TXDOT Austin Review IH 820 DC ML RampsFinal IAJR and DRC	10	307	08-May-19	17-May-19
[	TX-3CD	IH 820 DC ML RampsFinal IAJR and DRC - 1st Round TXDOT Austin Comments	1	219	20-May-19	20-May-19
[	TX-3CD	NTI Clears the1st Round Clears Comments IH 820 DC ML RampsFinal IAJR and DRC	10	219	21-May-19	03-Jun-19
[	TX-3CD	Submit to TXDOT Austin 1st Round cleared comments of IH 820 DC ML RampsFinal IAJR and DRC	1	219	04-Jun-19	04-Jun-19
[	TX-3CD	TXDOT Austin Review 2nd Round of IH 820 DC ML RampsFinal IAJR and DRC	10	307	05-Jun-19	14-Jun-19
[	TX-3CD	NTI Clears the 2nd Round Clears Comments IH 820 DC ML RampsFinal IAJR and DRC - Clear Com	10	219	17-Jun-19	28-Jun-19
[	TX-3CD	TXDOT Austin Closes Comments and Signs IH 820 DC ML RampsDRC	7	219	01-Jul-19	09-Jul-19
[	TX-3CD	Recieve Approved IH 820 DC ML Ramps DRC Documentation in Place	1	219	10-Jul-19	10-Jul-19
State of Texas			173	101	22-Aug-19	20-Apr-20
USACE			77	100	22-Aug-19	06-Dec-19
F	TX-3CD	Developer Prepare USACE Section 404 Clean Water Act Permit Application	50	100	22-Aug-19	30-Oct-19
F	TX-3CD	Developer Prepare Section 401 Clean Water Act Permit Application	50	100	22-Aug-19	30-Oct-19
F	TX-3CD	Submit to TXDOT USACE Section 404 Clean Water Act Permit Application	1	140	31-Oct-19	31-Oct-19
F	TX-3CD	Submit to TXDOT Section 401 Clean Water Act Permit Application	1	140	31-Oct-19	31-Oct-19
F	TX-3CD	TXDOT Review USACE Section 404 Clean Water Act Permit Application	10	140	01-Nov-19	10-Nov-19
F	TX-3CD	TXDOT Review Section 401 Clean Water Act Permit Application	10	140	01-Nov-19	10-Nov-19
F	TX-3CD	Obtain USACE Section 404 Clean Water Act Permit	20	100	11-Nov-19	06-Dec-19
F	TX-3CD	Obtain Section 401 Clean Water Act Permit	20	100	11-Nov-19	06-Dec-19
TCEQ			46	101	17-Feb-20	19-Feb-20
F	TX-3CD	Developer Prepare TCEQ Permit Application	20	100	17-Feb-20	13-Mar-20
F	TX-3CD	TXDOT Review TCEQ Application	10	141	14-Mar-20	23-Mar-20
F	TX-3CD	Submit to TXDOT TCEQ Permit Application	0	141	14-Mar-20	14-Mar-20
F	TX-3CD	Obtain TCEQ Permit	20	101	24-Mar-20	20-Apr-20
TPDES-SWPPP Stormwater Construction General Permit			46	151	09-Dec-19	10-Feb-20
F	TX-3CD	Developer Prepare TPDES Permit Application	20	150	09-Dec-19	03-Jan-20
F	TX-3CD	Submit to TXDOT TPDES Permit Application	0	211	04-Jan-20	04-Jan-20
F	TX-3CD	TXDOT Review TPDES Application	10	211	04-Jan-20	13-Jan-20
F	TX-3CD	Obtain TPDES Permit	20	151	14-Jan-20	10-Feb-20
TPWD (Texas Parks and Wildlife Dept.) Unregulated Habitat Field Survey			32	142	26-Nov-19	08-Jan-20
A	TX-3CD	C3 TPWD UHF Survey	20	143	26-Nov-19	23-Dec-19
A	TX-3CD	Submit to TXDOT TPWD UHF Survey	1	143	24-Dec-19	24-Dec-19
A	TX-3CD	TXDOT District Review C3 TPWD UHF Survey	10	200	25-Dec-19	03-Jan-20
A	TX-3CD	C3 TPWD UHF Survey - Clear Comments	2	142	06-Jan-20	07-Jan-20
A	TX-3CD	Forward C3 TPWD UHF Survey to TPWD	1	142	08-Jan-20	08-Jan-20
TPWD (Texas Parks and Wildlife Dept.) Habitat Mitigation Plan			30	144	09-Jan-20	19-Feb-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
A	TX-3CD	C3 Develop Habit Mitigation Plan	20	142	09-Jan-20	05-Feb-20
A	TX-3CD	Submit to TXDOT Habit Mitigation Plan	1	142	06-Feb-20	06-Feb-20
A	TX-3CD	TXDOT Review C3 Habit Mitigation Plan	10	200	07-Feb-20	16-Feb-20
A	TX-3CD	C3 Habit Mitigation Plan - Clear Comments	2	144	17-Feb-20	18-Feb-20
A	TX-3CD	Forward C3 Habit Mitigation Plan TPWD	1	144	19-Feb-20	19-Feb-20
Freshwater Mussel Threatened & Endangered Habitat Survey			32	174	26-Nov-19	08-Jan-20
A	TX-3CD	C3 FMTEH Survey	20	174	26-Nov-19	23-Dec-19
A	TX-3CD	Submit to TXDOT C3 FMTEH Survey	1	174	24-Dec-19	24-Dec-19
A	TX-3CD	TXDOT Review C3 FMTEH Survey	10	244	25-Dec-19	03-Jan-20
A	TX-3CD	C3 FMTEH Survey - Clear Comments	2	174	06-Jan-20	07-Jan-20
A	TX-3CD	Forward C3 FMTEH Survey to TPWD	1	174	08-Jan-20	08-Jan-20
SWPPP Notice of Intent			20	128	14-Feb-20	12-Mar-20
F	TX-3CD	NOI Letter SWPP Control Plans	20	128	14-Feb-20	12-Mar-20
Local Government			60	297	29-Apr-19	19-Jul-19
PEF	TX-3CD	Develop and Submit Local Government Permiting	60	297	29-Apr-19	19-Jul-19
Project Managment Submittals			47	347	07-Mar-19	10-May-19
Post NTP 1 Submittals			47	347	07-Mar-19	10-May-19
Project Administration Plan			27	367	07-Mar-19	12-Apr-19
A	TX-3CD	Project Administration Plan Annual Update (revised as required)	5	367	07-Mar-19	13-Mar-19
A	TX-3CD	Submit Project Administration Plan Annual Update (revised as required)	1	367	14-Mar-19	14-Mar-19
A	TX-3CD	TXDOT/IE Review, Project Administration Plan Annual Update (revised as required)	10	367	15-Mar-19	28-Mar-19
A	TX-3CD	Resolve Comments & Obtain Approval, Project Adminstration Plan Annual Update (revised as required)	10	367	29-Mar-19	11-Apr-19
A	TX-3CD	Project Administration Plan Annual Update (revised as required) in Place	1	367	12-Apr-19	12-Apr-19
Insurance for Project			2	28	07-Mar-19	08-Mar-19
A	TX-3CD	Develop and Submit, Insurance Certifications	1	28	07-Mar-19	07-Mar-19
A	TX-3CD	Insurance Certifications in Place	1	28	08-Mar-19	08-Mar-19
Performance Bond			23	371	07-Mar-19	08-Apr-19
A	TX-3CD	P&P Bonds	5	371	07-Mar-19	13-Mar-19
A	TX-3CD	Submit P&P Bonds	1	371	14-Mar-19	14-Mar-19
A	TX-3CD	TxDOT/IE Review & Comments Performance P&P Bonds	10	371	15-Mar-19	28-Mar-19
A	TX-3CD	Incorporate & Resolve TxDOT/IE Comments Performance P&P Bonds	5	371	29-Mar-19	04-Apr-19
A	TX-3CD	P&P Bonds Plan in Place	1	371	08-Apr-19	08-Apr-19
Schedule of Values			42	352	07-Mar-19	03-May-19
A	TX-3CD	Develop and Submit, Schedule of Values	20	352	07-Mar-19	03-Apr-19
A	TX-3CD	Submit Schedule of Values	1	352	04-Apr-19	04-Apr-19
A	TX-3CD	TxDOT/IE Review, Schedule of Values	10	352	05-Apr-19	18-Apr-19
A	TX-3CD	Resolve Comments & Obtain Approval, Schedule of Values	10	352	19-Apr-19	02-May-19
A	TX-3CD	Schedule of Values in Place	1	352	03-May-19	03-May-19
Project Baseline Schedule			47	347	07-Mar-19	10-May-19
A	TX-3CD	Develop and Submit, PBS Schedule	20	347	07-Mar-19	03-Apr-19
A	TX-3CD	Submit PBS Schedule	1	347	04-Apr-19	04-Apr-19
A	TX-3CD	TxDOT/IE Review, PBS Schedule	15	347	05-Apr-19	25-Apr-19
A	TX-3CD	Resolve Comments & Obtain Approval, PBS Schedule	10	347	26-Apr-19	09-May-19
A	TX-3CD	Project Baseline Schedule in Place	1	347	10-May-19	10-May-19
3C Right-of-Way Acquisition Sta 1028+00 to 1401+00			469	351	04-Apr-19	19-Jan-21
Acquisition By Developer			469	351	04-Apr-19	19-Jan-21
3C1 - Eagle Pwky to SH 170 Sta-1028 to 1176			423	373	04-Apr-19	16-Nov-20
2884J	TX-3CD	3C1 Parcels Cleared for Construction	1	373	16-Nov-20	16-Nov-20
Northbound Parcels			422	373	04-Apr-19	13-Nov-20
PARCEL 074U			363	432	04-Apr-19	24-Aug-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C1 Parcel 074U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 074U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 074U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 074U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 074U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 074U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 074U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 074U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 074U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 074U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 074U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 074U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 074U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 074U, Parcel Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 082U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 082U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 082U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 082U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 082U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 082U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 082U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 082U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 082U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 082U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 082U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 082U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 082U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 082U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 082U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 085U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 085U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 085U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 085U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 085U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 085U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 085U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 085U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 085U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 085U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 085U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 085U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 085U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 085U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 085U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 089U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 089U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 089U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 089U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 089U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 089U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 089U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19

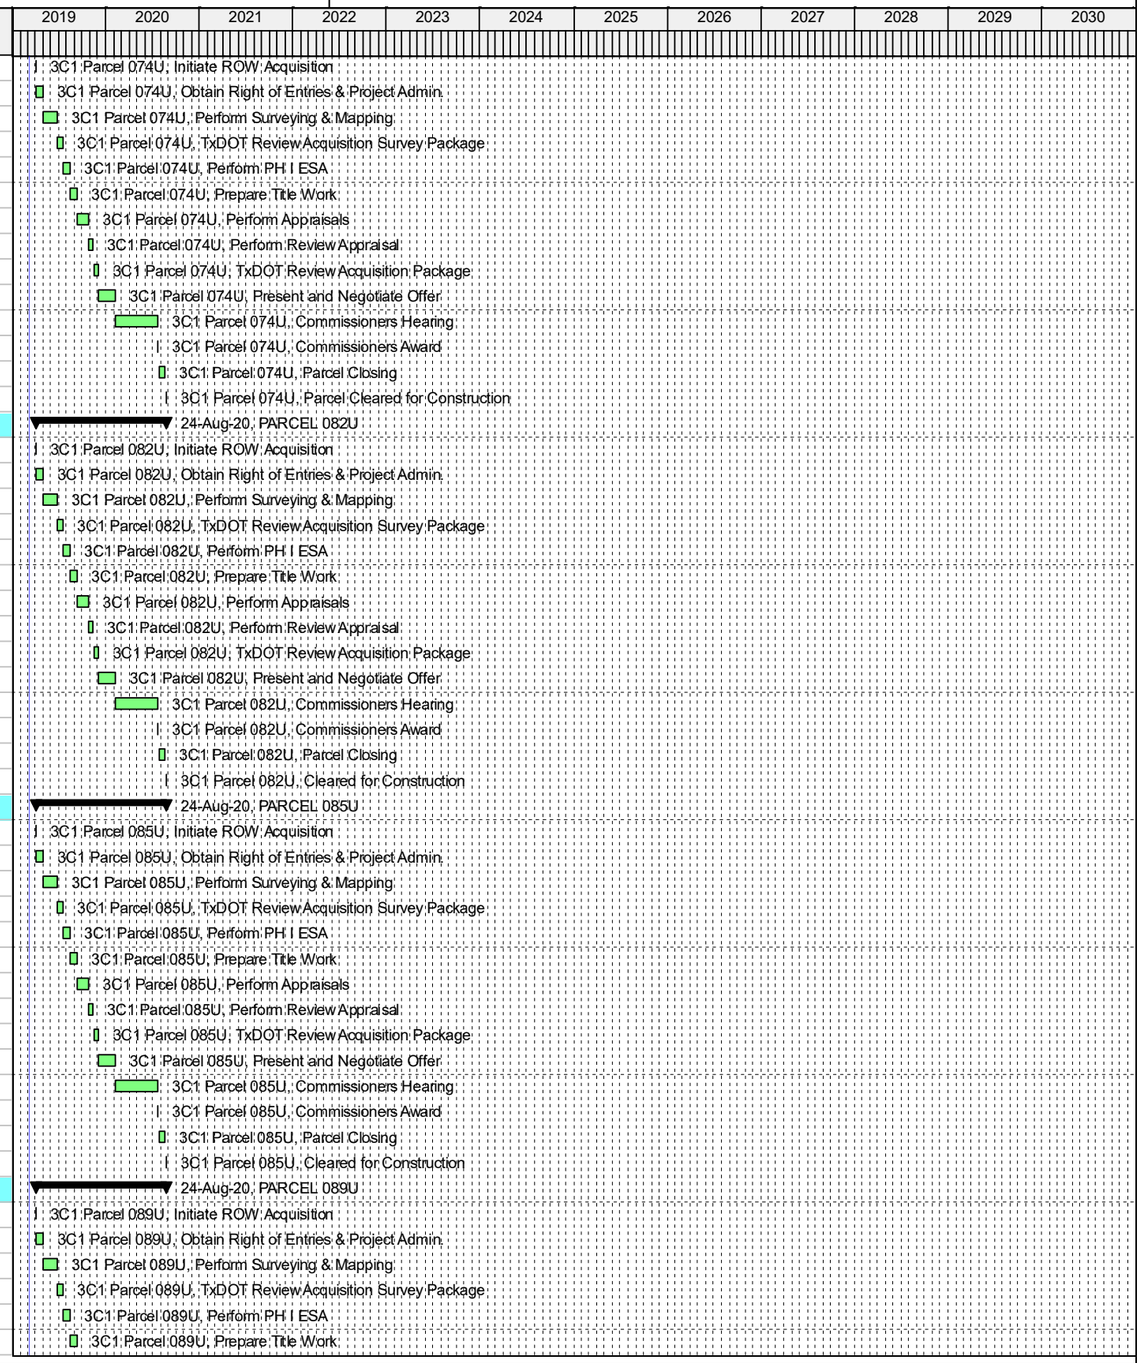

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C1 Parcel 089U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 089U, Perform Review Appraisal	15	19-Fet	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 089U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 089U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 089U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 089U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 089U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 089U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 118			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 118, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 118, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 118, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 118, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 118, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 118, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 118, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 118, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 118, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 118, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 118, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 118, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 118, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 118, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 117			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 117, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 117, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 117, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 117, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 117, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 117, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 117, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 117, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 117, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 117, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 117, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 117, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 117, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 117, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 115			422	373	04-Apr-19	13-Nov-20
F	TX-3CD	3C1 Parcel 115, Initiate ROW Acquisition	10	373	04-Apr-19	17-Apr-19
F	TX-3CD	3C1 Parcel 115, Obtain Right of Entries & Project Admin.	20	373	18-Apr-19	15-May-19
F	TX-3CD	3C1 Parcel 115, Perform Surveying & Mapping	40	373	16-May-19	10-Jul-19
F	TX-3CD	3C1 Parcel 115, TxDOT Review Acquisition Survey Package	15	373	11-Jul-19	31-Jul-19
F	TX-3CD	3C1 Parcel 115, Perform PH I ESA	20	373	01-Aug-19	28-Aug-19
F	TX-3CD	3C1 Parcel 115, Prepare Title Work	30	373	29-Aug-19	09-Oct-19
F	TX-3CD	3C1 Parcel 115, Perform Appraisals	30	373	10-Oct-19	20-Nov-19
F	TX-3CD	3C1 Parcel 115, Perform Review Appraisal	20	373	21-Nov-19	18-Dec-19
F	TX-3CD	3C1 Parcel 115, TxDOT Review Acquisition Package	15	373	19-Dec-19	08-Jan-20
F	TX-3CD	3C1 Parcel 115, Present and Negotiate Offer	60	373	09-Jan-20	01-Apr-20
F	TX-3CD	3C1 Parcel 115, Commissioners Hearing	140	373	02-Apr-20	14-Oct-20
F	TX-3CD	3C1 Parcel 115, Commissioners Award	1	373	15-Oct-20	15-Oct-20

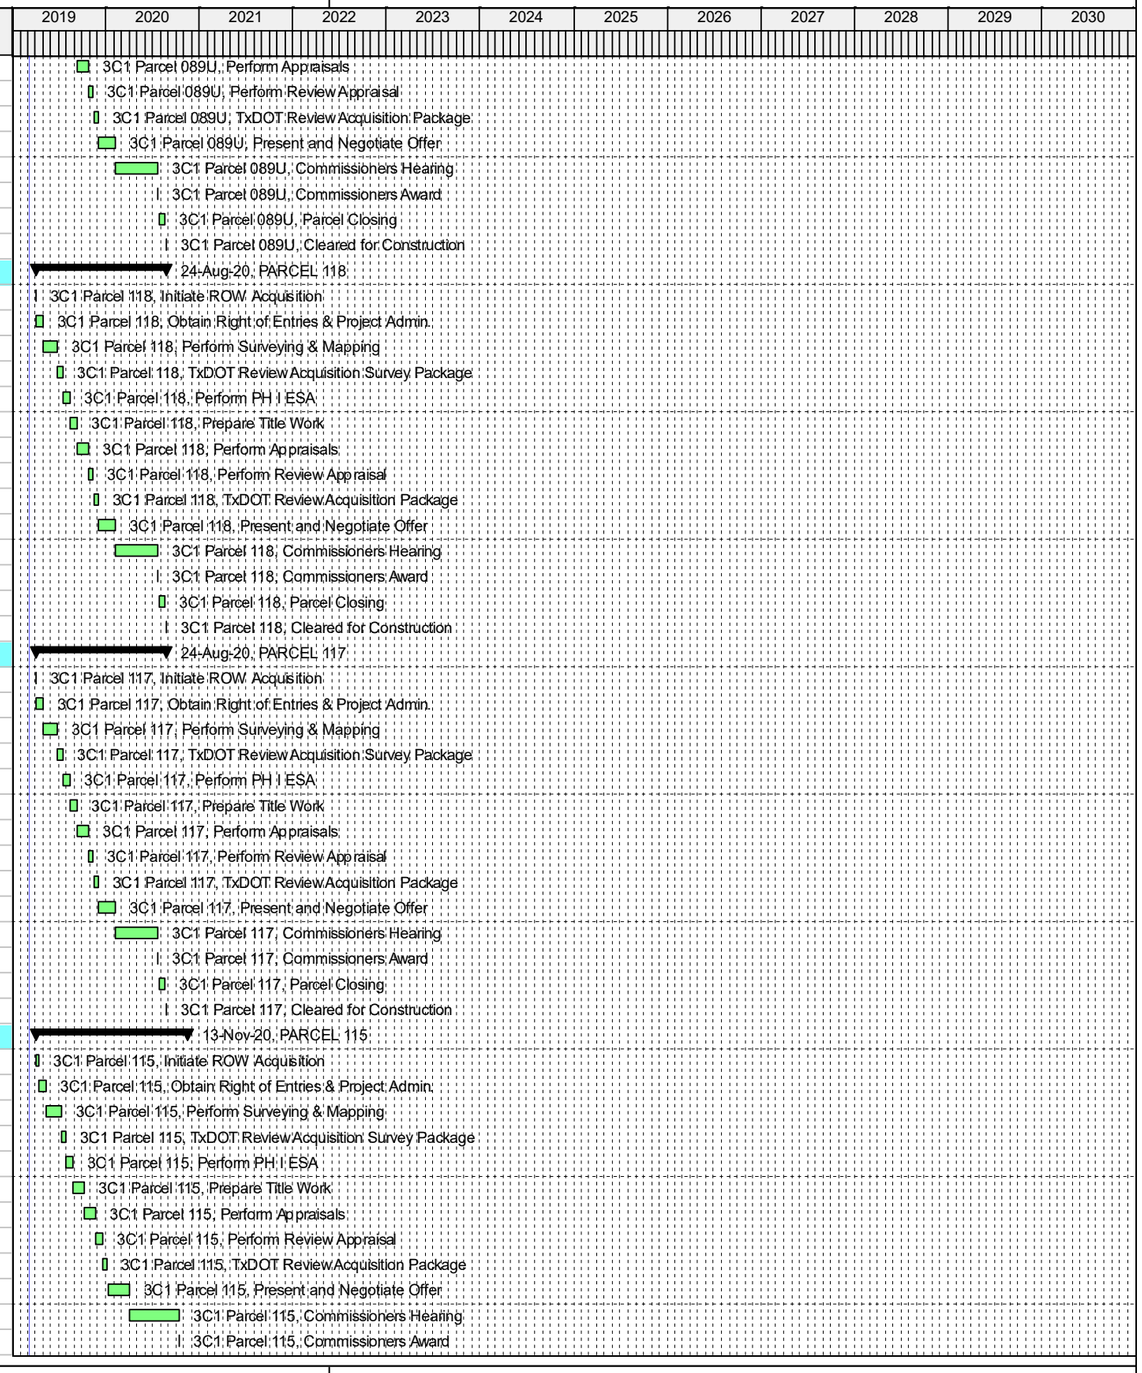

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C1 Parcel 115, Parcel Closing	20	373	16-Oct-20	12-Nov-20
F	TX-3CD	3C1 Parcel 115, Cleared for Construction	1	373	13-Nov-20	13-Nov-20
PARCEL 110			422	373	04-Apr-19	13-Nov-20
F	TX-3CD	3C1 Parcel 110, Initiate ROW Acquisition	10	373	04-Apr-19	17-Apr-19
F	TX-3CD	3C1 Parcel 110, Obtain Right of Entries & Project Admin.	20	373	18-Apr-19	15-May-19
F	TX-3CD	3C1 Parcel 110, Perform Surveying & Mapping	40	373	16-May-19	10-Jul-19
F	TX-3CD	3C1 Parcel 110, TxDOT Review Acquisition Survey Package	15	373	11-Jul-19	31-Jul-19
F	TX-3CD	3C1 Parcel 110, Perform PH I ESA	20	373	01-Aug-19	28-Aug-19
F	TX-3CD	3C1 Parcel 110, Prepare Title Work	30	373	29-Aug-19	09-Oct-19
F	TX-3CD	3C1 Parcel 110, Perform Appraisals	30	373	10-Oct-19	20-Nov-19
F	TX-3CD	3C1 Parcel 110, Perform Review Appraisal	20	373	21-Nov-19	18-Dec-19
F	TX-3CD	3C1 Parcel 110, TxDOT Review Acquisition Package	15	373	19-Dec-19	08-Jan-20
F	TX-3CD	3C1 Parcel 110, Present and Negotiate Offer	60	373	09-Jan-20	01-Apr-20
F	TX-3CD	3C1 Parcel 110, Commissioners Hearing	140	373	02-Apr-20	14-Oct-20
F	TX-3CD	3C1 Parcel 110, Commissioners Award	1	373	15-Oct-20	15-Oct-20
F	TX-3CD	3C1 Parcel 110, Parcel Closing	20	373	16-Oct-20	12-Nov-20
F	TX-3CD	3C1 Parcel 110, Cleared for Construction	1	373	13-Nov-20	13-Nov-20
PARCEL 088U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 088U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 088U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 088U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 088U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 088U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 088U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 088U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 088U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 088U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 088U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 088U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 088U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 088U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 088U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
Southbound Parcels			422	373	04-Apr-19	13-Nov-20
PARCEL 077			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 077, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 077, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 077, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 077, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 077, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 077, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 077, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 077, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 077, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 077, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 077, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 077, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 077, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 077, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 084U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 084U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 084U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19

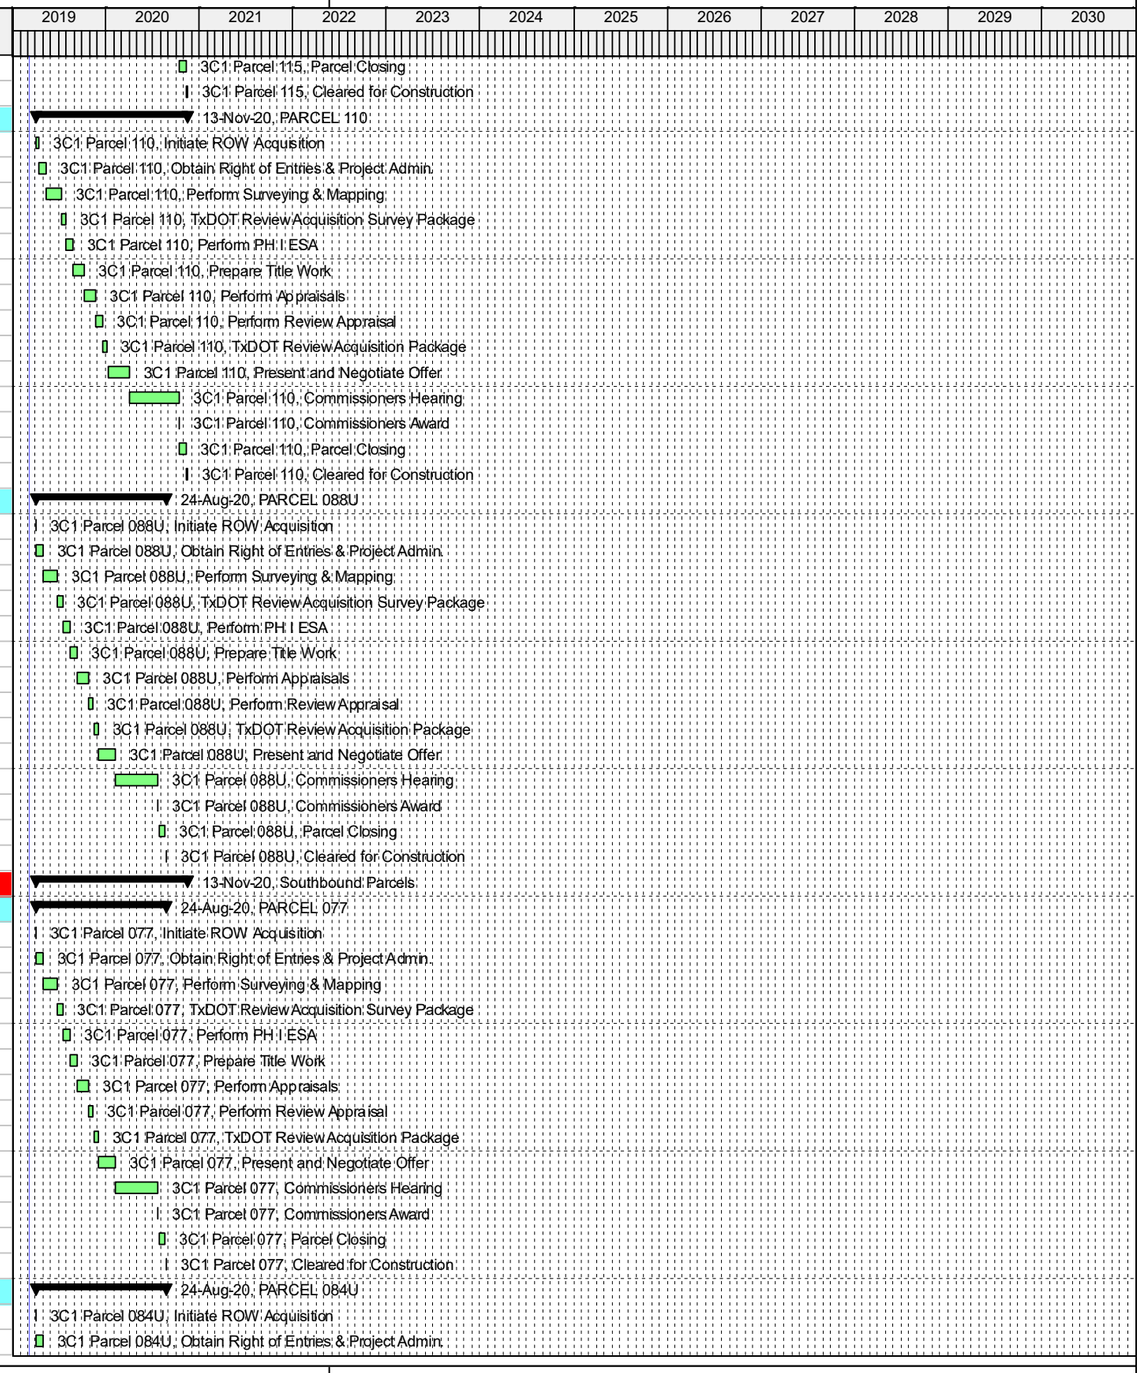

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C1 Parcel 084U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 084U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 084U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 084U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 084U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 084U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 084U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 084U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 084U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 084U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 084U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 084U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 086U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 086U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 086U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 086U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 086U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 086U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 086U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 086U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 086U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 086U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 086U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 086U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 086U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 086U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 086U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 087U			422	373	04-Apr-19	13-Nov-20
F	TX-3CD	3C1 Parcel 087U, Initiate ROW Acquisition	10	373	04-Apr-19	17-Apr-19
F	TX-3CD	3C1 Parcel 087U, Obtain Right of Entries & Project Admin.	20	373	18-Apr-19	15-May-19
F	TX-3CD	3C1 Parcel 087U, Perform Surveying & Mapping	40	373	16-May-19	10-Jul-19
F	TX-3CD	3C1 Parcel 087U, TxDOT Review Acquisition Survey Package	15	373	11-Jul-19	31-Jul-19
F	TX-3CD	3C1 Parcel 087U, Perform PH I ESA	20	373	01-Aug-19	28-Aug-19
F	TX-3CD	3C1 Parcel 087U, Prepare Title Work	30	373	29-Aug-19	09-Oct-19
F	TX-3CD	3C1 Parcel 087U, Perform Appraisals	30	373	10-Oct-19	20-Nov-19
F	TX-3CD	3C1 Parcel 087U, Perform Review Appraisal	20	373	21-Nov-19	18-Dec-19
F	TX-3CD	3C1 Parcel 087U, TxDOT Review Acquisition Package	15	373	19-Dec-19	08-Jan-20
F	TX-3CD	3C1 Parcel 087U, Present and Negotiate Offer	60	373	09-Jan-20	01-Apr-20
F	TX-3CD	3C1 Parcel 087U, Commissioners Hearing	140	373	02-Apr-20	14-Oct-20
F	TX-3CD	3C1 Parcel 087U, Commissioners Award	1	373	15-Oct-20	15-Oct-20
F	TX-3CD	3C1 Parcel 087U, Parcel Closing	20	373	16-Oct-20	12-Nov-20
F	TX-3CD	3C1 Parcel 087U, Cleared for Construction	1	373	13-Nov-20	13-Nov-20
PARCEL 090U			422	373	04-Apr-19	13-Nov-20
F	TX-3CD	3C1 Parcel 090U, Initiate ROW Acquisition	10	373	04-Apr-19	17-Apr-19
F	TX-3CD	3C1 Parcel 090U, Obtain Right of Entries & Project Admin.	20	373	18-Apr-19	15-May-19
F	TX-3CD	3C1 Parcel 090U, Perform Surveying & Mapping	40	373	16-May-19	10-Jul-19
F	TX-3CD	3C1 Parcel 090U, TxDOT Review Acquisition Survey Package	15	373	11-Jul-19	31-Jul-19
F	TX-3CD	3C1 Parcel 090U, Perform PH I ESA	20	373	01-Aug-19	28-Aug-19
F	TX-3CD	3C1 Parcel 090U, Prepare Title Work	30	373	29-Aug-19	09-Oct-19
F	TX-3CD	3C1 Parcel 090U, Perform Appraisals	30	373	10-Oct-19	20-Nov-19
F	TX-3CD	3C1 Parcel 090U, Perform Review Appraisal	20	373	21-Nov-19	18-Dec-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C1 Parcel 090U, TxDOT Review Acquisition Package	15	373	19-Dec-19	08-Jan-20
F	TX-3CD	3C1 Parcel 090U, Present and Negotiate Offer	60	373	09-Jan-20	01-Apr-20
F	TX-3CD	3C1 Parcel 090U, Commissioners Hearing	140	373	02-Apr-20	14-Oct-20
F	TX-3CD	3C1 Parcel 090U, Commissioners Award	1	373	15-Oct-20	15-Oct-20
F	TX-3CD	3C1 Parcel 090U, Parcel Closing	20	373	16-Oct-20	12-Nov-20
F	TX-3CD	3C1 Parcel 090U, Cleared for Construction	1	373	13-Nov-20	13-Nov-20
PARCEL 091U			422	373	04-Apr-19	13-Nov-20
F	TX-3CD	3C1 Parcel 091U, Initiate ROW Acquisition	10	373	04-Apr-19	17-Apr-19
F	TX-3CD	3C1 Parcel 091U, Obtain Right of Entries & Project Admin.	20	373	18-Apr-19	15-May-19
F	TX-3CD	3C1 Parcel 091U, Perform Surveying & Mapping	40	373	16-May-19	10-Jul-19
F	TX-3CD	3C1 Parcel 091U, TxDOT Review Acquisition Survey Package	15	373	11-Jul-19	31-Jul-19
F	TX-3CD	3C1 Parcel 091U, Perform PH I ESA	20	373	01-Aug-19	28-Aug-19
F	TX-3CD	3C1 Parcel 091U, Prepare Title Work	30	373	29-Aug-19	09-Oct-19
F	TX-3CD	3C1 Parcel 091U, Perform Appraisals	30	373	10-Oct-19	20-Nov-19
F	TX-3CD	3C1 Parcel 091U, Perform Review Appraisal	20	373	21-Nov-19	18-Dec-19
F	TX-3CD	3C1 Parcel 091U, TxDOT Review Acquisition Package	15	373	19-Dec-19	08-Jan-20
F	TX-3CD	3C1 Parcel 091U, Present and Negotiate Offer	60	373	09-Jan-20	01-Apr-20
F	TX-3CD	3C1 Parcel 091U, Commissioners Hearing	140	373	02-Apr-20	14-Oct-20
F	TX-3CD	3C1 Parcel 091U, Commissioners Award	1	373	15-Oct-20	15-Oct-20
F	TX-3CD	3C1 Parcel 091U, Parcel Closing	20	373	16-Oct-20	12-Nov-20
F	TX-3CD	3C1 Parcel 091U, Cleared for Construction	1	373	13-Nov-20	13-Nov-20
PARCEL 096U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 096U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 096U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 096U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 096U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 096U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 096U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 096U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 096U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 096U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 096U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 096U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 096U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 096U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 096U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 097U			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 097U, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 097U, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 097U, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 097U, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 097U, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 097U, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 097U, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 097U, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 097U, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 097U, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 097U, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 097U, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 097U, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 097U, Cleared for Construction	1	432	24-Aug-20	24-Aug-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
PARCEL 097AU			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 097AU, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 097AU, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 097AU, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 097AU, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 097AU, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 097AU, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 097AU, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 097AU, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 097AU, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 097AU, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 097AU, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 097AU, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 097AU, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 097AU, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
PARCEL 097BU			363	432	04-Apr-19	24-Aug-20
F	TX-3CD	3C1 Parcel 097BU, Initiate ROW Acquisition	1	432	04-Apr-19	04-Apr-19
F	TX-3CD	3C1 Parcel 097BU, Obtain Right of Entries & Project Admin.	20	432	05-Apr-19	02-May-19
F	TX-3CD	3C1 Parcel 097BU, Perform Surveying & Mapping	40	432	03-May-19	27-Jun-19
F	TX-3CD	3C1 Parcel 097BU, TxDOT Review Acquisition Survey Package	15	432	28-Jun-19	18-Jul-19
F	TX-3CD	3C1 Parcel 097BU, Perform PH I ESA	20	432	19-Jul-19	15-Aug-19
F	TX-3CD	3C1 Parcel 097BU, Prepare Title Work	20	432	16-Aug-19	12-Sep-19
F	TX-3CD	3C1 Parcel 097BU, Perform Appraisals	30	432	13-Sep-19	24-Oct-19
F	TX-3CD	3C1 Parcel 097BU, Perform Review Appraisal	15	432	25-Oct-19	14-Nov-19
F	TX-3CD	3C1 Parcel 097BU, TxDOT Review Acquisition Package	15	432	15-Nov-19	05-Dec-19
F	TX-3CD	3C1 Parcel 097BU, Present and Negotiate Offer	45	432	06-Dec-19	06-Feb-20
F	TX-3CD	3C1 Parcel 097BU, Commissioners Hearing	120	432	07-Feb-20	23-Jul-20
F	TX-3CD	3C1 Parcel 097BU, Commissioners Award	1	432	24-Jul-20	24-Jul-20
F	TX-3CD	3C1 Parcel 097BU, Parcel Closing	20	432	27-Jul-20	21-Aug-20
F	TX-3CD	3C1 Parcel 097BU, Cleared for Construction	1	432	24-Aug-20	24-Aug-20
3C2 - SH 170 to Golden Triangle Blvd Sta-1176 to 1280			444	375	04-Apr-19	15-Dec-20
R3C2(	TX-3CD	3C2 Parcels Cleared for Construction	1	366	15-Dec-20	15-Dec-20
Northbound Parcels			422	387	04-Apr-19	13-Nov-20
PARCEL 057AU			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 057AU, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 057AU, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 057AU, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 057AU, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 057AU, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 057AU, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 057AU, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 057AU, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 057AU, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 057AU, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 057AU, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 057AU, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 057AU, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 057AU, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 057BU			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 057BU, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 057BU, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C2 Parcel 057BU, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 057BU, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 057BU, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 057BU, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 057BU, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 057BU, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 057BU, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 057BU, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 057BU, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 057BU, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 057BU, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 057BU, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 059U			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 059U, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 059U, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 059U, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 059U, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 059U, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 059U, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 059U, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 059U, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 059U, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 059U, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 059U, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 059U, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 059U, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 059U, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 062			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 062, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 062, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 062, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 062, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 062, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 062, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 062, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 062, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 062, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 062, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 062, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 062, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 062, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 062, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 063			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 063, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 063, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 063, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 063, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 063, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 063, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 063, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 063, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19

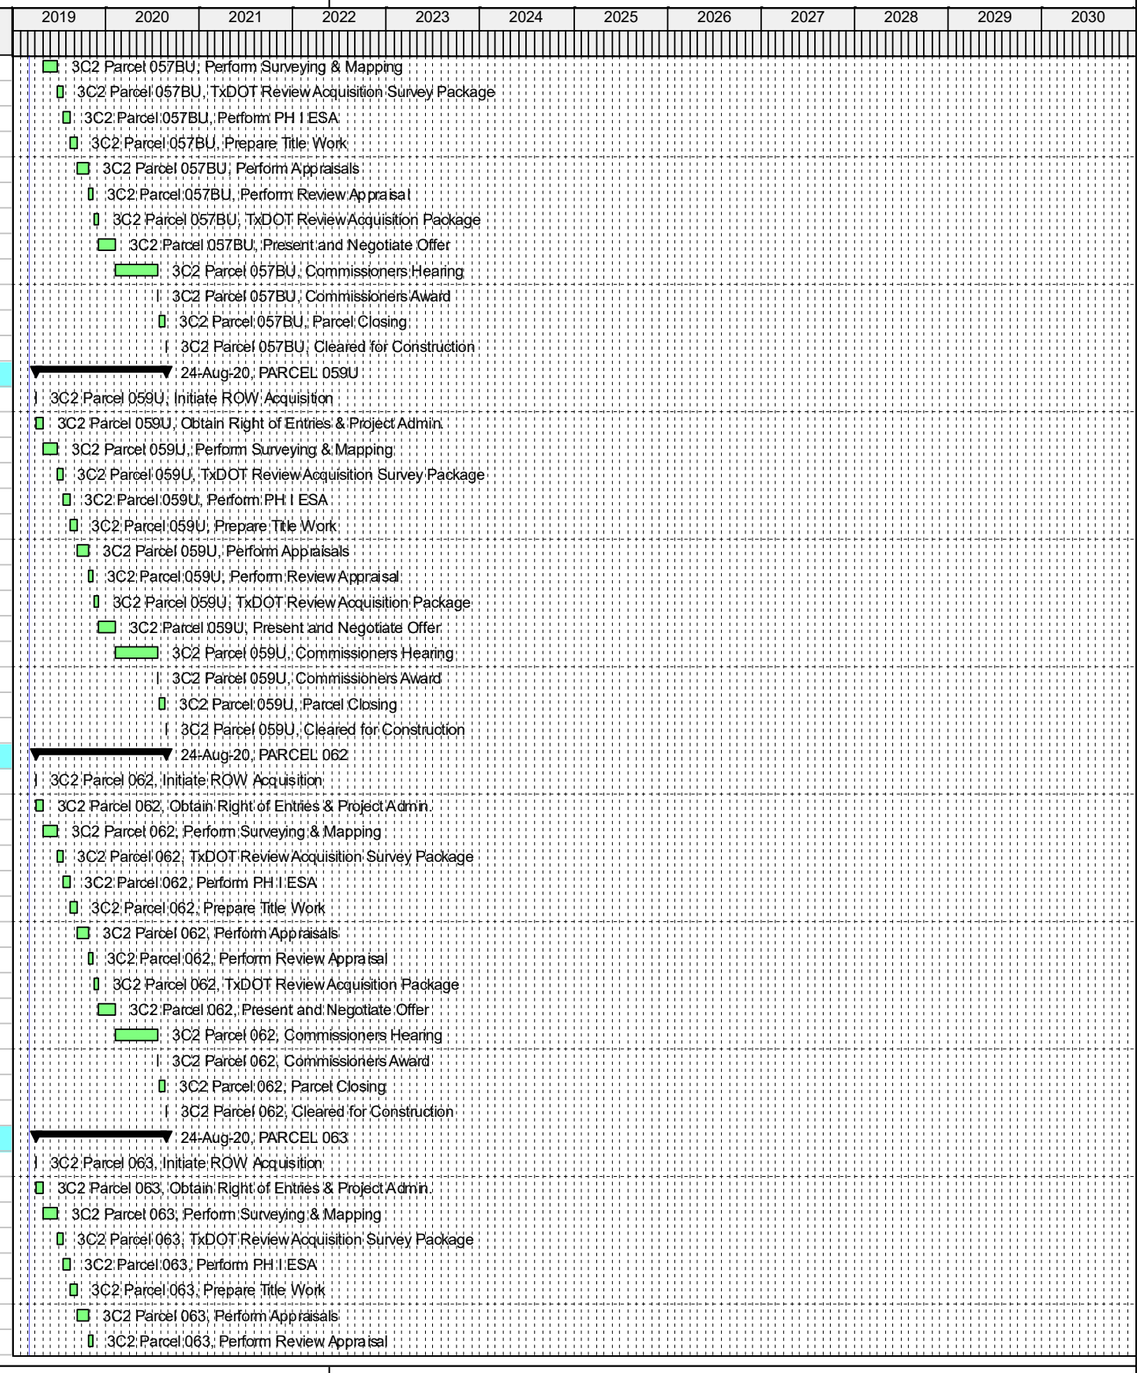

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C2 Parcel 063, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 063, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 063, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 063, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 063, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 063, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 063U			422	387	04-Apr-19	13-Nov-20
F	TX-3CD	3C2 Parcel 063U, Initiate ROW Acquisition	10	387	04-Apr-19	17-Apr-19
F	TX-3CD	3C2 Parcel 063U, Obtain Right of Entries & Project Admin.	20	387	18-Apr-19	15-May-19
F	TX-3CD	3C2 Parcel 063U, Perform Surveying & Mapping	40	387	16-May-19	10-Jul-19
F	TX-3CD	3C2 Parcel 063U, TxDOT Review Acquisition Survey Package	15	387	11-Jul-19	31-Jul-19
F	TX-3CD	3C2 Parcel 063U, Perform PH I ESA	20	387	01-Aug-19	28-Aug-19
F	TX-3CD	3C2 Parcel 063U, Prepare Title Work	30	387	29-Aug-19	09-Oct-19
F	TX-3CD	3C2 Parcel 063U, Perform Appraisals	30	387	10-Oct-19	20-Nov-19
F	TX-3CD	3C2 Parcel 063U, Perform Review Appraisal	20	387	21-Nov-19	18-Dec-19
F	TX-3CD	3C2 Parcel 063U, TxDOT Review Acquisition Package	15	387	19-Dec-19	08-Jan-20
F	TX-3CD	3C2 Parcel 063U, Present and Negotiate Offer	60	387	09-Jan-20	01-Apr-20
F	TX-3CD	3C2 Parcel 063U, Commissioners Hearing	140	387	02-Apr-20	14-Oct-20
F	TX-3CD	3C2 Parcel 063U, Commissioners Award	1	387	15-Oct-20	15-Oct-20
F	TX-3CD	3C2 Parcel 063U, Parcel Closing	20	387	16-Oct-20	12-Nov-20
F	TX-3CD	3C2 Parcel 063U, Cleared for Construction	1	387	13-Nov-20	13-Nov-20
PARCEL 069U			422	387	04-Apr-19	13-Nov-20
F	TX-3CD	3C2 Parcel 069U, Initiate ROW Acquisition	10	387	04-Apr-19	17-Apr-19
F	TX-3CD	3C2 Parcel 069U, Obtain Right of Entries & Project Admin.	20	387	18-Apr-19	15-May-19
F	TX-3CD	3C2 Parcel 069U, Perform Surveying & Mapping	40	387	16-May-19	10-Jul-19
F	TX-3CD	3C2 Parcel 069U, TxDOT Review Acquisition Survey Package	15	387	11-Jul-19	31-Jul-19
F	TX-3CD	3C2 Parcel 069U, Perform PH I ESA	20	387	01-Aug-19	28-Aug-19
F	TX-3CD	3C2 Parcel 069U, Prepare Title Work	30	387	29-Aug-19	09-Oct-19
F	TX-3CD	3C2 Parcel 069U, Perform Appraisals	30	387	10-Oct-19	20-Nov-19
F	TX-3CD	3C2 Parcel 069U, Perform Review Appraisal	20	387	21-Nov-19	18-Dec-19
F	TX-3CD	3C2 Parcel 069U, TxDOT Review Acquisition Package	15	387	19-Dec-19	08-Jan-20
F	TX-3CD	3C2 Parcel 069U, Present and Negotiate Offer	60	387	09-Jan-20	01-Apr-20
F	TX-3CD	3C2 Parcel 069U, Commissioners Hearing	140	387	02-Apr-20	14-Oct-20
F	TX-3CD	3C2 Parcel 069U, Commissioners Award	1	387	15-Oct-20	15-Oct-20
F	TX-3CD	3C2 Parcel 069U, Parcel Closing	20	387	16-Oct-20	12-Nov-20
F	TX-3CD	3C2 Parcel 069U, Cleared for Construction	1	387	13-Nov-20	13-Nov-20
Southbound Parcels			443	376	04-Apr-19	14-Dec-20
PARCEL 058U			422	387	04-Apr-19	13-Nov-20
F	TX-3CD	3C2 Parcel 058U, Initiate ROW Acquisition	10	387	04-Apr-19	17-Apr-19
F	TX-3CD	3C2 Parcel 058U, Obtain Right of Entries & Project Admin.	20	387	18-Apr-19	15-May-19
F	TX-3CD	3C2 Parcel 058U, Perform Surveying & Mapping	40	387	16-May-19	10-Jul-19
F	TX-3CD	3C2 Parcel 058U, TxDOT Review Acquisition Survey Package	15	387	11-Jul-19	31-Jul-19
F	TX-3CD	3C2 Parcel 058U, Perform PH I ESA	20	387	01-Aug-19	28-Aug-19
F	TX-3CD	3C2 Parcel 058U, Prepare Title Work	30	387	29-Aug-19	09-Oct-19
F	TX-3CD	3C2 Parcel 058U, Perform Appraisals	30	387	10-Oct-19	20-Nov-19
F	TX-3CD	3C2 Parcel 058U, Perform Review Appraisal	20	387	21-Nov-19	18-Dec-19
F	TX-3CD	3C2 Parcel 058U, TxDOT Review Acquisition Package	15	387	19-Dec-19	08-Jan-20
F	TX-3CD	3C2 Parcel 058U, Present and Negotiate Offer	60	387	09-Jan-20	01-Apr-20
F	TX-3CD	3C2 Parcel 058U, Commissioners Hearing	140	387	02-Apr-20	14-Oct-20
F	TX-3CD	3C2 Parcel 058U, Commissioners Award	1	387	15-Oct-20	15-Oct-20
F	TX-3CD	3C2 Parcel 058U, Parcel Closing	20	387	16-Oct-20	12-Nov-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C2 Parcel 058U, Cleared for Construction	1	387	13-Nov-20	13-Nov-20
PARCEL 060U			422	387	04-Apr-19	13-Nov-20
F	TX-3CD	3C2 Parcel 058U, Initiate ROW Acquisition	10	387	04-Apr-19	17-Apr-19
F	TX-3CD	3C2 Parcel 058U, Obtain Right of Entries & Project Admin.	20	387	18-Apr-19	15-May-19
F	TX-3CD	3C2 Parcel 058U, Perform Surveying & Mapping	40	387	16-May-19	10-Jul-19
F	TX-3CD	3C2 Parcel 058U, TxDOT Review Acquisition Survey Package	15	387	11-Jul-19	31-Jul-19
F	TX-3CD	3C2 Parcel 058U, Perform PH I ESA	20	387	01-Aug-19	28-Aug-19
F	TX-3CD	3C2 Parcel 058U, Prepare Title Work	30	387	29-Aug-19	09-Oct-19
F	TX-3CD	3C2 Parcel 058U, Perform Appraisals	30	387	10-Oct-19	20-Nov-19
F	TX-3CD	3C2 Parcel 058U, Perform Review Appraisal	20	387	21-Nov-19	18-Dec-19
F	TX-3CD	3C2 Parcel 058U, TxDOT Review Acquisition Package	15	387	19-Dec-19	08-Jan-20
F	TX-3CD	3C2 Parcel 058U, Present and Negotiate Offer	60	387	09-Jan-20	01-Apr-20
F	TX-3CD	3C2 Parcel 058U, Commissioners Hearing	140	387	02-Apr-20	14-Oct-20
F	TX-3CD	3C2 Parcel 058U, Commissioners Award	1	387	15-Oct-20	15-Oct-20
F	TX-3CD	3C2 Parcel 058U, Parcel Closing	20	387	16-Oct-20	12-Nov-20
F	TX-3CD	3C2 Parcel 058U, Cleared for Construction	1	387	13-Nov-20	13-Nov-20
PARCEL 061			443	366	04-Apr-19	14-Dec-20
F	TX-3CD	3C2 Parcel 061, Initiate ROW Acquisition	1	366	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 061, Obtain Right of Entries & Project Admin.	20	366	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 061, Perform Surveying & Mapping	40	366	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 061, TxDOT Review Acquisition Survey Package	15	366	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 061, Perform PH I ESA	20	366	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 061, Prepare Title Work	20	366	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 061, Perform Appraisals	30	366	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 061, Perform Review Appraisal	15	366	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 061, TxDOT Review Acquisition Package	15	366	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 061, Present and Negotiate Offer	45	366	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 061, Commissioners Hearing	120	366	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 061, Commissioners Award	1	366	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 061, Parcel Closing	20	366	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 061, Prepare for Relocation	60	366	24-Aug-20	13-Nov-20
F	TX-3CD	3C2 Parcel 061, Execute Relocation	20	366	16-Nov-20	11-Dec-20
F	TX-3CD	3C2 Parcel 061, Cleared for Construction	1	366	14-Dec-20	14-Dec-20
PARCEL 061U			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 061U, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 061U, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
TPV	TX-3CD	3C2 Parcel 061U, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 061U, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 061U, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 061U, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 061U, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 061U, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 061U, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 061U, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 061U, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 061U, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 061U, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 061U, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 064			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 064, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 064, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C2 Parcel 064, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 064, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 064, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 064, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 064, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 064, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 064, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 064, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 064, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 064, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 064, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 064, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 058			443	376	04-Apr-19	14-Dec-20
F	TX-3CD	3C2 Parcel 058, Initiate ROW Acquisition	1	376	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 058, Obtain Right of Entries & Project Admin.	20	376	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 058, Perform Surveying & Mapping	40	376	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 058, TxDOT Review Acquisition Survey Package	15	376	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 058, Perform PH I ESA	20	376	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 058, Prepare Title Work	20	376	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 058, Perform Appraisals	30	376	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 058, Perform Review Appraisal	15	376	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 058, TxDOT Review Acquisition Package	15	376	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 058, Present and Negotiate Offer	45	376	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 058, Commissioners Hearing	120	376	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 058, Commissioners Award	1	376	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 058, Parcel Closing	20	376	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 058, Prepare for Relocation	60	376	24-Aug-20	13-Nov-20
F	TX-3CD	3C2 Parcel 058, Execute Relocation	20	376	16-Nov-20	11-Dec-20
F	TX-3CD	3C2 Parcel 058, Cleared for Construction	1	376	14-Dec-20	14-Dec-20
PARCEL 065			443	376	04-Apr-19	14-Dec-20
F	TX-3CD	3C2 Parcel 065, Initiate ROW Acquisition	1	376	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 065, Obtain Right of Entries & Project Admin.	20	376	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 065, Perform Surveying & Mapping	40	376	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 065, TxDOT Review Acquisition Survey Package	15	376	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 065, Perform PH I ESA	20	376	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 065, Prepare Title Work	20	376	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 065, Perform Appraisals	30	376	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 065, Perform Review Appraisal	15	376	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 065, TxDOT Review Acquisition Package	15	376	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 065, Present and Negotiate Offer	45	376	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 065, Commissioners Hearing	120	376	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 065, Commissioners Award	1	376	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 065, Parcel Closing	20	376	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 065, Prepare for Relocation	60	376	24-Aug-20	13-Nov-20
F	TX-3CD	3C2 Parcel 065, Execute Relocation	20	376	16-Nov-20	11-Dec-20
F	TX-3CD	3C2 Parcel 065, Cleared for Construction	1	376	14-Dec-20	14-Dec-20
PARCEL 066			422	387	04-Apr-19	13-Nov-20
F	TX-3CD	3C2 Parcel 066, Initiate ROW Acquisition	10	387	04-Apr-19	17-Apr-19
F	TX-3CD	3C2 Parcel 066, Obtain Right of Entries & Project Admin.	20	387	18-Apr-19	15-May-19
F	TX-3CD	3C2 Parcel 066, Perform Surveying & Mapping	40	387	16-May-19	10-Jul-19
F	TX-3CD	3C2 Parcel 066, TxDOT Review Acquisition Survey Package	15	387	11-Jul-19	31-Jul-19

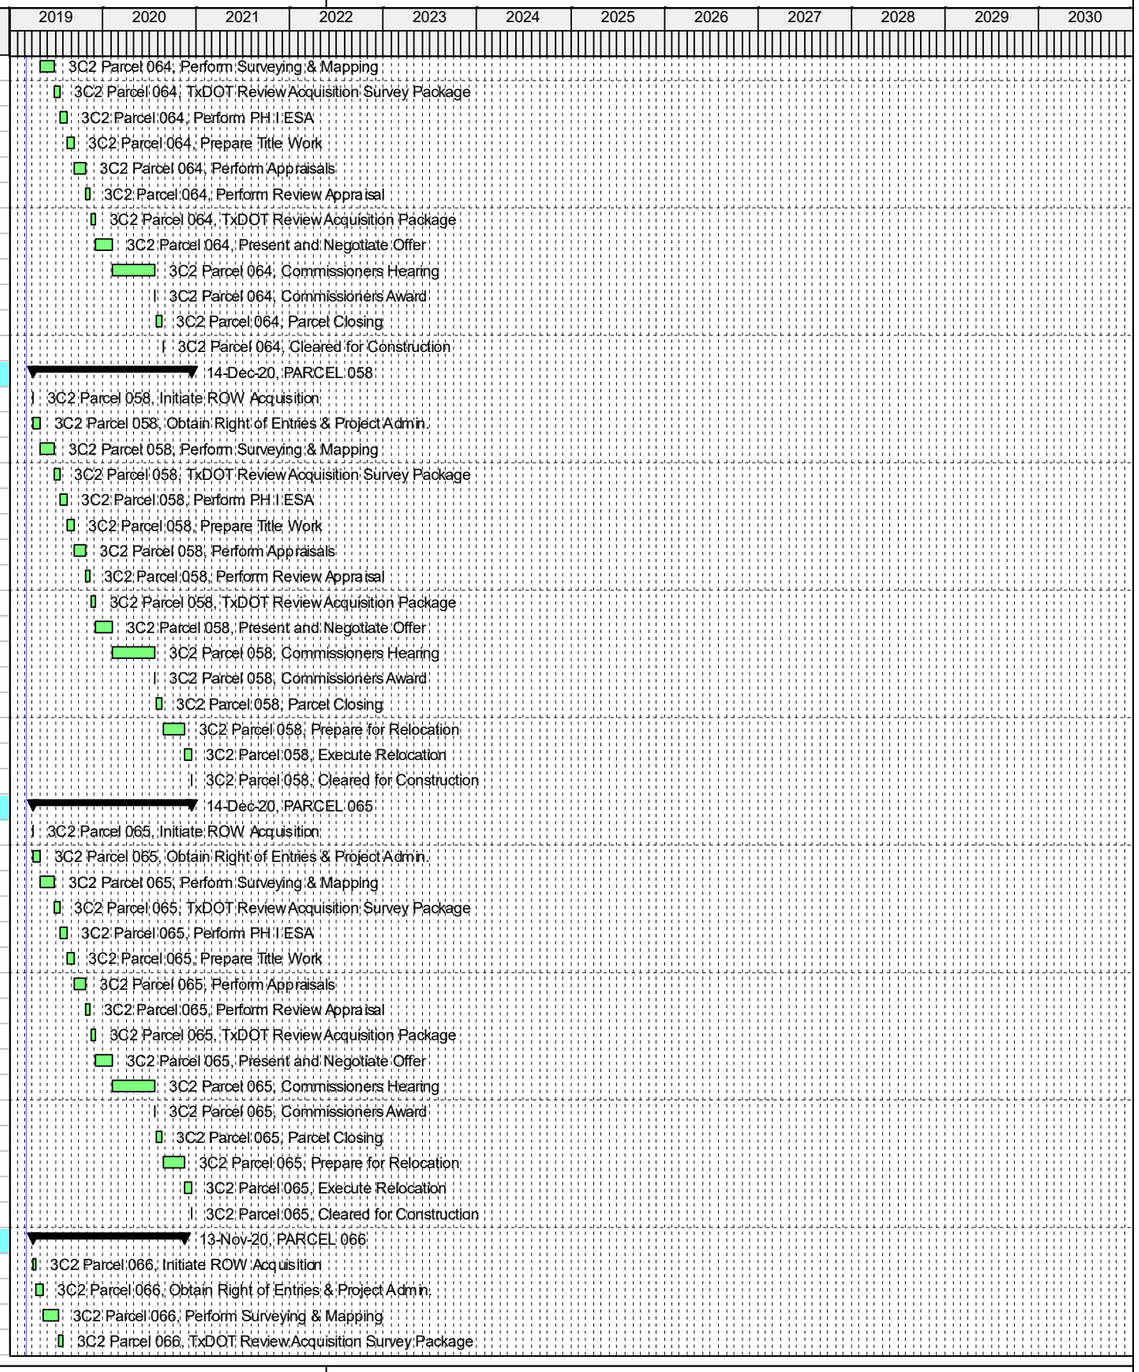

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
f	TX-3CD	3C2 Parcel 066, Perform PH I ESA	20	387	01-Aug-19	28-Aug-19
f	TX-3CD	3C2 Parcel 066, Prepare Title Work	30	387	29-Aug-19	09-Oct-19
f	TX-3CD	3C2 Parcel 066, Perform Appraisals	30	387	10-Oct-19	20-Nov-19
f	TX-3CD	3C2 Parcel 066, Perform Review Appraisal	20	387	21-Nov-19	18-Dec-19
f	TX-3CD	3C2 Parcel 066, TxDOT Review Acquisition Package	15	387	19-Dec-19	08-Jan-20
f	TX-3CD	3C2 Parcel 066, Present and Negotiate Offer	60	387	09-Jan-20	01-Apr-20
f	TX-3CD	3C2 Parcel 066, Commissioners Hearing	140	387	02-Apr-20	14-Oct-20
f	TX-3CD	3C2 Parcel 066, Commissioners Award	1	387	15-Oct-20	15-Oct-20
f	TX-3CD	3C2 Parcel 066, Parcel Closing	20	387	16-Oct-20	12-Nov-20
f	TX-3CD	3C2 Parcel 066, Cleared for Construction	1	387	13-Nov-20	13-Nov-20
PARCEL 067			363	446	04-Apr-19	24-Aug-20
f	TX-3CD	3C2 Parcel 067, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
f	TX-3CD	3C2 Parcel 067, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
f	TX-3CD	3C2 Parcel 067, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
f	TX-3CD	3C2 Parcel 067, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
f	TX-3CD	3C2 Parcel 067, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
f	TX-3CD	3C2 Parcel 067, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
f	TX-3CD	3C2 Parcel 067, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
f	TX-3CD	3C2 Parcel 067, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
f	TX-3CD	3C2 Parcel 067, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
f	TX-3CD	3C2 Parcel 067, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
f	TX-3CD	3C2 Parcel 067, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
f	TX-3CD	3C2 Parcel 067, Commissioners Award	1	446	24-Jul-20	24-Jul-20
f	TX-3CD	3C2 Parcel 067, Parcel Closing	20	446	27-Jul-20	21-Aug-20
f	TX-3CD	3C2 Parcel 067, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 073			363	446	04-Apr-19	24-Aug-20
f	TX-3CD	3C2 Parcel 073, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
f	TX-3CD	3C2 Parcel 073, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
f	TX-3CD	3C2 Parcel 073, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
f	TX-3CD	3C2 Parcel 073, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
f	TX-3CD	3C2 Parcel 073, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
f	TX-3CD	3C2 Parcel 073, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
f	TX-3CD	3C2 Parcel 073, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
f	TX-3CD	3C2 Parcel 073, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
f	TX-3CD	3C2 Parcel 073, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
f	TX-3CD	3C2 Parcel 073, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
f	TX-3CD	3C2 Parcel 073, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
f	TX-3CD	3C2 Parcel 073, Commissioners Award	1	446	24-Jul-20	24-Jul-20
f	TX-3CD	3C2 Parcel 073, Parcel Closing	20	446	27-Jul-20	21-Aug-20
f	TX-3CD	3C2 Parcel 073, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 072			363	446	04-Apr-19	24-Aug-20
f	TX-3CD	3C2 Parcel 072, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
f	TX-3CD	3C2 Parcel 072, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
f	TX-3CD	3C2 Parcel 072, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
f	TX-3CD	3C2 Parcel 072, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
f	TX-3CD	3C2 Parcel 072, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
f	TX-3CD	3C2 Parcel 072, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
f	TX-3CD	3C2 Parcel 072, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
f	TX-3CD	3C2 Parcel 072, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
f	TX-3CD	3C2 Parcel 072, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
f	TX-3CD	3C2 Parcel 072, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C2 Parcel 072, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 072, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 072, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 072, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
PARCEL 070			363	446	04-Apr-19	24-Aug-20
F	TX-3CD	3C2 Parcel 070, Initiate ROW Acquisition	1	446	04-Apr-19	04-Apr-19
F	TX-3CD	3C2 Parcel 070, Obtain Right of Entries & Project Admin.	20	446	05-Apr-19	02-May-19
F	TX-3CD	3C2 Parcel 070, Perform Surveying & Mapping	40	446	03-May-19	27-Jun-19
F	TX-3CD	3C2 Parcel 070, TxDOT Review Acquisition Survey Package	15	446	28-Jun-19	18-Jul-19
F	TX-3CD	3C2 Parcel 070, Perform PH I ESA	20	446	19-Jul-19	15-Aug-19
F	TX-3CD	3C2 Parcel 070, Prepare Title Work	20	446	16-Aug-19	12-Sep-19
F	TX-3CD	3C2 Parcel 070, Perform Appraisals	30	446	13-Sep-19	24-Oct-19
F	TX-3CD	3C2 Parcel 070, Perform Review Appraisal	15	446	25-Oct-19	14-Nov-19
F	TX-3CD	3C2 Parcel 070, TxDOT Review Acquisition Package	15	446	15-Nov-19	05-Dec-19
F	TX-3CD	3C2 Parcel 070, Present and Negotiate Offer	45	446	06-Dec-19	06-Feb-20
F	TX-3CD	3C2 Parcel 070, Commissioners Hearing	120	446	07-Feb-20	23-Jul-20
F	TX-3CD	3C2 Parcel 070, Commissioners Award	1	446	24-Jul-20	24-Jul-20
F	TX-3CD	3C2 Parcel 070, Parcel Closing	20	446	27-Jul-20	21-Aug-20
F	TX-3CD	3C2 Parcel 070, Cleared for Construction	1	446	24-Aug-20	24-Aug-20
3C3 - Golden Triangle Blvd to N. Tarant Pkwy Sta-1280 to 1401			469	351	04-Apr-19	19-Jan-21
R3C3(	TX-3CD	3C3 Parcels Cleared for Construction	1	351	19-Jan-21	19-Jan-21
Northbound Parcels			443	376	04-Apr-19	14-Dec-20
PARCEL 012E			443	376	04-Apr-19	14-Dec-20
F	TX-3CD	3C3 Parcel 012E, Initiate ROW Acquisition	1	376	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 012E, Obtain Right of Entries & Project Admin.	20	376	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 012E, Perform Surveying & Mapping	40	376	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 012E, TxDOT Review Acquisition Survey Package	15	376	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 012E, Perform PH I ESA	20	376	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 012E, Prepare Title Work	20	376	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 012E, Perform Appraisals	30	376	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 012E, Perform Review Appraisal	15	376	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 012E, TxDOT Review Acquisition Package	15	376	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 012E, Present and Negotiate Offer	45	376	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 012E, Commissioners Hearing	120	376	07-Feb-20	23-Jul-20
F	TX-3CD	3C3 Parcel 012E, Commissioners Award	1	376	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 012E, Parcel Closing	20	376	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 012E, Prepare for Relocation	60	376	24-Aug-20	13-Nov-20
F	TX-3CD	3C3 Parcel 012E, Execute Relocation	20	376	16-Nov-20	11-Dec-20
F	TX-3CD	3C3 Parcel 012E, Cleared for Construction	1	376	14-Dec-20	14-Dec-20
PARCEL 041			443	376	04-Apr-19	14-Dec-20
F	TX-3CD	3C3 Parcel 041, Initiate ROW Acquisition	1	376	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 041, Obtain Right of Entries & Project Admin.	20	376	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 041, Perform Surveying & Mapping	40	376	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 041, TxDOT Review Acquisition Survey Package	15	376	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 041, Perform PH I ESA	20	376	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 041, Prepare Title Work	20	376	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 041, Perform Appraisals	30	376	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 041, Perform Review Appraisal	15	376	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 041, TxDOT Review Acquisition Package	15	376	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 041, Present and Negotiate Offer	45	376	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 041, Commissioners Hearing	120	376	07-Feb-20	23-Jul-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
A	TX-3CD	3C3 Parcel 041, Commissioners Award	1	376	24-Jul-20	24-Jul-20
A	TX-3CD	3C3 Parcel 041, Parcel Closing	20	376	27-Jul-20	21-Aug-20
A	TX-3CD	3C3 Parcel 041, Prepare for Relocation	60	376	24-Aug-20	13-Nov-20
A	TX-3CD	3C3 Parcel 041, Execute Relocation	20	376	16-Nov-20	11-Dec-20
A	TX-3CD	3C3 Parcel 041, Cleared for Construction	1	376	14-Dec-20	14-Dec-20
PARCEL 043			363	456	04-Apr-19	24-Aug-20
A	TX-3CD	3C3 Parcel 043, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
A	TX-3CD	3C3 Parcel 043, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
A	TX-3CD	3C3 Parcel 043, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
A	TX-3CD	3C3 Parcel 043, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
A	TX-3CD	3C3 Parcel 043, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
A	TX-3CD	3C3 Parcel 043, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
A	TX-3CD	3C3 Parcel 043, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
A	TX-3CD	3C3 Parcel 043, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
A	TX-3CD	3C3 Parcel 043, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
A	TX-3CD	3C3 Parcel 043, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
A	TX-3CD	3C3 Parcel 043, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
A	TX-3CD	3C3 Parcel 043, Commissioners Award	1	456	24-Jul-20	24-Jul-20
A	TX-3CD	3C3 Parcel 043, Parcel Closing	20	456	27-Jul-20	21-Aug-20
A	TX-3CD	3C3 Parcel 043, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
Southbound Parcels			468	351	04-Apr-19	18-Jan-21
PARCEL 027			363	456	04-Apr-19	24-Aug-20
A	TX-3CD	3C3 Parcel 027, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
A	TX-3CD	3C3 Parcel 027, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
A	TX-3CD	3C3 Parcel 027, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
A	TX-3CD	3C3 Parcel 027, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
A	TX-3CD	3C3 Parcel 027, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
A	TX-3CD	3C3 Parcel 027, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
A	TX-3CD	3C3 Parcel 027, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
A	TX-3CD	3C3 Parcel 027, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
A	TX-3CD	3C3 Parcel 027, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
A	TX-3CD	3C3 Parcel 027, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
A	TX-3CD	3C3 Parcel 027, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
A	TX-3CD	3C3 Parcel 027, Commissioners Award	1	456	24-Jul-20	24-Jul-20
A	TX-3CD	3C3 Parcel 027, Parcel Closing	20	456	27-Jul-20	21-Aug-20
A	TX-3CD	3C3 Parcel 027, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 012W			363	456	04-Apr-19	24-Aug-20
A	TX-3CD	3C3 Parcel 012W, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
A	TX-3CD	3C3 Parcel 012W, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
A	TX-3CD	3C3 Parcel 012W, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
A	TX-3CD	3C3 Parcel 012W, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
A	TX-3CD	3C3 Parcel 012W, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
A	TX-3CD	3C3 Parcel 012W, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
A	TX-3CD	3C3 Parcel 012W, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
A	TX-3CD	3C3 Parcel 012W, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
A	TX-3CD	3C3 Parcel 012W, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
A	TX-3CD	3C3 Parcel 012W, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
A	TX-3CD	3C3 Parcel 012W, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
A	TX-3CD	3C3 Parcel 012W, Commissioners Award	1	456	24-Jul-20	24-Jul-20
A	TX-3CD	3C3 Parcel 012W, Parcel Closing	20	456	27-Jul-20	21-Aug-20
A	TX-3CD	3C3 Parcel 012W, Cleared for Construction	1	456	24-Aug-20	24-Aug-20

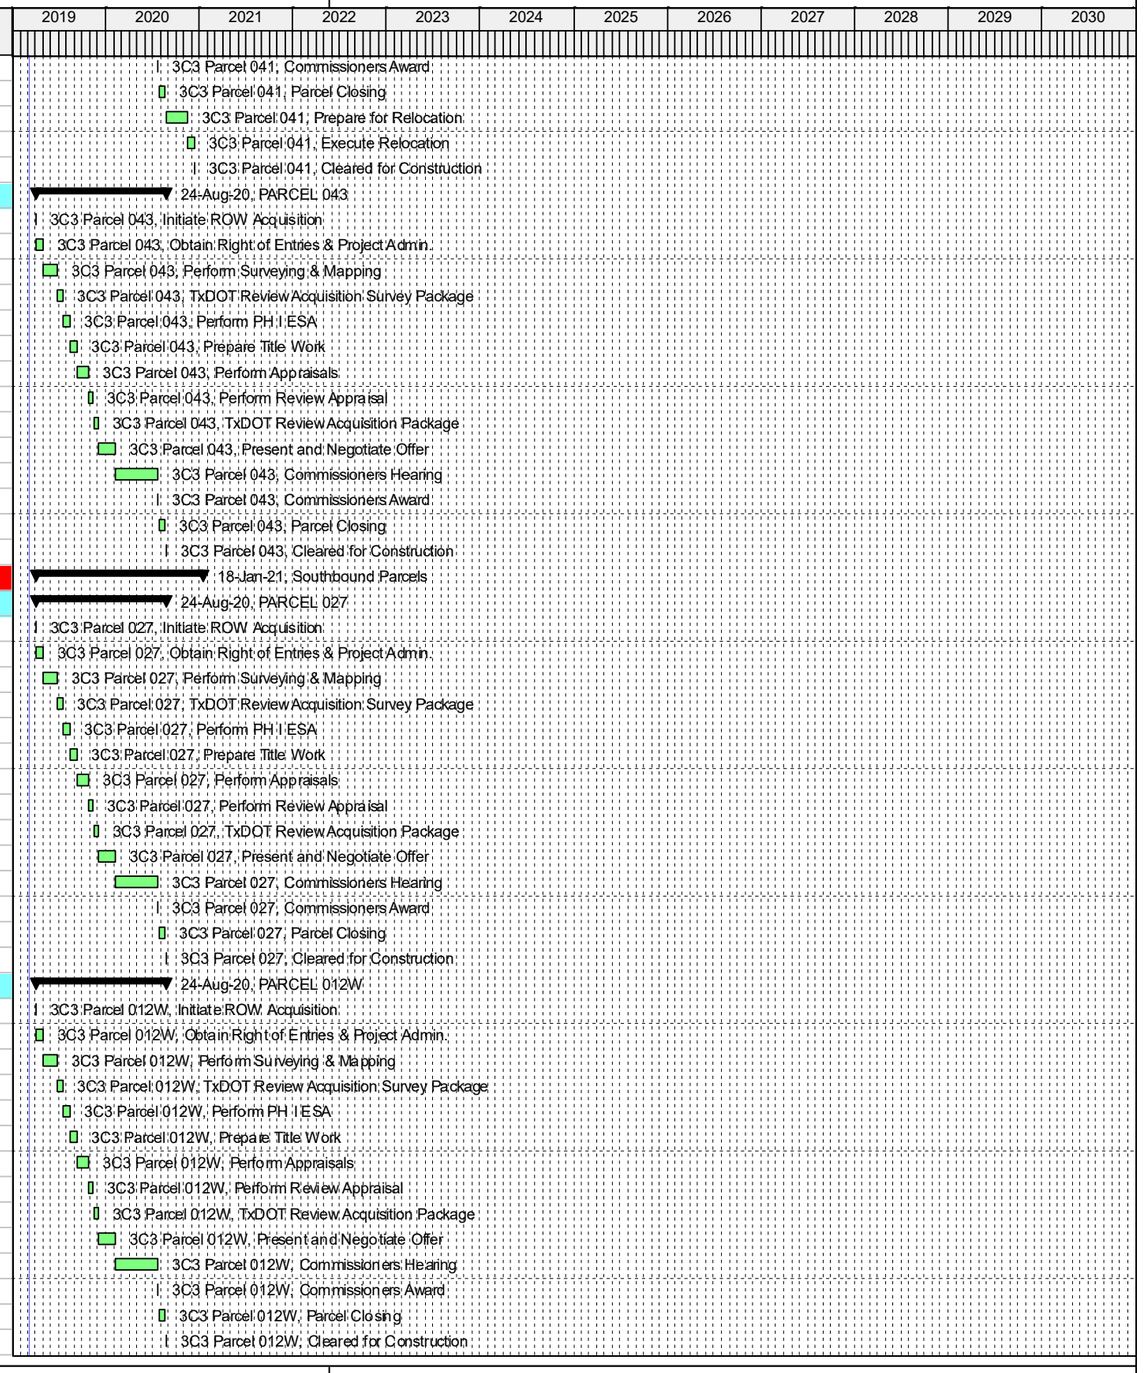

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
PARCEL 027U			422	397	04-Apr-19	13-Nov-20
F	TX-3CD	3C3 Parcel 027U, Initiate ROW Acquisition	10	397	04-Apr-19	17-Apr-19
F	TX-3CD	3C3 Parcel 027U, Obtain Right of Entries & Project Admin.	20	397	18-Apr-19	15-May-19
F	TX-3CD	3C3 Parcel 027U, Perform Surveying & Mapping	40	397	16-May-19	10-Jul-19
F	TX-3CD	3C3 Parcel 027U, TxDOT Review Acquisition Survey Package	15	397	11-Jul-19	31-Jul-19
F	TX-3CD	3C3 Parcel 027U, Perform PH I ESA	20	397	01-Aug-19	28-Aug-19
F	TX-3CD	3C3 Parcel 027U, Prepare Title Work	30	397	29-Aug-19	09-Oct-19
F	TX-3CD	3C3 Parcel 027U, Perform Appraisals	30	397	10-Oct-19	20-Nov-19
F	TX-3CD	3C3 Parcel 027U, Perform Review Appraisal	20	397	21-Nov-19	18-Dec-19
F	TX-3CD	3C3 Parcel 027U, TxDOT Review Acquisition Package	15	397	19-Dec-19	08-Jan-20
F	TX-3CD	3C3 Parcel 027U, Present and Negotiate Offer	60	397	09-Jan-20	01-Apr-20
F	TX-3CD	3C3 Parcel 027U, Commissioners Hearing	140	397	02-Apr-20	14-Oct-20
F	TX-3CD	3C3 Parcel 027U, Commissioners Award	1	397	15-Oct-20	15-Oct-20
F	TX-3CD	3C3 Parcel 027U, Parcel Closing	20	397	16-Oct-20	12-Nov-20
F	TX-3CD	3C3 Parcel 027U, Cleared for Construction	1	397	13-Nov-20	13-Nov-20
PARCEL 032U			422	397	04-Apr-19	13-Nov-20
F	TX-3CD	3C3 Parcel 032U, Initiate ROW Acquisition	10	397	04-Apr-19	17-Apr-19
F	TX-3CD	3C3 Parcel 032U, Obtain Right of Entries & Project Admin.	20	397	18-Apr-19	15-May-19
F	TX-3CD	3C3 Parcel 032U, Perform Surveying & Mapping	40	397	16-May-19	10-Jul-19
F	TX-3CD	3C3 Parcel 032U, TxDOT Review Acquisition Survey Package	15	397	11-Jul-19	31-Jul-19
F	TX-3CD	3C3 Parcel 032U, Perform PH I ESA	20	397	01-Aug-19	28-Aug-19
F	TX-3CD	3C3 Parcel 032U, Prepare Title Work	30	397	29-Aug-19	09-Oct-19
F	TX-3CD	3C3 Parcel 032U, Perform Appraisals	30	397	10-Oct-19	20-Nov-19
F	TX-3CD	3C3 Parcel 032U, Perform Review Appraisal	20	397	21-Nov-19	18-Dec-19
F	TX-3CD	3C3 Parcel 032U, TxDOT Review Acquisition Package	15	397	19-Dec-19	08-Jan-20
F	TX-3CD	3C3 Parcel 032U, Present and Negotiate Offer	60	397	09-Jan-20	01-Apr-20
F	TX-3CD	3C3 Parcel 032U, Commissioners Hearing	140	397	02-Apr-20	14-Oct-20
F	TX-3CD	3C3 Parcel 032U, Commissioners Award	1	397	15-Oct-20	15-Oct-20
F	TX-3CD	3C3 Parcel 032U, Parcel Closing	20	397	16-Oct-20	12-Nov-20
F	TX-3CD	3C3 Parcel 032U, Cleared for Construction	1	397	13-Nov-20	13-Nov-20
PARCEL 035U			422	397	04-Apr-19	13-Nov-20
F	TX-3CD	3C3 Parcel 035U, Initiate ROW Acquisition	10	397	04-Apr-19	17-Apr-19
F	TX-3CD	3C3 Parcel 035U, Obtain Right of Entries & Project Admin.	20	397	18-Apr-19	15-May-19
F	TX-3CD	3C3 Parcel 035U, Perform Surveying & Mapping	40	397	16-May-19	10-Jul-19
F	TX-3CD	3C3 Parcel 035U, TxDOT Review Acquisition Survey Package	15	397	11-Jul-19	31-Jul-19
F	TX-3CD	3C3 Parcel 035U, Perform PH I ESA	20	397	01-Aug-19	28-Aug-19
F	TX-3CD	3C3 Parcel 035U, Prepare Title Work	30	397	29-Aug-19	09-Oct-19
F	TX-3CD	3C3 Parcel 035U, Perform Appraisals	30	397	10-Oct-19	20-Nov-19
F	TX-3CD	3C3 Parcel 035U, Perform Review Appraisal	20	397	21-Nov-19	18-Dec-19
F	TX-3CD	3C3 Parcel 035U, TxDOT Review Acquisition Package	15	397	19-Dec-19	08-Jan-20
F	TX-3CD	3C3 Parcel 035U, Present and Negotiate Offer	60	397	09-Jan-20	01-Apr-20
F	TX-3CD	3C3 Parcel 035U, Commissioners Hearing	140	397	02-Apr-20	14-Oct-20
F	TX-3CD	3C3 Parcel 035U, Commissioners Award	1	397	15-Oct-20	15-Oct-20
F	TX-3CD	3C3 Parcel 035U, Parcel Closing	20	397	16-Oct-20	12-Nov-20
F	TX-3CD	3C3 Parcel 035U, Cleared for Construction	1	397	13-Nov-20	13-Nov-20
PARCEL 036U			422	397	04-Apr-19	13-Nov-20
F	TX-3CD	3C3 Parcel 036U, Initiate ROW Acquisition	10	397	04-Apr-19	17-Apr-19
F	TX-3CD	3C3 Parcel 036U, Obtain Right of Entries & Project Admin.	20	397	18-Apr-19	15-May-19
F	TX-3CD	3C3 Parcel 036U, Perform Surveying & Mapping	40	397	16-May-19	10-Jul-19
F	TX-3CD	3C3 Parcel 036U, TxDOT Review Acquisition Survey Package	15	397	11-Jul-19	31-Jul-19
F	TX-3CD	3C3 Parcel 036U, Perform PH I ESA	20	397	01-Aug-19	28-Aug-19

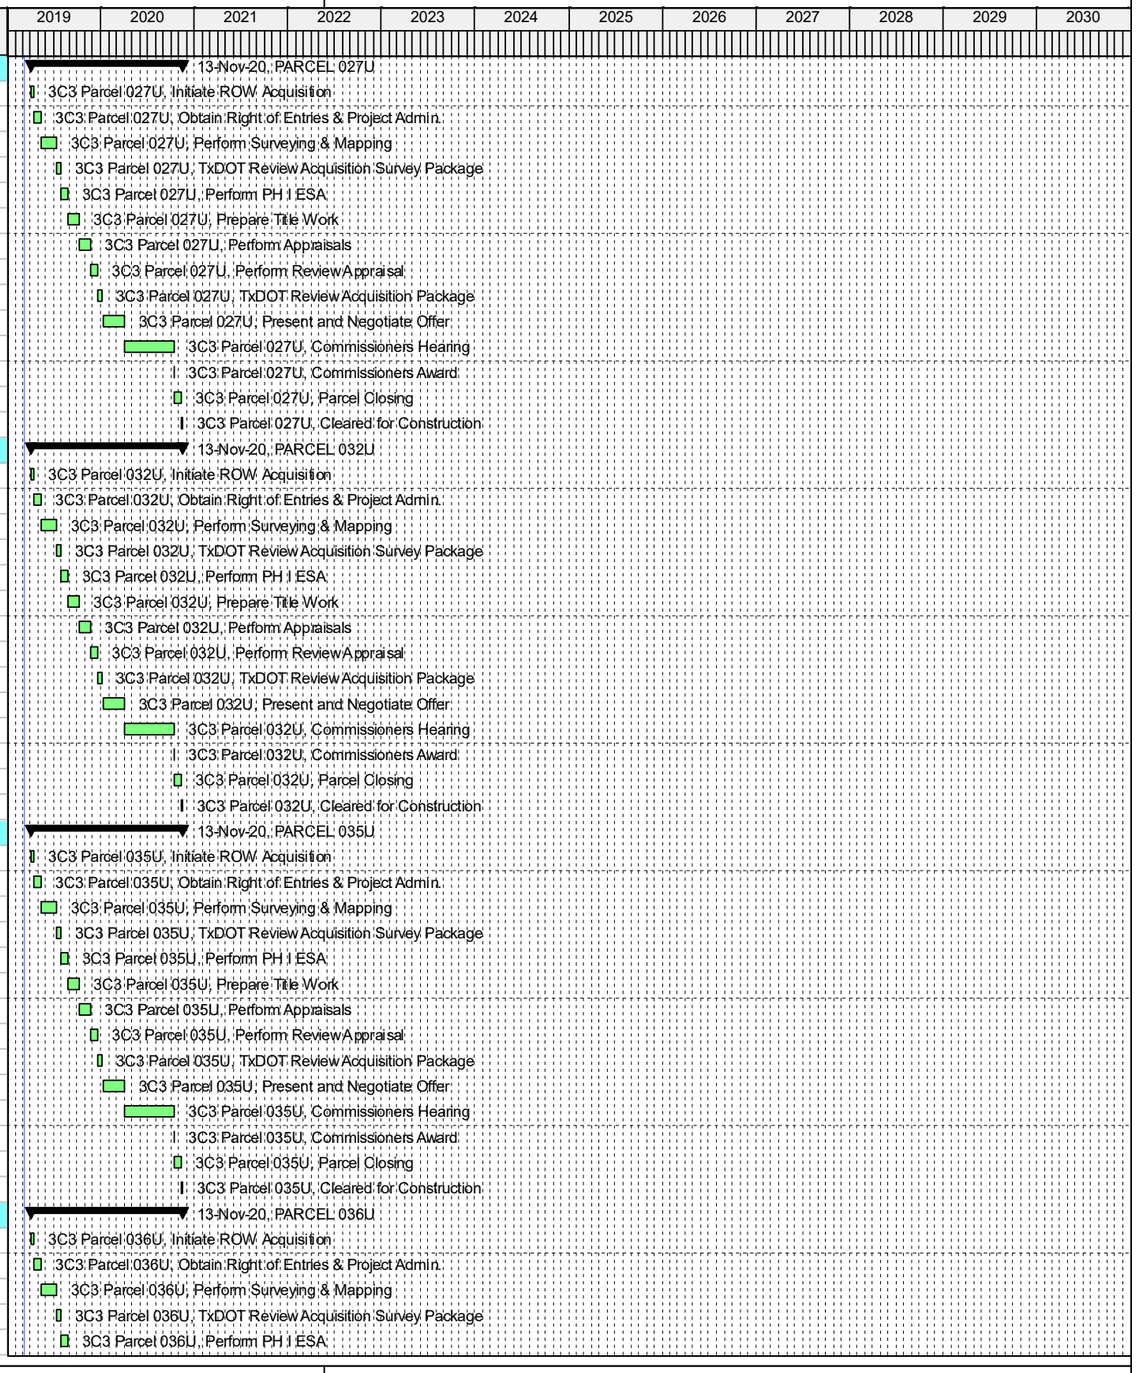

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	3C3 Parcel 036U, Prepare Title Work	30	397	29-Aug-19	09-Oct-19
	TX-3CD	3C3 Parcel 036U, Perform Appraisals	30	397	10-Oct-19	20-Nov-19
	TX-3CD	3C3 Parcel 036U, Perform Review Appraisal	20	397	21-Nov-19	18-Dec-19
	TX-3CD	3C3 Parcel 036U, TxDOT Review Acquisition Package	15	397	19-Dec-19	08-Jan-20
	TX-3CD	3C3 Parcel 036U, Present and Negotiate Offer	60	397	09-Jan-20	01-Apr-20
	TX-3CD	3C3 Parcel 036U, Commissioners Hearing	140	397	02-Apr-20	14-Oct-20
	TX-3CD	3C3 Parcel 036U, Commissioners Award	1	397	15-Oct-20	15-Oct-20
	TX-3CD	3C3 Parcel 036U, Parcel Closing	20	397	16-Oct-20	12-Nov-20
	TX-3CD	3C3 Parcel 036U, Cleared for Construction	1	397	13-Nov-20	13-Nov-20
PARCEL 037U			363	456	04-Apr-19	24-Aug-20
	TX-3CD	3C3 Parcel 037U, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
	TX-3CD	3C3 Parcel 037U, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
	TX-3CD	3C3 Parcel 037U, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
	TX-3CD	3C3 Parcel 037U, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
	TX-3CD	3C3 Parcel 037U, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
	TX-3CD	3C3 Parcel 037U, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
	TX-3CD	3C3 Parcel 037U, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
	TX-3CD	3C3 Parcel 037U, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
	TX-3CD	3C3 Parcel 037U, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
	TX-3CD	3C3 Parcel 037U, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
	TX-3CD	3C3 Parcel 037U, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
	TX-3CD	3C3 Parcel 037U, Commissioners Award	1	456	24-Jul-20	24-Jul-20
	TX-3CD	3C3 Parcel 037U, Parcel Closing	20	456	27-Jul-20	21-Aug-20
	TX-3CD	3C3 Parcel 037U, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 042			363	456	04-Apr-19	24-Aug-20
	TX-3CD	3C3 Parcel 042, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
	TX-3CD	3C3 Parcel 042, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
	TX-3CD	3C3 Parcel 042, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
	TX-3CD	3C3 Parcel 042, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
	TX-3CD	3C3 Parcel 042, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
	TX-3CD	3C3 Parcel 042, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
	TX-3CD	3C3 Parcel 042, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
	TX-3CD	3C3 Parcel 042, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
	TX-3CD	3C3 Parcel 042, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
	TX-3CD	3C3 Parcel 042, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
	TX-3CD	3C3 Parcel 042, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
	TX-3CD	3C3 Parcel 042, Commissioners Award	1	456	24-Jul-20	24-Jul-20
	TX-3CD	3C3 Parcel 042, Parcel Closing	20	456	27-Jul-20	21-Aug-20
	TX-3CD	3C3 Parcel 042, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 044			363	456	04-Apr-19	24-Aug-20
	TX-3CD	3C3 Parcel 044, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
	TX-3CD	3C3 Parcel 044, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
	TX-3CD	3C3 Parcel 044, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
	TX-3CD	3C3 Parcel 044, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
	TX-3CD	3C3 Parcel 044, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
	TX-3CD	3C3 Parcel 044, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
	TX-3CD	3C3 Parcel 044, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
	TX-3CD	3C3 Parcel 044, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
	TX-3CD	3C3 Parcel 044, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
	TX-3CD	3C3 Parcel 044, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
	TX-3CD	3C3 Parcel 044, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C3 Parcel 044, Commissioners Award	1	456	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 044, Parcel Closing	20	456	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 044, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 045			363	456	04-Apr-19	24-Aug-20
F	TX-3CD	3C3 Parcel 045, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 045, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 045, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 045, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 045, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 045, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 045, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 045, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 045, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 045, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 045, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
F	TX-3CD	3C3 Parcel 045, Commissioners Award	1	456	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 045, Parcel Closing	20	456	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 045, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 052			363	456	04-Apr-19	24-Aug-20
F	TX-3CD	3C3 Parcel 052, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 052, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 052, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 052, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 052, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 052, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 052, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 052, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 052, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 052, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 052, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
F	TX-3CD	3C3 Parcel 052, Commissioners Award	1	456	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 052, Parcel Closing	20	456	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 052, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 055			363	456	04-Apr-19	24-Aug-20
F	TX-3CD	3C3 Parcel 055, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 055, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 055, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 055, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 055, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 055, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 055, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 055, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 055, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 055, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 055, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
F	TX-3CD	3C3 Parcel 055, Commissioners Award	1	456	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 055, Parcel Closing	20	456	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 055, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 056A			468	351	04-Apr-19	18-Jan-21
F	TX-3CD	3C3 Parcel 056A, Initiate ROW Acquisition	1	351	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 056A, Obtain Right of Entries & Project Admin.	20	351	05-Apr-19	02-May-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
F	TX-3CD	3C3 Parcel 056A, Perform Surveying & Mapping	40	351	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 056A, TxDOT Review Acquisition Survey Package	15	351	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 056A, Perform PH I ESA	20	351	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 056A, Prepare Title Work	20	351	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 056A, Perform Appraisals	30	351	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 056A, Perform Review Appraisal	20	351	25-Oct-19	21-Nov-19
F	TX-3CD	3C3 Parcel 056A, TxDOT Review Acquisition Package	15	351	22-Nov-19	12-Dec-19
F	TX-3CD	3C3 Parcel 056A, Present and Negotiate Offer	45	351	13-Dec-19	13-Feb-20
F	TX-3CD	3C3 Parcel 056A, Commissioners Hearing	140	351	14-Feb-20	27-Aug-20
F	TX-3CD	3C3 Parcel 056A, Commissioners Award	1	351	28-Aug-20	28-Aug-20
F	TX-3CD	3C3 Parcel 056A, Parcel Closing	20	351	31-Aug-20	25-Sep-20
F	TX-3CD	3C3 Parcel 056A, Prepare for Relocation	60	351	28-Sep-20	18-Dec-20
F	TX-3CD	3C3 Parcel 056A, Execute Relocation	20	351	21-Dec-20	15-Jan-21
F	TX-3CD	3C3 Parcel 056A, Cleared for Construction	1	351	18-Jan-21	18-Jan-21
PARCEL 056			363	456	04-Apr-19	24-Aug-20
F	TX-3CD	3C3 Parcel 056, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 056, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 056, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 056, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 056, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 056, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 056, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 056, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 056, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 056, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 056, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
F	TX-3CD	3C3 Parcel 056, Commissioners Award	1	456	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 056, Parcel Closing	20	456	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 056, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
PARCEL 056B			363	456	04-Apr-19	24-Aug-20
F	TX-3CD	3C3 Parcel 056B, Initiate ROW Acquisition	1	456	04-Apr-19	04-Apr-19
F	TX-3CD	3C3 Parcel 056B, Obtain Right of Entries & Project Admin.	20	456	05-Apr-19	02-May-19
F	TX-3CD	3C3 Parcel 056B, Perform Surveying & Mapping	40	456	03-May-19	27-Jun-19
F	TX-3CD	3C3 Parcel 056B, TxDOT Review Acquisition Survey Package	15	456	28-Jun-19	18-Jul-19
F	TX-3CD	3C3 Parcel 056B, Perform PH I ESA	20	456	19-Jul-19	15-Aug-19
F	TX-3CD	3C3 Parcel 056B, Prepare Title Work	20	456	16-Aug-19	12-Sep-19
F	TX-3CD	3C3 Parcel 056B, Perform Appraisals	30	456	13-Sep-19	24-Oct-19
F	TX-3CD	3C3 Parcel 056B, Perform Review Appraisal	15	456	25-Oct-19	14-Nov-19
F	TX-3CD	3C3 Parcel 056B, TxDOT Review Acquisition Package	15	456	15-Nov-19	05-Dec-19
F	TX-3CD	3C3 Parcel 056B, Present and Negotiate Offer	45	456	06-Dec-19	06-Feb-20
F	TX-3CD	3C3 Parcel 056B, Commissioners Hearing	120	456	07-Feb-20	23-Jul-20
F	TX-3CD	3C3 Parcel 056B, Commissioners Award	1	456	24-Jul-20	24-Jul-20
F	TX-3CD	3C3 Parcel 056B, Parcel Closing	20	456	27-Jul-20	21-Aug-20
F	TX-3CD	3C3 Parcel 056B, Cleared for Construction	1	456	24-Aug-20	24-Aug-20
3C Utility Adjustments Sta 1028+00 to 1401+00			601	562	18-Mar-19	05-Jul-21
Utility Coordination			280	682	18-Mar-19	10-Apr-20
Administration and Planning			280	682	18-Mar-19	10-Apr-20
Conceptual Design			149	429	18-Mar-19	10-Oct-19
UCI	TX-3CD	Mobilization of Utility Group	20	298	18-Mar-19	12-Apr-19
UCI	TX-3CD	Utility Planning, Scope & Budget	40	318	18-Mar-19	10-May-19

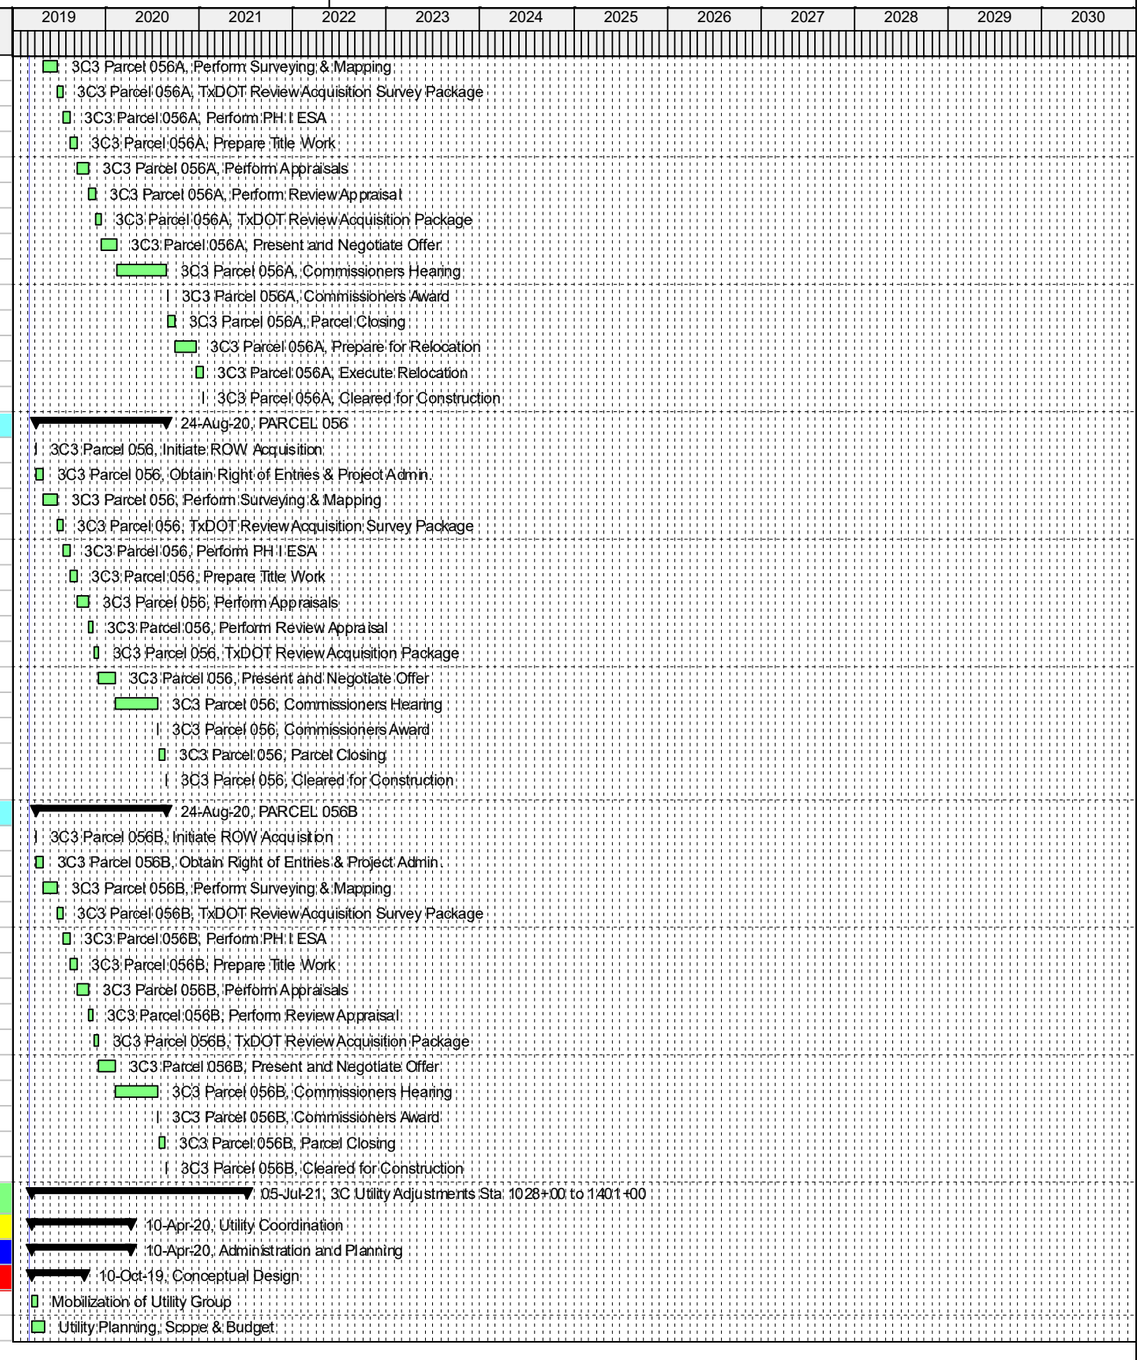

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
UCI	TX-3CD	Initial Meetings with Utility Owners	40	298	15-Apr-19	07-Jun-19
UCI	TX-3CD	Perform Level A & B SUE	40	298	10-Jun-19	02-Aug-19
UCI	TX-3CD	Prepare Utility Strip Map and Tracking Report	40	430	08-Jul-19	30-Aug-19
UCI	TX-3CD	Develop Utility Adjustment Concept Plan	40	430	22-Jul-19	13-Sep-19
UCI	TX-3CD	Submit Utility Adjustment Concept Plan	0	430	16-Sep-19	16-Sep-19
UCI	TX-3CD	TxDOT/IE Review Utility Adjustment Concept Plan	14	601	16-Sep-19	29-Sep-19
UCI	TX-3CD	Utility Adjustment Concept Plan - Clear Comments	10	601	30-Sep-19	09-Oct-19
UCI	TX-3CD	Utility Adjustment Concept Plan in Place	1	429	10-Oct-19	10-Oct-19
Master Agreements (MUAA's)			180	682	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Cross Tex Energy	180	302	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Centurylink	180	353	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with One Source	180	576	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with City of Ft. Worth	180	298	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Atmos Energy	180	357	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Cowtown Pipeline	180	464	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with AT&T Telecom	180	362	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Sunoco	180	312	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Oncor	180	362	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Trinity River Authority	180	682	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Verizon	180	387	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Quicksliver Pipeline	180	682	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Zayo	180	649	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Tri-County Electric	180	362	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Fiberlight	180	417	05-Aug-19	10-Apr-20
UM	TX-3CD	Negotiate MUAA with Private Electric	180	444	05-Aug-19	10-Apr-20
Utility Relocations			321	562	13-Apr-20	05-Jul-21
3C1 - Non-Conflicts Eagle Pwky to SH 170 Sta-1028 to 1176			201	682	13-Apr-20	19-Jan-21
U3C1N	TX-3CD	3C Utility Non-Conflict Packages Completed	0	682	19-Jan-21	19-Jan-21
3C1 - Northbound Relocates			201	682	13-Apr-20	18-Jan-21
3C1 - AT&T			201	682	13-Apr-20	18-Jan-21
3C1 - AT&T - Conflict 0313-2-T1 STA 1136 to 1178			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0313-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0313-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0313-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0313-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0313-2-T1	5	682	12-Jan-21	18-Jan-21
3C1 - City of FT Worth			201	682	13-Apr-20	18-Jan-21
3C1 - City of FT Worth - Conflict 0114 STA 1122 to 1122			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0114-6-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0114-6-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0114-6-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0114-6-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth Plans and As-builts - Conflict 0114-6-W1	5	682	12-Jan-21	18-Jan-21
3C1 - City of FT Worth - Conflict 0115 STA 1124 to 1124			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0115-6-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0115-6-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0115-6-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0115-6-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth Plans and As-builts - Conflict 0115-6-W1	5	682	12-Jan-21	18-Jan-21
3C1 - City of FT Worth - Conflict 0120 STA 1133 to 1133			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0119-6-W1	180	682	13-Apr-20	18-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0119-6-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0119-6-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0119-6-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth Plans and As-builts - Conflict 0119-6-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0122 STA 1133 to 1133		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0122-6-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0122-6-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0122-6-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0122-6-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth Plans and As-builts - Conflict 0122-6-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0124 STA 1161 to 1161		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0124-6-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0124-6-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0124-6-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0124-6-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth Plans and As-builts - Conflict 0124-6-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - One Source		201	682	13-Apr-20	18-Jan-21
	3C1 - One Source - Conflict 0901-1-FO4 STA 1124 to 1132		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0901-1-FO4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0901-1-FO4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0901-1-FO4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0901-1-FO4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Plans and As-builts - Conflict 0901-1-FO4	5	682	12-Jan-21	18-Jan-21
	3C1 - One Source - Conflict 0902-1-T2 STA 1124 to 1132		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0902-1-T2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0902-1-T2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0902-1-T2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0902-1-T2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Plans and As-builts - Conflict 0902-1-T2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor		201	682	13-Apr-20	18-Jan-21
	3C1 - Oncor - Conflict 1001-1-E2 STA 1024 to 1038		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1001-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1001-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1001-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1001-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1001-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1013-1-E2 STA 1134 to 1193		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1013-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1013-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1013-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1013-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Plans and As-builts - Conflict 1013-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Quicksilver Pipeline		201	682	13-Apr-20	18-Jan-21
	3C1 - Quicksilver Pipeline - Conflict 163-8-G3 STA 1034 to 1043		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Quicksliver Pipeline Assembly Package - Conflict 1201-8-G3	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Quicksliver Pipeline Assembly Package - Conflict 1201-8-G3	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Quicksliver Pipeline Assembly Package - Conflict 1201-8-G3	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Quicksliver Pipeline Assembly Package - Conflict 1201-8-G3	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Quicksliver Plans and As-builts - Conflict 1201-8-G3	5	682	12-Jan-21	18-Jan-21
	3C1 - Quicksilver Pipeline - Conflict 164-1-E2 STA 1096 to 1115		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Quicksliver Pipeline Assembly Package - Conflict 1202-8-G3	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Quicksliver Pipeline Assembly Package - Conflict 1202-8-G3	5	682	21-Dec-20	25-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Submit Quicksliver Pipeline Assembly Package - Conflict 1202-8-G3	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Quicksliver Pipeline Assembly Package - Conflict 1202-8-G3	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Quicksliver Pipeline Plans and As-builts - Conflict 1202-8-G3	5	682	12-Jan-21	18-Jan-21
3C1 - Atmos Energy			201	682	13-Apr-20	18-Jan-21
3C1 - Atmos Energy - Conflict 1403-2-G1 STA 1116 to 1119			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 1403-6-G1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 1403-6-G1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 1403-6-G1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 1403-6-G1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 1403-6-G1	5	682	12-Jan-21	18-Jan-21
3C1 - Atmos Energy - Conflict 1404-6-G1 STA 1133 to 1134			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 1404-6-G1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 1404-6-G1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 1404-6-G1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 1404-6-G1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Atmos Energy Plans and As-builts - Conflict 1404-6-G1	5	682	12-Jan-21	18-Jan-21
3C1 - Cowtown Pipeline			201	682	13-Apr-20	18-Jan-21
3C1 - Cowtown Pipeline - Conflict 1501-12-G2 STA 1034 to 1043			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Cowtown Pipeline Energy Assembly Package - Conflict 1501-12-G2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Cowtown Pipeline Assembly Package - Conflict 1501-12-G2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Cowtown Pipeline Assembly Package - Conflict 1501-12-G2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Cowtown Pipeline Assembly Package - Conflict 1501-12-G2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Cowtown Pipeline Plans and As-builts - Conflict 1501-12-G2	5	682	12-Jan-21	18-Jan-21
3C1 - Cowtown Pipeline - Conflict 1502-6-G2 STA 1034 to 1043			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Cowtown Pipeline Energy Assembly Package - Conflict 1502-6-G2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Cowtown Pipeline Assembly Package - Conflict 1502-6-G2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Cowtown Pipeline Assembly Package - Conflict 1502-6-G2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Cowtown Pipeline Assembly Package - Conflict 1502-6-G2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Cowtown Pipeline Final Inspection and As-builts - Conflict 1502-6-G2	5	682	12-Jan-21	18-Jan-21
3C1 - Cowtown Pipeline - Conflict 1503-6-G2 STA 1096 to 1116			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Cowtown Pipeline Energy Assembly Package - Conflict 1503-6-G2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Cowtown Pipeline Assembly Package - Conflict 1503-6-G2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Cowtown Pipeline Assembly Package - Conflict 1503-6-G2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Cowtown Pipeline Assembly Package - Conflict 1503-6-G2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Cowtown Pipeline Final Inspection and As-builts - Conflict 1503-6-G2	5	682	12-Jan-21	18-Jan-21
3C1 - Cowtown Pipeline - Conflict 1504-12-G2 STA 1096 to 1116			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Cowtown Pipeline Energy Assembly Package - Conflict 1504-12-G2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Cowtown Pipeline Assembly Package - Conflict 1504-12-G2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Cowtown Pipeline Assembly Package - Conflict 1504-12-G2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Cowtown Pipeline Assembly Package - Conflict 1504-12-G2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Cowtown Pipeline Final Inspection and As-builts - Conflict 1504-12-G2	5	682	12-Jan-21	18-Jan-21
3C1 - Verizon			201	682	13-Apr-20	18-Jan-21
3C1 - Verizon - Conflict 0803-3-FO3 STA 1133 to 1135			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0803-3-FO3	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0803-3-FO3	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0803-3-FO3	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0803-3-FO3	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Verizon Plans and As-builts - Conflict 0803-3-FO3	5	682	12-Jan-21	18-Jan-21
3C1 - Verizon - Conflict 0805-3-FO3 STA 1135 to 1184			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 096-3-FO3	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 096-3-FO3	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 096-3-FO3	1	682	28-Dec-20	28-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 096-3-FO3	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Verizon Plans and As-builts - Conflict 096-3-FO3	5	682	12-Jan-21	18-Jan-21
3C1 - Crossing Relocates			201	682	13-Apr-20	18-Jan-21
3C1 - Trinity River Authority			201	682	13-Apr-20	18-Jan-21
3C1 - TRA - Conflict 0201 STA 1043 to 1043			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of TRA Assembly Package - Conflict 0201-27-WW2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review TRA Assembly Package - Conflict 0201-27-WW2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit TRA Assembly Package - Conflict 0201-27-WW2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review TRA Assembly Package - Conflict 0201-27-WW2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	TRA Final Inspection and As-builts - Conflict 0201-27-WW2	5	682	12-Jan-21	18-Jan-21
3C1 - TRA - Conflict 0202 STA 1043 to 1066			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of TRA Assembly Package - Conflict 0202-21-WW2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review TRA Assembly Package - Conflict 0202-21-WW2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit TRA Assembly Package - Conflict 0202-21-WW2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review TRA Assembly Package - Conflict 0202-21-WW2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	TRA Final Inspection and As-builts - Conflict 0202-21-WW2	5	682	12-Jan-21	18-Jan-21
3C1 - TRA - Conflict 0203 STA 1121 to 1124			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of TRA Assembly Package - Conflict 0203-24-WW2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review TRA Assembly Package - Conflict 0203-24-WW2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit TRA Assembly Package - Conflict 0203-24-WW2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review TRA Assembly Package - Conflict 0203-24-WW2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	TRA Final Inspection and As-builts - Conflict 0203-24-WW2	5	682	12-Jan-21	18-Jan-21
3C1 - TRA - Conflict 0204 STA 1121 to 1121			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of TRA Assembly Package - Conflict 0204-10-WW2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review TRA Assembly Package - Conflict 0204-10-WW2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit TRA Assembly Package - Conflict 0204-10-WW2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review TRA Assembly Package - Conflict 0204-10-WW2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	TRA Final Inspection and As-builts - Conflict 0204-10-WW2	5	682	12-Jan-21	18-Jan-21
3C1 - Southbound Relocates			201	682	13-Apr-20	18-Jan-21
3C1 - AT&T			201	682	13-Apr-20	18-Jan-21
3C1 - AT&T - Conflict 0301-2-T1 STA 1020 to 1038			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0301-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0301-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0301-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0301-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0301-2-T1	5	682	12-Jan-21	18-Jan-21
3C1 - AT&T - Conflict 0302-3-T1 STA 1038 to 1040			201	584	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0302-3-T1	180	584	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0302-3-T1	5	584	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0302-3-T1	1	584	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0302-3-T1	10	584	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0302-3-T1	5	584	12-Jan-21	18-Jan-21
3C1 - AT&T - Conflict 0303-2-T1 STA 1122 to 1136			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0303-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0303-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0303-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0303-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0303-2-T1	5	682	12-Jan-21	18-Jan-21
3C1 - AT&T - Conflict 0304-2-T1 STA 1040 to 1064			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0304-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0304-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0304-2-T1	1	682	28-Dec-20	28-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0304-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0304-2-T1	5	682	12-Jan-21	18-Jan-21
	3C1 - AT&T - Conflict 0310-1-FO1 STA 1134 to 1139		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0310-1-FO1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0310-1-FO1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0310-1-FO1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0310-1-FO1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0310-1-FO1	5	682	12-Jan-21	18-Jan-21
	3C1 - AT&T - Conflict 0311-2-T1 STA 1139 to 1157		201	584	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0311-2-T1	180	584	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0311-2-T1	5	584	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0311-2-T1	1	584	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0311-2-T1	10	584	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0311-2-T1	5	584	12-Jan-21	18-Jan-21
	3C1 - AT&T - Conflict 0312-2-T1 STA 1138 to 1156		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0312-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0312-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0312-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0312-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0312-2-T1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth		201	682	13-Apr-20	18-Jan-21
	3C1 - City of FT Worth - Conflict 0101 STA 1024 to 1044		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0101-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0101-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0101-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0101-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0101-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0102 STA 1024 to 1056		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0102-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0102-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0102-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0102-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0102-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0103 STA 1025 to 1025		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0103-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0103-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0103-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0103-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0103-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0104 STA 1027 to 1027		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0104-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0104-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0104-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0104-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0104-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0105 STA 1034 to 1034		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0105-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0105-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0105-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0105-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0105-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0106 STA 1043 to 1043		201	682	13-Apr-20	18-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0106-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0106-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0106-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0106-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0106-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0107 STA 1040 to 1040		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0107-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0107-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0107-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0107-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0107-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0109 STA 1043 to 1043		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0109-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0109-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0109-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0109-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0109-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0110 STA 1044 to 1044		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0110-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0110-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0110-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0110-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0110-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0111 STA 1079 to 1079		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0111-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0111-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0111-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0111-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0111-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0112 STA 1117 to 1117		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 012-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 012-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 012-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 012-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 012-W1	5	682	12-Jan-21	18-Jan-21
	3C1 - City of FT Worth - Conflict 0113 STA 1044 to 1117		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0113-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0113-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0113-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0113-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0113-WW1	5	682	12-Jan-21	18-Jan-21
	3C1 - Verizon		201	682	13-Apr-20	18-Jan-21
	3C1 - Verizon - Conflict 0801-1-FO2 STA 1119 to 1131		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 092-3-FO2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 092-3-FO2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 092-3-FO2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 092-3-FO2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 092-3-FO2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor		201	682	13-Apr-20	18-Jan-21
	3C1 - Oncor - Conflict -1004-2-E2 STA 1080 to 1080		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1004-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1004-1-E2	5	682	21-Dec-20	25-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Submit Oncor Assembly Package - Conflict 1004-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1004-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Plans and As-builts - Conflict 1004-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1002-1-E2 STA 1038 to 1080		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1002-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1002-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1002-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1002-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Plans and As-builts - Conflict 1002-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1003-1-E2 STA 1078 to 1079		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1003-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1003-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1003-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1003-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Plans and As-builts - Conflict 1003-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1005-1-E2 STA 1080 to 1082		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1005-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1005-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1005-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1005-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1005-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1006-1-E2 STA 1117 to 1117		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1006-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1006-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1006-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1006-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1006-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1010-1-E2 STA 1126 to 1133		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1010-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1010-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1010-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1010-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1010-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1012-1-E2 STA 1134 to 1134		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1012-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1012-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1012-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1012-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1012-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1014-1-E2 STA 1136 to 1140		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1014-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1014-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1014-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1014-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1014-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Oncor - Conflict 1015-1-OHE1 STA 1140 to 1165		201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 124-1-E2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 124-1-E2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 124-1-E2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 124-1-E2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 124-1-E2	5	682	12-Jan-21	18-Jan-21
	3C1 - Atmos Energy		201	682	13-Apr-20	18-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		3C1 - Atmos Energy - Conflict 1403-6-G1 STA 1116 to 1119	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 1408-6-G1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 1408-6-G1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 1408-6-G1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 1408-6-G1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Atmos Energy Plans and As-builts - Conflict 1408-6-G1	5	682	12-Jan-21	18-Jan-21
		3C1 - Private Electric	201	682	13-Apr-20	18-Jan-21
		3C1 - Private Electric - Conflict 1701-10-W2 STA 1117 to 1117	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Private Electric Assembly Package - Conflict 1701-10-W2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Private Electric Assembly Package - Conflict 1701-10-W2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Private Electric Assembly Package - Conflict 1701-10-W2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Private Electric Assembly Package - Conflict 1701-10-W2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Private Electric Final Inspection and As-builts - Conflict 1701-10-W2	5	682	12-Jan-21	18-Jan-21
		3C1 - Private Electric - Conflict 1702-2-W2 STA 1117 to 1117	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Private Electric Assembly Package - Conflict 1702-2-W2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Private Electric Assembly Package - Conflict 1702-2-W2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Private Electric Assembly Package - Conflict 1702-2-W2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Private Electric Assembly Package - Conflict 1702-2-W2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Private Electric Final Inspection and As-builts - Conflict 1702-2-W2	5	682	12-Jan-21	18-Jan-21
		3C2 - Non-Conflicts SH 170 to Golden Triangle Blvd Sta-1176 to 1280-1	201	682	13-Apr-20	18-Jan-21
		3C2 - Northbound Relocates	201	682	13-Apr-20	18-Jan-21
		3C2 - AT&T	201	682	13-Apr-20	18-Jan-21
		3C2 - AT&T - Conflict 0314-2-T1 STA 1136 to 1178	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0314-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0314-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0314-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0314-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0314-2-T1	5	682	12-Jan-21	18-Jan-21
		3C2 - City of FT Worth	201	682	13-Apr-20	18-Jan-21
		3C2 - City of FT Worth - Conflict 0139 STA 1024 SH 170	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0139-4-E4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0139-4-E4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0139-4-E4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0139-4-E4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0139-4-E4	5	682	12-Jan-21	18-Jan-21
		3C2 - City of FT Worth - Conflict 0140 STA 1024 SH 170	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0140-1-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0140-1-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0140-1-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0140-1-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0140-1-W1	5	682	12-Jan-21	18-Jan-21
		3C2 - City of FT Worth - Conflict 0141 STA 1024 SH 170	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0141-1-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0141-1-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0141-1-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0141-1-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0141-1-W1	5	682	12-Jan-21	18-Jan-21
		3C2 - City of FT Worth - Conflict 0142 STA 1024 SH 170	201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0142-1-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0142-1-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0142-1-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0142-1-W1	10	682	29-Dec-20	11-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	City of Ft. Worth As-builts - Conflict 0142-1-W1	5	682	12-Jan-21	18-Jan-21
3C2 - City of FT Worth - Conflict 0150 STA 1024 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0150-1-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0150-1-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0150-1-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0150-1-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0150-1-WW1	5	682	12-Jan-21	18-Jan-21
3C2 - Tri-County Electric			201	682	13-Apr-20	18-Jan-21
3C2 - Tri-County Electric - Conflict 0601-3-E1 STA 1345 to 1386			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0602-1-OHE2	5	682	12-Jan-21	18-Jan-21
3C2 - Tri-County Electric - Conflict 0602-3-E1 STA 1345 to 1348			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0602-1-OHE2	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0602-1-OHE2	5	682	12-Jan-21	18-Jan-21
3C2 - Tri-County Electric - Conflict 0605-3-E1 STA 1002 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0605-3-E1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0605-3-E1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0605-3-E1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0605-3-E1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0605-3-E1	5	682	12-Jan-21	18-Jan-21
3C2 - Verizon			201	682	13-Apr-20	18-Jan-21
3C2 - Verizon - Conflict 0804-1-T3 STA 1184 to 12194			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0804-1-T3	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0804-1-T3	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0804-1-T3	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0804-1-T3	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0804-1-T3	5	682	12-Jan-21	18-Jan-21
3C2 - Verizon - Conflict 0811-1-FO3 STA 1005 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0811-1-FO3	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0811-1-FO3	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0811-1-FO3	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0811-1-FO3	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0811-1-FO3	5	682	12-Jan-21	18-Jan-21
3C2 - Crossing Relocates			201	682	13-Apr-20	18-Jan-21
3C2 - City of FT Worth			201	682	13-Apr-20	18-Jan-21
3C2 - City of FT Worth - Conflict 0151 STA 1024 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0151-12-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0151-12-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0151-12-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0151-12-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0151-12-WW1	5	682	12-Jan-21	18-Jan-21
3C2 - Tri-County Electric			201	682	13-Apr-20	18-Jan-21
3C2 - Tri-County Electric - Conflict 0606-3-E1 STA 1026 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0606-3-E1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0606-3-E1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0606-3-E1	1	682	28-Dec-20	28-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0606-3-E1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0606-3-E1	5	682	12-Jan-21	18-Jan-21
3C2 - Sunoco			201	682	13-Apr-20	18-Jan-21
3C2 - Sunoco - Conflict 1302-4-G4 STA 1182 to 1193			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Sunoco Assembly Package - Conflict 1302-4-G4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Sunoco Assembly Package - Conflict 1302-4-G4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Sunoco Assembly Package - Conflict 1302-4-G4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Sunoco Assembly Package - Conflict 1302-4-G4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Sunoco Final Inspection and As-builts - Conflict 1302-4-G4	5	682	12-Jan-21	18-Jan-21
3C2 - Southbound Relocates			201	682	13-Apr-20	18-Jan-21
3C2 - Tri-County Electric			201	682	13-Apr-20	18-Jan-21
3C2 - Tri-County Electric - Conflict 0607-3-E1 STA 1002 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0607-3-E1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0607-3-E1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0607-3-E1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0607-3-E1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0607-3-E1	5	682	12-Jan-21	18-Jan-21
3C2 - Tri-County Electric - Conflict 0604-3-E1 STA 1301 to 1355			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0604-3-E1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0604-3-E1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0604-3-E1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0604-3-E1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0604-3-E1	5	682	12-Jan-21	18-Jan-21
3C3 - Non-Conflicts Golden Triangle Blvd to N. Tarant Pkwy Sta-1280 to 1401-1			201	682	13-Apr-20	18-Jan-21
3C3 - Northbound Relocates			201	682	13-Apr-20	18-Jan-21
3C3 - AT&T			201	682	13-Apr-20	18-Jan-21
3C3 - AT&T - Conflict 0330-2-T1 STA 1355 to 1400			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0330-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0330-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0330-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0330-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0330-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - AT&T - Conflict 0331-2-FO1 STA 1002 SH 170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0331-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0331-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0331-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0331-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0331-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth			201	682	13-Apr-20	18-Jan-21
3C3 - City of FT Worth - Conflict 0143 STA 1356 to 1356			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0143-12-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0143-12-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0143-12-W1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth - Conflict 0146 STA 1353 to 1361			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0146-8-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0146-8-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0146-8-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0146-8-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0146-8-W1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth - Conflict 0147 STA 1364 to 1400			201	682	13-Apr-20	18-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0147-10-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0147-10-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0147-10-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0147-10-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0147-10-W1	5	682	12-Jan-21	18-Jan-21
3C3 - One Source			201	682	13-Apr-20	18-Jan-21
3C3 - One Source - Conflict 0906-5-FO4 STA 1355 to 1360			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0906-5-FO4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0906-5-FO4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0906-5-FO4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0906-5-FO4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0906-5-FO4	5	682	12-Jan-21	18-Jan-21
3C3 - One Source - Conflict 0907-3-FO4 STA 1360 to 1386			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0907-3-FO4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0907-3-FO4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0907-3-FO4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0907-3-FO4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0907-3-FO4	5	682	12-Jan-21	18-Jan-21
3C3 - One Source - Conflict 0909-3-FO4 STA 1346 to 1349			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0909-3-FO4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0909-3-FO4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0909-3-FO4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0909-3-FO4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0909-3-FO4	5	682	12-Jan-21	18-Jan-21
3C3 - One Source - Conflict 0910-3-FO4 STA 1349 to 1345			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0910-3-FO4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0910-3-FO4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0910-3-FO4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0910-3-FO4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0910-3-FO4	5	682	12-Jan-21	18-Jan-21
3C3 - Crossing Relocates			201	682	13-Apr-20	18-Jan-21
3C3 - City of FT Worth			201	682	13-Apr-20	18-Jan-21
3C3 - City of FT Worth - Conflict 0144 STA 1406 to 1406			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0144-16-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0144-16-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0144-16-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0144-16-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0144-16-W1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth - Conflict 0149 STA 1405 to 1405			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0149-20-WW1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0149-20-WW1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0149-20-WW1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0149-20-WW1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0149-20-WW1	5	682	12-Jan-21	18-Jan-21
3C3 - Southbound Relocates			201	682	13-Apr-20	18-Jan-21
3C3 - AT&T			201	682	13-Apr-20	18-Jan-21
3C3 - AT&T - Conflict 0322-2-T1 STA 1136 to 1178			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0322-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0322-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0322-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0322-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0322-2-T1	5	682	12-Jan-21	18-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
3C3 - AT&T - Conflict 0323-2-T1 STA 1136 to 1178-1			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0323-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0323-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0323-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0323-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0323-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - AT&T - Conflict 0324-2-T1 STA 1136 to 1178-3			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0324-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0324-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0324-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0324-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0324-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - AT&T - Conflict 0325-2-T1 STA 1136 to 1178-2			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0325-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0325-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0325-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0325-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0325-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - AT&T - Conflict 0326-2-T1 STA 1136 to 1178-5			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0326-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0326-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0326-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0326-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0326-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - AT&T - Conflict 0327-2-T1 STA 1136 to 1178-4			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0327-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0327-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0327-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0327-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0327-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - AT&T - Conflict 0328-2-T1 STA 1136 to 1178-6			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0328-2-T1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0328-2-T1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0328-2-T1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0328-2-T1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	AT&T Plans and As-builts - Conflict 0328-2-T1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth			201	682	13-Apr-20	18-Jan-21
3C3 - City of FT Worth - Conflict 0145 STA 1380 to 1381			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0143-12-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0143-12-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0143-12-W1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth - Conflict 0148 STA 1397 to 1405			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0143-12-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0143-12-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0143-12-W1	5	682	12-Jan-21	18-Jan-21
3C3 - City of FT Worth - Conflict 0152 STA 1305 to 1340			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0143-12-W1	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	5	682	21-Dec-20	25-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0143-12-W1	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0143-12-W1	10	682	29-Dec-20	11-Jan-21
	TX-3CD	City of Ft. Worth As-builts - Conflict 0143-12-W1	5	682	12-Jan-21	18-Jan-21
3C3 - One Source			201	682	13-Apr-20	18-Jan-21
3C3 - One Source - Conflict 0908-1-FO4 STA 1346 to 1355			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0908-1-FO4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0908-1-FO4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0908-1-FO4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0908-1-FO4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0908-1-FO4	5	682	12-Jan-21	18-Jan-21
3C3 - Sunoco			201	682	13-Apr-20	18-Jan-21
3C2 - Sunoco - Conflict 168-4-G4 STA 994 SH170			201	682	13-Apr-20	18-Jan-21
	TX-3CD	Preparation of Sunoco Assembly Package - Conflict 168-4-G4	180	682	13-Apr-20	18-Dec-20
	TX-3CD	QA/QC Team Review Sunoco Assembly Package - Conflict 168-4-G4	5	682	21-Dec-20	25-Dec-20
	TX-3CD	Submit Sunoco Assembly Package - Conflict 168-4-G4	1	682	28-Dec-20	28-Dec-20
	TX-3CD	TxDOT Review Sunoco Assembly Package - Conflict 168-4-G4	10	682	29-Dec-20	11-Jan-21
	TX-3CD	Sunoco Final Inspection and As-builts - Conflict 168-4-G4	5	682	12-Jan-21	18-Jan-21
3C1 - Conflicts Eagle Pwky to SH 170 Sta-1028 to 1176			321	491	13-Apr-20	05-Jul-21
3C1 - Northbound Relocates			266	546	13-Apr-20	19-Apr-21
3C1 - AT&T			256	556	13-Apr-20	05-Apr-21
3C1 - AT&T - Conflict 0305-1-T1 STA 1122 to 1136			256	556	13-Apr-20	05-Apr-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0305-T1	200	556	13-Apr-20	15-Jan-21
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0305-T1	5	556	18-Jan-21	22-Jan-21
	TX-3CD	Submit AT&T Assembly Package - Conflict 0305-T1	1	556	25-Jan-21	25-Jan-21
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0305-T1	10	556	26-Jan-21	08-Feb-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0305-T1	20	556	09-Feb-21	08-Mar-21
	TX-3CD	AT&T Utility Civil Works - Conflict 0305-T1	10	556	09-Mar-21	22-Mar-21
	TX-3CD	AT&T Utility Installation - Conflict 0305-T1	10	556	09-Mar-21	22-Mar-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0305-T1	5	556	23-Mar-21	29-Mar-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0305-T1	5	556	30-Mar-21	05-Apr-21
3C1 - AT&T - Conflict 0306-1-FO1 STA 1122 to 1136			256	556	13-Apr-20	05-Apr-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0305-FO1	200	556	13-Apr-20	15-Jan-21
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0305-FO1	5	556	18-Jan-21	22-Jan-21
	TX-3CD	Submit AT&T Assembly Package - Conflict 0305-FO1	1	556	25-Jan-21	25-Jan-21
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0305-FO1	10	556	26-Jan-21	08-Feb-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0305-FO1	20	556	09-Feb-21	08-Mar-21
	TX-3CD	AT&T Utility Civil Works - Conflict 0305-FO1	10	556	09-Mar-21	22-Mar-21
	TX-3CD	AT&T Utility Installation - Conflict 0305-FO1	10	556	09-Mar-21	22-Mar-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0305-FO1	5	556	23-Mar-21	29-Mar-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0305-FO1	5	556	30-Mar-21	05-Apr-21
3C1 - City of FT Worth			261	524	13-Apr-20	12-Apr-21
3C1 - City of FT Worth - Conflict 0116 STA 1130 to 1132			261	524	13-Apr-20	12-Apr-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0116-16-W1	205	524	13-Apr-20	22-Jan-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0116-16-W1	5	524	25-Jan-21	29-Jan-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0116-16-W1	1	524	01-Feb-21	01-Feb-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0116-16-W1	10	524	02-Feb-21	15-Feb-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0116-16-W1	20	524	16-Feb-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0116-16-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0116-16-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0116-16-W1	5	524	30-Mar-21	05-Apr-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0116-16-W1	5	524	06-Apr-21	12-Apr-21
3C1 - City of FT Worth - Conflict 0117 STA 1130 to 1132			261	524	13-Apr-20	12-Apr-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0117-8-W1	205	524	13-Apr-20	22-Jan-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0117-8-W1	5	524	25-Jan-21	29-Jan-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0117-8-W1	1	524	01-Feb-21	01-Feb-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0117-8-W1	10	524	02-Feb-21	15-Feb-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0117-8-W1	20	524	16-Feb-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0117-8-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0117-8-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0117-8-W1	5	524	30-Mar-21	05-Apr-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0117-8-W1	5	524	06-Apr-21	12-Apr-21
3C1 - City of FT Worth - Conflict 0120 STA 1133 to 1133			261	524	13-Apr-20	12-Apr-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0120-8-W1	205	524	13-Apr-20	22-Jan-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0120-8-W1	5	524	25-Jan-21	29-Jan-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0120-8-W1	1	524	01-Feb-21	01-Feb-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0120-8-W1	10	524	02-Feb-21	15-Feb-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0120-8-W1	20	524	16-Feb-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0120-8-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0120-8-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0120-8-W1	5	524	30-Mar-21	05-Apr-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0120-8-W1	5	524	06-Apr-21	12-Apr-21
3C1 - City of FT Worth - Conflict 0121 STA 1133 to 1133			261	524	13-Apr-20	12-Apr-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0121-8-W1	205	524	13-Apr-20	22-Jan-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0121-8-W1	5	524	25-Jan-21	29-Jan-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0121-8-W1	1	524	01-Feb-21	01-Feb-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0121-8-W1	10	524	02-Feb-21	15-Feb-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0121-8-W1	20	524	16-Feb-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0121-8-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0121-8-W1	10	524	16-Mar-21	29-Mar-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0121-8-W1	5	524	30-Mar-21	05-Apr-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0121-8-W1	5	524	06-Apr-21	12-Apr-21
3C1 - Oncor			266	546	13-Apr-20	19-Apr-21
3C1 - Oncor - Conflict 1007-3-E2 STA 1122 to 1133			266	546	13-Apr-20	19-Apr-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1007-1-E2	210	546	13-Apr-20	29-Jan-21
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1007-1-E2	5	546	01-Feb-21	05-Feb-21
	TX-3CD	Submit Oncor Assembly Package - Conflict 1007-1-E2	1	546	08-Feb-21	08-Feb-21
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1007-1-E2	10	546	09-Feb-21	22-Feb-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1007-1-E2	20	546	23-Feb-21	22-Mar-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1007-1-E2	10	546	23-Mar-21	05-Apr-21
	TX-3CD	Oncor Utility Installation - Conflict 1007-1-E2	10	546	23-Mar-21	05-Apr-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1007-1-E2	5	546	06-Apr-21	12-Apr-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1007-1-E2	5	546	13-Apr-21	19-Apr-21
3C1 - Oncor - Conflict 1008-3-E2 STA 1131 to 1132			266	546	13-Apr-20	19-Apr-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1008-1-E2	210	546	13-Apr-20	29-Jan-21
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1008-1-E2	5	546	01-Feb-21	05-Feb-21
	TX-3CD	Submit Oncor Assembly Package - Conflict 1008-1-E2	1	546	08-Feb-21	08-Feb-21
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1008-1-E2	10	546	09-Feb-21	22-Feb-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1008-1-E2	20	546	23-Feb-21	22-Mar-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1008-1-E2	10	546	23-Mar-21	05-Apr-21
	TX-3CD	Oncor Utility Installation - Conflict 1008-1-E2	10	546	23-Mar-21	05-Apr-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1008-1-E2	5	546	06-Apr-21	12-Apr-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1008-1-E2	5	546	13-Apr-21	19-Apr-21
3C1 - Oncor - Conflict 1021-1-E2 STA 1159 to 1161			266	546	13-Apr-20	19-Apr-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1021-1-E2	210	546	13-Apr-20	29-Jan-21
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1021-1-E2	5	546	01-Feb-21	05-Feb-21
	TX-3CD	Submit Oncor Assembly Package - Conflict 1021-1-E2	1	546	08-Feb-21	08-Feb-21
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1021-1-E2	10	546	09-Feb-21	22-Feb-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1021-1-E2	20	546	23-Feb-21	22-Mar-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1021-1-E2	10	546	23-Mar-21	05-Apr-21
	TX-3CD	Oncor Utility Installation - Conflict 1021-1-E2	10	546	23-Mar-21	05-Apr-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1021-1-E2	5	546	06-Apr-21	12-Apr-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1021-1-E2	5	546	13-Apr-21	19-Apr-21
3C1 - Atmos Energy			196	616	13-Apr-20	11-Jan-21
3C1 - Atmos Energy - Conflict 1402-6-G1 STA 1116 to 1174			196	616	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 1402-6-G1	100	656	13-Apr-20	28-Aug-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 1402-6-G1	5	656	31-Aug-20	04-Sep-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 1402-6-G1	1	656	07-Sep-20	07-Sep-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 1402-6-G1	10	656	08-Sep-20	21-Sep-20
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 1402-6-G1	20	616	17-Nov-20	14-Dec-20
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 1402-6-G1	10	616	15-Dec-20	28-Dec-20
	TX-3CD	Atmos Energy Utility Installation - Conflict 1402-6-G1	10	616	15-Dec-20	28-Dec-20
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 1402-6-G1	5	616	29-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 1402-6-G1	5	616	05-Jan-21	11-Jan-21
3C1 - Crossing Relocates			321	464	13-Apr-20	05-Jul-21
3C1 - AT&T			211	373	13-Apr-20	01-Feb-21
3C1 - AT&T - Conflict 0307-1FO1 STA 1133			211	373	13-Apr-20	01-Feb-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0307-1-FO1	120	393	13-Apr-20	25-Sep-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0307-1-FO1	5	393	28-Sep-20	02-Oct-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0307-1-FO1	1	393	05-Oct-20	05-Oct-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0307-1-FO1	10	393	06-Oct-20	19-Oct-20
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0307-1-FO1	20	373	17-Nov-20	14-Dec-20
	TX-3CD	AT&T Utility Civil Works - Conflict 0307-1-FO1	10	373	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Utility Installation - Conflict 0307-1-FO1	10	373	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0307-1-FO1	20	373	29-Dec-20	25-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0307-1-FO1	5	373	26-Jan-21	01-Feb-21
3C1 - AT&T - Conflict 0308-2FO1 STA 1135			211	373	13-Apr-20	01-Feb-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0308-2-FO1	100	413	13-Apr-20	28-Aug-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0308-2-FO1	5	413	31-Aug-20	04-Sep-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0308-2-FO1	1	413	07-Sep-20	07-Sep-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0308-2-FO1	10	413	08-Sep-20	21-Sep-20
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0308-2-FO1	20	373	17-Nov-20	14-Dec-20
	TX-3CD	AT&T Utility Civil Works - Conflict 0308-2-FO1	10	373	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Utility Installation - Conflict 0308-2-FO1	10	373	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0308-2-FO1	20	373	29-Dec-20	25-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0308-2-FO1	5	373	26-Jan-21	01-Feb-21
3C1 - AT&T - Conflict 0309-2-T1 STA 1135			196	388	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0309-2-T1	100	428	13-Apr-20	28-Aug-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0309-2-T1	5	428	31-Aug-20	04-Sep-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0309-2-T1	1	428	07-Sep-20	07-Sep-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0309-2-T1	10	428	08-Sep-20	21-Sep-20
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0309-2-T1	20	388	17-Nov-20	14-Dec-20
	TX-3CD	AT&T Utility Civil Works - Conflict 0309-2-T1	10	388	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Utility Installation - Conflict 0309-2-T1	10	388	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0309-2-T1	5	388	29-Dec-20	04-Jan-21

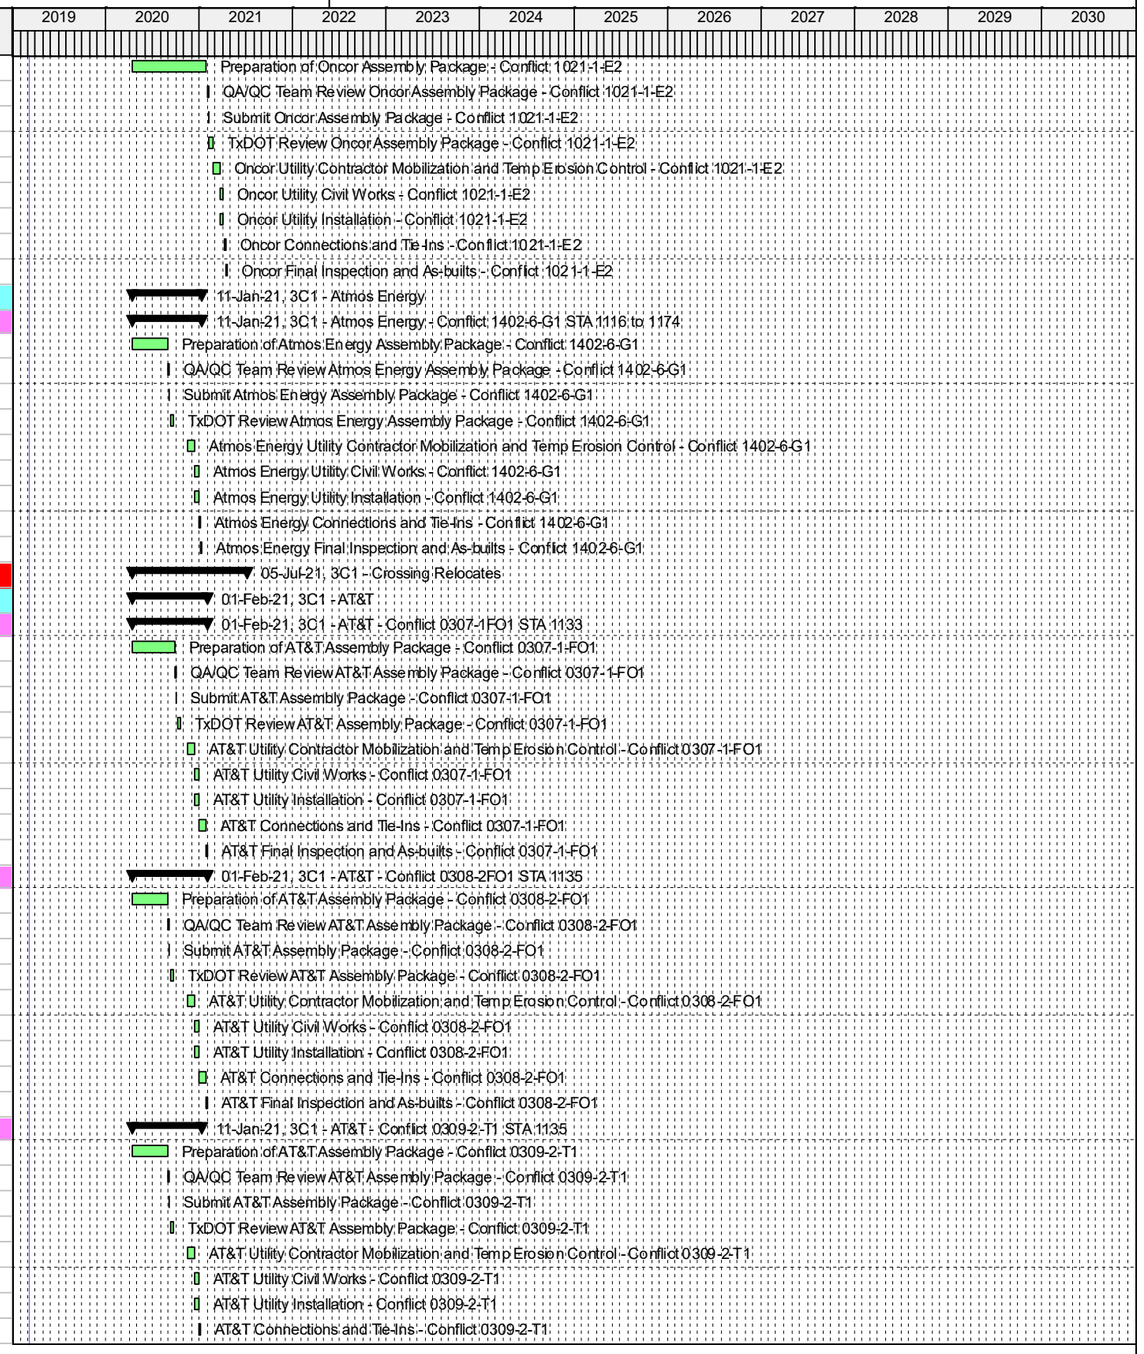

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0309-2-T1	5	388	05-Jan-21	11-Jan-21
3C1 - City of FT Worth			286	298	13-Apr-20	17-May-21
3C1 - City of FT Worth - Conflict 0118 STA 1133 to 1133			286	298	13-Apr-20	17-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 018-30-W1	225	298	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0118-30-W1	5	298	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0118-30-W1	1	298	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0118-30-W1	10	298	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0118-30-W1	20	298	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0118-30-W1	10	298	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0118-30-W1	10	298	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0118-30-W1	10	298	27-Apr-21	10-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0118-30-W1	5	298	11-May-21	17-May-21
3C1 - Fiberlight			196	397	13-Apr-20	11-Jan-21
3C1 - Fiberlight - Conflict 0501-1-FO6 STA 1133			196	397	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of Fiberlight Assembly Package - Conflict 0501-1-FO6	120	417	13-Apr-20	25-Sep-20
	TX-3CD	QA/QC Team Review Fiberlight Assembly Package - Conflict 0501-1-FO6	5	417	28-Sep-20	02-Oct-20
	TX-3CD	Submit Fiberlight Assembly Package - Conflict 0501-1-FO6	1	417	05-Oct-20	05-Oct-20
	TX-3CD	TxDOT Review Fiberlight Assembly Package - Conflict 0501-1-FO6	10	417	06-Oct-20	19-Oct-20
	TX-3CD	Fiberlight Utility Contractor Mobilization and Temp Erosion Control - Conflict 0501-1-FO6	20	397	17-Nov-20	14-Dec-20
	TX-3CD	Fiberlight Utility Civil Works - Conflict 0501-1-FO6	10	397	15-Dec-20	28-Dec-20
	TX-3CD	Fiberlight Utility Installation - Conflict 0501-1-FO6	10	397	15-Dec-20	28-Dec-20
	TX-3CD	Fiberlight Connections and Tie-Ins - Conflict 0501-1-FO6	5	397	29-Dec-20	04-Jan-21
	TX-3CD	Fiberlight Final Inspection and As-builts - Conflict 0501-1-FO6	5	397	05-Jan-21	11-Jan-21
3C1 - Verizon			216	377	13-Apr-20	08-Feb-21
3C1 - Verizon - Conflict 0802-3-FO3 STA 1133 to 1133			216	377	13-Apr-20	08-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0802-3-FO3	120	397	13-Apr-20	25-Sep-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0802-3-FO3	5	397	28-Sep-20	02-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0802-3-FO3	1	397	05-Oct-20	05-Oct-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0802-3-FO3	10	397	06-Oct-20	19-Oct-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0802-3-FO3	20	377	17-Nov-20	14-Dec-20
	TX-3CD	Verizon Utility Civil Works - Conflict 0802-3-FO3	15	377	15-Dec-20	04-Jan-21
	TX-3CD	Verizon Utility Installation - Conflict 0802-3-FO3	15	377	15-Dec-20	04-Jan-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0802-3-FO3	20	377	05-Jan-21	01-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0802-3-FO3	5	377	02-Feb-21	08-Feb-21
3C1 - Oncor			196	589	13-Apr-20	11-Jan-21
3C1 - Oncor - Conflict 1009-3-E2 STA 1131 to 1131			196	589	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1009-3-E2	125	604	13-Apr-20	02-Oct-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1009-3-E2	5	604	05-Oct-20	09-Oct-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1009-3-E2	1	604	12-Oct-20	12-Oct-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1009-3-E2	10	604	13-Oct-20	26-Oct-20
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1009-3-E2	20	589	17-Nov-20	14-Dec-20
	TX-3CD	Oncor Utility Civil Works - Conflict 1009-3-E2	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Oncor Utility Installation - Conflict 1009-3-E2	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1009-3-E2	5	589	29-Dec-20	04-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1009-3-E2	5	589	05-Jan-21	11-Jan-21
3C1 - Oncor - Conflict 1016-1-OHE1 STA 1079 to 1079			196	589	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1016-1-OHE1	125	604	13-Apr-20	02-Oct-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1016-1-OHE1	5	604	05-Oct-20	09-Oct-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1016-1-OHE1	1	604	12-Oct-20	12-Oct-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1016-1-OHE1	10	604	13-Oct-20	26-Oct-20
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1016-1-OHE1	20	589	17-Nov-20	14-Dec-20

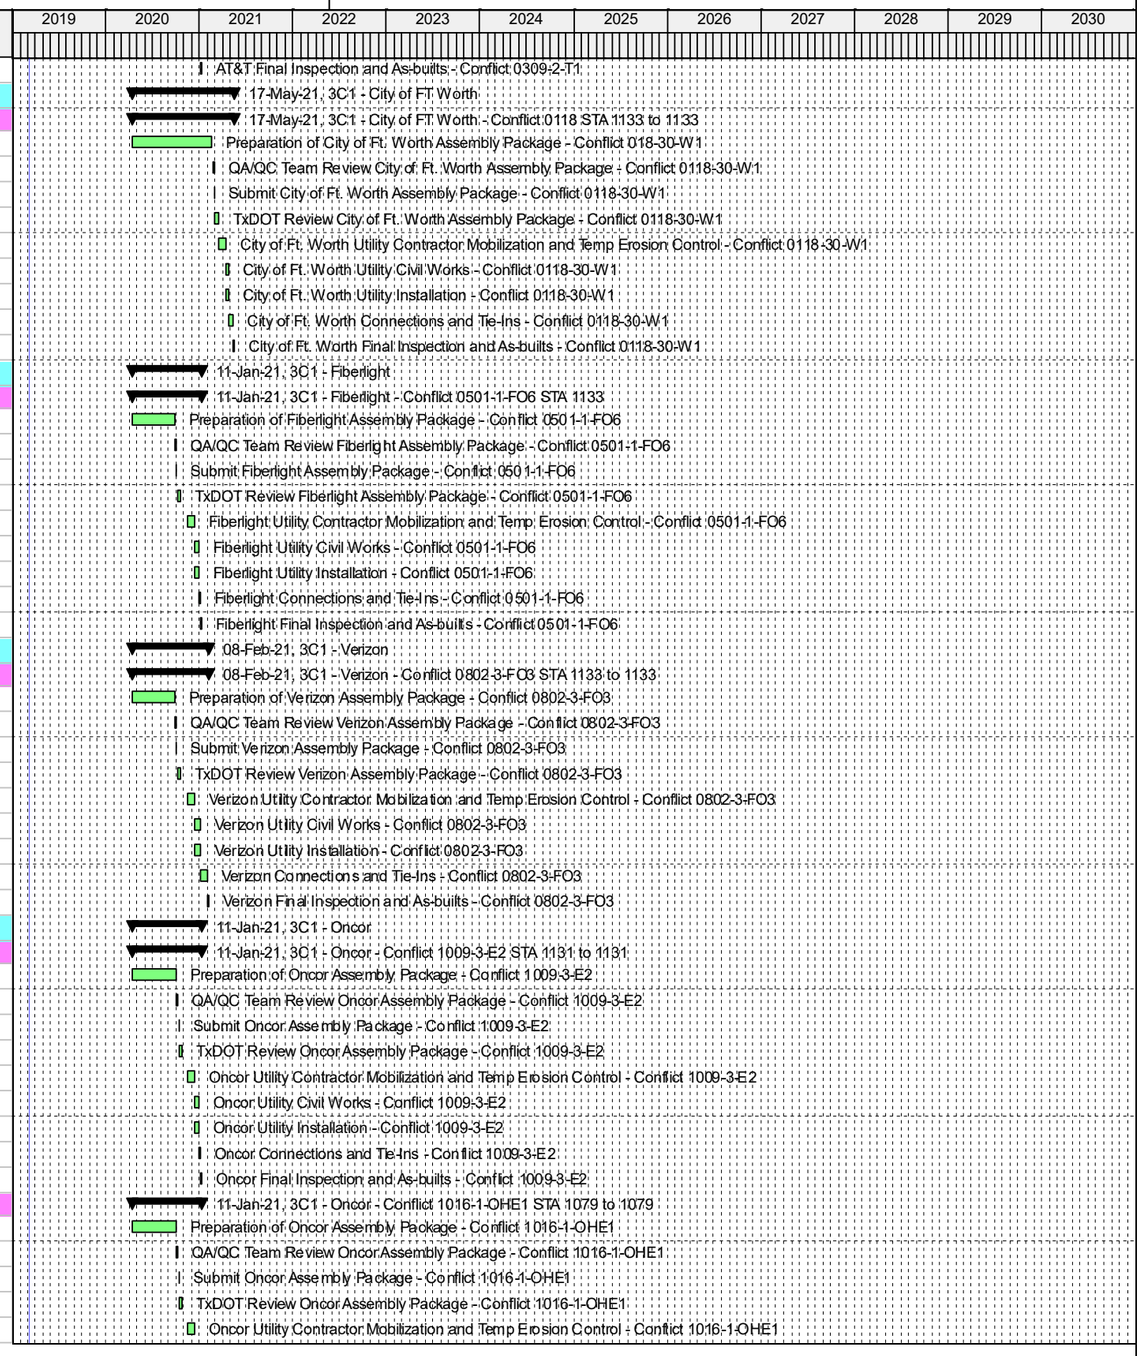

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Oncor Utility Civil Works - Conflict 1016-1-OHE1	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Oncor Utility Installation - Conflict 1016-1-OHE1	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1016-1-OHE1	5	589	29-Dec-20	04-Jan-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1016-1-OHE1	5	589	05-Jan-21	11-Jan-21
3C1 - Atmos Energy			196	589	13-Apr-20	11-Jan-21
3C1 - Atmos Energy - Conflict 1401-8-G1 STA 1116 to 1116			196	589	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 1401-6-G1	120	609	13-Apr-20	25-Sep-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 1401-6-G1	5	609	28-Sep-20	02-Oct-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 1401-6-G1	1	609	05-Oct-20	05-Oct-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 1401-6-G1	10	609	06-Oct-20	19-Oct-20
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 1401-6-G1	20	589	17-Nov-20	14-Dec-20
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 1401-6-G1	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Atmos Energy Utility Installation - Conflict 1401-6-G1	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 1401-6-G1	5	589	29-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 1401-6-G1	5	589	05-Jan-21	11-Jan-21
3C1 - Cowtown Pipeline			321	464	13-Apr-20	05-Jul-21
3C1 - Cowtown Pipeline - Conflict 1505-20-G2 STA 1032 to 1032			321	464	13-Apr-20	05-Jul-21
	TX-3CD	Preparation of Cowtown Pipeline Energy Assembly Package - Conflict 1505-20-G2	255	464	13-Apr-20	02-Apr-21
	TX-3CD	QA/QC Team Review Cowtown Pipeline Assembly Package - Conflict 1505-20-G2	5	464	05-Apr-21	09-Apr-21
	TX-3CD	Submit Cowtown Pipeline Assembly Package - Conflict 1505-20-G2	1	464	12-Apr-21	12-Apr-21
	TX-3CD	TxDOT Review Cowtown Pipeline Assembly Package - Conflict 1505-20-G2	10	464	13-Apr-21	26-Apr-21
	TX-3CD	Cowtown Pipeline Utility Contractor Mobilization and Temp Erosion Control - Conflict 1505-20-G2	20	464	27-Apr-21	24-May-21
	TX-3CD	Cowtown Pipeline Utility Civil Works - Conflict 1505-20-G2	20	464	25-May-21	21-Jun-21
	TX-3CD	Cowtown Pipeline Utility Installation - Conflict 1505-20-G2	10	474	25-May-21	07-Jun-21
	TX-3CD	Cowtown Pipeline Connections and Tie-Ins - Conflict 1505-20-G2	5	464	22-Jun-21	28-Jun-21
	TX-3CD	Cowtown Pipeline Final Inspection and As-builts - Conflict 1505-20-G2	5	464	29-Jun-21	05-Jul-21
3C1 - Zayo			196	589	13-Apr-20	11-Jan-21
3C1 - Zayo - Conflict 0701-1-FO5 STA 1133			196	589	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of Zayo Assembly Package - Conflict 0701-1-FO5	80	649	13-Apr-20	31-Jul-20
	TX-3CD	QA/QC Team Review Zayo Assembly Package - Conflict 0701-1-FO5	5	649	03-Aug-20	07-Aug-20
	TX-3CD	Submit Zayo Assembly Package - Conflict 0701-1-FO5	1	649	10-Aug-20	10-Aug-20
	TX-3CD	TxDOT Review Zayo Assembly Package - Conflict 0701-1-FO5	10	649	11-Aug-20	24-Aug-20
	TX-3CD	Zayo Utility Contractor Mobilization and Temp Erosion Control - Conflict 0701-1-FO5	20	589	17-Nov-20	14-Dec-20
	TX-3CD	Zayo Utility Civil Works - Conflict 0701-1-FO5	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Zayo Utility Installation - Conflict 0701-1-FO5	10	589	15-Dec-20	28-Dec-20
	TX-3CD	Zayo Connections and Tie-Ins - Conflict 0701-1-FO5	5	589	29-Dec-20	04-Jan-21
	TX-3CD	Zayo Final Inspection and As-builts - Conflict 0701-1-FO5	5	589	05-Jan-21	11-Jan-21
3C1 - Southbound Relocates			281	504	13-Apr-20	10-May-21
3C1 - City of FT Worth			281	504	13-Apr-20	10-May-21
3C1 - City of FT Worth - Conflict 0108 STA 1056 to 10567			281	504	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0108-24FM-WW1	225	504	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0108-24FM-WW1	5	504	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0108-24FM-WW1	1	504	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0108-24FM-WW1	10	504	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0108-24FM-WW1	20	504	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0108-24FM-WW1	10	504	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0108-24FM-WW1	10	504	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0108-24FM-WW1	5	504	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0108-24FM-WW1	5	504	04-May-21	10-May-21
3C1 - Oncor			281	504	13-Apr-20	10-May-21
3C1 - Oncor - Conflict 1011-1-E2 STA 1130 to 1134			281	504	13-Apr-20	10-May-21

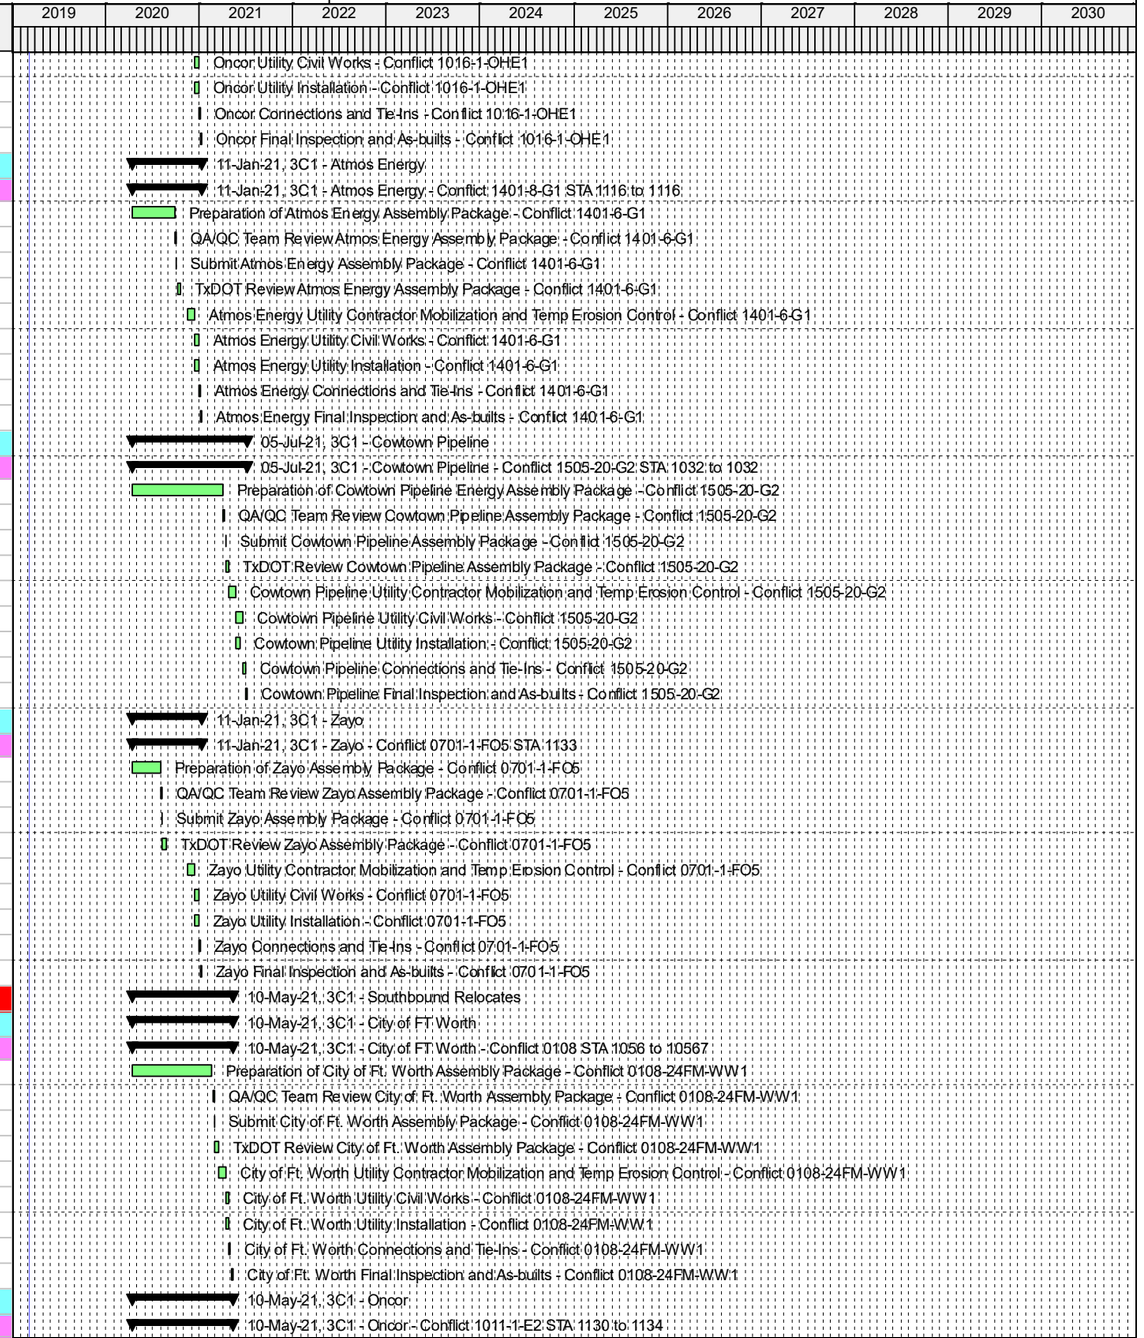

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1011-1-E2	225	504	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1011-1-E2	5	504	22-Feb-21	26-Feb-21
	TX-3CD	Submit Oncor Assembly Package - Conflict 1011-1-E2	1	504	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1011-1-E2	10	504	02-Mar-21	15-Mar-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1011-1-E2	20	504	16-Mar-21	12-Apr-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1011-1-E2	10	504	13-Apr-21	26-Apr-21
	TX-3CD	Oncor Utility Installation - Conflict 1011-1-E2	10	504	13-Apr-21	26-Apr-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1011-1-E2	5	504	27-Apr-21	03-May-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1011-1-E2	5	504	04-May-21	10-May-21
3C2 - Conflicts SH 170 to Golden Triangle Blvd Sta-1176 to 1280			291	521	13-Apr-20	24-May-21
3C2 - Northbound Relocates			291	521	13-Apr-20	24-May-21
3C2 - AT&T			196	616	13-Apr-20	11-Jan-21
3C2 - AT&T - Conflict 0315-1-T1 STA 1185 to 1277			196	616	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0315-T1	130	626	13-Apr-20	09-Oct-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0315-T1	5	626	12-Oct-20	16-Oct-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0315-T1	1	626	19-Oct-20	19-Oct-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0315-T1	10	626	20-Oct-20	02-Nov-20
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0315-T1	20	616	17-Nov-20	14-Dec-20
	TX-3CD	AT&T Utility Civil Works - Conflict 0315-T1	10	616	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Utility Installation - Conflict 0315-T1	10	616	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0315-T1	5	616	29-Dec-20	04-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0315-T1	5	616	05-Jan-21	11-Jan-21
3C2 - AT&T - Conflict 0317-1-FO1 STA 1243 to 1277			196	616	13-Apr-20	11-Jan-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0317-FO1	130	626	13-Apr-20	09-Oct-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0317-FO1	5	626	12-Oct-20	16-Oct-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0317-FO1	1	626	19-Oct-20	19-Oct-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0317-FO1	10	626	20-Oct-20	02-Nov-20
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0317-FO1	20	616	17-Nov-20	14-Dec-20
	TX-3CD	AT&T Utility Civil Works - Conflict 0317-FO1	10	616	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Utility Installation - Conflict 0317-FO1	10	616	15-Dec-20	28-Dec-20
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0317-FO1	5	616	29-Dec-20	04-Jan-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0317-FO1	5	616	05-Jan-21	11-Jan-21
3C2 - City of FT Worth			291	302	13-Apr-20	24-May-21
3C2 - City of FT Worth - Conflict 0125 STA 1243 to 1264			291	302	13-Apr-20	24-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0125-16-W1	225	302	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0125-16-W1	5	302	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0125-16-W1	1	302	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0125-16-W1	10	302	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0125-16-W1	20	302	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0125-16-W1	20	302	13-Apr-21	10-May-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0125-16-W1	20	302	13-Apr-21	10-May-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0125-16-W1	5	302	11-May-21	17-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0125-16-W1	5	302	18-May-21	24-May-21
3C2 - City of FT Worth - Conflict 0130 STA 1246 to 1264			281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0130-8-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0130-8-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0130-8-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0130-8-WW1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0130-8-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0130-8-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0130-8-WW1	10	312	13-Apr-21	26-Apr-21

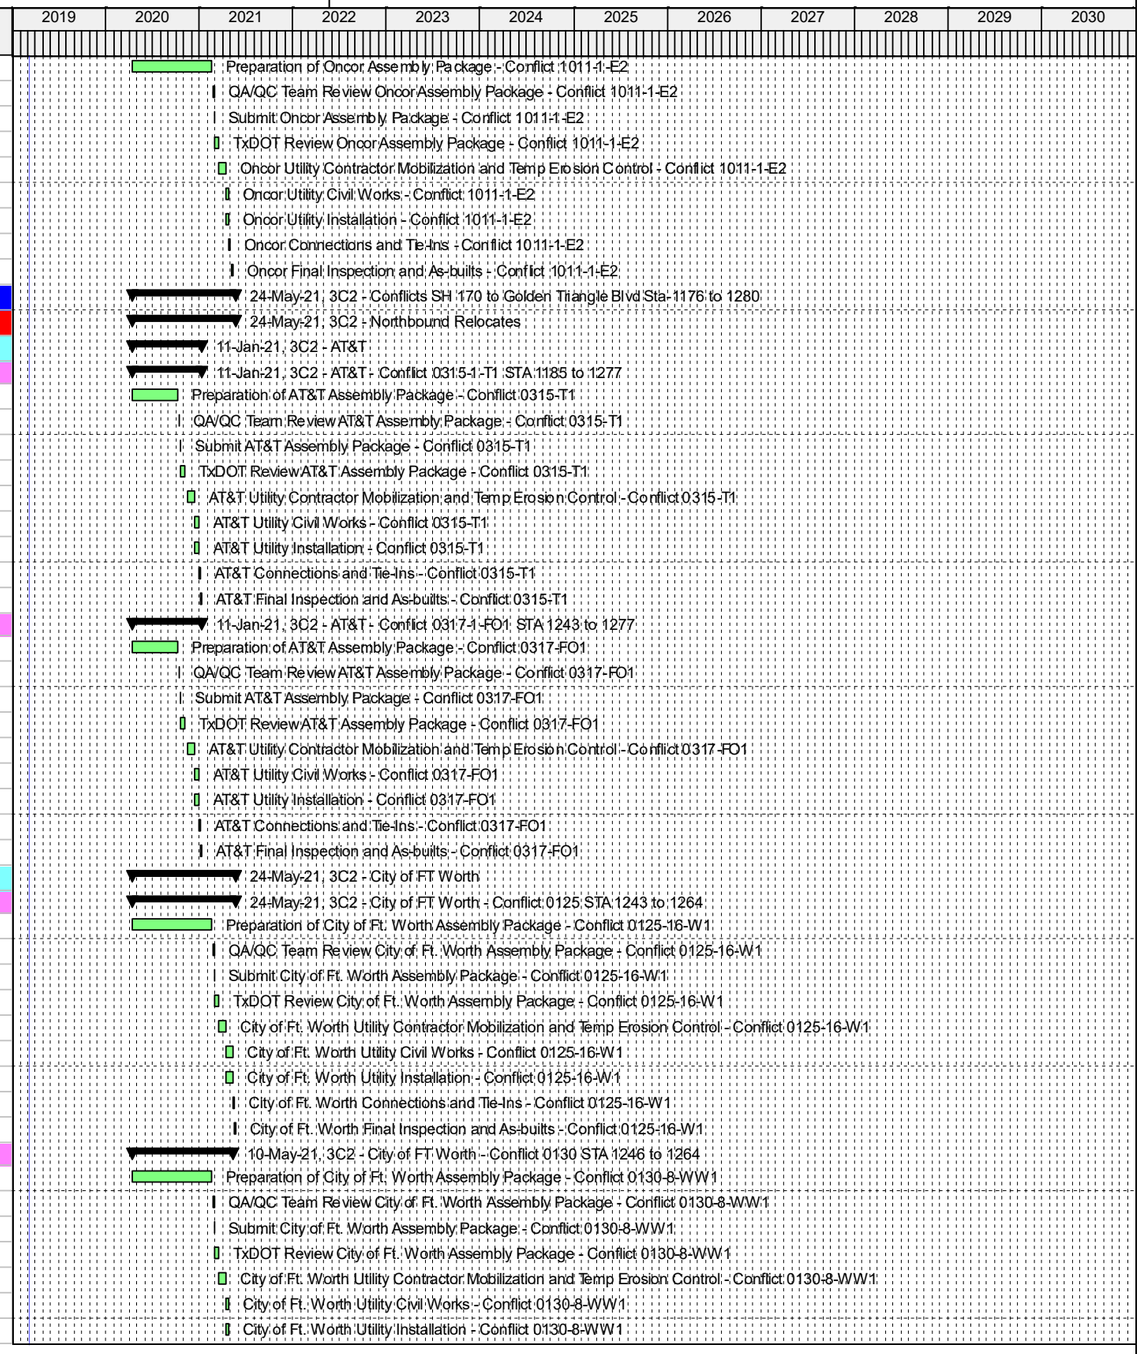

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0130-8-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0130-8-WW1	5	312	04-May-21	10-May-21
	3C2 - City of FT Worth - Conflict 0131 STA 1264 to 1274		281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0131-10-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0131-10-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0131-10-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0131-10-WW1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0131-10-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0131-10-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0131-10-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0131-10-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0131-10-WW1	5	312	04-May-21	10-May-21
	3C2 - City of FT Worth - Conflict 0132 STA 1274 to 1275		281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0132-15-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0132-15-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0132-15-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0132-15-WW1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0132-15-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0132-15-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0132-15-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0132-15-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0132-15-WW1	5	312	04-May-21	10-May-21
	3C2 - Tri-County Electric		217	376	13-Apr-20	09-Feb-21
	3C2 - Tri-County Electric - Conflict 0608-3-E1 STA 1133 to 1133		217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0608-3-E1	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0608-3-E1	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0608-3-E1	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0608-3-E1	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 0608-3-E1	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 0608-3-E1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 0608-3-E1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 0608-3-E1	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0608-3-E1	5	376	03-Feb-21	09-Feb-21
	3C2 - Verizon		227	366	13-Apr-20	23-Feb-21
	3C2 - Verizon - Conflict 0806-4-FO3 STA 1188 to 1245		217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0806-4-FO3	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0806-4-FO3	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0806-4-FO3	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0806-4-FO3	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0806-4-FO3	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Verizon Utility Civil Works - Conflict 0806-4-FO3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Utility Installation - Conflict 0806-4-FO3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0806-4-FO3	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0806-4-FO3	5	376	03-Feb-21	09-Feb-21
	3C2 - Verizon - Conflict 0807-5-FO3 STA 1245 to 1275		227	366	13-Apr-20	23-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0807-5-FO3	140	387	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0807-5-FO3	5	387	26-Oct-20	30-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0807-5-FO3	1	387	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0807-5-FO3	10	387	03-Nov-20	16-Nov-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0807-5-FO3	20	366	16-Dec-20	12-Jan-21
	TX-3CD	Verizon Utility Civil Works - Conflict 0807-5-FO3	15	366	13-Jan-21	02-Feb-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Verizon Utility Installation - Conflict 0807-5-FO3	15	366	13-Jan-21	02-Feb-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0807-5-FO3	10	366	03-Feb-21	16-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0807-5-FO3	5	366	17-Feb-21	23-Feb-21
3C2 - Verizon - Conflict 0808-1-T3 STA 1230 to 1268			217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0808-1-T3	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0808-1-T3	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0808-1-T3	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0808-1-T3	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0808-1-T3	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Verizon Utility Civil Works - Conflict 0808-1-T3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Utility Installation - Conflict 0808-1-T3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0808-1-T3	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0808-1-T3	5	376	03-Feb-21	09-Feb-21
3C2 - Verizon - Conflict 0809-2-FO3 STA 1244 to 1245			217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0809-2-FO3	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0809-2-FO3	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0809-2-FO3	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0809-2-FO3	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0809-2-FO3	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Verizon Utility Civil Works - Conflict 0809-2-FO3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Utility Installation - Conflict 0809-2-FO3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0809-2-FO3	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0809-2-FO3	5	376	03-Feb-21	09-Feb-21
3C2 - Verizon - Conflict 0810-1-T3 STA 1244 to 1245			217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0810-1-T3	140	393	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0810-1-T3	5	393	26-Oct-20	30-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0810-1-T3	1	393	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0810-1-T3	14	393	03-Nov-20	20-Nov-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0810-1-T3	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Verizon Utility Civil Works - Conflict 0810-1-T3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Utility Installation - Conflict 0810-1-T3	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0810-1-T3	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0810-1-T3	5	376	03-Feb-21	09-Feb-21
3C2 - Verizon - Conflict 0812-2-T3 STA 1228 to 1277			227	366	13-Apr-20	23-Feb-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 0812-1-OHT1	140	387	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 0812-1-OHT1	5	387	26-Oct-20	30-Oct-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 0812-1-OHT1	1	387	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 0812-1-OHT1	10	387	03-Nov-20	16-Nov-20
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 0812-1-OHT1	20	366	16-Dec-20	12-Jan-21
	TX-3CD	Verizon Utility Civil Works - Conflict 0812-1-OHT1	20	366	13-Jan-21	09-Feb-21
	TX-3CD	Verizon Utility Installation - Conflict 0812-1-OHT1	20	366	13-Jan-21	09-Feb-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 0812-1-OHT1	5	366	10-Feb-21	16-Feb-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 0812-1-OHT1	5	366	17-Feb-21	23-Feb-21
3C2 - Oncor			217	376	13-Apr-20	09-Feb-21
3C2 - Oncor - Conflict 1017-1-OHE1 STA 1180 to 1228			217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1017-1-OHE1	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1017-1-OHE1	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1017-1-OHE1	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1017-1-OHE1	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1017-1-OHE1	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1017-1-OHE1	10	376	13-Jan-21	26-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Oncor Utility Installation - Conflict 1017-1-OHE1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1017-1-OHE1	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1017-1-OHE1	5	376	03-Feb-21	09-Feb-21
3C2 - Oncor - Conflict 1018-1-OHE1 STA 1200 to 1205			217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1018-1-OHE1	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1018-1-OHE1	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1018-1-OHE1	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1018-1-OHE1	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1018-1-OHE1	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1018-1-OHE1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Oncor Utility Installation - Conflict 1018-1-OHE1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1018-1-OHE1	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1018-1-OHE1	5	376	03-Feb-21	09-Feb-21
3C2 - Oncor - Conflict 1020-1-OHE1 STA 1227 to 1343			217	376	13-Apr-20	09-Feb-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1020-1-OHE1	140	397	13-Apr-20	23-Oct-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1020-1-OHE1	5	397	26-Oct-20	30-Oct-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1020-1-OHE1	1	397	02-Nov-20	02-Nov-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1020-1-OHE1	10	397	03-Nov-20	16-Nov-20
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1020-1-OHE1	20	376	16-Dec-20	12-Jan-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1020-1-OHE1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Oncor Utility Installation - Conflict 1020-1-OHE1	10	376	13-Jan-21	26-Jan-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1020-1-OHE1	5	376	27-Jan-21	02-Feb-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1020-1-OHE1	5	376	03-Feb-21	09-Feb-21
3C2 - Atmos Energy			236	357	13-Apr-20	08-Mar-21
3C2 - Atmos Energy - Conflict 1407-6-G1 STA 1243 to 1258			236	357	13-Apr-20	08-Mar-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 1407-6-G1	175	357	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 1407-6-G1	5	357	14-Dec-20	18-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 1407-6-G1	1	357	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 1407-6-G1	10	357	22-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 1407-6-G1	20	357	05-Jan-21	01-Feb-21
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 1407-6-G1	15	357	02-Feb-21	22-Feb-21
	TX-3CD	Atmos Energy Utility Installation - Conflict 1407-6-G1	15	357	02-Feb-21	22-Feb-21
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 1407-6-G1	5	357	23-Feb-21	01-Mar-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 1407-6-G1	5	357	02-Mar-21	08-Mar-21
3C2 - Crossing Relocates			291	521	13-Apr-20	24-May-21
3C2 - City of FT Worth			281	394	13-Apr-20	10-May-21
3C2 - City of FT Worth - Conflict 0126 STA 1264 to 1264			281	394	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0126-36-W1	225	394	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0126-36-W1	5	394	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0126-36-W1	1	394	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0126-36-W1	10	394	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0126-36-W1	20	394	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0126-36-W1	10	394	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0126-36-W1	10	394	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0126-36-W1	5	394	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0126-36-W1	5	394	04-May-21	10-May-21
3C2 - City of FT Worth - Conflict 0133 STA 1274 to 1274			281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0133-30-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0133-30-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0133-30-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0133-30-WW1	10	312	02-Mar-21	15-Mar-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0133-30-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0133-30-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0133-30-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0133-30-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0133-30-WW1	5	312	04-May-21	10-May-21
3C2 - Centurylink			231	353	13-Apr-20	01-Mar-21
3C2 - Centurylink - Conflict 0401-1-FO7 STA 1276			231	353	13-Apr-20	01-Mar-21
	TX-3CD	Preparation of Centurylink Assembly Package - Conflict 0401-1-FO7	175	353	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Centurylink Assembly Package - Conflict 0401-1-FO7	5	353	14-Dec-20	18-Dec-20
	TX-3CD	Submit Centurylink Assembly Package - Conflict 0401-1-FO7	1	353	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Centurylink Assembly Package - Conflict 0401-1-FO7	10	353	22-Dec-20	04-Jan-21
	TX-3CD	Centurylink Utility Contractor Mobilization and Temp Erosion Control - Conflict 0401-1-FO7	20	353	05-Jan-21	01-Feb-21
	TX-3CD	Centurylink Utility Civil Works - Conflict 0401-1-FO7	10	353	02-Feb-21	15-Feb-21
	TX-3CD	Centurylink Utility Installation - Conflict 0401-1-FO7	10	353	02-Feb-21	15-Feb-21
	TX-3CD	Centurylink Connections and Tie-Ins - Conflict 0401-1-FO7	5	353	16-Feb-21	22-Feb-21
	TX-3CD	Centurylink Final Inspection and As-builts - Conflict 0401-1-FO7	5	353	23-Feb-21	01-Mar-21
3C2 - Tri-County Electric			231	362	13-Apr-20	01-Mar-21
3C2 - Tri-County Electric - Conflict 0603-1-OHE2 STA 1243 to 1243			231	362	13-Apr-20	01-Mar-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 0603-1-OHE2	175	362	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 0603-1-OHE2	5	362	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 0603-1-OHE2	1	362	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 0603-1-OHE2	10	362	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 0603-1-OHE2	20	362	05-Jan-21	01-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 0603-1-OHE2	10	362	02-Feb-21	15-Feb-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 0603-1-OHE2	10	362	02-Feb-21	15-Feb-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 0603-1-OHE2	5	362	16-Feb-21	22-Feb-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 0603-1-OHE2	5	362	23-Feb-21	01-Mar-21
3C2 - One Source			231	581	13-Apr-20	01-Mar-21
3C2 - One Source - Conflict 0903-3-FO4 STA 1243 to 1243			231	581	13-Apr-20	01-Mar-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0903-3-FO4	175	581	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0903-3-FO4	5	581	14-Dec-20	18-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0903-3-FO4	1	581	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0903-3-FO4	10	581	22-Dec-20	04-Jan-21
	TX-3CD	One Source Utility Contractor Mobilization and Temp Erosion Control - Conflict 0903-3-FO4	20	581	05-Jan-21	01-Feb-21
	TX-3CD	One Source Utility Civil Works - Conflict 0903-3-FO4	10	581	02-Feb-21	15-Feb-21
	TX-3CD	One Source Utility Installation - Conflict 0903-3-FO4	10	581	02-Feb-21	15-Feb-21
	TX-3CD	One Source Connections and Tie-Ins - Conflict 0903-3-FO4	5	581	16-Feb-21	22-Feb-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0903-3-FO4	5	581	23-Feb-21	01-Mar-21
3C2 - Oncor			231	362	13-Apr-20	01-Mar-21
3C2 - Oncor - Conflict 1019-1-OHE1 STA 1227 to 1227			231	362	13-Apr-20	01-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 1019-1-OHE1	175	362	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 1019-1-OHE1	5	362	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 1019-1-OHE1	1	362	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 1019-1-OHE1	10	362	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 1019-1-OHE1	20	362	05-Jan-21	01-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 1019-1-OHE1	10	362	02-Feb-21	15-Feb-21
	TX-3CD	Oncor Utility Installation - Conflict 1019-1-OHE1	10	362	02-Feb-21	15-Feb-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 1019-1-OHE1	5	362	16-Feb-21	22-Feb-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 1019-1-OHE1	5	362	23-Feb-21	01-Mar-21
3C2 - Sunoco			281	312	13-Apr-20	10-May-21
3C2 - Sunoco - Conflict 1301-16-G4 STA 1184 to 1195			281	312	13-Apr-20	10-May-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Preparation of Sunoco Assembly Package - Conflict 1301-16-G4	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review Sunoco Assembly Package - Conflict 1301-16-G4	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit Sunoco Assembly Package - Conflict 1301-16-G4	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review Sunoco Assembly Package - Conflict 1301-16-G4	10	312	02-Mar-21	15-Mar-21
	TX-3CD	Sunoco Utility Contractor Mobilization and Temp Erosion Control - Conflict 1301-16-G4	20	312	16-Mar-21	12-Apr-21
	TX-3CD	Sunoco Utility Civil Works - Conflict 1301-16-G4	10	312	13-Apr-21	26-Apr-21
	TX-3CD	Sunoco Utility Installation - Conflict 1301-16-G4	10	312	13-Apr-21	26-Apr-21
	TX-3CD	Sunoco Connections and Tie-Ins - Conflict 1301-16-G4	5	312	27-Apr-21	03-May-21
	TX-3CD	Sunoco Final Inspection and As-builts - Conflict 1301-16-G4	5	312	04-May-21	10-May-21
3C2 - CrossTex Energy			291	302	13-Apr-20	24-May-21
3C2 - CrossTex Energy - Conflict 1601-10-G5 STA 1194 to 1194			291	302	13-Apr-20	24-May-21
	TX-3CD	Preparation of Cross Tex Energy Assembly Package - Conflict 1601-20-G2	225	302	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review Cross Tex Energy Assembly Package - Conflict 1601-20-G2	5	302	22-Feb-21	26-Feb-21
	TX-3CD	Submit Cross Tex Energy Assembly Package - Conflict 1601-20-G2	1	302	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review Cross Tex Energy Assembly Package - Conflict 1601-20-G2	10	302	02-Mar-21	15-Mar-21
	TX-3CD	Cross Tex Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 1601-20-G2	20	302	16-Mar-21	12-Apr-21
	TX-3CD	Cross Tex Energy Utility Civil Works - Conflict 1601-20-G2	20	302	13-Apr-21	10-May-21
	TX-3CD	Cross Tex Energy Utility Installation - Conflict 1601-20-G2	20	302	13-Apr-21	10-May-21
	TX-3CD	Cross Tex Energy Connections and Tie-Ins - Conflict 1601-20-G2	5	302	11-May-21	17-May-21
	TX-3CD	Cross Tex Energy Final Inspection and As-builts - Conflict 1601-20-G2	5	302	18-May-21	24-May-21
3C2 - Southbound Relocates			281	312	13-Apr-20	10-May-21
3C2 - AT&T			231	362	13-Apr-20	01-Mar-21
3C2 - AT&T - Conflict 0319-2-T1 STA 1277 to 1277			231	362	13-Apr-20	01-Mar-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0319-2-T1	175	362	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0319-2-T1	5	362	14-Dec-20	18-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0319-2-T1	1	362	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0319-2-T1	10	362	22-Dec-20	04-Jan-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0319-2-T1	20	362	05-Jan-21	01-Feb-21
	TX-3CD	AT&T Utility Civil Works - Conflict 0319-2-T1	10	362	02-Feb-21	15-Feb-21
	TX-3CD	AT&T Utility Installation - Conflict 0319-2-T1	10	362	02-Feb-21	15-Feb-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0319-2-T1	5	362	16-Feb-21	22-Feb-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0319-2-T1	5	362	23-Feb-21	01-Mar-21
3C2 - City of FT Worth			281	312	13-Apr-20	10-May-21
3C2 - City of FT Worth - Conflict 0127 STA 1244 to 1264			281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0127-12-W1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0127-12-W1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0127-12-W1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0127-12-W1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0127-12-W1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0127-12-W1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0127-12-W1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0127-12-W1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0127-12-W1	5	312	04-May-21	10-May-21
3C2 - City of FT Worth - Conflict 0128 STA 1264 to 1276			281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0128-24-W1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0128-24-W1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0128-24-W1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0128-24-W1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0128-24-W1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0128-24-W1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0128-24-W1	10	312	13-Apr-21	26-Apr-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0128-24-W1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0128-24-W1	5	312	04-May-21	10-May-21
	3C2 - City of FT Worth - Conflict 0129 STA 1264 to 1276		281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0129-12-W1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0129-12-W1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0129-12-W1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0129-12-W1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0129-12-W1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0129-12-W1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0129-12-W1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0129-12-W1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0129-12-W1	5	312	04-May-21	10-May-21
	3C2 - City of FT Worth - Conflict 0134 STA 1254 to 1274		281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0134-8-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0134-8-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0134-8-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0134-8-WW1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0134-8-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0134-8-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0134-8-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0134-8-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0134-8-WW1	5	312	04-May-21	10-May-21
	3C2 - City of FT Worth - Conflict 0135 STA 1274 to 1276		281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0135-15-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0135-15-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0135-15-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0135-15-WW1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0135-15-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0135-15-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0135-15-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0135-15-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0135-15-WW1	5	312	04-May-21	10-May-21
	3C2 - City of FT Worth - Conflict 0136 STA 1276 to 1281		281	312	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0136-10-WW1	225	312	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0136-10-WW1	5	312	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0136-10-WW1	1	312	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0136-10-WW1	10	312	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0136-10-WW1	20	312	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0136-10-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0136-10-WW1	10	312	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0136-10-WW1	5	312	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0136-10-WW1	5	312	04-May-21	10-May-21
	3C3 - Conflicts Golden Triangle Blvd to N. Tarant Pkwy Sta-1280 to 1401		281	531	13-Apr-20	10-May-21
	3C3 - Northbound Relocates		257	418	13-Apr-20	06-Apr-21
	3C3 - AT&T		257	418	13-Apr-20	06-Apr-21
	3C3 - AT&T - Conflict 0329-2-FO1 STA 1276 to 1347		257	418	13-Apr-20	06-Apr-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0329-2-FO1	175	429	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0329-2-FO1	5	429	14-Dec-20	18-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0329-2-FO1	1	429	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0329-2-FO1	10	429	22-Dec-20	04-Jan-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0329-2-FO1	20	418	20-Jan-21	16-Feb-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	AT&T Utility Civil Works - Conflict 0329-2-FO1	20	418	17-Feb-21	16-Mar-21
	TX-3CD	AT&T Utility Installation - Conflict 0329-2-FO1	20	418	17-Feb-21	16-Mar-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0329-2-FO1	10	418	17-Mar-21	30-Mar-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0329-2-FO1	5	418	31-Mar-21	06-Apr-21
3C3 - Verizon			242	433	13-Apr-20	16-Mar-21
3C3 - Verizon - Conflict 105-4-FO3 STA 1003 SH170 to 1026 SH170			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 105-4-FO3	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 105-4-FO3	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 105-4-FO3	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 105-4-FO3	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 105-4-FO3	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Verizon Utility Civil Works - Conflict 105-4-FO3	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Verizon Utility Installation - Conflict 105-4-FO3	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 105-4-FO3	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 105-4-FO3	5	433	10-Mar-21	16-Mar-21
3C3 - Verizon - Conflict 106-1-FO3 STA 1005 SH170 to 1026 SH170			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 106-1-FO3	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 106-1-FO3	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 106-1-FO3	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 106-1-FO3	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 106-1-FO3	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Verizon Utility Civil Works - Conflict 106-1-FO3	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Verizon Utility Installation - Conflict 106-1-FO3	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 106-1-FO3	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 106-1-FO3	5	433	10-Mar-21	16-Mar-21
3C3 - Verizon - Conflict 107-1-T3 STA 1003 SH170 to 1026 SH170			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Verizon Assembly Package - Conflict 107-1-T3	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Verizon Assembly Package - Conflict 107-1-T3	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Verizon Assembly Package - Conflict 107-1-T3	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Verizon Assembly Package - Conflict 107-1-T3	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Verizon Utility Contractor Mobilization and Temp Erosion Control - Conflict 107-1-T3	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Verizon Utility Civil Works - Conflict 107-1-T3	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Verizon Utility Installation - Conflict 107-1-T3	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Verizon Connections and Tie-Ins - Conflict 107-1-T3	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Verizon Final Inspection and As-builts - Conflict 107-1-T3	5	433	10-Mar-21	16-Mar-21
3C3 - Tri-County Electric			257	418	13-Apr-20	06-Apr-21
3C2 - Tri-County Electric - Conflict 0604-2-OHE1 STA 1276 to 1342			257	418	13-Apr-20	06-Apr-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 083-2-OHE1	175	429	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 083-2-OHE1	5	429	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 083-2-OHE1	1	429	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 083-2-OHE1	10	429	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 083-2-OHE1	20	418	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 083-2-OHE1	20	418	17-Feb-21	16-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 083-2-OHE1	20	418	17-Feb-21	16-Mar-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 083-2-OHE1	10	418	17-Mar-21	30-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 083-2-OHE1	5	418	31-Mar-21	06-Apr-21
3C2 - Tri-County Electric - Conflict 0607-2-E1 STA 1292 to 1386			257	418	13-Apr-20	06-Apr-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 086-2-E1	175	429	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 086-2-E1	5	429	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 086-2-E1	1	429	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 086-2-E1	10	429	22-Dec-20	04-Jan-21

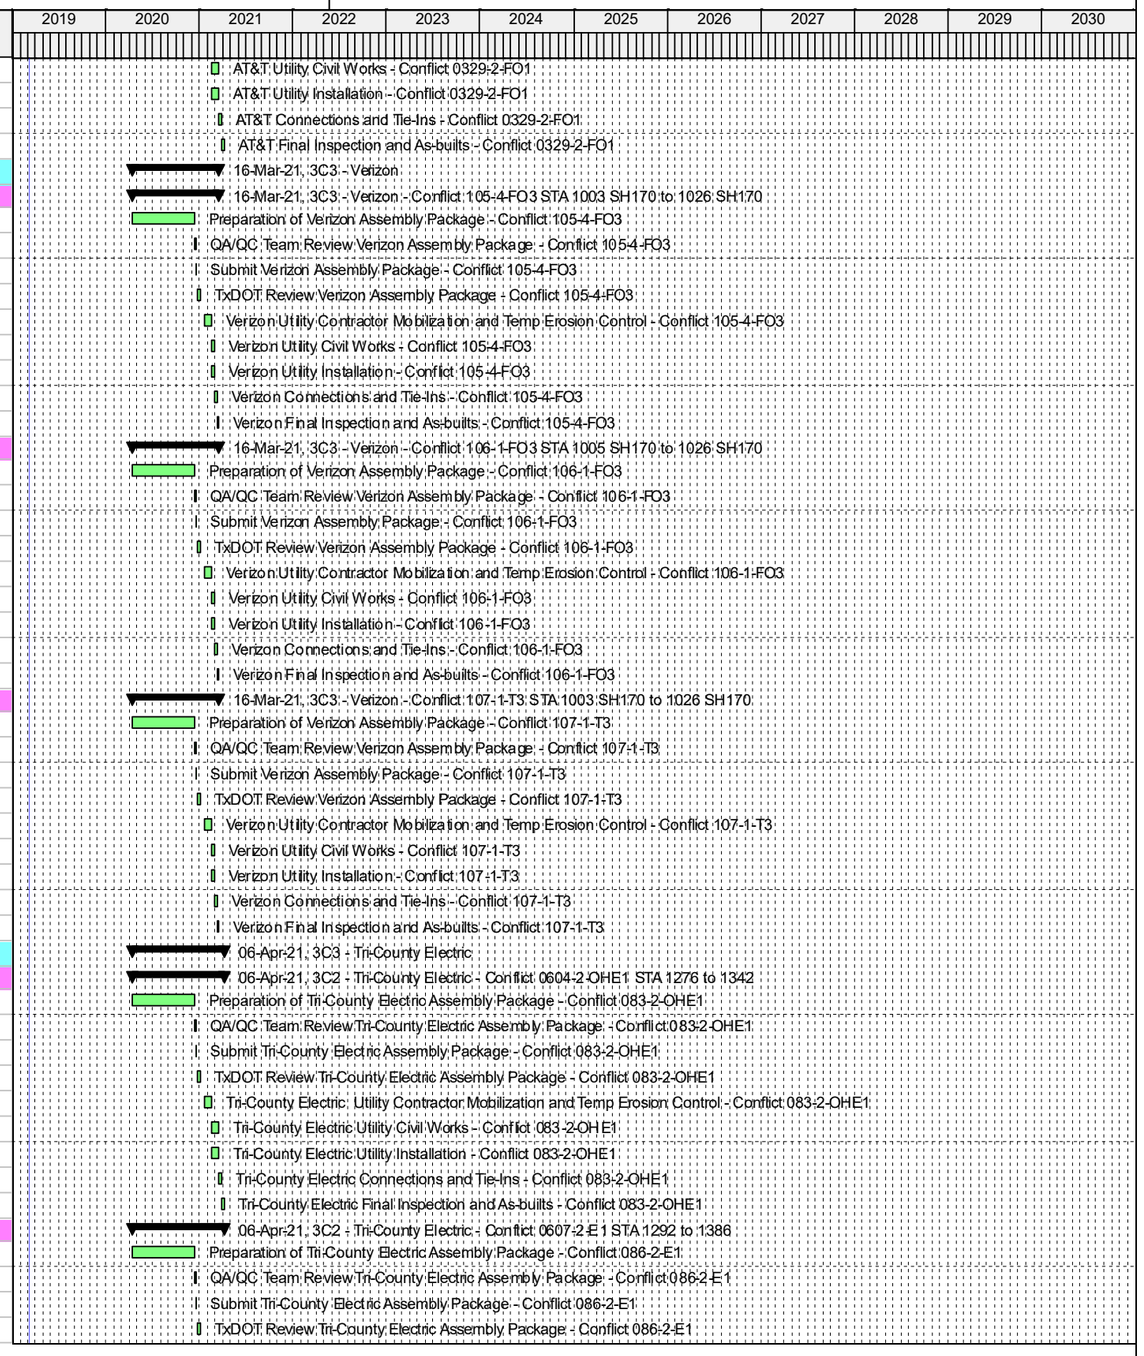

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 086-2-E1	20	418	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 086-2-E1	20	418	17-Feb-21	16-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 086-2-E1	20	418	17-Feb-21	16-Mar-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 086-2-E1	10	418	17-Mar-21	30-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 086-2-E1	5	418	31-Mar-21	06-Apr-21
3C2 - Tri-County Electric - Conflict 0608-2-E1 STA 1276 to 1342			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 087-2-E1	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 087-2-E1	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 087-2-E1	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 087-2-E1	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 087-2-E1	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 087-2-E1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 087-2-E1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 087-2-E1	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 087-2-E1	5	433	10-Mar-21	16-Mar-21
3C3 - Oncor			242	433	13-Apr-20	16-Mar-21
3C3 - Oncor - Conflict 143-1-E2 STA 1349 to 1349			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 143-1-E2	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 143-1-E2	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 143-1-E2	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 143-1-E2	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 143-1-E2	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 143-1-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 143-1-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 143-1-E2	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 143-1-E2	5	433	10-Mar-21	16-Mar-21
3C3 - Oncor - Conflict 144-1-E2 STA 1400 to 1400			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 144-1-E2	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 144-1-E2	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 144-1-E2	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 144-1-E2	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 144-1-E2	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 144-1-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 144-1-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 144-1-E2	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 144-1-E2	5	433	10-Mar-21	16-Mar-21
3C3 - Oncor - Conflict 145-3-E2 STA 1003 SH170 to 1003 SH170			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 145-3-E2	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 145-3-E2	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 145-3-E2	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 145-3-E2	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 145-3-E2	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 145-3-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 145-3-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 145-3-E2	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 145-3-E2	5	433	10-Mar-21	16-Mar-21
3C3 - Oncor - Conflict 149-1-OHE2 STA 1387 to 1400			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 149-3-OHE2	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 149-3-OHE2	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 149-3-OHE2	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 149-3-OHE2	10	444	22-Dec-20	04-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 149-3-OHE2	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 149-3-OHE2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 149-3-OHE2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 149-3-OHE2	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 149-3-OHE2	5	433	10-Mar-21	16-Mar-21
3C3 - Atmos Energy			242	433	13-Apr-20	16-Mar-21
3C3 - Atmos Energy - Conflict 175-6-G1 STA 1352 to 1361			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 175-6-G1	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 175-6-G1	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 175-6-G1	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 175-6-G1	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 175-6-G1	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 175-6-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Utility Installation - Conflict 175-6-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 175-6-G1	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 175-6-G1	5	433	10-Mar-21	16-Mar-21
3C3 - Atmos Energy - Conflict 176-6-G1 STA 1364 to 1387			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 176-6-G1	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 176-6-G1	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 176-6-G1	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 176-6-G1	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 176-6-G1	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 176-6-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Utility Installation - Conflict 176-6-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 176-6-G1	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 176-6-G1	5	433	10-Mar-21	16-Mar-21
3C3 - Atmos Energy - Conflict 181-6-G1 STA 1340 to 1343			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 181-6-G1	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 181-6-G1	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 181-6-G1	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 181-6-G1	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 181-6-G1	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 181-6-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Utility Installation - Conflict 181-6-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 181-6-G1	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 181-6-G1	5	433	10-Mar-21	16-Mar-21
3C3 - Private Electric			242	433	13-Apr-20	16-Mar-21
3C3 - Private Electric - Conflict 198-1-E5 STA 1348 to 1351			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Private Electric Assembly Package - Conflict 198-1-E5	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Private Electric Assembly Package - Conflict 198-1-E5	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Private Electric Assembly Package - Conflict 198-1-E5	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Private Electric Assembly Package - Conflict 198-1-E5	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Private Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 198-1-E5	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Private Electric Utility Civil Works - Conflict 198-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Utility Installation - Conflict 198-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Connections and Tie-Ins - Conflict 198-1-E5	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Private Electric Final Inspection and As-builts - Conflict 198-1-E5	5	433	10-Mar-21	16-Mar-21
3C3 - Private Electric - Conflict 199-1-E5 STA 1352 to 1361			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Private Electric Assembly Package - Conflict 199-1-E5	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Private Electric Assembly Package - Conflict 199-1-E5	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Private Electric Assembly Package - Conflict 199-1-E5	1	444	21-Dec-20	21-Dec-20

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	TxDOT Review Private Electric Assembly Package - Conflict 199-1-E5	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Private Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 199-1-E5	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Private Electric Utility Civil Works - Conflict 199-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Utility Installation - Conflict 199-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Connections and Tie-Ins - Conflict 199-1-E5	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Private Electric Final Inspection and As-builts - Conflict 199-1-E5	5	433	10-Mar-21	16-Mar-21
3C3 - Private Electric - Conflict 200-1-E5 STA 1367 to 1372			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Private Electric Assembly Package - Conflict 200-1-E5	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Private Electric Assembly Package - Conflict 200-1-E5	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Private Electric Assembly Package - Conflict 200-1-E5	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Private Electric Assembly Package - Conflict 200-1-E5	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Private Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 200-1-E5	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Private Electric Utility Civil Works - Conflict 200-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Utility Installation - Conflict 200-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Connections and Tie-Ins - Conflict 200-1-E5	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Private Electric Final Inspection and As-builts - Conflict 200-1-E5	5	433	10-Mar-21	16-Mar-21
3C3 - Private Electric - Conflict 201-1-E5 STA 1396 to 1397			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Private Electric Assembly Package - Conflict 201-1-E5	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Private Electric Assembly Package - Conflict 201-1-E5	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Private Electric Assembly Package - Conflict 201-1-E5	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Private Electric Assembly Package - Conflict 201-1-E5	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Private Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 201-1-E5	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Private Electric Utility Civil Works - Conflict 201-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Utility Installation - Conflict 201-1-E5	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Private Electric Connections and Tie-Ins - Conflict 201-1-E5	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Private Electric Final Inspection and As-builts - Conflict 201-1-E5	5	433	10-Mar-21	16-Mar-21
3C3 - Crossing Relocates			281	531	13-Apr-20	10-May-21
3C3 - City of FT Worth			281	394	13-Apr-20	10-May-21
3C3 - City of FT Worth - Conflict 0137 STA 1343 to 1343			281	394	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0137-42-W1	225	394	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0137-42-W1	5	394	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0137-42-W1	1	394	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0137-42-W1	10	394	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0137-42-W1	20	394	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0137-42-W1	10	394	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0137-42-W1	10	394	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0137-42-W1	5	394	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0137-42-W1	5	394	04-May-21	10-May-21
3C3 - City of FT Worth - Conflict 0138 STA 1346 to 1346			281	394	13-Apr-20	10-May-21
	TX-3CD	Preparation of City of Ft. Worth Assembly Package - Conflict 0138-48-W1	225	394	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review City of Ft. Worth Assembly Package - Conflict 0138-48-W1	5	394	22-Feb-21	26-Feb-21
	TX-3CD	Submit City of Ft. Worth Assembly Package - Conflict 0138-48-W1	1	394	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review City of Ft. Worth Assembly Package - Conflict 0138-48-W1	10	394	02-Mar-21	15-Mar-21
	TX-3CD	City of Ft. Worth Utility Contractor Mobilization and Temp Erosion Control - Conflict 0138-48-W1	20	394	16-Mar-21	12-Apr-21
	TX-3CD	City of Ft. Worth Utility Civil Works - Conflict 0138-48-W1	10	394	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Utility Installation - Conflict 0138-48-W1	10	394	13-Apr-21	26-Apr-21
	TX-3CD	City of Ft. Worth Connections and Tie-Ins - Conflict 0138-48-W1	5	394	27-Apr-21	03-May-21
	TX-3CD	City of Ft. Worth Final Inspection and As-builts - Conflict 0138-48-W1	5	394	04-May-21	10-May-21
3C3 - Tri-County Electric			242	433	13-Apr-20	16-Mar-21
3C2 - Tri-County Electric - Conflict 0604-2-OHE1 STA 1277 to 1300			242	351	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 084-2-OHE1	175	362	13-Apr-20	11-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 084-2-OHE1	5	362	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 084-2-OHE1	1	362	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 084-2-OHE1	10	362	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 084-2-OHE1	20	351	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 084-2-OHE1	10	351	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 084-2-OHE1	10	351	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 084-2-OHE1	5	351	03-Mar-21	09-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 084-2-OHE1	5	351	10-Mar-21	16-Mar-21
3C2 - Tri-County Electric - Conflict 0606-2-OHE1 STA 1292 to 1292			242	351	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 085-2-OHE1	175	362	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 085-2-OHE1	5	362	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 085-2-OHE1	1	362	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 085-2-OHE1	10	362	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 085-2-OHE1	20	351	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 085-2-OHE1	10	351	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 085-2-OHE1	10	351	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 085-2-OHE1	5	351	03-Mar-21	09-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 085-2-OHE1	5	351	10-Mar-21	16-Mar-21
3C2 - Tri-County Electric - Conflict 0609-2-OHE1 STA 1355 to 1355			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 088-2-OHE1	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 088-2-OHE1	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 088-2-OHE1	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 088-2-OHE1	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 088-2-OHE1	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 088-2-OHE1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 088-2-OHE1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 088-2-OHE1	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 088-2-OHE1	5	433	10-Mar-21	16-Mar-21
3C3 - One Source			247	565	13-Apr-20	23-Mar-21
3C3 - One Source - Conflict 0905-1-OHT2 STA 1355 to 1355			247	565	13-Apr-20	23-Mar-21
	TX-3CD	Preparation of One Source Assembly Package - Conflict 0905-3-FO4	175	576	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review One Source Assembly Package - Conflict 0905-3-FO4	5	576	14-Dec-20	18-Dec-20
	TX-3CD	Submit One Source Assembly Package - Conflict 0905-3-FO4	1	576	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review One Source Assembly Package - Conflict 0905-3-FO4	10	576	22-Dec-20	04-Jan-21
	TX-3CD	One Source Utility Contractor Mobilization and Temp Erosion Control - Conflict 0905-3-FO4	20	565	20-Jan-21	16-Feb-21
	TX-3CD	One Source Utility Civil Works - Conflict 0905-3-FO4	10	565	17-Feb-21	02-Mar-21
	TX-3CD	One Source Utility Installation - Conflict 0905-3-FO4	10	565	17-Feb-21	02-Mar-21
	TX-3CD	One Source Connections and Tie-Ins - Conflict 0905-3-FO4	10	565	03-Mar-21	16-Mar-21
	TX-3CD	One Source Final Inspection and As-builts - Conflict 0905-3-FO4	5	565	17-Mar-21	23-Mar-21
3C3 - Oncor			242	433	13-Apr-20	16-Mar-21
3C3 - Oncor - Conflict 146-1-E2 STA 1387 to 1387			242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 146-1-E2	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 146-1-E2	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 146-1-E2	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 146-1-E2	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 146-1-E2	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 146-1-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 146-1-E2	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 146-1-E2	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 146-1-E2	5	433	10-Mar-21	16-Mar-21
3C3 - Atmos Energy			242	433	13-Apr-20	16-Mar-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		3C3 - Atmos Energy - Conflict 180-10-G1 STA 1343 to 1343	242	433	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 180-10-G1	175	444	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 180-10-G1	5	444	14-Dec-20	18-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 180-10-G1	1	444	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 180-10-G1	10	444	22-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 180-10-G1	20	433	20-Jan-21	16-Feb-21
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 180-10-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Utility Installation - Conflict 180-10-G1	10	433	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 180-10-G1	5	433	03-Mar-21	09-Mar-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 180-10-G1	5	433	10-Mar-21	16-Mar-21
		3C3 - Southbound Relocates	281	444	13-Apr-20	10-May-21
		3C3 - AT&T	242	483	13-Apr-20	16-Mar-21
		3C3 - AT&T - Conflict 0320-OHFO1 STA 1277 to 1300	242	19-Feb	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0320-OHFO1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0320-OHFO1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0320-OHFO1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0320-OHFO1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0320-OHFO1	20	483	20-Jan-21	16-Feb-21
	TX-3CD	AT&T Utility Civil Works - Conflict 0320-OHFO1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	AT&T Utility Installation - Conflict 0320-OHFO1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0320-OHFO1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0320-OHFO1	5	483	10-Mar-21	16-Mar-21
		3C3 - AT&T - Conflict 0321-2-T1 STA 1282 to 1301	242	483	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0321-2-T1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0321-2-T1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0321-2-T1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0321-2-T1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0321-2-T1	20	483	20-Jan-21	16-Feb-21
	TX-3CD	AT&T Utility Civil Works - Conflict 0321-2-T1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	AT&T Utility Installation - Conflict 0321-2-T1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0321-2-T1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0321-2-T1	5	483	10-Mar-21	16-Mar-21
		3C3 - AT&T - Conflict 0332-OHFO1 STA 1277 to 1300	242	483	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of AT&T Assembly Package - Conflict 0332-OHT1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review AT&T Assembly Package - Conflict 0332-OHT1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit AT&T Assembly Package - Conflict 0332-OHT1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review AT&T Assembly Package - Conflict 0332-OHT1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	AT&T Utility Contractor Mobilization and Temp Erosion Control - Conflict 0332-OHT1	20	483	20-Jan-21	16-Feb-21
	TX-3CD	AT&T Utility Civil Works - Conflict 0332-OHT1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	AT&T Utility Installation - Conflict 0332-OHT1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	AT&T Connections and Tie-Ins - Conflict 0332-OHT1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	AT&T Final Inspection and As-builts - Conflict 0332-OHT1	5	483	10-Mar-21	16-Mar-21
		3C3 - Tri-County Electric	242	483	13-Apr-20	16-Mar-21
		3C2 - Tri-County Electric - Conflict 0609-2-OHE1 STA 1355 to 1386	242	483	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Tri-County Electric Assembly Package - Conflict 089-2-OHE1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Tri-County Electric Assembly Package - Conflict 089-2-OHE1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit Tri-County Electric Assembly Package - Conflict 089-2-OHE1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Tri-County Electric Assembly Package - Conflict 089-2-OHE1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	Tri-County Electric Utility Contractor Mobilization and Temp Erosion Control - Conflict 089-2-OHE1	20	483	20-Jan-21	16-Feb-21
	TX-3CD	Tri-County Electric Utility Civil Works - Conflict 089-2-OHE1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Tri-County Electric Utility Installation - Conflict 089-2-OHE1	10	483	17-Feb-21	02-Mar-21

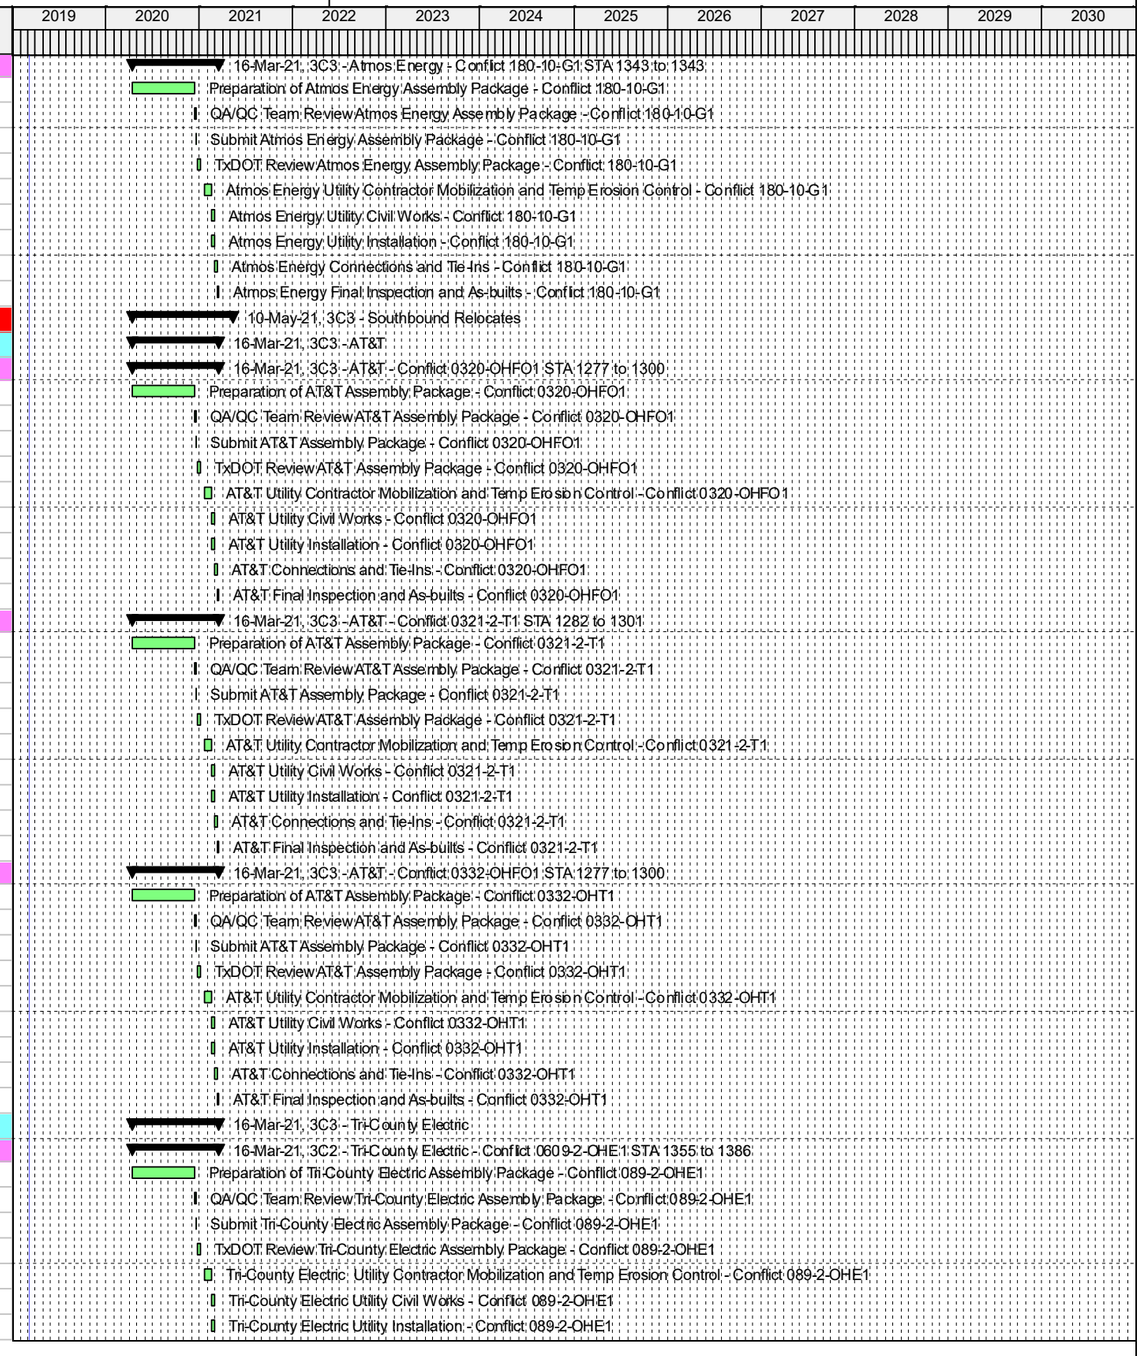

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Tri-County Electric Connections and Tie-Ins - Conflict 089-2-OHE1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	Tri-County Electric Final Inspection and As-builts - Conflict 089-2-OHE1	5	483	10-Mar-21	16-Mar-21
3C3 - Oncor			252	473	13-Apr-20	30-Mar-21
3C3 - Oncor - Conflict 142-1-OHE2 STA 1300 to 1347			252	473	13-Apr-20	30-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 142-1-OHE2	175	484	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 142-1-OHE2	5	484	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 142-1-OHE2	1	484	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 142-1-OHE2	10	484	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 142-1-OHE2	20	473	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 142-1-OHE2	20	473	17-Feb-21	16-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 142-1-OHE2	20	473	17-Feb-21	16-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 142-1-OHE2	5	473	17-Mar-21	23-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 142-1-OHE2	5	473	24-Mar-21	30-Mar-21
3C3 - Oncor - Conflict 147-1-OHE1 STA 997 SH170 to 997 SH170			242	483	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 147-1-OHE1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 147-1-OHE1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 147-1-OHE1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 147-1-OHE1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 147-1-OHE1	20	483	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 147-1-OHE1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 147-1-OHE1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 147-1-OHE1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 147-1-OHE1	5	483	10-Mar-21	16-Mar-21
3C3 - Oncor - Conflict 148-1-OHE1 STA 1355 to 1387			242	483	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Oncor Assembly Package - Conflict 148-1-OHE1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Oncor Assembly Package - Conflict 148-1-OHE1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit Oncor Assembly Package - Conflict 148-1-OHE1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Oncor Assembly Package - Conflict 148-1-OHE1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	Oncor Utility Contractor Mobilization and Temp Erosion Control - Conflict 148-1-OHE1	20	483	20-Jan-21	16-Feb-21
	TX-3CD	Oncor Utility Civil Works - Conflict 148-1-OHE1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Utility Installation - Conflict 148-1-OHE1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Oncor Connections and Tie-Ins - Conflict 148-1-OHE1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	Oncor Final Inspection and As-builts - Conflict 148-1-OHE1	5	483	10-Mar-21	16-Mar-21
3C3 - Sunoco			281	444	13-Apr-20	10-May-21
3C2 - Sunoco - Conflict 167-16-G4 STA 994 SH170			281	444	13-Apr-20	10-May-21
	TX-3CD	Preparation of Sunoco Assembly Package - Conflict 167-4-G4	225	444	13-Apr-20	19-Feb-21
	TX-3CD	QA/QC Team Review Sunoco Assembly Package - Conflict 167-4-G4	5	444	22-Feb-21	26-Feb-21
	TX-3CD	Submit Sunoco Assembly Package - Conflict 167-4-G4	1	444	01-Mar-21	01-Mar-21
	TX-3CD	TxDOT Review Sunoco Assembly Package - Conflict 167-4-G4	10	444	02-Mar-21	15-Mar-21
	TX-3CD	Sunoco Utility Contractor Mobilization and Temp Erosion Control - Conflict 167-4-G4	20	444	16-Mar-21	12-Apr-21
	TX-3CD	Sunoco Utility Civil Works - Conflict 167-4-G4	10	444	13-Apr-21	26-Apr-21
	TX-3CD	Sunoco Utility Installation - Conflict 167-4-G4	10	444	13-Apr-21	26-Apr-21
	TX-3CD	Sunoco Connections and Tie-Ins - Conflict 167-4-G4	5	444	27-Apr-21	03-May-21
	TX-3CD	Sunoco Final Inspection and As-builts - Conflict 167-4-G4	5	444	04-May-21	10-May-21
3C3 - Atmos Energy			242	483	13-Apr-20	16-Mar-21
3C3 - Atmos Energy - Conflict 179-6-G1 STA 1305 to 1344			242	483	13-Apr-20	16-Mar-21
	TX-3CD	Preparation of Atmos Energy Assembly Package - Conflict 179-6-G1	175	494	13-Apr-20	11-Dec-20
	TX-3CD	QA/QC Team Review Atmos Energy Assembly Package - Conflict 179-6-G1	5	494	14-Dec-20	18-Dec-20
	TX-3CD	Submit Atmos Energy Assembly Package - Conflict 179-6-G1	1	494	21-Dec-20	21-Dec-20
	TX-3CD	TxDOT Review Atmos Energy Assembly Package - Conflict 179-6-G1	10	494	22-Dec-20	04-Jan-21
	TX-3CD	Atmos Energy Utility Contractor Mobilization and Temp Erosion Control - Conflict 179-6-G1	20	483	20-Jan-21	16-Feb-21

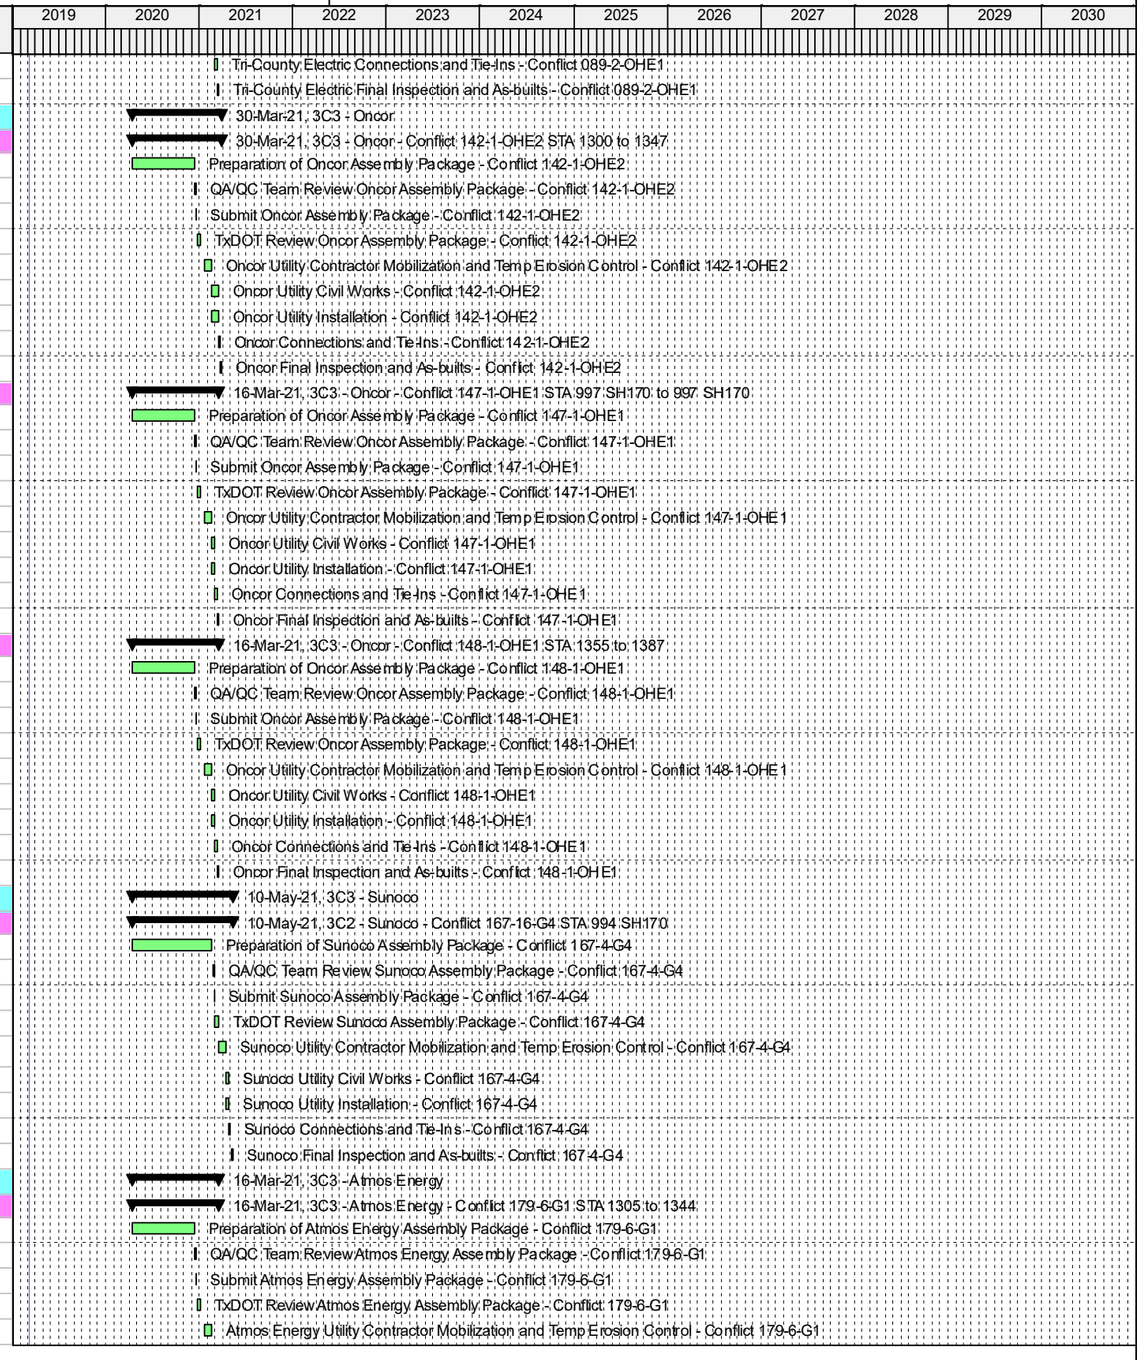

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Atmos Energy Utility Civil Works - Conflict 179-6-G1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Utility Installation - Conflict 179-6-G1	10	483	17-Feb-21	02-Mar-21
	TX-3CD	Atmos Energy Connections and Tie-Ins - Conflict 179-6-G1	5	483	03-Mar-21	09-Mar-21
	TX-3CD	Atmos Energy Final Inspection and As-builts - Conflict 179-6-G1	5	483	10-Mar-21	16-Mar-21
3C Design Sta 1028+00 to 1401+00			394	766	07-Mar-19	08-Sep-20
General Activities and Field Work			117	0	07-Mar-19	16-Aug-19
Design Mobilization			20	0	07-Mar-19	03-Apr-19
DESM	TX-3CD	3C Mobilize Design Staff	20	0	07-Mar-19	03-Apr-19
Schematics			67	22	04-Apr-19	07-Jul-19
DSCH	TX-3CD	3C Develop & Analysis of Changes to Schematics	40	21	04-Apr-19	29-May-19
DSCH	TX-3CD	3C QA/QC Review Final Schematics	5	21	30-May-19	05-Jun-19
DSCH	TX-3CD	Submit Final Schematics	1	21	06-Jun-19	06-Jun-19
DSCH	TX-3CD	Final Schematics/TxDOT & IE Review & Comments	10	30	07-Jun-19	16-Jun-19
DSCH	TX-3CD	Final Schematics Comment Resolution	20	30	17-Jun-19	06-Jul-19
DSCH	TX-3CD	Final Schematics Approved	1	30	07-Jul-19	07-Jul-19
Survey Works			97	0	04-Apr-19	16-Aug-19
DSUR	TX-3CD	Preliminary Survey Plan	7	0	04-Apr-19	12-Apr-19
DSUR	TX-3CD	Perform Field Work for Aerial Survey	20	0	15-Apr-19	10-May-19
DSUR	TX-3CD	Perform Control and Field Survey	20	20	15-Apr-19	10-May-19
DSUR	TX-3CD	Perform Aerial Survey	20	0	13-May-19	07-Jun-19
DSUR	TX-3CD	Survey Data Analysis and Calculations	20	0	10-Jun-19	05-Jul-19
DSUR	TX-3CD	95% TDM Model and Contour Maps	5	0	08-Jul-19	12-Jul-19
DSUR	TX-3CD	QA/QC Review TDM Model and Contour Maps	5	0	15-Jul-19	19-Jul-19
DSUR	TX-3CD	Submit TDM Model and Contour Maps	1	0	22-Jul-19	22-Jul-19
DSUR	TX-3CD	Survey TxDOT Review and Comments	10	0	23-Jul-19	01-Aug-19
DSUR	TX-3CD	Survey Comments Cleared	10	0	02-Aug-19	15-Aug-19
DSUR	TX-3CD	Final Survey for Facility Design	1	0	16-Aug-19	16-Aug-19
Develop Specifications			153	15	04-Apr-19	05-Nov-19
DPRE10[illegible]	TX-3CD	Design Consultants QA/QC Management System in Place	20	14	04-Apr-19	01-May-19
DPRE10[illegible]	TX-3CD	Bridge Design Specifications Completed	0	123	06-Jun-19	06-Jun-19
DPRE111	TX-3CD	Traffic Management Specifications Completed	0	120	11-Jun-19	11-Jun-19
DPRE11[illegible]	TX-3CD	Traffic Control Specifications Completed	0	111	24-Jun-19	24-Jun-19
DPRE12[illegible]	TX-3CD	Tradfic signal Systems Specifications Completed	0	107	28-Jun-19	28-Jun-19
DPRE13[illegible]	TX-3CD	Illumination Specifications Completed	0	106	01-Jul-19	01-Jul-19
DPRE12[illegible]	TX-3CD	Landscaping Specifications Completed	0	96	15-Jul-19	15-Jul-19
DPRE12[illegible]	TX-3CD	Sign & Marking Specifications Completed	0	90	23-Jul-19	23-Jul-19
DPRE13[illegible]	TX-3CD	Niose Wall Specifications Completed	0	84	31-Jul-19	31-Jul-19
DPRE13[illegible]	TX-3CD	Geotechnical Specifications Completed	0	78	08-Aug-19	08-Aug-19
DPRE13[illegible]	TX-3CD	Pavement Design Specifications Completed	0	70	20-Aug-19	20-Aug-19
DPRE13[illegible]	TX-3CD	Drainage Design Report Completed	0	68	22-Aug-19	22-Aug-19
DPRE13[illegible]	TX-3CD	Roadway Design Specifications Completed	0	66	26-Aug-19	26-Aug-19
DPRE13[illegible]	TX-3CD	Retaining Wall Design Specifications Completed	0	30	15-Oct-19	15-Oct-19
DPRE13[illegible]	TX-3CD	General Structure Specifications Completed	0	30	15-Oct-19	15-Oct-19
DPRE13[illegible]	TX-3CD	ITCS & TCS Specifications Completed	0	15	05-Nov-19	05-Nov-19
Geotechnical Design			90	163	04-Apr-19	07-Aug-19
General			20	14	04-Apr-19	01-May-19
DPRE	TX-3CD	Analysis of the Existing Geotechnical Documents	20	14	04-Apr-19	01-May-19
Earthwork Geotech			60	88	02-May-19	24-Jul-19
DPRE	TX-3CD	Earthworks Geotechnical Field and Laboratory Works Stage 1	20	68	02-May-19	29-May-19
DPRE	TX-3CD	Earthworks Geotechnical Field and Laboratory Works Stage 2	20	68	30-May-19	26-Jun-19
DPRE	TX-3CD	Earthworks Field and Laboratory Works Factual Geotechnical Report	20	68	27-Jun-19	24-Jul-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
DPRE	TX-3CD	Earthworks Geotechnical Analysis and Calculations Early Design Packages	10	68	27-Jun-19	10-Jul-19
DPRE	TX-3CD	Earthworks Geotechnical Analysis and Calculations Standard Design Packages	10	98	27-Jun-19	10-Jul-19
Bridge Geotech			50	203	04-Apr-19	12-Jun-19
Standard Bridge Geotech			40	213	04-Apr-19	29-May-19
DPI	TX-3CD	Bridges Geotechnical Field and Laboratory Works Stage 1	10	118	04-Apr-19	17-Apr-19
DPI	TX-3CD	Bridges Geotechnical Field and Laboratory Works Stage 2	20	213	18-Apr-19	15-May-19
DPI	TX-3CD	Bridges Field and Laboratory Works Factual Geotechnical Report	10	213	16-May-19	29-May-19
DPI	TX-3CD	Bridges Geotechnical Analysis and Calculations	10	213	16-May-19	29-May-19
Early Bridge Geotech			50	118	04-Apr-19	12-Jun-19
DPI	TX-3CD	Early Bridge Geotechnical Field and Laboratory Works	20	118	04-Apr-19	01-May-19
DPI	TX-3CD	Early Bridge Field and Laboratory Works Factual Geotechnical Report	10	118	02-May-19	15-May-19
DPI	TX-3CD	Early Bridge Geotechnical Analysis and Calculations	20	118	16-May-19	12-Jun-19
Drainage Geotech			70	68	02-May-19	07-Aug-19
DPRE	TX-3CD	Culvert and Drainage Structures Geotechnical Field and Laboratory Works	20	49	02-May-19	29-May-19
DPRE	TX-3CD	Culvert and Drainage Structures Field and Laboratory Works Factual Geotechnical Report	20	49	30-May-19	26-Jun-19
DPRE	TX-3CD	Culvert and Drainage Structures Geotechnical Analysis and Calculations	10	68	27-Jun-19	10-Jul-19
DPRE	TX-3CD	Culvert and Drainage Structures General Geotechnical Recommendations for the Design	10	68	11-Jul-19	24-Jul-19
DPRE	TX-3CD	Culvert and Drainage Structures Final Geotechnical Report Early Design Packages	5	78	11-Jul-19	17-Jul-19
DPRE	TX-3CD	Culvert and Drainage Structures Final Geotechnical Report Standard Design Packages	10	68	25-Jul-19	07-Aug-19
Wall Geotech			65	14	02-May-19	31-Jul-19
DPRE	TX-3CD	Earthworks and Retaining Walls Geotechnical Field and Laboratory Works	20	14	02-May-19	29-May-19
DPRE	TX-3CD	Earthworks and Retaining Walls Field and Laboratory Works Factual Geotechnical Report	10	14	30-May-19	12-Jun-19
DPRE	TX-3CD	Earthworks and Retaining Walls Geotechnical Analysis and Calculations Early Design Packages	10	14	13-Jun-19	26-Jun-19
DPRE	TX-3CD	Earthworks and Retaining Walls Geotechnical Analysis and Calculations Standard Design Packages	10	14	13-Jun-19	26-Jun-19
DPRE	TX-3CD	Miscellaneous Structures Geotechnical Field and Laboratory Works	10	14	27-Jun-19	10-Jul-19
DPRE	TX-3CD	Miscellaneous Structures Field and Laboratory Works Factual Geotechnical Report	5	14	11-Jul-19	17-Jul-19
DPRE	TX-3CD	Miscellaneous Structures Geotechnical Analysis and Calculations	10	14	18-Jul-19	31-Jul-19
Pavement Design			98	70	04-Apr-19	19-Aug-19
Data Analysis and Draft Report			80	68	04-Apr-19	24-Jul-19
DPRE	TX-3CD	Existing Geotechnical and Traffic Data	20	128	04-Apr-19	01-May-19
DPRE	TX-3CD	Revise Pavement Design Criteria (if required as most standards are all ready approved)	10	68	27-Jun-19	10-Jul-19
DPRE	TX-3CD	Pavement Design Analysis and Calculations	10	68	11-Jul-19	24-Jul-19
Final Design and Report			18	70	25-Jul-19	19-Aug-19
DPRE	TX-3CD	Pavement Design General Recommendations(if required as most standards are all ready approved)	10	68	25-Jul-19	07-Aug-19
DPRE	TX-3CD	Submit Pavement Design Standards	1	68	08-Aug-19	08-Aug-19
DPRE	TX-3CD	TXDoT/IE Review Pavement Design General Recommendations	10	96	09-Aug-19	18-Aug-19
DPRE	TX-3CD	Final Pavement Design Standards	1	70	19-Aug-19	19-Aug-19
Drainage Design			100	68	04-Apr-19	21-Aug-19
Drainage			100	68	04-Apr-19	21-Aug-19
Hydrologic and Hydraulic Design			60	108	04-Apr-19	26-Jun-19
DPI	TX-3CD	Preliminary Investigation. Existing Data Collection	20	118	04-Apr-19	01-May-19
DPI	TX-3CD	Drainage Area Map	20	118	02-May-19	29-May-19
DPI	TX-3CD	Interior Drainage Area Map	20	118	02-May-19	29-May-19
DPI	TX-3CD	Hydrologic-Hydraulic Design Criteria	20	49	30-May-19	26-Jun-19
DPI	TX-3CD	Culverts Hydraulic Design	20	98	30-May-19	26-Jun-19
DPI	TX-3CD	Review of the Effects of Allowable Computed Headwater.	20	98	30-May-19	26-Jun-19
DPI	TX-3CD	Ditches Hydraulic and Shear Stress Design. Lining Design	20	98	30-May-19	26-Jun-19
DPI	TX-3CD	Drainage Miscellaneous Elements Hydraulic Design (junction boxes, special inlets...)	20	98	30-May-19	26-Jun-19
DPI	TX-3CD	Drainage Report for Major Stream Crossings	20	108	30-May-19	26-Jun-19
DPI	TX-3CD	Hydrologic Analysis and Computations. Discharges. Preliminary Culverts Locations	20	98	30-May-19	26-Jun-19
DPI	TX-3CD	Storm Sewers, Drop Inlets and Deck Drain Hydraulic Design	20	98	30-May-19	26-Jun-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Preliminary System Design			30	98	30-May-19	10-Jul-19
DPI	TX-3CD	Standardized Rip-Rap Design	20	108	30-May-19	26-Jun-19
DPI	TX-3CD	Scour Analysis	20	108	30-May-19	26-Jun-19
DPI	TX-3CD	Culverts Layout and Geometry	20	98	13-Jun-19	10-Jul-19
Detailed Drainage Design			30	68	11-Jul-19	21-Aug-19
DPI	TX-3CD	Drainage Elements Structural	10	78	11-Jul-19	24-Jul-19
DPI	TX-3CD	Develop of Drainage	10	78	11-Jul-19	24-Jul-19
DPI	TX-3CD	Drainage Elements Structural Design	20	68	25-Jul-19	21-Aug-19
DPI	TX-3CD	Drainage Design Report	10	68	08-Aug-19	21-Aug-19
Roadway Design			30	66	15-Jul-19	23-Aug-19
Detailed Design			30	66	15-Jul-19	23-Aug-19
DPRE	TX-3CD	Add 3A to Documents for Roadway Design Criteria	20	17	15-Jul-19	09-Aug-19
DPRE	TX-3CD	Submit 3A as 3C Roadway Design Criteria	1	66	12-Aug-19	12-Aug-19
DPRE	TX-3CD	TxDOT/IE review of 3A as 3C Roadway Design Criteria	10	92	13-Aug-19	22-Aug-19
DPRE	TX-3CD	3C Roadway Design Stanards	1	66	23-Aug-19	23-Aug-19
Segment 3C - Bridge Design			306	831	04-Apr-19	04-Jun-20
DBRPRE	TX-3CD	Bridges Tpology Study	10	108	04-Apr-19	17-Apr-19
DBRPRE	TX-3CD	Bridges Typical X-Section Study	10	108	18-Apr-19	01-May-19
DBRPRE	TX-3CD	Bridges Substructure Study	10	108	02-May-19	15-May-19
DBRPRE	TX-3CD	Bridges Abutment Study	10	108	16-May-19	29-May-19
DBRPRE	TX-3CD	Bridges Conceptual Design Study	5	108	30-May-19	05-Jun-19
Bridge Rehab			99	993	06-Jun-19	22-Oct-19
Establish Criteria Procedures			20	991	06-Jun-19	03-Jul-19
DBI	TX-3CD	BR 29 Existing Bridge Info Review and Field Check	10	991	06-Jun-19	19-Jun-19
DBI	TX-3CD	BR 29 Bridge Design Criteria Review	10	991	20-Jun-19	03-Jul-19
Bridge Review			31	991	04-Jul-19	15-Aug-19
DBI	TX-3CD	BR 29 Review General Arrangement Reports	30	991	04-Jul-19	14-Aug-19
DBI	TX-3CD	BR 29 Review Detailed Calcs	30	991	04-Jul-19	14-Aug-19
DBI	TX-3CD	BR 29 Geotechnical Review & Checks	1	991	15-Aug-19	15-Aug-19
Design Rehab Notebooks			48	993	16-Aug-19	22-Oct-19
DBI	TX-3CD	BR 29 Develop Complete Plans / Spec / Refurbishment Notebooks	20	991	16-Aug-19	12-Sep-19
DBI	TX-3CD	BR 29 Submit Complete Plans / Spec / Refurbishment Notebooks	1	991	13-Sep-19	13-Sep-19
DBI	TX-3CD	BR 29 TxDOT/IE Review & Comment Complete Plans / Spec / Refurbishment Notebooks	10	1389	14-Sep-19	23-Sep-19
DBI	TX-3CD	BR 29 Clear Comments Complete Plans / Spec / Refurbishment Notebooks	20	993	24-Sep-19	21-Oct-19
DBI	TX-3CD	BR 29 Complete Plans / Spec / Refurbishment Notebooks - IFC	1	993	22-Oct-19	22-Oct-19
3C1 - Bridge Design			209	812	19-Aug-19	04-Jun-20
BR 102.1 Henrietta Creek			129	892	19-Aug-19	13-Feb-20
Establish Criteria Procedures			20	735	19-Aug-19	13-Sep-19
[	TX-3CD	BR 102.1 Existing Bridge Info Review and Check	10	735	19-Aug-19	30-Aug-19
[	TX-3CD	BR 102.1 Bridge Design Criteria	10	735	02-Sep-19	13-Sep-19
Bridge Layouts			40	735	16-Sep-19	08-Nov-19
[	TX-3CD	BR 102.1 Develop Bridge Final Geometry Plans	20	755	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.1 Develop General Arrangement Plans	20	735	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.1 Develop Detailed Calc	20	735	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.1 Geotechnical Review & Checks	20	735	14-Oct-19	08-Nov-19
Substructure Design			39	733	11-Nov-19	02-Jan-20
[	TX-3CD	BR 102.1 Develop Detail Drawings Substructure	20	735	11-Nov-19	06-Dec-19
[	TX-3CD	BR 102.1 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	735	09-Dec-19	09-Dec-19
[	TX-3CD	BR 102.1 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	1027	09-Dec-19	18-Dec-19
[	TX-3CD	BR 102.1 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	733	19-Dec-19	01-Jan-20
[	TX-3CD	BR 102.1 General Arrangement & Substructure Plans-IFC	1	733	02-Jan-20	02-Jan-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Superstructure Design			49	892	09-Dec-19	13-Feb-20
[	TX-3CD	BR 102.1 Develop Complete Plans / Spec / Design Notebooks	30	892	09-Dec-19	17-Jan-20
[	TX-3CD	BR 102.1 Develop Design Superstructure Plans	20	794	09-Dec-19	03-Jan-20
[	TX-3CD	BR 102.1 Develop Detail Drawings for Deck	20	794	09-Dec-19	03-Jan-20
[	TX-3CD	BR 102.1 Submit Superstructure	0	794	06-Jan-20	06-Jan-20
[	TX-3CD	BR 102.1 TxDOT/IE Review & Comments Superstructure Plans	10	1112	07-Jan-20	16-Jan-20
[	TX-3CD	BR 102.1 Clear Comments Superstructure Plans	10	794	17-Jan-20	30-Jan-20
[	TX-3CD	BR 102.1 Submit Complete Plans / Spec / Design Notebooks	0	892	20-Jan-20	20-Jan-20
[	TX-3CD	BR 102.1 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1248	20-Jan-20	29-Jan-20
[	TX-3CD	BR 102.1 Clear Comments Complete Plans / Spec / Design Notebooks	10	892	30-Jan-20	12-Feb-20
[	TX-3CD	BR 102.1 Superstructure Plans - IFC	1	794	31-Jan-20	31-Jan-20
[	TX-3CD	BR 102.1 Complete Plans / Spec / Design Notebooks - IFC	1	892	13-Feb-20	13-Feb-20
BR 102.2 Henrietta Creek			110	618	19-Aug-19	17-Jan-20
Establish Criteria Procedures			20	391	19-Aug-19	13-Sep-19
[	TX-3CD	BR 102.2 Existing Bridge Info Review and Check	10	391	19-Aug-19	30-Aug-19
[	TX-3CD	BR 102.2 Bridge Design Criteria	10	391	02-Sep-19	13-Sep-19
Bridge Layouts			21	391	16-Sep-19	14-Oct-19
[	TX-3CD	BR 102.2 Develop Bridge Final Geometry Plans	20	392	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.2 Develop General Arrangement Plans	20	391	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.2 Develop Detailed Calc	20	391	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.2 Geotechnical Review & Checks	1	391	14-Oct-19	14-Oct-19
Substructure Design			39	391	15-Oct-19	06-Dec-19
[	TX-3CD	BR 102.2 Develop Detail Drawings Substructure	20	391	15-Oct-19	11-Nov-19
[	TX-3CD	BR 102.2 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	391	12-Nov-19	12-Nov-19
[	TX-3CD	BR 102.2 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	547	12-Nov-19	21-Nov-19
[	TX-3CD	BR 102.2 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	391	22-Nov-19	05-Dec-19
[	TX-3CD	BR 102.2 General Arrangement & Substructure Plans-IFC	1	391	06-Dec-19	06-Dec-19
Superstructure Design			49	618	12-Nov-19	17-Jan-20
[	TX-3CD	BR 102.2 Develop Complete Plans / Spec / Design Notebooks	30	619	12-Nov-19	23-Dec-19
[	TX-3CD	BR 102.2 Develop Design Superstructure Plans	20	413	12-Nov-19	09-Dec-19
[	TX-3CD	BR 102.2 Develop Detail Drawings for Deck	20	413	12-Nov-19	09-Dec-19
[	TX-3CD	BR 102.2 Submit Superstructure	0	413	10-Dec-19	10-Dec-19
[	TX-3CD	BR 102.2 TxDOT/IE Review & Comments Superstructure Plans	10	578	11-Dec-19	20-Dec-19
[	TX-3CD	BR 102.2 Clear Comments Superstructure Plans	10	412	23-Dec-19	03-Jan-20
[	TX-3CD	BR 102.2 Submit Complete Plans / Spec / Design Notebooks	0	619	24-Dec-19	24-Dec-19
[	TX-3CD	BR 102.2 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	866	24-Dec-19	02-Jan-20
[	TX-3CD	BR 102.2 Clear Comments Complete Plans / Spec / Design Notebooks	10	618	03-Jan-20	16-Jan-20
[	TX-3CD	BR 102.2 Superstructure Plans - IFC	1	412	06-Jan-20	06-Jan-20
[	TX-3CD	BR 102.2 Complete Plans / Spec / Design Notebooks - IFC	1	618	17-Jan-20	17-Jan-20
BR 102.3 Henrietta Creek			169	847	19-Aug-19	09-Apr-20
Establish Criteria Procedures			20	750	19-Aug-19	13-Sep-19
[	TX-3CD	BR 102.3 Existing Bridge Info Review and Check	10	750	19-Aug-19	30-Aug-19
[	TX-3CD	BR 102.3 Bridge Design Criteria	10	750	02-Sep-19	13-Sep-19
Bridge Layouts			40	750	16-Sep-19	08-Nov-19
[	TX-3CD	BR 102.3 Develop Bridge Final Geometry Plans	20	770	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.3 Develop General Arrangement Plans	20	750	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.3 Develop Detailed Calc	20	750	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.3 Geotechnical Review & Checks	20	750	14-Oct-19	08-Nov-19
Substructure Design			39	750	11-Nov-19	02-Jan-20
[	TX-3CD	BR 102.3 Develop Detail Drawings Substructure	20	750	11-Nov-19	06-Dec-19
[	TX-3CD	BR 102.3 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	750	09-Dec-19	09-Dec-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 102.3 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	1050	09-Dec-19	18-Dec-19
[	TX-3CD	BR 102.3 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	750	19-Dec-19	01-Jan-20
[	TX-3CD	BR 102.3 General Arrangement & Substructure Plans-IFC	1	750	02-Jan-20	02-Jan-20
Superstructure Design			89	847	09-Dec-19	09-Apr-20
[	TX-3CD	BR 102.3 Develop Detail Drawings for Deck	20	751	09-Dec-19	03-Jan-20
[	TX-3CD	BR 102.3 Develop Design Superstructure Plans	20	751	06-Jan-20	31-Jan-20
[	TX-3CD	BR 102.3 Submit Superstructure	0	751	03-Feb-20	03-Feb-20
[	TX-3CD	BR 102.3 Develop Complete Plans / Spec / Design Notebooks	30	847	03-Feb-20	13-Mar-20
[	TX-3CD	BR 102.3 TxDOT/IE Review & Comments Superstructure Plans	10	1051	04-Feb-20	13-Feb-20
[	TX-3CD	BR 102.3 Clear Comments Superstructure Plans	10	751	14-Feb-20	27-Feb-20
[	TX-3CD	BR 102.3 Superstructure Plans - IFC	1	751	28-Feb-20	28-Feb-20
[	TX-3CD	BR 102.3 Submit Complete Plans / Spec / Design Notebooks	0	847	16-Mar-20	16-Mar-20
[	TX-3CD	BR 102.3 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1185	16-Mar-20	25-Mar-20
[	TX-3CD	BR 102.3 Clear Comments Complete Plans / Spec / Design Notebooks	10	847	26-Mar-20	08-Apr-20
[	TX-3CD	BR 102.3 Complete Plans / Spec / Design Notebooks - IFC	1	847	09-Apr-20	09-Apr-20
BR 102.4 Henrietta Creek			169	778	19-Aug-19	09-Apr-20
Establish Criteria Procedures			20	645	19-Aug-19	13-Sep-19
[	TX-3CD	BR 102.4 Existing Bridge Info Review and Check	10	645	19-Aug-19	30-Aug-19
[	TX-3CD	BR 102.4 Bridge Design Criteria	10	645	02-Sep-19	13-Sep-19
Bridge Layouts			40	645	16-Sep-19	08-Nov-19
[	19-Feb-	BR 102.4 Develop Bridge Final Geometry Plans	20	665	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.4 Develop General Arrangement Plans	20	645	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.4 Develop Detailed Calc	20	645	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.4 Geotechnical Review & Checks	20	645	14-Oct-19	08-Nov-19
Substructure Design			39	656	11-Nov-19	02-Jan-20
[	TX-3CD	BR 102.4 Develop Detail Drawings Substructure	20	645	11-Nov-19	06-Dec-19
[	TX-3CD	BR 102.4 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	656	09-Dec-19	09-Dec-19
[	TX-3CD	BR 102.4 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	918	09-Dec-19	18-Dec-19
[	TX-3CD	BR 102.4 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	656	19-Dec-19	01-Jan-20
[	TX-3CD	BR 102.4 General Arrangement & Substructure Plans-IFC	1	656	02-Jan-20	02-Jan-20
Superstructure Design			89	778	09-Dec-19	09-Apr-20
[	TX-3CD	BR 102.4 Develop Detail Drawings for Deck	20	645	09-Dec-19	03-Jan-20
[	TX-3CD	BR 102.4 Develop Design Superstructure Plans	20	645	06-Jan-20	31-Jan-20
[	TX-3CD	BR 102.4 Submit Superstructure	0	645	03-Feb-20	03-Feb-20
[	TX-3CD	BR 102.4 Develop Complete Plans / Spec / Design Notebooks	30	780	03-Feb-20	13-Mar-20
[	TX-3CD	BR 102.4 TxDOT/IE Review & Comments Superstructure Plans	10	903	04-Feb-20	13-Feb-20
[	TX-3CD	BR 102.4 Clear Comments Superstructure Plans	10	645	14-Feb-20	27-Feb-20
[	TX-3CD	BR 102.4 Superstructure Plans - IFC	1	645	28-Feb-20	28-Feb-20
[	TX-3CD	BR 102.4 Submit Complete Plans / Spec / Design Notebooks	0	780	16-Mar-20	16-Mar-20
[	TX-3CD	BR 102.4 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1090	16-Mar-20	25-Mar-20
[	TX-3CD	BR 102.4 Clear Comments Complete Plans / Spec / Design Notebooks	10	778	26-Mar-20	08-Apr-20
[	TX-3CD	BR 102.4 Complete Plans / Spec / Design Notebooks - IFC	1	778	09-Apr-20	09-Apr-20
BR 102.5 Henrietta Creek			169	292	19-Aug-19	09-Apr-20
Establish Criteria Procedures			20	184	19-Aug-19	13-Sep-19
[	TX-3CD	BR 102.5 Existing Bridge Info Review and Check	10	184	19-Aug-19	30-Aug-19
[	TX-3CD	BR 102.5 Bridge Design Criteria	10	184	02-Sep-19	13-Sep-19
Bridge Layouts			40	184	16-Sep-19	08-Nov-19
[	TX-3CD	BR 102.5 Develop Bridge Final Geometry Plans	20	204	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.5 Develop General Arrangement Plans	20	184	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.5 Develop Detailed Calc	20	184	16-Sep-19	11-Oct-19
[	TX-3CD	BR 102.5 Geotechnical Review & Checks	20	184	14-Oct-19	08-Nov-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Substructure Design			39	183	11-Nov-19	02-Jan-20
[	TX-3CD	BR 102.5 Develop Detail Drawings Substructure	20	184	11-Nov-19	06-Dec-19
[	TX-3CD	BR 102.5 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	185	09-Dec-19	09-Dec-19
[	TX-3CD	BR 102.5 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	257	09-Dec-19	18-Dec-19
[	TX-3CD	BR 102.5 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	183	19-Dec-19	01-Jan-20
[	TX-3CD	BR 102.5 General Arrangement & Substructure Plans-IFC	1	183	02-Jan-20	02-Jan-20
Superstructure Design			89	292	09-Dec-19	09-Apr-20
[	TX-3CD	BR 102.5 Develop Detail Drawings for Deck	20	184	09-Dec-19	03-Jan-20
[	TX-3CD	BR 102.5 Develop Design Superstructure Plans	20	184	06-Jan-20	31-Jan-20
[	TX-3CD	BR 102.5 Submit Superstructure	0	184	03-Feb-20	03-Feb-20
[	TX-3CD	BR 102.5 Develop Complete Plans / Spec / Design Notebooks	30	292	03-Feb-20	13-Mar-20
[	TX-3CD	BR 102.5 TxDOT/IE Review & Comments Superstructure Plans	10	258	04-Feb-20	13-Feb-20
[	TX-3CD	BR 102.5 Clear Comments Superstructure Plans	10	184	14-Feb-20	27-Feb-20
[	TX-3CD	BR 102.5 Superstructure Plans - IFC	1	184	28-Feb-20	28-Feb-20
[	TX-3CD	BR 102.5 Submit Complete Plans / Spec / Design Notebooks	0	292	16-Mar-20	16-Mar-20
[	TX-3CD	BR 102.5 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	408	16-Mar-20	25-Mar-20
[	TX-3CD	BR 102.5 Clear Comments Complete Plans / Spec / Design Notebooks	10	292	26-Mar-20	08-Apr-20
[	TX-3CD	BR 102.5 Complete Plans / Spec / Design Notebooks - IFC	1	292	09-Apr-20	09-Apr-20
BR 103.1 Westport Pkwy			199	534	19-Aug-19	21-May-20
Establish Criteria Procedures			30	342	19-Aug-19	27-Sep-19
[	TX-3CD	BR 103.1 Existing Bridge Info Review and Check	15	342	19-Aug-19	06-Sep-19
[	TX-3CD	BR 103.1 Bridge Design Criteria	15	342	09-Sep-19	27-Sep-19
Bridge Layouts			60	342	30-Sep-19	20-Dec-19
[	TX-3CD	BR 103.1 Develop General Arrangement Plans	20	342	30-Sep-19	25-Oct-19
[	TX-3CD	BR 103.1 Develop Bridge Final Geometry Plans	20	362	28-Oct-19	22-Nov-19
[	TX-3CD	BR 103.1 Develop Detailed Calc	20	342	28-Oct-19	22-Nov-19
[	TX-3CD	BR 103.1 Geotechnical Review & Checks	20	342	25-Nov-19	20-Dec-19
Substructure Design			39	342	23-Dec-19	13-Feb-20
[	TX-3CD	BR 103.1 Develop Detail Drawings Substructure	20	342	23-Dec-19	17-Jan-20
[	TX-3CD	BR 103.1 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	342	20-Jan-20	20-Jan-20
[	TX-3CD	BR 103.1 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	478	20-Jan-20	29-Jan-20
[	TX-3CD	BR 103.1 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	342	30-Jan-20	12-Feb-20
[	TX-3CD	BR 103.1 General Arrangement & Substructure Plans-IFC	1	342	13-Feb-20	13-Feb-20
Superstructure Design			89	534	20-Jan-20	21-May-20
[	TX-3CD	BR 103.1 Develop Detail Drawings for Deck	20	344	20-Jan-20	14-Feb-20
[	TX-3CD	BR 103.1 Develop Design Superstructure Plans	20	344	17-Feb-20	13-Mar-20
[	TX-3CD	BR 103.1 Develop Complete Plans / Spec / Design Notebooks	30	535	16-Mar-20	24-Apr-20
[	TX-3CD	BR 103.1 Submit Superstructure	0	344	16-Mar-20	16-Mar-20
[	TX-3CD	BR 103.1 TxDOT/IE Review & Comments Superstructure Plans	10	481	17-Mar-20	26-Mar-20
[	TX-3CD	BR 103.1 Clear Comments Superstructure Plans	10	343	27-Mar-20	09-Apr-20
[	TX-3CD	BR 103.1 Superstructure Plans - IFC	1	343	10-Apr-20	10-Apr-20
[	TX-3CD	BR 103.1 Submit Complete Plans / Spec / Design Notebooks	0	535	27-Apr-20	27-Apr-20
[	TX-3CD	BR 103.1 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	748	27-Apr-20	06-May-20
[	TX-3CD	BR 103.1 Clear Comments Complete Plans / Spec / Design Notebooks	10	534	07-May-20	20-May-20
[	TX-3CD	BR 103.1 Complete Plans / Spec / Design Notebooks - IFC	1	534	21-May-20	21-May-20
BR 103.2 Westport Pkwy			179	761	19-Aug-19	23-Apr-20
Establish Criteria Procedures			30	610	19-Aug-19	27-Sep-19
[	TX-3CD	BR 103.2 Existing Bridge Info Review and Check	15	610	19-Aug-19	06-Sep-19
[	TX-3CD	BR 103.2 Bridge Design Criteria	15	610	09-Sep-19	27-Sep-19
Bridge Layouts			60	610	30-Sep-19	20-Dec-19
[	TX-3CD	BR 103.2 Develop General Arrangement Plans	20	610	30-Sep-19	25-Oct-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 103.2 Develop Detailed Calc	20	610	28-Oct-19	22-Nov-19
[	TX-3CD	BR 103.2 Develop Bridge Final Geometry Plans	20	630	28-Oct-19	22-Nov-19
[	TX-3CD	BR 103.2 Geotechnical Review & Checks	20	610	25-Nov-19	20-Dec-19
Substructure Design			39	624	23-Dec-19	13-Feb-20
[	TX-3CD	BR 103.2 Develop Detail Drawings Substructure	20	610	23-Dec-19	17-Jan-20
[	TX-3CD	BR 103.2 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	625	20-Jan-20	20-Jan-20
[	TX-3CD	BR 103.2 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	874	20-Jan-20	29-Jan-20
[	TX-3CD	BR 103.2 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	624	30-Jan-20	12-Feb-20
[	TX-3CD	BR 103.2 General Arrangement & Substructure Plans-IFC	1	624	13-Feb-20	13-Feb-20
Superstructure Design			69	761	20-Jan-20	23-Apr-20
[	TX-3CD	BR 103.2 Develop Detail Drawings for Deck	20	610	20-Jan-20	14-Feb-20
[	TX-3CD	BR 103.2 Develop Complete Plans / Spec / Design Notebooks	30	761	17-Feb-20	27-Mar-20
[	TX-3CD	BR 103.2 Develop Design Superstructure Plans	20	610	17-Feb-20	13-Mar-20
[	TX-3CD	BR 103.2 Submit Superstructure	0	610	16-Mar-20	16-Mar-20
[	TX-3CD	BR 103.2 TxDOT/IE Review & Comments Superstructure Plans	10	854	17-Mar-20	26-Mar-20
[	TX-3CD	BR 103.2 Clear Comments Superstructure Plans	10	610	27-Mar-20	09-Apr-20
[	TX-3CD	BR 103.2 Submit Complete Plans / Spec / Design Notebooks	0	761	30-Mar-20	30-Mar-20
[	TX-3CD	BR 103.2 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1065	30-Mar-20	08-Apr-20
[	TX-3CD	BR 103.2 Clear Comments Complete Plans / Spec / Design Notebooks	10	761	09-Apr-20	22-Apr-20
[	TX-3CD	BR 103.2 Superstructure Plans - IFC	1	610	10-Apr-20	10-Apr-20
[	TX-3CD	BR 103.2 Complete Plans / Spec / Design Notebooks - IFC	1	761	23-Apr-20	23-Apr-20
BR 103.3 Westport Pkwy			209	257	19-Aug-19	04-Jun-20
Establish Criteria Procedures			40	144	19-Aug-19	11-Oct-19
[	TX-3CD	BR 103.3 Existing Bridge Info Review and Check	30	144	19-Aug-19	27-Sep-19
[	TX-3CD	BR 103.3 Bridge Design Criteria	10	144	30-Sep-19	11-Oct-19
Bridge Layouts			60	144	14-Oct-19	03-Jan-20
[	TX-3CD	BR 103.3 Develop General Arrangement Plans	20	144	14-Oct-19	08-Nov-19
[	TX-3CD	BR 103.3 Develop Bridge Final Geometry Plans	20	164	11-Nov-19	06-Dec-19
[	TX-3CD	BR 103.3 Develop Detailed Calc	20	144	11-Nov-19	06-Dec-19
[	TX-3CD	BR 103.3 Geotechnical Review & Checks	20	144	09-Dec-19	03-Jan-20
Substructure Design			39	143	06-Jan-20	27-Feb-20
[	TX-3CD	BR 103.3 Develop Detail Drawings Substructure	20	144	06-Jan-20	31-Jan-20
[	TX-3CD	BR 103.3 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	145	03-Feb-20	03-Feb-20
[	TX-3CD	BR 103.3 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	201	03-Feb-20	12-Feb-20
[	TX-3CD	BR 103.3 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	143	13-Feb-20	26-Feb-20
[	TX-3CD	BR 103.3 General Arrangement & Substructure Plans-IFC	1	143	27-Feb-20	27-Feb-20
Superstructure Design			89	257	03-Feb-20	04-Jun-20
[	TX-3CD	BR 103.3 Develop Detail Drawings for Deck	20	144	03-Feb-20	28-Feb-20
[	TX-3CD	BR 103.3 Develop Design Superstructure Plans	20	144	02-Mar-20	27-Mar-20
[	TX-3CD	BR 103.3 Develop Complete Plans / Spec / Design Notebooks	30	257	30-Mar-20	08-May-20
[	TX-3CD	BR 103.3 Submit Superstructure	0	144	30-Mar-20	30-Mar-20
[	TX-3CD	BR 103.3 TxDOT/IE Review & Comments Superstructure Plans	10	202	31-Mar-20	09-Apr-20
[	TX-3CD	BR 103.3 Clear Comments Superstructure Plans	10	144	10-Apr-20	23-Apr-20
[	TX-3CD	BR 103.3 Superstructure Plans - IFC	1	144	24-Apr-20	24-Apr-20
[	TX-3CD	BR 103.3 Submit Complete Plans / Spec / Design Notebooks	0	257	11-May-20	11-May-20
[	TX-3CD	BR 103.3 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	359	11-May-20	20-May-20
[	TX-3CD	BR 103.3 Clear Comments Complete Plans / Spec / Design Notebooks	10	257	21-May-20	03-Jun-20
[	TX-3CD	BR 103.3 Complete Plans / Spec / Design Notebooks - IFC	1	257	04-Jun-20	04-Jun-20
3C2 - Bridge Design			192	887	06-Jun-19	28-Feb-20
BR 108.1 Keller-Hicks Rd			183	462	06-Jun-19	17-Feb-20
Bridge Layouts			31	315	05-Sep-19	17-Oct-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 108.1 Develop Bridge Final Geometry Plans	20	326	05-Sep-19	02-Oct-19
[	TX-3CD	BR 108.1 Develop General Arrangement Plans	30	315	05-Sep-19	16-Oct-19
[	TX-3CD	BR 108.1 Develop Detailed Calc	30	315	05-Sep-19	16-Oct-19
[	TX-3CD	BR 108.1 Geotechnical Review & Checks	1	315	17-Oct-19	17-Oct-19
Establish Criteria Procedures			65	315	06-Jun-19	04-Sep-19
[	TX-3CD	BR 108.1 Existing Bridge Info Review and Check	55	315	06-Jun-19	21-Aug-19
[	TX-3CD	BR 108.1 Bridge Design Criteria	10	315	22-Aug-19	04-Sep-19
Substructure Design			37	316	18-Oct-19	09-Dec-19
[	TX-3CD	BR 108.1 Develop Detail Drawings Substructure	20	315	18-Oct-19	14-Nov-19
[	TX-3CD	BR 108.1 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	316	15-Nov-19	15-Nov-19
[	TX-3CD	BR 108.1 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	442	15-Nov-19	24-Nov-19
[	TX-3CD	BR 108.1 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	316	25-Nov-19	06-Dec-19
[	TX-3CD	BR 108.1 General Arrangement & Substructure Plans-IFC	1	316	09-Dec-19	09-Dec-19
Superstructure Design			67	462	15-Nov-19	17-Feb-20
[	TX-3CD	BR 108.1 Develop Design Superstructure Plans	20	315	15-Nov-19	12-Dec-19
[	TX-3CD	BR 108.1 Develop Detail Drawings for Deck	20	315	15-Nov-19	12-Dec-19
[	TX-3CD	BR 108.1 Develop Complete Plans / Spec / Design Notebooks	20	461	13-Dec-19	09-Jan-20
[	TX-3CD	BR 108.1 Submit Superstructure	0	315	13-Dec-19	13-Dec-19
[	TX-3CD	BR 108.1 TxDOT/IE Review & Comments Superstructure Plans	10	442	14-Dec-19	23-Dec-19
[	TX-3CD	BR 108.1 Clear Comments Superstructure Plans	20	316	24-Dec-19	20-Jan-20
[	TX-3CD	BR 108.1 Submit Complete Plans / Spec / Design Notebooks	0	461	10-Jan-20	10-Jan-20
[	TX-3CD	BR 108.1 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	646	10-Jan-20	19-Jan-20
[	TX-3CD	BR 108.1 Clear Comments Complete Plans / Spec / Design Notebooks	20	462	20-Jan-20	14-Feb-20
[	TX-3CD	BR 108.1 Superstructure Plans - IFC	1	316	21-Jan-20	21-Jan-20
[	TX-3CD	BR 108.1 Complete Plans / Spec / Design Notebooks - IFC	1	462	17-Feb-20	17-Feb-20
BR 108.2 Keller-Hicks Rd			183	885	06-Jun-19	17-Feb-20
Bridge Layouts			31	747	05-Sep-19	17-Oct-19
[	TX-3CD	BR 108.2 Develop Bridge Final Geometry Plans	20	758	05-Sep-19	02-Oct-19
[	TX-3CD	BR 108.2 Develop General Arrangement Plans	30	747	05-Sep-19	16-Oct-19
[	TX-3CD	BR 108.2 Develop Detailed Calc	30	747	05-Sep-19	16-Oct-19
[	TX-3CD	BR 108.2 Geotechnical Review & Checks	1	747	17-Oct-19	17-Oct-19
Establish Criteria Procedures			65	747	06-Jun-19	04-Sep-19
[	TX-3CD	BR 108.2 Existing Bridge Info Review and Check	55	747	06-Jun-19	21-Aug-19
[	TX-3CD	BR 108.2 Bridge Design Criteria	10	747	22-Aug-19	04-Sep-19
Substructure Design			37	752	18-Oct-19	09-Dec-19
[	TX-3CD	BR 108.2 Develop Detail Drawings Substructure	20	747	18-Oct-19	14-Nov-19
[	TX-3CD	BR 108.2 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	751	15-Nov-19	15-Nov-19
[	TX-3CD	BR 108.2 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	1052	15-Nov-19	24-Nov-19
[	TX-3CD	BR 108.2 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	752	25-Nov-19	06-Dec-19
[	TX-3CD	BR 108.2 General Arrangement & Substructure Plans-IFC	1	752	09-Dec-19	09-Dec-19
Superstructure Design			67	885	15-Nov-19	17-Feb-20
[	TX-3CD	BR 108.2 Develop Design Superstructure Plans	20	747	15-Nov-19	12-Dec-19
[	TX-3CD	BR 108.2 Develop Detail Drawings for Deck	20	747	15-Nov-19	12-Dec-19
[	TX-3CD	BR 108.2 Submit Superstructure	0	747	13-Dec-19	13-Dec-19
[	TX-3CD	BR 108.2 Develop Complete Plans / Spec / Design Notebooks	20	883	13-Dec-19	09-Jan-20
[	TX-3CD	BR 108.2 TxDOT/IE Review & Comments Superstructure Plans	10	1047	14-Dec-19	23-Dec-19
[	TX-3CD	BR 108.2 Clear Comments Superstructure Plans	20	749	24-Dec-19	20-Jan-20
[	TX-3CD	BR 108.2 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1237	10-Jan-20	19-Jan-20
[	TX-3CD	BR 108.2 Submit Complete Plans / Spec / Design Notebooks	0	883	10-Jan-20	10-Jan-20
[	TX-3CD	BR 108.2 Clear Comments Complete Plans / Spec / Design Notebooks	20	885	20-Jan-20	14-Feb-20
[	TX-3CD	BR 108.2 Superstructure Plans - IFC	1	749	21-Jan-20	21-Jan-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 108.2 Complete Plans / Spec / Design Notebooks - IFC	1	885	17-Feb-20	17-Feb-20
BR 108.3 Keller-Hicks Rd			183	622	06-Jun-19	17-Feb-20
Bridge Layouts			31	446	05-Sep-19	17-Oct-19
[	TX-3CD	BR 108.3 Develop Bridge Final Geometry Plans	20	457	05-Sep-19	02-Oct-19
[	TX-3CD	BR 108.3 Develop General Arrangement Plans	30	446	05-Sep-19	16-Oct-19
[	TX-3CD	BR 108.3 Develop Detailed Calc	30	446	05-Sep-19	16-Oct-19
[	TX-3CD	BR 108.3 Geotechnical Review & Checks	1	446	17-Oct-19	17-Oct-19
Establish Criteria Procedures			65	446	06-Jun-19	04-Sep-19
[	TX-3CD	BR 108.3 Existing Bridge Info Review and Check	55	446	06-Jun-19	21-Aug-19
[	TX-3CD	BR 108.3 Bridge Design Criteria	10	446	22-Aug-19	04-Sep-19
Substructure Design			37	446	18-Oct-19	09-Dec-19
[	TX-3CD	BR 108.3 Develop Detail Drawings Substructure	20	446	18-Oct-19	14-Nov-19
[	TX-3CD	BR 108.3 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	624	15-Nov-19	24-Nov-19
[	TX-3CD	BR 108.3 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	446	15-Nov-19	15-Nov-19
[	TX-3CD	BR 108.3 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	446	25-Nov-19	06-Dec-19
[	TX-3CD	BR 108.3 General Arrangement & Substructure Plans-IFC	1	446	09-Dec-19	09-Dec-19
Superstructure Design			67	622	15-Nov-19	17-Feb-20
[	TX-3CD	BR 108.3 Develop Design Superstructure Plans	20	475	15-Nov-19	12-Dec-19
[	TX-3CD	BR 108.3 Develop Detail Drawings for Deck	20	475	15-Nov-19	12-Dec-19
[	TX-3CD	BR 108.3 Develop Complete Plans / Spec / Design Notebooks	20	621	13-Dec-19	09-Jan-20
[	TX-3CD	BR 108.3 Submit Superstructure	0	475	13-Dec-19	13-Dec-19
[	TX-3CD	BR 108.3 TxDOT/IE Review & Comments Superstructure Plans	10	666	14-Dec-19	23-Dec-19
[	TX-3CD	BR 108.3 Clear Comments Superstructure Plans	20	476	24-Dec-19	20-Jan-20
[	TX-3CD	BR 108.3 Submit Complete Plans / Spec / Design Notebooks	0	621	10-Jan-20	10-Jan-20
[	TX-3CD	BR 108.3 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	870	10-Jan-20	19-Jan-20
[	TX-3CD	BR 108.3 Clear Comments Complete Plans / Spec / Design Notebooks	20	622	20-Jan-20	14-Feb-20
[	TX-3CD	BR 108.3 Superstructure Plans - IFC	1	476	21-Jan-20	21-Jan-20
[	TX-3CD	BR 108.3 Complete Plans / Spec / Design Notebooks - IFC	1	622	17-Feb-20	17-Feb-20
BR 111.1 Golden Triangle Blvd			178	467	06-Jun-19	10-Feb-20
Establish Criteria Procedures			60	320	06-Jun-19	28-Aug-19
[	TX-3CD	BR 111.1 Existing Bridge Info Review and Check	50	320	06-Jun-19	14-Aug-19
[	TX-3CD	BR 111.1 Bridge Design Criteria	10	320	15-Aug-19	28-Aug-19
Bridge Layouts			31	320	29-Aug-19	10-Oct-19
[	TX-3CD	BR 111.1 Develop Bridge Final Geometry Plans	20	331	29-Aug-19	25-Sep-19
[	TX-3CD	BR 111.1 Develop General Arrangement Plans	30	320	29-Aug-19	09-Oct-19
[	TX-3CD	BR 111.1 Develop Detailed Calc	30	320	29-Aug-19	09-Oct-19
[	TX-3CD	BR 111.1 Geotechnical Review & Checks	1	320	10-Oct-19	10-Oct-19
Substructure Design			37	324	11-Oct-19	02-Dec-19
[	TX-3CD	BR 111.1 Develop Detail Drawings Substructure	20	320	11-Oct-19	07-Nov-19
[	TX-3CD	BR 111.1 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	322	08-Nov-19	08-Nov-19
[	TX-3CD	BR 111.1 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	452	08-Nov-19	17-Nov-19
[	TX-3CD	BR 111.1 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	324	18-Nov-19	29-Nov-19
[	TX-3CD	BR 111.1 General Arrangement & Substructure Plans-IFC	1	324	02-Dec-19	02-Dec-19
Superstructure Design			67	467	08-Nov-19	10-Feb-20
[	TX-3CD	BR 111.1 Develop Design Superstructure Plans	20	320	08-Nov-19	05-Dec-19
[	TX-3CD	BR 111.1 Develop Detail Drawings for Deck	20	320	08-Nov-19	05-Dec-19
[	TX-3CD	BR 111.1 Develop Complete Plans / Spec / Design Notebooks	20	466	06-Dec-19	02-Jan-20
[	TX-3CD	BR 111.1 Submit Superstructure	0	320	06-Dec-19	06-Dec-19
[	TX-3CD	BR 111.1 TxDOT/IE Review & Comments Superstructure Plans	10	449	07-Dec-19	16-Dec-19
[	TX-3CD	BR 111.1 Clear Comments Superstructure Plans	20	321	17-Dec-19	13-Jan-20
[	TX-3CD	BR 111.1 Submit Complete Plans / Spec / Design Notebooks	0	466	03-Jan-20	03-Jan-20

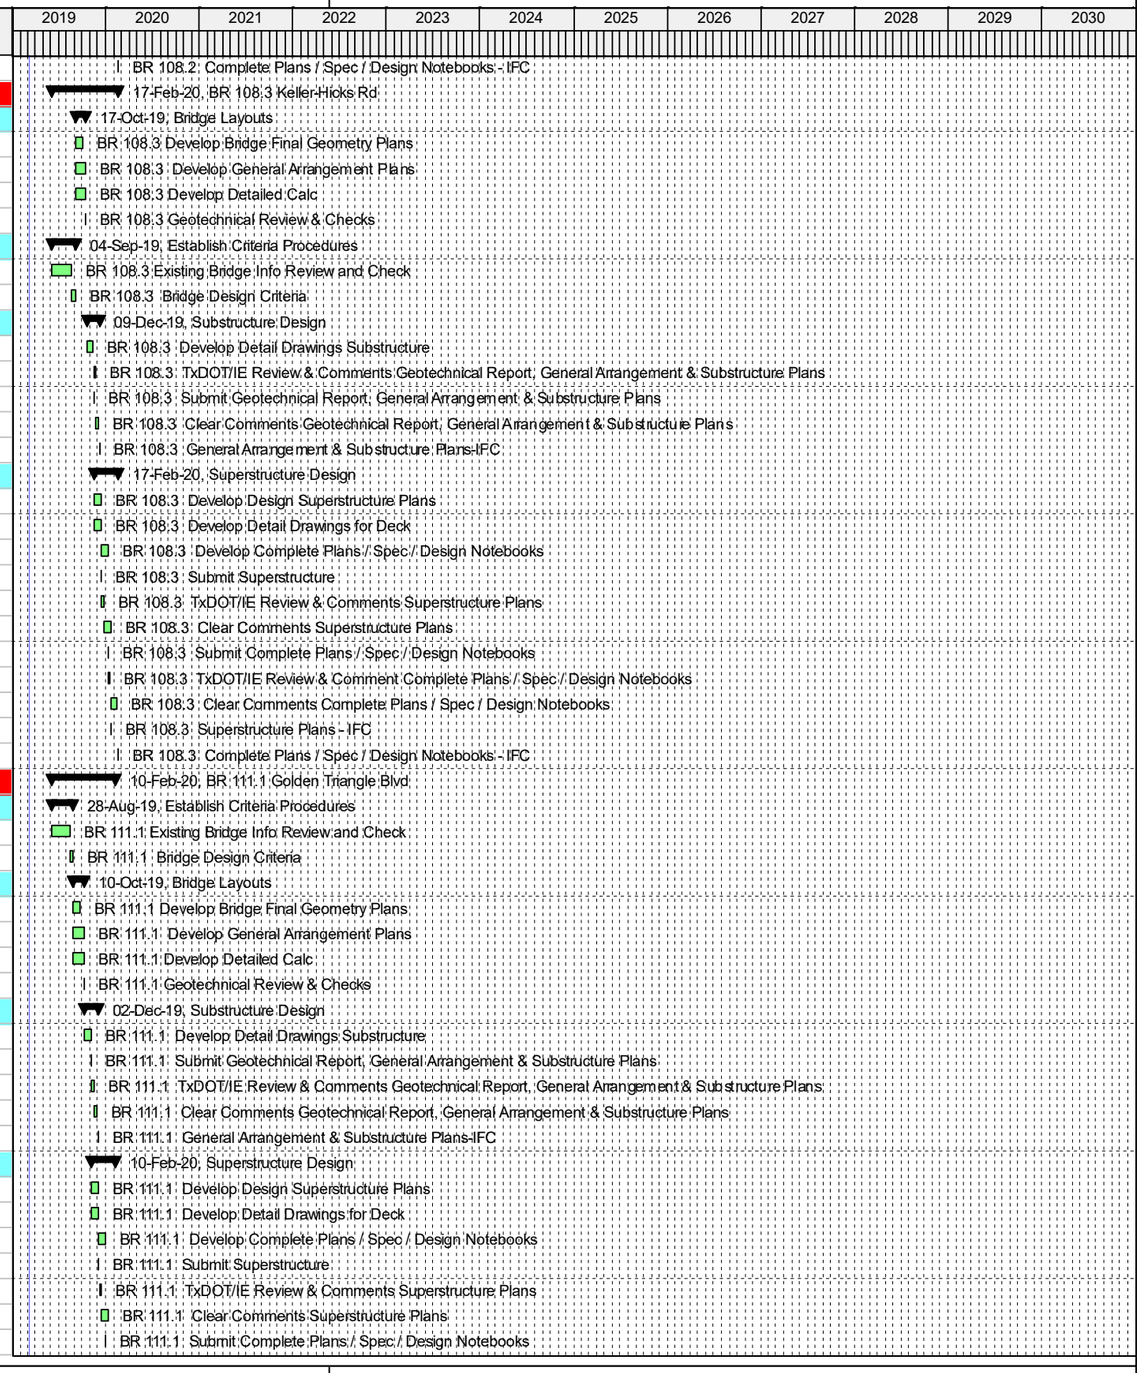

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 111.1 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	653	03-Jan-20	12-Jan-20
[	TX-3CD	BR 111.1 Clear Comments Complete Plans / Spec / Design Notebooks	20	467	13-Jan-20	07-Feb-20
[	TX-3CD	BR 111.1 Superstructure Plans - IFC	1	321	14-Jan-20	14-Jan-20
[	TX-3CD	BR 111.1 Complete Plans / Spec / Design Notebooks - IFC	1	467	10-Feb-20	10-Feb-20
BR 111.2 Golden Triangle Blvd			192	876	06-Jun-19	28-Feb-20
Establish Criteria Procedures			70	740	06-Jun-19	11-Sep-19
[	TX-3CD	BR 111.2 Existing Bridge Info Review and Check	60	740	06-Jun-19	28-Aug-19
[	TX-3CD	BR 111.2 Bridge Design Criteria	10	740	29-Aug-19	11-Sep-19
Bridge Layouts			31	740	12-Sep-19	24-Oct-19
[	TX-3CD	BR 111.2 Develop Bridge Final Geometry Plans	20	751	12-Sep-19	09-Oct-19
[	TX-3CD	BR 111.2 Develop General Arrangement Plans	30	740	12-Sep-19	23-Oct-19
[	TX-3CD	BR 111.2 Develop Detailed Calc	30	740	12-Sep-19	23-Oct-19
[	TX-3CD	BR 111.2 Geotechnical Review & Checks	1	740	24-Oct-19	24-Oct-19
Substructure Design			41	743	25-Oct-19	20-Dec-19
[	TX-3CD	BR 111.2 Develop Detail Drawings Substructure	20	740	25-Oct-19	21-Nov-19
[	TX-3CD	BR 111.2 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	14	1041	22-Nov-19	05-Dec-19
[	TX-3CD	BR 111.2 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	743	22-Nov-19	22-Nov-19
[	TX-3CD	BR 111.2 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	743	06-Dec-19	19-Dec-19
[	TX-3CD	BR 111.2 General Arrangement & Substructure Plans-IFC	1	743	20-Dec-19	20-Dec-19
Superstructure Design			71	876	22-Nov-19	28-Feb-20
[	TX-3CD	BR 111.2 Develop Design Superstructure Plans	20	740	22-Nov-19	19-Dec-19
[	TX-3CD	BR 111.2 Develop Detail Drawings for Deck	20	740	22-Nov-19	19-Dec-19
[	TX-3CD	BR 111.2 Develop Complete Plans / Spec / Design Notebooks	20	876	20-Dec-19	16-Jan-20
[	TX-3CD	BR 111.2 Submit Superstructure	0	740	20-Dec-19	20-Dec-19
[	TX-3CD	BR 111.2 TxDOT/IE Review & Comments Superstructure Plans	14	1036	21-Dec-19	03-Jan-20
[	TX-3CD	BR 111.2 Clear Comments Superstructure Plans	20	740	06-Jan-20	31-Jan-20
[	TX-3CD	BR 111.2 Submit Complete Plans / Spec / Design Notebooks	0	876	17-Jan-20	17-Jan-20
[	TX-3CD	BR 111.2 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	14	1226	17-Jan-20	30-Jan-20
[	TX-3CD	BR 111.2 Clear Comments Complete Plans / Spec / Design Notebooks	20	876	31-Jan-20	27-Feb-20
[	TX-3CD	BR 111.2 Superstructure Plans - IFC	1	740	03-Feb-20	03-Feb-20
[	TX-3CD	BR 111.2 Complete Plans / Spec / Design Notebooks - IFC	1	876	28-Feb-20	28-Feb-20
BR 111.3 Golden Triangle Blvd			192	613	06-Jun-19	28-Feb-20
Bridge Layouts			31	406	12-Sep-19	24-Oct-19
[	TX-3CD	BR 111.3 Develop Bridge Final Geometry Plans	20	417	12-Sep-19	09-Oct-19
[	TX-3CD	BR 111.3 Develop General Arrangement Plans	30	406	12-Sep-19	23-Oct-19
[	TX-3CD	BR 111.3 Develop Detailed Calc	30	406	12-Sep-19	23-Oct-19
[	TX-3CD	BR 111.3 Geotechnical Review & Checks	1	406	24-Oct-19	24-Oct-19
Establish Criteria Procedures			70	406	06-Jun-19	11-Sep-19
[	TX-3CD	BR 111.3 Existing Bridge Info Review and Check	60	406	06-Jun-19	28-Aug-19
[	TX-3CD	BR 111.3 Bridge Design Criteria	10	406	29-Aug-19	11-Sep-19
Substructure Design			41	437	25-Oct-19	20-Dec-19
[	TX-3CD	BR 111.3 Develop Detail Drawings Substructure	20	406	25-Oct-19	21-Nov-19
[	TX-3CD	BR 111.3 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	437	22-Nov-19	22-Nov-19
[	TX-3CD	BR 111.3 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	14	613	22-Nov-19	05-Dec-19
[	TX-3CD	BR 111.3 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	437	06-Dec-19	19-Dec-19
[	TX-3CD	BR 111.3 General Arrangement & Substructure Plans-IFC	1	437	20-Dec-19	20-Dec-19
Superstructure Design			71	613	22-Nov-19	28-Feb-20
[	TX-3CD	BR 111.3 Develop Design Superstructure Plans	20	406	22-Nov-19	19-Dec-19
[	TX-3CD	BR 111.3 Develop Detail Drawings for Deck	20	406	22-Nov-19	19-Dec-19
[	TX-3CD	BR 111.3 Develop Complete Plans / Spec / Design Notebooks	20	613	20-Dec-19	16-Jan-20
[	TX-3CD	BR 111.3 Submit Superstructure	0	406	20-Dec-19	20-Dec-19

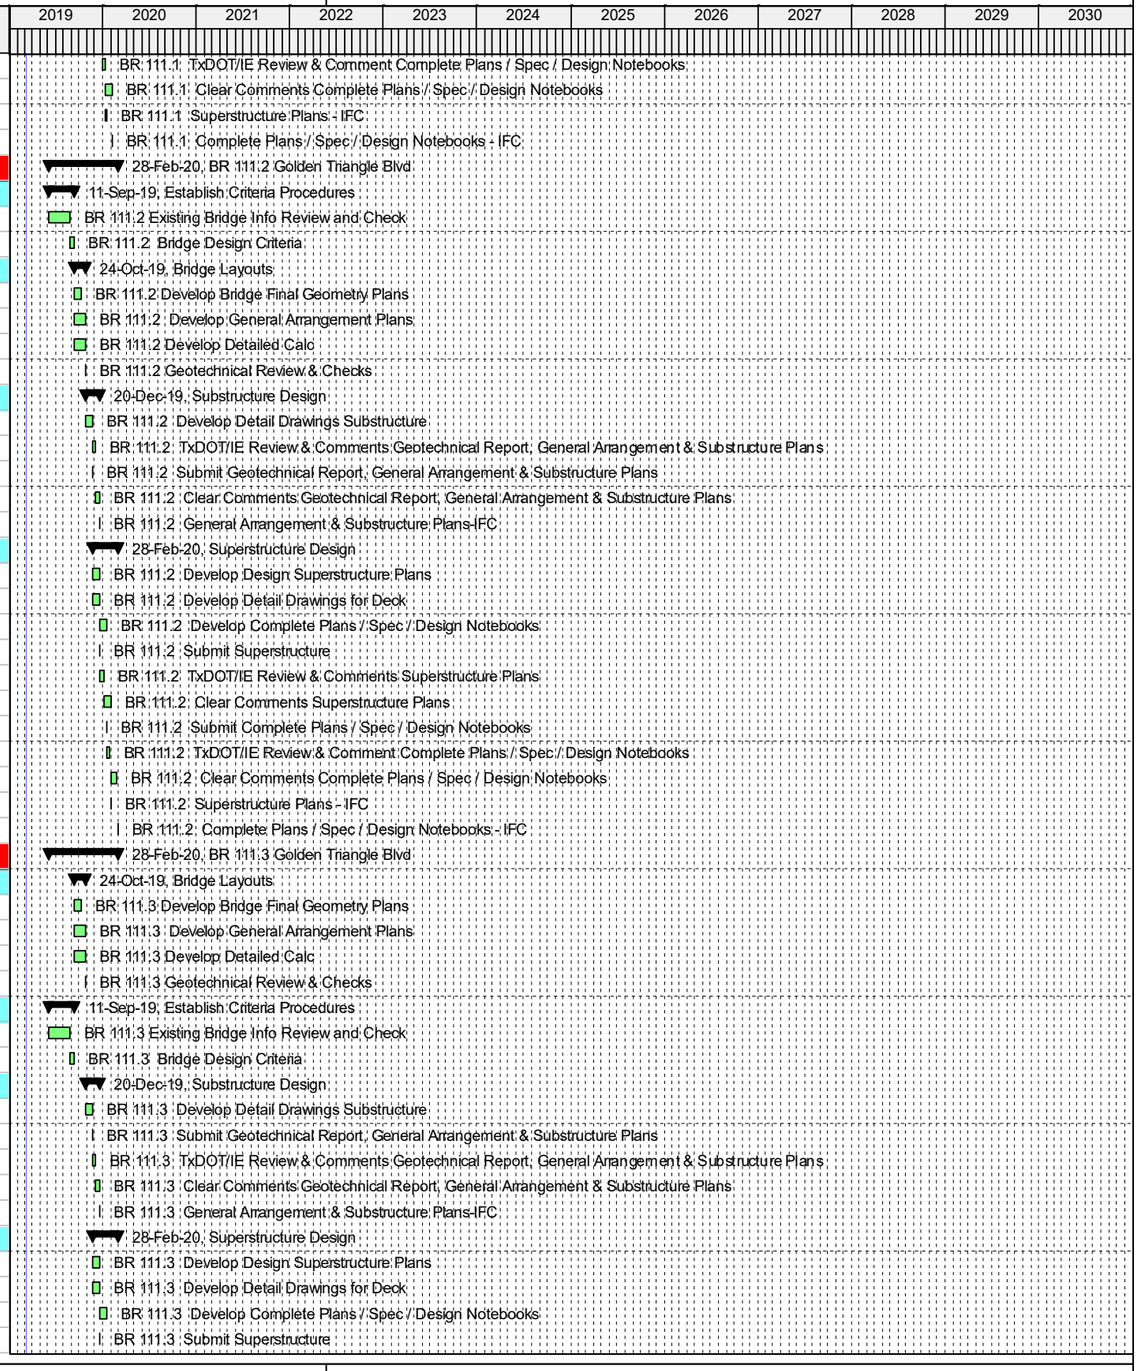

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 111.3 TxDOT/IE Review & Comments Superstructure Plans	14	570	21-Dec-19	03-Jan-20
[	TX-3CD	BR 111.3 Clear Comments Superstructure Plans	20	406	06-Jan-20	31-Jan-20
[	TX-3CD	BR 111.3 Submit Complete Plans / Spec / Design Notebooks	0	613	17-Jan-20	17-Jan-20
[	TX-3CD	BR 111.3 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	14	859	17-Jan-20	30-Jan-20
[	TX-3CD	BR 111.3 Clear Comments Complete Plans / Spec / Design Notebooks	20	613	31-Jan-20	27-Feb-20
[	TX-3CD	BR 111.3 Superstructure Plans - IFC	1	406	03-Feb-20	03-Feb-20
[	TX-3CD	BR 111.3 Complete Plans / Spec / Design Notebooks - IFC	1	613	28-Feb-20	28-Feb-20
BR 120, 121, 122 & 123 SH170 DC			182	633	06-Jun-19	14-Feb-20
Establish Criteria Procedures			60	208	06-Jun-19	28-Aug-19
[	TX-3CD	BR 120, 121, 122 & 123 Existing Bridge Info Review and Check	50	208	06-Jun-19	14-Aug-19
[	TX-3CD	BR 120, 121, 122 & 123 Bridge Design Criteria	10	208	15-Aug-19	28-Aug-19
Bridge Layouts			31	208	29-Aug-19	10-Oct-19
[	TX-3CD	BR 120, 121, 122 & 123 Develop Bridge Final Geometry Plans	20	219	29-Aug-19	25-Sep-19
[	TX-3CD	BR 120, 121, 122 & 123 Develop General Arrangement Plans	30	208	29-Aug-19	09-Oct-19
[	TX-3CD	BR 120, 121, 122 & 123 Develop Detailed Calc	30	208	29-Aug-19	09-Oct-19
[	TX-3CD	BR 120, 121, 122 & 123 Geotechnical Review & Checks	1	208	10-Oct-19	10-Oct-19
Substructure Design			41	683	11-Oct-19	06-Dec-19
[	TX-3CD	BR 120, 121, 122 & 123 Develop Detail Drawings Substructure	20	208	11-Oct-19	07-Nov-19
[	TX-3CD	BR 120, 121, 122 & 123 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	683	08-Nov-19	08-Nov-19
[	TX-3CD	BR 120, 121, 122 & 123 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement	14	957	08-Nov-19	21-Nov-19
[	TX-3CD	BR 120, 121, 122 & 123 Clear Comments Geotechnical Report, General Arrangement & Substructure	10	683	22-Nov-19	05-Dec-19
[	TX-3CD	BR 120, 121, 122 & 123 General Arrangement & Substructure Plans-IFC	1	683	06-Dec-19	06-Dec-19
Superstructure Design			71	368	08-Nov-19	14-Feb-20
[	19-Feb-	BR 120, 121, 122 & 123 Develop Design Superstructure Plans	20	208	08-Nov-19	05-Dec-19
[	TX-3CD	BR 120, 121, 122 & 123 Develop Detail Drawings for Deck	20	208	08-Nov-19	05-Dec-19
[	TX-3CD	BR 120, 121, 122 & 123 Develop Complete Plans / Spec / Design Notebooks	20	368	06-Dec-19	02-Jan-20
[	TX-3CD	BR 120, 121, 122 & 123 Submit Superstructure	0	208	06-Dec-19	06-Dec-19
[	TX-3CD	BR 120, 121, 122 & 123 TxDOT/IE Review & Comments Superstructure Plans	14	292	07-Dec-19	20-Dec-19
[	TX-3CD	BR 120, 121, 122 & 123 Clear Comments Superstructure Plans	20	208	23-Dec-19	17-Jan-20
[	TX-3CD	BR 120, 121, 122 & 123 Submit Complete Plans / Spec / Design Notebooks	0	368	03-Jan-20	03-Jan-20
[	TX-3CD	BR 120, 121, 122 & 123 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	14	516	03-Jan-20	16-Jan-20
[	TX-3CD	BR 120, 121, 122 & 123 Clear Comments Complete Plans / Spec / Design Notebooks	20	368	17-Jan-20	13-Feb-20
[	TX-3CD	BR 120, 121, 122 & 123 Superstructure Plans - IFC	1	208	20-Jan-20	20-Jan-20
[	TX-3CD	BR 120, 121, 122 & 123 Complete Plans / Spec / Design Notebooks - IFC	1	368	14-Feb-20	14-Feb-20
BR 114 &115			186	893	06-Jun-19	20-Feb-20
Establish Criteria Procedures			60	645	06-Jun-19	28-Aug-19
[	TX-3CD	BR 114 & 115 Existing Bridge Info Review and Check	50	645	06-Jun-19	14-Aug-19
[	TX-3CD	BR 114 & 115 Bridge Design Criteria	10	645	15-Aug-19	28-Aug-19
Bridge Layouts			31	645	29-Aug-19	10-Oct-19
[	TX-3CD	BR 114 & 115 Develop General Arrangement Plans	30	645	29-Aug-19	09-Oct-19
[	TX-3CD	BR 114 & 115 Develop Detailed Calc	30	645	29-Aug-19	09-Oct-19
[	TX-3CD	BR 114 & 115 Develop Bridge Final Geometry Plans	20	656	29-Aug-19	25-Sep-19
[	TX-3CD	BR 114 & 115 Geotechnical Review & Checks	1	645	10-Oct-19	10-Oct-19
Substructure Design			45	650	11-Oct-19	12-Dec-19
[	TX-3CD	BR 114 & 115 Develop Detail Drawings Substructure	20	645	11-Oct-19	07-Nov-19
[	TX-3CD	BR 114 & 115 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	650	08-Nov-19	08-Nov-19
[	TX-3CD	BR 114 & 115 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substruc	14	650	08-Nov-19	27-Nov-19
[	TX-3CD	BR 114 & 115 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	650	28-Nov-19	11-Dec-19
[	TX-3CD	BR 114 & 115 General Arrangement & Substructure Plans-IFC	1	650	12-Dec-19	12-Dec-19
Superstructure Design			75	893	08-Nov-19	20-Feb-20
[	TX-3CD	BR 114 & 115 Develop Design Superstructure Plans	20	645	08-Nov-19	05-Dec-19

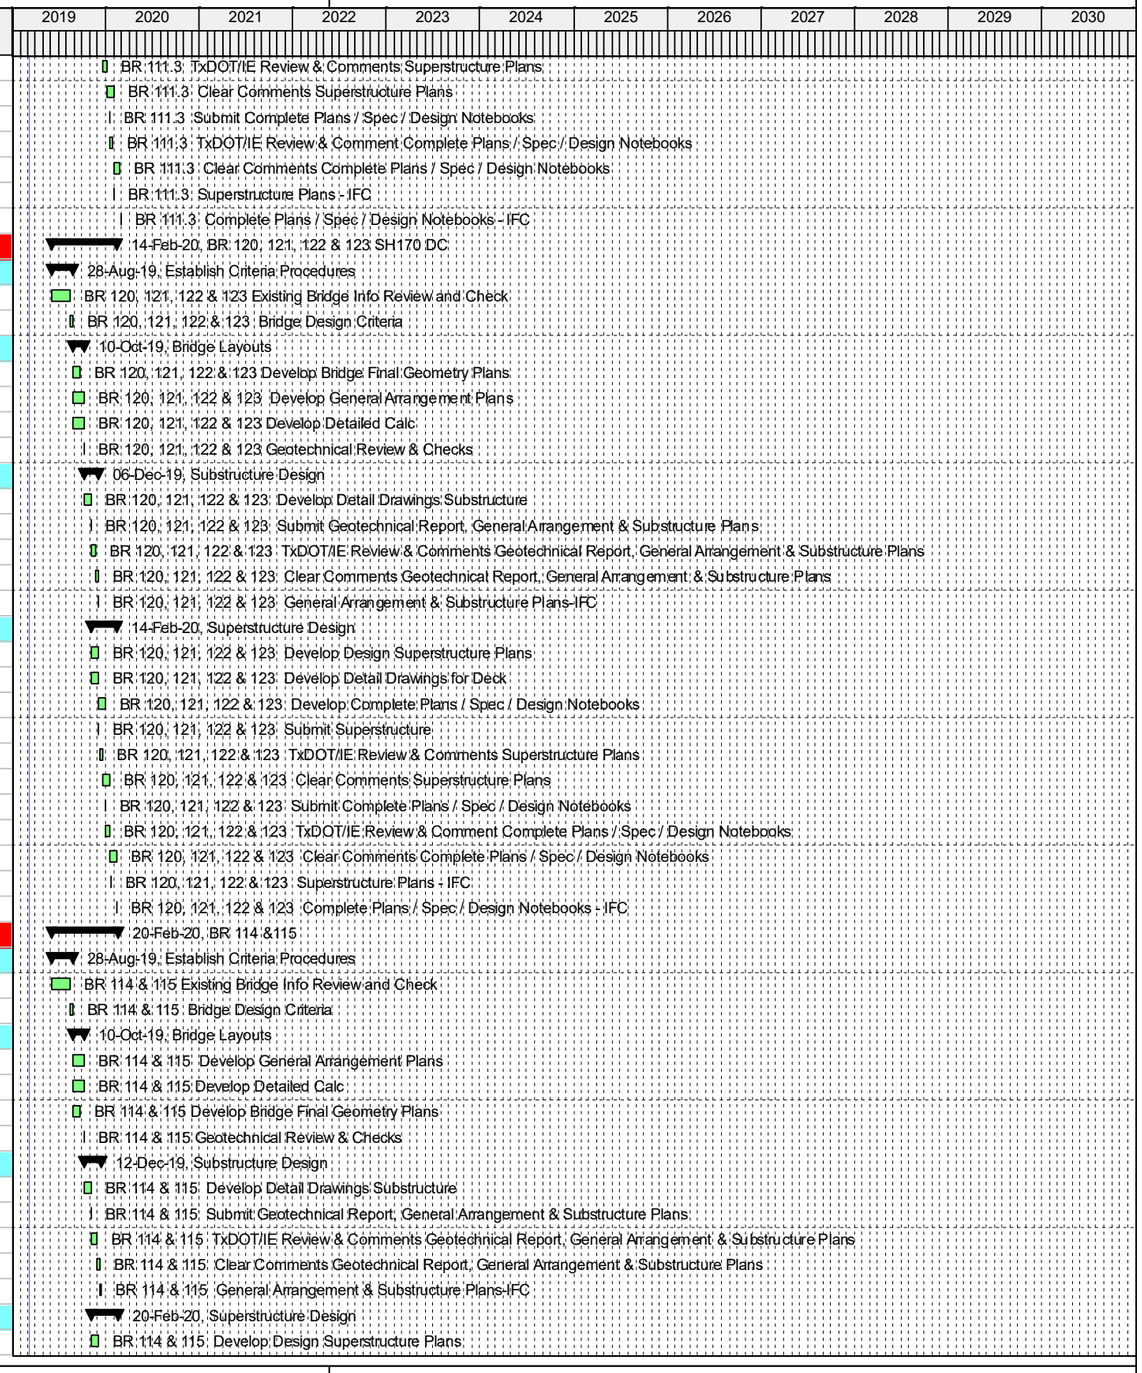

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 114 & 115 Develop Detail Drawings for Deck	20	645	08-Nov-19	05-Dec-19
[	TX-3CD	BR 114 & 115 Develop Complete Plans / Spec / Design Notebooks	20	893	06-Dec-19	02-Jan-20
[	TX-3CD	BR 114 & 115 Submit Superstructure	0	645	06-Dec-19	06-Dec-19
[	TX-3CD	BR 114 & 115 TxDOT/IE Review & Comments Superstructure Plans	14	645	09-Dec-19	26-Dec-19
[	TX-3CD	BR 114 & 115 Clear Comments Superstructure Plans	20	645	27-Dec-19	23-Jan-20
[	TX-3CD	BR 114 & 115 Submit Complete Plans / Spec / Design Notebooks	0	893	03-Jan-20	03-Jan-20
[	TX-3CD	BR 114 & 115 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	14	893	03-Jan-20	22-Jan-20
[	TX-3CD	BR 114 & 115 Clear Comments Complete Plans / Spec / Design Notebooks	20	893	23-Jan-20	19-Feb-20
[	TX-3CD	BR 114 & 115 Superstructure Plans - IFC	1	645	24-Jan-20	24-Jan-20
[	TX-3CD	BR 114 & 115 Complete Plans / Spec / Design Notebooks - IFC	1	893	20-Feb-20	20-Feb-20
3C3 - Bridge Design			139	929	06-Jun-19	17-Dec-19
BR 113.1 NB Heritage Trace Pkwy Braided Ramp			138	930	06-Jun-19	16-Dec-19
Establish Criteria Procedures			20	746	06-Jun-19	03-Jul-19
[	TX-3CD	BR 113.1 Existing Bridge Info Review and Check	10	746	06-Jun-19	19-Jun-19
[	TX-3CD	BR 113.1 Bridge Design Criteria	10	746	20-Jun-19	03-Jul-19
Bridge Layouts			31	746	04-Jul-19	15-Aug-19
[	TX-3CD	BR 113.1 Develop Bridge Final Geometry Plans	20	757	04-Jul-19	31-Jul-19
[	TX-3CD	BR 113.1 Develop General Arrangement Plans	30	746	04-Jul-19	14-Aug-19
[	TX-3CD	BR 113.1 Develop Detailed Calc	30	746	04-Jul-19	14-Aug-19
[	TX-3CD	BR 113.1 Geotechnical Review & Checks	1	746	15-Aug-19	15-Aug-19
Substructure Design			37	747	16-Aug-19	07-Oct-19
[	TX-3CD	BR 113.1 Develop Detail Drawings Substructure	20	746	16-Aug-19	12-Sep-19
[	TX-3CD	BR 113.1 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	746	13-Sep-19	13-Sep-19
[	TX-3CD	BR 113.1 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	1045	13-Sep-19	22-Sep-19
[	TX-3CD	BR 113.1 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	747	23-Sep-19	04-Oct-19
[	TX-3CD	BR 113.1 General Arrangement & Substructure Plans-IFC	1	747	07-Oct-19	07-Oct-19
Superstructure Design			67	930	13-Sep-19	16-Dec-19
[	TX-3CD	BR 113.1 Develop Design Superstructure Plans	10	792	13-Sep-19	26-Sep-19
[	TX-3CD	BR 113.1 Develop Detail Drawings for Deck	20	792	13-Sep-19	10-Oct-19
[	TX-3CD	BR 113.1 Develop Complete Plans / Spec / Design Notebooks	30	928	27-Sep-19	07-Nov-19
[	TX-3CD	BR 113.1 Submit Superstructure	0	792	27-Sep-19	27-Sep-19
[	TX-3CD	BR 113.1 TxDOT/IE Review & Comments Superstructure Plans	10	1110	28-Sep-19	07-Oct-19
[	TX-3CD	BR 113.1 Clear Comments Superstructure Plans	20	794	08-Oct-19	04-Nov-19
[	TX-3CD	BR 113.1 Superstructure Plans - IFC	1	794	05-Nov-19	05-Nov-19
[	TX-3CD	BR 113.1 Submit Complete Plans / Spec / Design Notebooks	0	928	08-Nov-19	08-Nov-19
[	TX-3CD	BR 113.1 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1300	08-Nov-19	17-Nov-19
[	TX-3CD	BR 113.1 Clear Comments Complete Plans / Spec / Design Notebooks	20	930	18-Nov-19	13-Dec-19
[	TX-3CD	BR 113.1 Complete Plans / Spec / Design Notebooks - IFC	1	930	16-Dec-19	16-Dec-19
BR 113.2 SB Heritage Trace Pkwy Braided Ramp			139	929	06-Jun-19	17-Dec-19
Establish Criteria Procedures			20	761	06-Jun-19	03-Jul-19
[	TX-3CD	BR 113.2 Existing Bridge Info Review and Check	10	761	06-Jun-19	19-Jun-19
[	TX-3CD	BR 113.2 Bridge Design Criteria	10	761	20-Jun-19	03-Jul-19
Bridge Layouts			31	761	04-Jul-19	15-Aug-19
[	TX-3CD	BR 113.2 Develop Bridge Final Geometry Plans	20	772	04-Jul-19	31-Jul-19
[	TX-3CD	BR 113.2 Develop General Arrangement Plans	30	761	04-Jul-19	14-Aug-19
[	TX-3CD	BR 113.2 Develop Detailed Calc	30	761	04-Jul-19	14-Aug-19
[	TX-3CD	BR 113.2 Geotechnical Review & Checks	1	761	15-Aug-19	15-Aug-19
Substructure Design			37	762	16-Aug-19	07-Oct-19
[	TX-3CD	BR 113.2 Develop Detail Drawings Substructure	20	761	16-Aug-19	12-Sep-19
[	TX-3CD	BR 113.2 Submit Geotechnical Report, General Arrangement & Substructure Plans	0	761	13-Sep-19	13-Sep-19
[	TX-3CD	BR 113.2 TxDOT/IE Review & Comments Geotechnical Report, General Arrangement & Substructure	10	1066	13-Sep-19	22-Sep-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	BR 113.2 Clear Comments Geotechnical Report, General Arrangement & Substructure Plans	10	762	23-Sep-19	04-Oct-19
[	TX-3CD	BR 113.2 General Arrangement & Substructure Plans-IFC	1	762	07-Oct-19	07-Oct-19
Superstructure Design			68	929	13-Sep-19	17-Dec-19
[	TX-3CD	BR 113.2 Develop Design Superstructure Plans	20	781	13-Sep-19	10-Oct-19
[	TX-3CD	BR 113.2 Develop Detail Drawings for Deck	20	781	13-Sep-19	10-Oct-19
[	TX-3CD	BR 113.2 Submit Superstructure	1	781	11-Oct-19	11-Oct-19
[	TX-3CD	BR 113.2 Develop Complete Plans / Spec / Design Notebooks	20	927	11-Oct-19	07-Nov-19
[	TX-3CD	BR 113.2 TxDOT/IE Review & Comments Superstructure Plans	10	1093	15-Oct-19	24-Oct-19
[	TX-3CD	BR 113.2 Clear Comments Superstructure Plans	20	781	25-Oct-19	21-Nov-19
[	TX-3CD	BR 113.2 Submit Complete Plans / Spec / Design Notebooks	1	927	08-Nov-19	08-Nov-19
[	TX-3CD	BR 113.2 TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebooks	10	1299	09-Nov-19	18-Nov-19
[	TX-3CD	BR 113.2 Clear Comments Complete Plans / Spec / Design Notebooks	20	929	19-Nov-19	16-Dec-19
[	TX-3CD	BR 113.2 Superstructure Plans - IFC	1	781	22-Nov-19	22-Nov-19
[	TX-3CD	BR 113.2 Complete Plans / Spec / Design Notebooks - IFC	1	929	17-Dec-19	17-Dec-19
BR 13A & 22 IH 820 Design			48	467	01-Aug-19	07-Oct-19
BR 13A & 22 Establish Criteria Procedures			10	22	01-Aug-19	14-Aug-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Conceptual Design Bridge	5	22	01-Aug-19	07-Aug-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Bridge Design Criteria & Geotech	5	22	08-Aug-19	14-Aug-19
BR 13A & 22 Bridge Layouts			6	22	15-Aug-19	22-Aug-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop Bridge Final Geometry Plans	5	23	15-Aug-19	21-Aug-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop General Arrangement Plans	5	22	15-Aug-19	21-Aug-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop Detailed Calc	5	22	15-Aug-19	21-Aug-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Geotechnical Review & Checks	1	22	22-Aug-19	22-Aug-19
BR 13A & 22 Substructure Design			22	166	23-Aug-19	23-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop Detail Drawings Substructure	10	22	23-Aug-19	05-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Submit Geotechnical Report, General Arrangement & Substructure Plans	0	166	06-Sep-19	06-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp TxDOT/IE Review & Comments Geotechnical Report, General Arrangemer	10	232	06-Sep-19	15-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Clear Comments Geotechnical Report, General Arrangement & Substructu	5	166	16-Sep-19	20-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp General Arrangement & Substructure Plans-IFC	1	166	23-Sep-19	23-Sep-19
BR 13A & 22 Superstructure Design			22	467	06-Sep-19	07-Oct-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop Complete Plans / Spec / Design Notebooks	10	466	06-Sep-19	19-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop Design Superstructure Plans	9	22	06-Sep-19	18-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Develop Detail Drawings for Deck	10	22	06-Sep-19	19-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Submit Superstructure	0	22	19-Sep-19	19-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Submit Complete Plans / Spec / Design Notebooks	0	466	20-Sep-19	20-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp TxDOT/IE Review & Comment Complete Plans / Spec / Design Notebook:	10	653	20-Sep-19	29-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp TxDOT/IE Review & Comments Superstructure Plans	10	32	20-Sep-19	29-Sep-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Clear Comments Complete Plans / Spec / Design Notebooks	5	467	30-Sep-19	04-Oct-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Clear Comments Superstructure Plans	5	24	30-Sep-19	04-Oct-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Complete Plans / Spec / Design Notebooks - IFC	1	467	07-Oct-19	07-Oct-19
DBI	TX-3CD	BR 13A & 22 IH 820 Ramp Superstructure Plans - IFC	1	24	07-Oct-19	07-Oct-19
Retaining Wall Design			78	30	27-Jun-19	14-Oct-19
DRTW10	TX-3CD	Preliminary Locations of the Retaining Walls	20	47	27-Jun-19	24-Jul-19
DRTW10	TX-3CD	Preliminary Layout of the Retaining Walls	10	30	19-Aug-19	30-Aug-19
DRTW10	TX-3CD	Existing Retaining Wall Info Review and Check	10	30	02-Sep-19	13-Sep-19
DRTW10	TX-3CD	RW Design Criteria	10	30	16-Sep-19	27-Sep-19
DRTW10	TX-3CD	RW Tipology/Material/Const Method Preliminary Analysis	10	30	16-Sep-19	27-Sep-19
DRTW10	TX-3CD	RW Geotechnical Recommendations	10	30	16-Sep-19	27-Sep-19
DRTW10	TX-3CD	RW Develop Final Geometry Plans	10	30	16-Sep-19	27-Sep-19
DRTW10	TX-3CD	RW Preliminary Geometry & Layout	10	30	16-Sep-19	27-Sep-19
DRTW10	TX-3CD	RW Develop Aesthetic Elements	10	30	30-Sep-19	11-Oct-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
DRTW10	TX-3CD	RW Wall Specifications Complete	1	30	14-Oct-19	14-Oct-19
Traffic Management			57	111	04-Apr-19	23-Jun-19
Traffic Control Planning			48	120	04-Apr-19	10-Jun-19
DTC1(	TX-3CD	Collecting of existing traffic data	20	118	04-Apr-19	01-May-19
DTC1(	TX-3CD	Criteria for traffic management design.	20	118	04-Apr-19	01-May-19
DTC1(	TX-3CD	Analysis of collected information	10	118	02-May-19	15-May-19
DTC1(	TX-3CD	Develop conceptual options for traffic management	10	118	02-May-19	15-May-19
DTC1(	TX-3CD	Definition of General construction phases	10	118	16-May-19	29-May-19
DTC1(	TX-3CD	Develop traffic management plans for Early Packages	1	118	30-May-19	30-May-19
DTC1(	TX-3CD	TxDOT review of Traffic Management Plans	10	166	31-May-19	09-Jun-19
DTC1(	TX-3CD	Traffic Management Plans Stanards	1	120	10-Jun-19	10-Jun-19
Traffic Control Systems			57	111	04-Apr-19	23-Jun-19
DTC1(	TX-3CD	Signalization layout with location	20	121	04-Apr-19	01-May-19
	TX-3CD	Traffic signals foundation design	10	121	04-Apr-19	17-Apr-19
DTC1(	TX-3CD	Traffic Studies Noise	20	121	04-Apr-19	01-May-19
DTC1(	TX-3CD	Traffic data collection	10	131	04-Apr-19	17-Apr-19
DTC1(	TX-3CD	Develop Traffic Control Systems Standards	20	121	02-May-19	29-May-19
DTC1(	TX-3CD	Traffic Studies Segments	20	121	02-May-19	29-May-19
DTC1(	TX-3CD	TxDOT review of Traffic Control Systems	10	155	13-Jun-19	22-Jun-19
DTC1(	TX-3CD	Traffic Control Systems Stanards	1	155	23-Jun-19	23-Jun-19
Environmental			227	100	04-Apr-19	14-Feb-20
Erosion Control/SWPPP Plans			50	100	09-Dec-19	14-Feb-20
DENV	TX-3CD	Develop SWPPP and Control Plans	30	100	09-Dec-19	17-Jan-20
DENV	TX-3CD	QA/QC of SWPPP and Control Plans	5	100	20-Jan-20	24-Jan-20
DENV	TX-3CD	Submit SWPPP and Control Plans	1	100	27-Jan-20	27-Jan-20
DENV	TX-3CD	TxDOT/IE Review SWPPP and Control Plans	10	140	28-Jan-20	06-Feb-20
DENV	TX-3CD	Finalize SWPPP and Control Plans	5	100	07-Feb-20	13-Feb-20
DENV	TX-3CD	Submit NOI to TCEQ	1	100	14-Feb-20	14-Feb-20
Noise Walls			84	84	04-Apr-19	30-Jul-19
DENV	TX-3CD	Collecting Traffic Data and Previous Existing Studies	20	84	04-Apr-19	01-May-19
DENV	TX-3CD	Develop Noise Study Analysis	20	84	02-May-19	29-May-19
DENV	TX-3CD	Noise Analysis Draft Report	20	84	30-May-19	26-Jun-19
DENV	TX-3CD	Noise Wall Locations Feasibility	20	84	03-Jul-19	30-Jul-19
Environmental Mitigation			96	159	15-Jul-19	25-Nov-19
DENV	TX-3CD	ESA III Develop Initial Removal Control Plans	60	159	15-Jul-19	04-Oct-19
DENV	TX-3CD	Develop Final Removal Control Plans	20	159	07-Oct-19	01-Nov-19
DENV	TX-3CD	Final Removal Control Plans to TxDOT/IE for the Facility	14	223	02-Nov-19	15-Nov-19
DENV	TX-3CD	Final Removal Control Plans - Clear Comments	5	159	18-Nov-19	22-Nov-19
DENV	TX-3CD	Forward to Required Agencies	1	159	25-Nov-19	25-Nov-19
Landscape & Aesthetics			117	51	04-Apr-19	13-Sep-19
Landscape			107	61	04-Apr-19	30-Aug-19
DLANI	TX-3CD	TxDOT Establish Landscaping & Aesthetics Committee	1	74	04-Apr-19	04-Apr-19
DLANI	TX-3CD	Identify Issues that Will Impact Corridor	10	81	05-Apr-19	18-Apr-19
DLANI	TX-3CD	Identify Materials, Forms, and Finishes	20	91	05-Apr-19	02-May-19
DLANI	TX-3CD	Identify Themes and Regional Examples	20	61	05-Apr-19	02-May-19
DLANI	TX-3CD	Identify Existing Character of Corridor	20	81	19-Apr-19	16-May-19
DLANI	TX-3CD	Detailed Presentation to Stakeholders	5	61	03-May-19	09-May-19
DLANI	TX-3CD	Establish Regional Appropriate Design Themes	20	61	10-May-19	06-Jun-19
DLANI	TX-3CD	Develop Plan Palette	20	66	10-May-19	06-Jun-19
DLANI	TX-3CD	Identify Cost Sharing Opportunities	5	61	07-Jun-19	13-Jun-19
DLANI	TX-3CD	Prepare Three Aesthetic Concepts	10	61	14-Jun-19	27-Jun-19

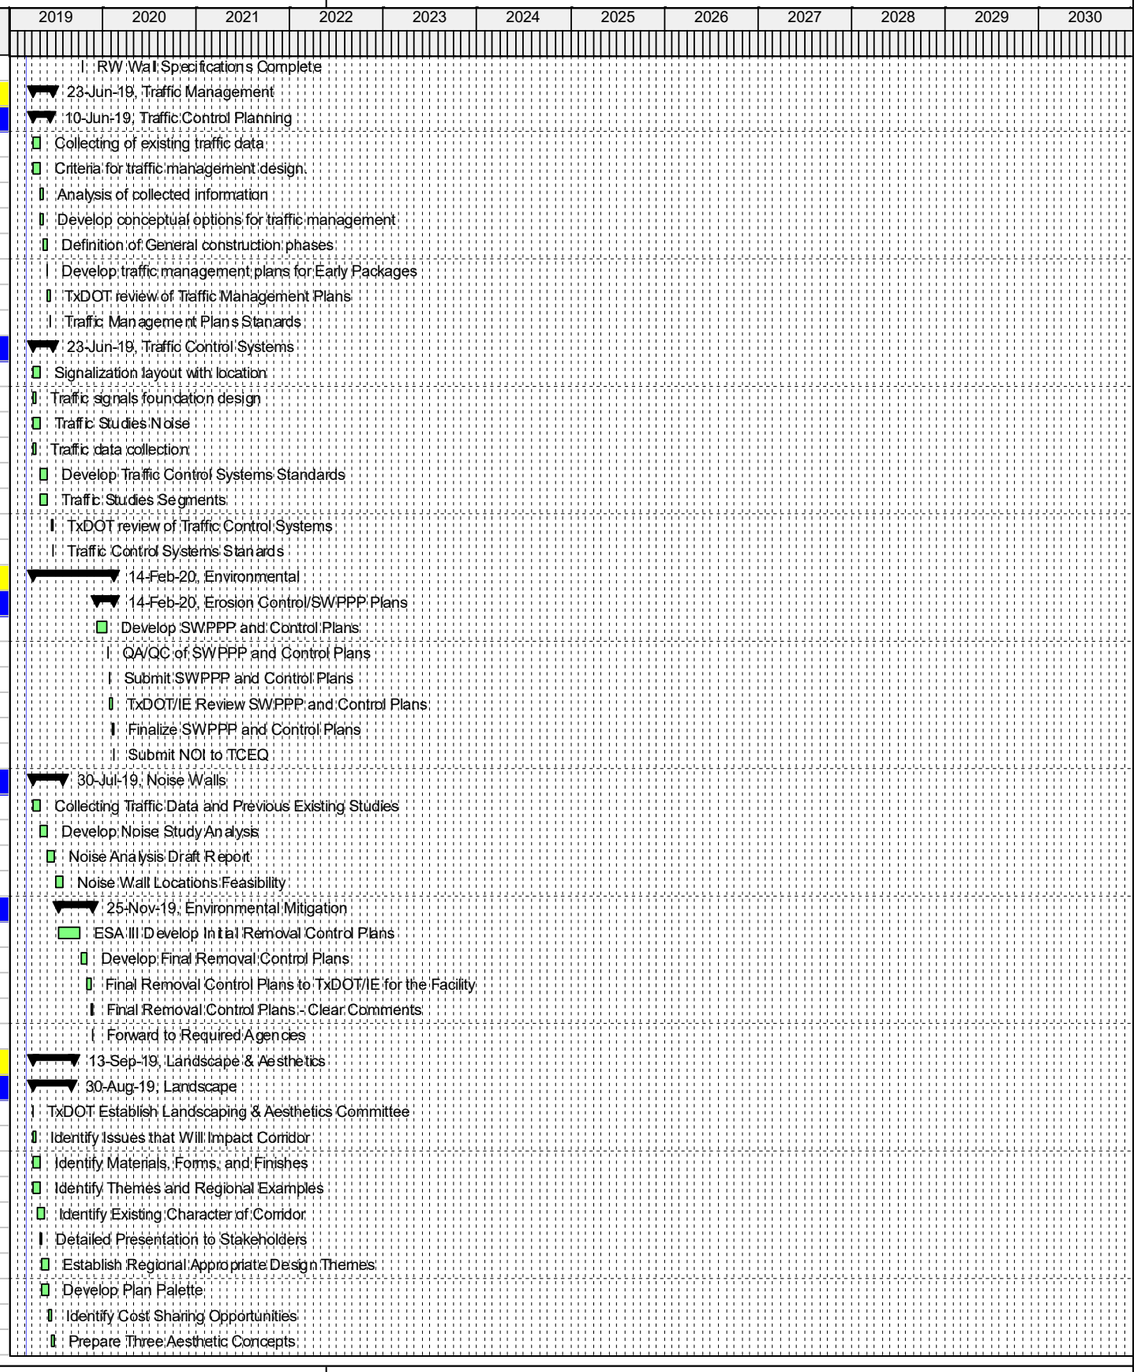

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
DLANI	TX-3CD	TxDOT Review/Approve Landscape Plan Concept	10	85	28-Jun-19	07-Jul-19
DLANI	TX-3CD	Landscape Plan Concept - Clear Comments	5	61	08-Jul-19	12-Jul-19
DLANI	TX-3CD	Final Drawings & Graphics for Landscaping Elements	10	61	15-Jul-19	26-Jul-19
DLANI	TX-3CD	Final Drawings & Graphics for Hardscape Elements	10	61	15-Jul-19	26-Jul-19
DLANI	TX-3CD	Final Drawings & Graphics for Misc Elements	10	61	15-Jul-19	26-Jul-19
DLANI	TX-3CD	Final Landscape Plan	10	61	29-Jul-19	09-Aug-19
DLANI	TX-3CD	Submittal for Final Landscape Plan	0	61	12-Aug-19	12-Aug-19
DLANI	TX-3CD	TxDOT/IE Approval of Final Landscape Plan	14	85	12-Aug-19	25-Aug-19
DLANI	TX-3CD	Final Landscape Plan Clear Comments	5	61	26-Aug-19	30-Aug-19
Aesthetics			116	51	05-Apr-19	13-Sep-19
DAES	TX-3CD	Identify Issues that Will Impact Corridor	14	52	05-Apr-19	24-Apr-19
DAES	TX-3CD	Identify Issues that Will Impact Corridor	12	59	25-Apr-19	10-May-19
DAES	TX-3CD	Identify Existing Character of Corridor	12	59	25-Apr-19	10-May-19
DAES	TX-3CD	Identify Materials, Forms, and Finishes	12	59	25-Apr-19	10-May-19
DAES	TX-3CD	Identify Themes and Regional Examples	12	59	25-Apr-19	10-May-19
DAES	TX-3CD	Initial Feedback from Stakeholder Meeting	14	52	25-Apr-19	14-May-19
DAES	TX-3CD	Detailed Presentation to Stakeholders	5	52	15-May-19	21-May-19
DAES	TX-3CD	Control Level & Consistency Through the Corridor	10	52	22-May-19	04-Jun-19
DAES	TX-3CD	Establish Regional Appropriate Design Themes	10	52	22-May-19	04-Jun-19
DAES	TX-3CD	Develop Aesthetic Concept	10	52	05-Jun-19	18-Jun-19
DAES	TX-3CD	Submit to TxDOT Three Aesthetic Concepts	1	52	19-Jun-19	19-Jun-19
DAES	TX-3CD	TxDOT Review/Approve Aesthetic Concept	10	72	20-Jun-19	29-Jun-19
DAES	TX-3CD	Aesthetic Concept - Clear Comments	5	51	01-Jul-19	05-Jul-19
DAES	TX-3CD	Final Drawings & Graphics for Bridge Elements	10	56	08-Jul-19	19-Jul-19
DAES	TX-3CD	Final Drawings & Graphics for Lighting, Signal, Signing and Gantry Elements	10	56	08-Jul-19	19-Jul-19
DAES	TX-3CD	Final Drawings & Graphics for Misc Elements	10	56	08-Jul-19	19-Jul-19
DAES	TX-3CD	Final Drawings & Graphics for Retaining Wall Elements	15	51	08-Jul-19	26-Jul-19
DAES	TX-3CD	Final Drawings & Graphics for Noise Wall Elements	15	51	08-Jul-19	26-Jul-19
DAES	TX-3CD	Final Aesthetic Plan	20	51	29-Jul-19	23-Aug-19
DAES	TX-3CD	Submittal for Final Aesthetic Plan	0	51	26-Aug-19	26-Aug-19
DAES	TX-3CD	TxDOT/IE Approval of Final Aesthetic Plan	14	71	26-Aug-19	08-Sep-19
DAES	TX-3CD	Final Aesthetic Plan Clear Comments	5	51	09-Sep-19	13-Sep-19
3C Electrical Design			303	837	04-Apr-19	01-Jun-20
DELECT	TX-3CD	Lighting Criteria for the Facility	20	106	04-Apr-19	01-May-19
DELECT	TX-3CD	Traffic data collection	20	107	04-Apr-19	01-May-19
DELECT	TX-3CD	Collecting Existing Lighting Information	20	106	04-Apr-19	01-May-19
DELECT	TX-3CD	Collecting Third Party Requirements for Lighting	20	106	04-Apr-19	01-May-19
DELECT	TX-3CD	Preliminary Lighting Layout	20	106	02-May-19	29-May-19
DELECT	TX-3CD	Collecting Existing Traffic Data Information	20	107	02-May-19	29-May-19
DELECT	TX-3CD	Develop warrant studies for intersection not currently signalized	20	127	02-May-19	29-May-19
DELECT	TX-3CD	Lighting Analysis and Calculations	20	106	30-May-19	26-Jun-19
DELECT	TX-3CD	Collecting Existing Traffic Data Information	20	107	30-May-19	26-Jun-19
DELECT	TX-3CD	Verification of TxDOTStandards for Approved Traffic Signal Systems	1	107	27-Jun-19	27-Jun-19
DELECT	TX-3CD	Verification of TxDOTStandards for Approved Lighting Design	1	106	28-Jun-19	28-Jun-19
3C1 Electrical			241	837	01-Jul-19	01-Jun-20
3C1 Illumination			241	822	01-Jul-19	01-Jun-20
DEI	TX-3CD	Area 3C1 Develop Illumination Plans (30% Plans)	20	945	01-Jul-19	26-Jul-19
DEI	TX-3CD	Area 3C1 Submit Illumination Plans for Review (30% Plans)	1	1325	27-Jul-19	27-Jul-19
DEI	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans (30% Plans)	10	1325	28-Jul-19	06-Aug-19
DEI	TX-3CD	Area 3C1 Illumination Plans - Clear Comments (30% Plans)	10	947	07-Aug-19	20-Aug-19
DEI	TX-3CD	Area 3C1 Illumination Plans - (30% Plans)	1	947	21-Aug-19	21-Aug-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
DEI	TX-3CD	Area 3C1 Develop Illumination Plans (60% Plans)	20	947	22-Aug-19	18-Sep-19
DEI	TX-3CD	Area 3C1 Submit Illumination Plans for Review (60% Plans)	1	1327	19-Sep-19	19-Sep-19
DEI	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans (60% Plans)	10	1327	20-Sep-19	29-Sep-19
DEI	TX-3CD	Area 3C1 Illumination Plans - Clear Comments (60% Plans)	10	949	30-Sep-19	11-Oct-19
DEI	TX-3CD	Area 3C1 Illumination Plans - (60% Plans)	1	949	14-Oct-19	14-Oct-19
Segment 3C1 Illumination			39	822	08-Apr-20	01-Jun-20
[	TX-3CD	Area 3C1 Develop Illumination Plans	20	823	08-Apr-20	05-May-20
[	TX-3CD	Area 3C1 Submit Illumination Plans for Review	1	1151	06-May-20	06-May-20
[	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans	10	1151	07-May-20	16-May-20
[	TX-3CD	Area 3C1 Final Illumination Plans - Clear Comments	10	822	18-May-20	29-May-20
[	TX-3CD	Area 3C1 Final Illumination Plans - IFC	1	822	01-Jun-20	01-Jun-20
3C1 Traffic Signal Systems			38	1040	01-Jul-19	21-Aug-19
DEI	TX-3CD	Area 3C Develop Traffic Signal Systems	20	1040	01-Jul-19	26-Jul-19
DEI	TX-3CD	Area 3C Submit Traffic Signal Systems for Review	1	1456	27-Jul-19	27-Jul-19
DEI	TX-3CD	Area 3C TxDOT/IE Review & Comment Traffic Signal Systems	10	1456	28-Jul-19	06-Aug-19
DEI	TX-3CD	Area 3C Final Traffic Signal Systems - Clear Comments	10	1040	07-Aug-19	20-Aug-19
DEI	TX-3CD	Area 3C Final Traffic Signal Systems - IFC	1	1040	21-Aug-19	21-Aug-19
Segment 3C1 Traffic Systems			38	1040	01-Jul-19	21-Aug-19
[	TX-3CD	Area 3C Develop Traffic System Plans	20	1040	01-Jul-19	26-Jul-19
[	TX-3CD	Area 3C Submit Traffic System Plans for Review	1	1456	27-Jul-19	27-Jul-19
[	TX-3CD	Area 3C TxDOT/IE Review & Comment Traffic System Plans	10	1456	28-Jul-19	06-Aug-19
[	TX-3CD	Area 3C Final Traffic System Plans - Clear Comments	10	1040	07-Aug-19	20-Aug-19
[	TX-3CD	Area 3C Final Traffic System Plans - IFC	1	1040	21-Aug-19	21-Aug-19
3C2 Electrical			241	837	01-Jul-19	01-Jun-20
3C2 Illumination			241	822	01-Jul-19	01-Jun-20
DEI	TX-3CD	Area 3C1 Develop Illumination Plans (30% Plans)	20	945	01-Jul-19	26-Jul-19
DEI	TX-3CD	Area 3C1 Submit Illumination Plans for Review (30% Plans)	1	1325	27-Jul-19	27-Jul-19
DEI	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans (30% Plans)	10	1325	28-Jul-19	06-Aug-19
DEI	TX-3CD	Area 3C1 Illumination Plans - Clear Comments (30% Plans)	10	947	07-Aug-19	20-Aug-19
DEI	TX-3CD	Area 3C1 Illumination Plans - (30% Plans)	1	947	21-Aug-19	21-Aug-19
DEI	TX-3CD	Area 3C1 Develop Illumination Plans (60% Plans)	20	947	22-Aug-19	18-Sep-19
DEI	TX-3CD	Area 3C1 Submit Illumination Plans for Review (60% Plans)	1	1327	19-Sep-19	19-Sep-19
DEI	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans (60% Plans)	10	1327	20-Sep-19	29-Sep-19
DEI	TX-3CD	Area 3C1 Illumination Plans - Clear Comments (60% Plans)	10	949	30-Sep-19	11-Oct-19
DEI	TX-3CD	Area 3C1 Illumination Plans - (60% Plans)	1	949	14-Oct-19	14-Oct-19
Segment 3C2 Illumination			39	822	08-Apr-20	01-Jun-20
[	TX-3CD	Area 3C1 Develop Illumination Plans	20	823	08-Apr-20	05-May-20
[	TX-3CD	Area 3C1 Submit Illumination Plans for Review	1	1151	06-May-20	06-May-20
[	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans	10	1151	07-May-20	16-May-20
[	TX-3CD	Area 3C1 Final Illumination Plans - Clear Comments	10	822	18-May-20	29-May-20
[	TX-3CD	Area 3C1 Final Illumination Plans - IFC	1	822	01-Jun-20	01-Jun-20
3C2 Traffic Signal Systems			38	1040	01-Jul-19	21-Aug-19
DEI	TX-3CD	Area 3C Develop Traffic Signal Systems	20	1040	01-Jul-19	26-Jul-19
DEI	TX-3CD	Area 3C Submit Traffic Signal Systems for Review	1	1456	27-Jul-19	27-Jul-19
DEI	TX-3CD	Area 3C TxDOT/IE Review & Comment Traffic Signal Systems	10	1456	28-Jul-19	06-Aug-19
DEI	TX-3CD	Area 3C Final Traffic Signal Systems - Clear Comments	10	1040	07-Aug-19	20-Aug-19
DEI	TX-3CD	Area 3C Final Traffic Signal Systems - IFC	1	1040	21-Aug-19	21-Aug-19
Segment 3C2 Traffic Systems			38	1040	01-Jul-19	21-Aug-19
[	TX-3CD	Area 3C Develop Traffic System Plans	20	1040	01-Jul-19	26-Jul-19
[	TX-3CD	Area 3C Submit Traffic System Plans for Review	1	1456	27-Jul-19	27-Jul-19
[	TX-3CD	Area 3C TxDOT/IE Review & Comment Traffic System Plans	10	1456	28-Jul-19	06-Aug-19

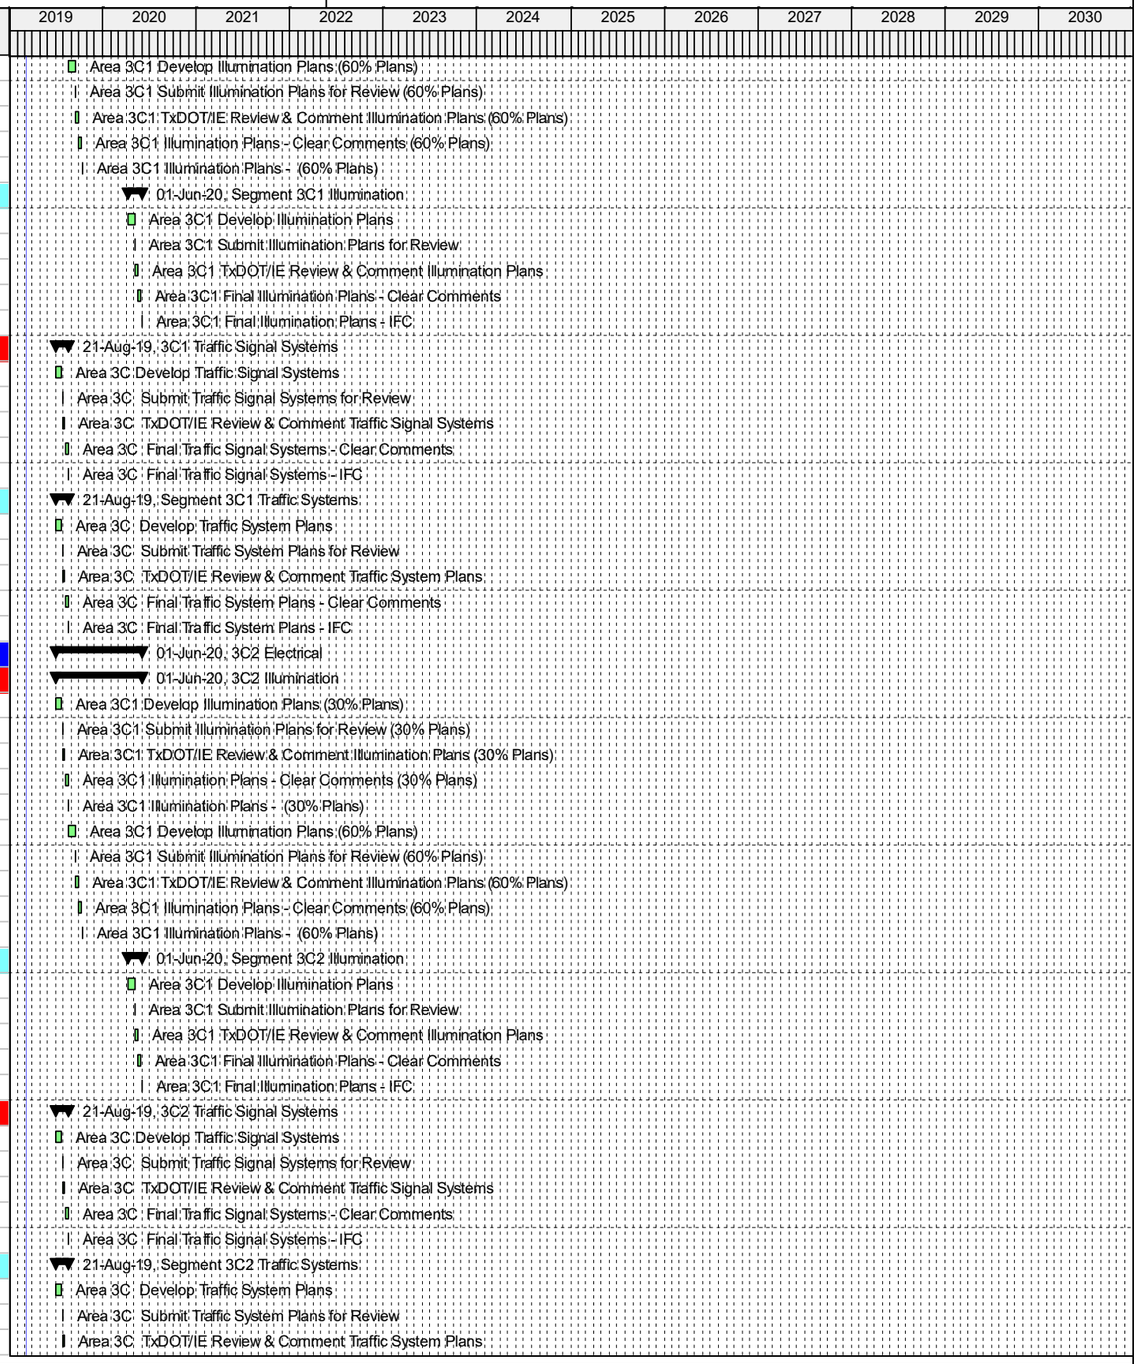

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
[	TX-3CD	Area 3C Final Traffic System Plans - Clear Comments	10	1040	07-Aug-19	20-Aug-19
[	TX-3CD	Area 3C Final Traffic System Plans - IFC	1	1040	21-Aug-19	21-Aug-19
3C3 Electrical			241	837	01-Jul-19	01-Jun-20
3C3 Illumination			241	822	01-Jul-19	01-Jun-20
DEI	TX-3CD	Area 3C1 Develop Illumination Plans (30% Plans)	20	945	01-Jul-19	26-Jul-19
DEI	TX-3CD	Area 3C1 Submit Illumination Plans for Review (30% Plans)	1	1325	27-Jul-19	27-Jul-19
DEI	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans (30% Plans)	10	1325	28-Jul-19	06-Aug-19
DEI	TX-3CD	Area 3C1 Illumination Plans - Clear Comments (30% Plans)	10	947	07-Aug-19	20-Aug-19
DEI	TX-3CD	Area 3C1 Illumination Plans - (30% Plans)	1	947	21-Aug-19	21-Aug-19
DEI	TX-3CD	Area 3C1 Develop Illumination Plans (60% Plans)	20	947	22-Aug-19	18-Sep-19
DEI	TX-3CD	Area 3C1 Submit Illumination Plans for Review (60% Plans)	1	1327	19-Sep-19	19-Sep-19
DEI	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans (60% Plans)	10	1327	20-Sep-19	29-Sep-19
DEI	TX-3CD	Area 3C1 Illumination Plans - Clear Comments (60% Plans)	10	949	30-Sep-19	11-Oct-19
DEI	TX-3CD	Area 3C1 Illumination Plans - (60% Plans)	1	949	14-Oct-19	14-Oct-19
Segment 3C3 Illumination			39	822	08-Apr-20	01-Jun-20
[	TX-3CD	Area 3C1 Develop Illumination Plans	20	823	08-Apr-20	05-May-20
[	TX-3CD	Area 3C1 Submit Illumination Plans for Review	1	1151	06-May-20	06-May-20
[	TX-3CD	Area 3C1 TxDOT/IE Review & Comment Illumination Plans	10	1151	07-May-20	16-May-20
[	TX-3CD	Area 3C1 Final Illumination Plans - Clear Comments	10	822	18-May-20	29-May-20
[	TX-3CD	Area 3C1 Final Illumination Plans - IFC	1	822	01-Jun-20	01-Jun-20
3C3 Traffic Signal Systems			38	1040	01-Jul-19	21-Aug-19
DEI	TX-3CD	Area 3C Develop Traffic Signal Systems	20	1040	01-Jul-19	26-Jul-19
DEI	TX-3CD	Area 3C Submit Traffic Signal Systems for Review	1	1456	27-Jul-19	27-Jul-19
DEI	TX-3CD	Area 3C TxDOT/IE Review & Comment Traffic Signal Systems	10	1456	28-Jul-19	06-Aug-19
DEI	TX-3CD	Area 3C Final Traffic Signal Systems - Clear Comments	10	1040	07-Aug-19	20-Aug-19
DEI	TX-3CD	Area 3C Final Traffic Signal Systems - IFC	1	1040	21-Aug-19	21-Aug-19
Segment 3C3 Traffic Systems			38	1040	01-Jul-19	21-Aug-19
[	TX-3CD	Area 3C Develop Traffic System Plans	20	1040	01-Jul-19	26-Jul-19
[	TX-3CD	Area 3C Submit Traffic System Plans for Review	1	1456	27-Jul-19	27-Jul-19
[	TX-3CD	Area 3C TxDOT/IE Review & Comment Traffic System Plans	10	1456	28-Jul-19	06-Aug-19
[	TX-3CD	Area 3C Final Traffic System Plans - Clear Comments	10	1040	07-Aug-19	20-Aug-19
[	TX-3CD	Area 3C Final Traffic System Plans - IFC	1	1040	21-Aug-19	21-Aug-19
ITS &TCS Design			81	15	15-Jul-19	04-Nov-19
Duct Bank System & Power Supply			20	17	15-Jul-19	09-Aug-19
DITS1(	TX-3CD	Determine Conduit Needs for Tolling	20	17	15-Jul-19	09-Aug-19
ITS/TCS Equipment & Structures			81	15	15-Jul-19	04-Nov-19
DITS1(	TX-3CD	Determine Final Tolling Features Location	20	17	15-Jul-19	09-Aug-19
DITS1(	TX-3CD	Tolling Infrastructure Foundation Design	20	14	18-Jul-19	14-Aug-19
DITS1(	TX-3CD	Design Verification to 3A & Procure Tolling Equipment	40	14	15-Aug-19	09-Oct-19
DITS1(	TX-3CD	TxDOT/IE for Review and Comments of the Tolling Equipment with Locations	10	20	10-Oct-19	19-Oct-19
DITS1(	TX-3CD	Tolling Equipment Design clear comments	10	15	21-Oct-19	01-Nov-19
DITS1(	TX-3CD	Tolling Equipment Design Standards	1	15	04-Nov-19	04-Nov-19
Signage and Marking Design			113	1007	02-May-19	07-Oct-19
Signing Specifications			74	171	02-May-19	13-Aug-19
DSM1(	TX-3CD	Develop draft Plan for preliminary operational signing schematics	20	89	02-May-19	29-May-19
DSM1(	TX-3CD	Submittal to TxDOT/IE for review and comments of the draft preliminary operational signing schematics	10	125	30-May-19	08-Jun-19
DSM1(	TX-3CD	Draft Plan for preliminary operational signing schematics, clear comments	10	89	30-May-19	12-Jun-19
DSM1(	TX-3CD	Signing criteria	5	170	13-Jun-19	19-Jun-19
DSM1(	TX-3CD	Signing criteria	10	89	13-Jun-19	26-Jun-19
DSM1(	TX-3CD	Sign foundations calculations	10	89	13-Jun-19	26-Jun-19
DSM1(	TX-3CD	Special signs location	10	170	20-Jun-19	03-Jul-19

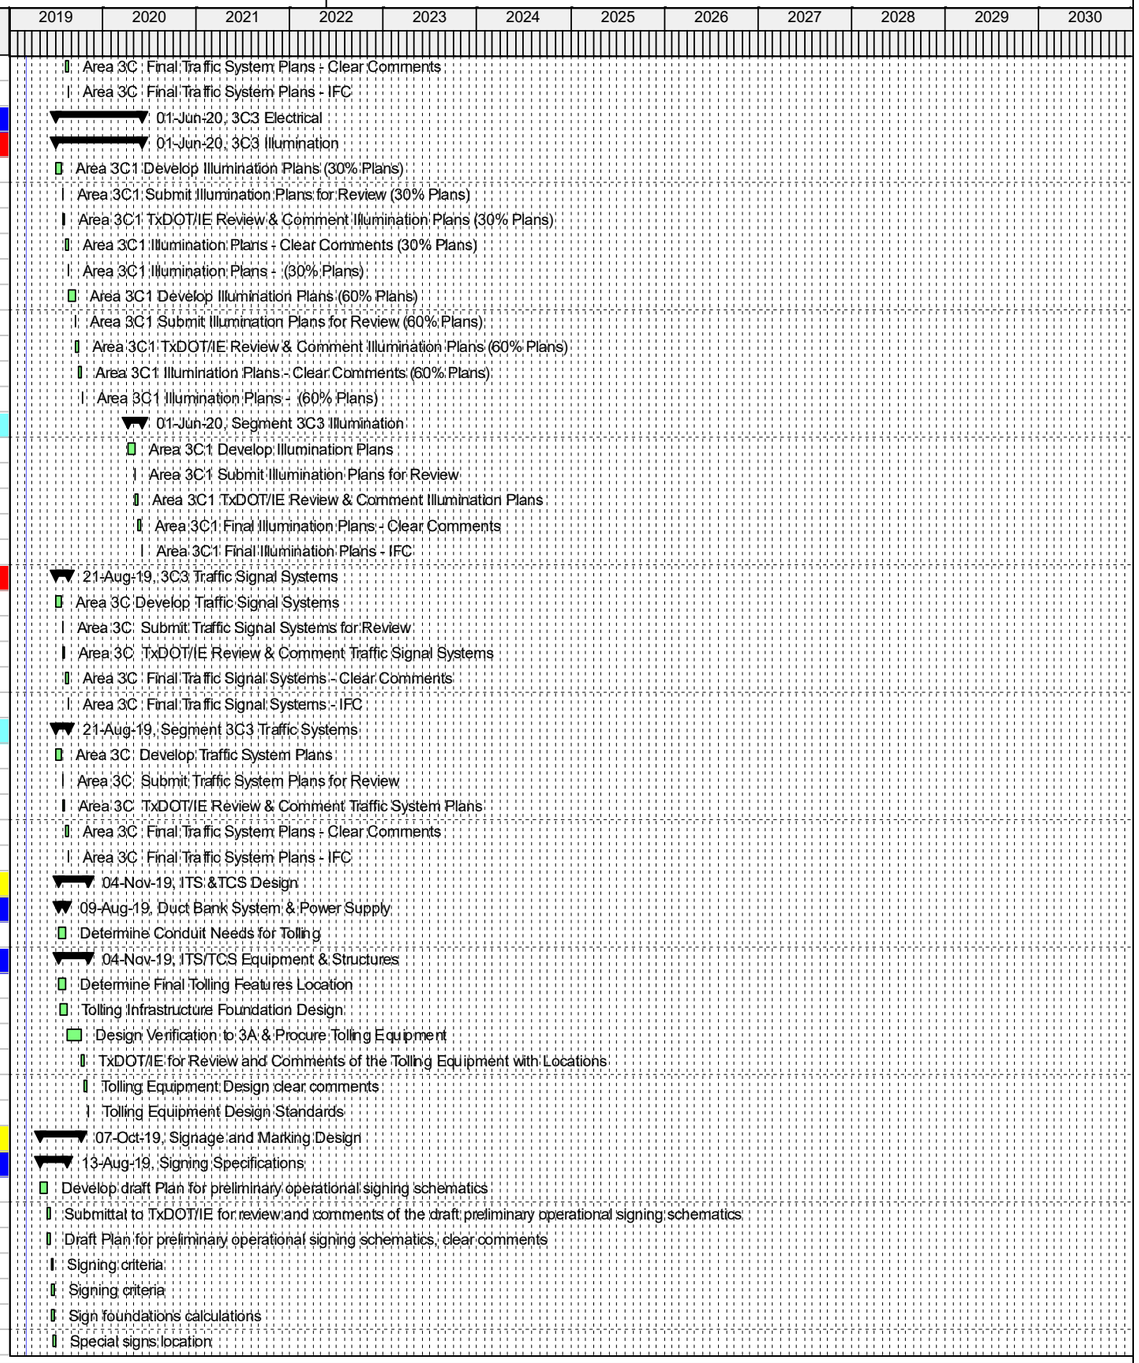

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
DSM1	TX-3CD	Submittal to TxDOT/IE for review and comments of the signing and pavement marking Stanards	10	125	27-Jun-19	06-Jul-19
DSM1	TX-3CD	Develop signing and delineation layout with location Stage 2	10	170	04-Jul-19	17-Jul-19
DSM1	TX-3CD	Signing and pavement marking Stanards, clear comments	10	90	08-Jul-19	19-Jul-19
DSM1	TX-3CD	Preliminary Signing Lay-out Submittal to TxDOT/IE	1	170	18-Jul-19	18-Jul-19
DSM1	TX-3CD	Preliminary Signing Lay-out TxDOT/IE for review and comments	10	239	20-Jul-19	29-Jul-19
DSM1	TX-3CD	Signing and pavement marking Stanards	1	90	22-Jul-19	22-Jul-19
DSM1	TX-3CD	Preliminary Signing Lay-out, clear comments	10	171	30-Jul-19	12-Aug-19
DSM1	TX-3CD	Signing Lay-out Established	1	171	13-Aug-19	13-Aug-19
Signage			39	1007	14-Aug-19	07-Oct-19
Small Signs Pavement Markings			39	1007	14-Aug-19	07-Oct-19
DSI	TX-3CD	Area H Develop Signing, Delineation & Pavement Markings Plans	20	1008	14-Aug-19	10-Sep-19
DSI	TX-3CD	Area HSubmit Signing, Delineation & Pavement Markings Plans to TxDOT/IE for Review	10	1411	11-Sep-19	20-Sep-19
DSI	TX-3CD	Area H Final Signing, Delineation & Pavement Markings Plans - Clear Comments	10	1007	23-Sep-19	04-Oct-19
DSI	TX-3CD	Area H Final Signing, Delineation & Pavement Markings Plans - IFC	1	1007	07-Oct-19	07-Oct-19
Overhead			20	1008	14-Aug-19	10-Sep-19
DSI	TX-3CD	Area H Develop Signing,Overhead Plans	20	1008	14-Aug-19	10-Sep-19
Roadway Design Packages Segment 3C Eagle Pwky to N. Tarant Pkwy Sta 1028 to 1401			302	337	15-Jul-19	08-Sep-20
Roadway Design Packages Segment 3C 30 % Eagle Pwky to N. Tarant Pkwy Sta 1028 to 1401			96	0	15-Jul-19	25-Nov-19
DP3C	TX-3CD	Segment C3 Geopack Analysis	20	5	15-Jul-19	09-Aug-19
DP3C	TX-3CD	Segment C3 Develop Preliminary Roadway Horizontal and Vertical Alignment for ML	30	5	15-Jul-19	23-Aug-19
DP3C	TX-3CD	Segment C3 Preliminary Roadway Plans (Plan and Profile 30%)	40	5	12-Aug-19	04-Oct-19
DP3C	TX-3CD	Segment C3 Develop Preliminary Roadway Horizontal and Vertical Alignment for Xing Streets	40	0	19-Aug-19	11-Oct-19
DP3C	TX-3CD	Segment C3 Submit Preliminary Road Plans to TxDOT/IE for Review and Comments	1	0	14-Oct-19	14-Oct-19
DP3C	TX-3CD	Segment C3 TxDOT/IE Review and Comments Preliminary Road Plans	10	0	16-Oct-19	25-Oct-19
DP3C	TX-3CD	Segment C3 Preliminary Road Plans (Plan and Profile 30%) - Clear Comments	20	0	28-Oct-19	22-Nov-19
DP3C	TX-3CD	Segment C3 30% Design Packages Complete	1	0	25-Nov-19	25-Nov-19
Roadway Design Packages Segment 3C 60 % Eagle Pwky to N. Tarant Pkwy Sta 1028 to 1401			96	0	26-Nov-19	07-Apr-20
DP3C	TX-3CD	Segment C3 Develop Complete Roadway Design Package (Plan and Profile 60%)	55	0	26-Nov-19	10-Feb-20
DP3C	TX-3CD	Segment C3 Roadway Design Package Complete and QA/QC Review	5	0	21-Feb-20	27-Feb-20
DP3C	TX-3CD	Segment C3 Submit Complete Roadway Design Package for TxDOT/IE Review	1	0	28-Feb-20	28-Feb-20
DP3C	TX-3CD	Segment C3 TxDOT/IE Review Roadway Design Package	10	0	29-Feb-20	09-Mar-20
DP3C	TX-3CD	Segment C3 Complete Roadway Design Package - Clear Comments	20	0	10-Mar-20	06-Apr-20
DP3C	TX-3CD	Segment C3 Complete Roadway Design Package - (Plan and Profile 60%)	1	0	07-Apr-20	07-Apr-20
3C1 - Eagle Pwky to SH 170 Sta-1028 to 1176 Roadway Package			110	0	08-Apr-20	08-Sep-20
Package Preparation			80	0	08-Apr-20	28-Jul-20
DP3	TX-3CD	Area 3C1 Develop Final Roadway Design Package	80	0	08-Apr-20	28-Jul-20
QA/QC Review			5	0	10-Aug-20	14-Aug-20
DP3	TX-3CD	Area 3C1 Roadway Design Package Final and QA/QC Review	5	0	10-Aug-20	14-Aug-20
Submittal			0	0	15-Aug-20	15-Aug-20
DP3	TX-3CD	Area 3C1 Submit Final Roadway Design Package for TxDOT/IE Review	0	0	15-Aug-20	15-Aug-20
TXDOT/IE Reviews			10	0	15-Aug-20	24-Aug-20
DP3	TX-3CD	Area 3C1 TxDOT/IE Review Final Roadway Design Package	10	0	15-Aug-20	24-Aug-20
Comment Resolution			11	0	25-Aug-20	08-Sep-20
DP3	TX-3CD	Area 3C1 Final Roadway Design Package - Clear Comments	10	0	25-Aug-20	07-Sep-20
DP3	TX-3CD	Area 3C1 Final Roadway Design Package - IFC	1	0	08-Sep-20	08-Sep-20
3C2 - SH 170 to Golden Triangle Blvd Sta-1176 to 1280 Roadway Packages			90	140	08-Apr-20	11-Aug-20
Package Preparation			60	140	08-Apr-20	30-Jun-20
DP3	TX-3CD	Area 3C2 Develop Final Roadway Design Package	60	140	08-Apr-20	30-Jun-20
QA/QC Review			5	140	13-Jul-20	17-Jul-20
DP3	TX-3CD	Area 3C2 Final Roadway Design Package and QA/QC Review	5	140	13-Jul-20	17-Jul-20
Submittal			0	196	18-Jul-20	18-Jul-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
DP:	TX-3CD	Area 3C2 Submit Final Roadway Design Package for TxDOT/IE Review	0	196	18-Jul-20	18-Jul-20
TXDOT/IE Reviews			10	196	18-Jul-20	27-Jul-20
DP:	TX-3CD	Area 3C2 TxDOT/IE Review Final Roadway Design Package	10	196	18-Jul-20	27-Jul-20
Comment Resolution			11	140	28-Jul-20	11-Aug-20
DP:	TX-3CD	Area 3C2 Final Roadway Design Package - Clear Comments	10	140	28-Jul-20	10-Aug-20
DP:	TX-3CD	Area 3C2 Final Roadway Design Package - IFC	1	140	11-Aug-20	11-Aug-20
3C3 - Golden Triangle Blvd to N. Tarant Pkwy Sta 1280 to 1401 Roadway Packages			110	337	08-Apr-20	08-Sep-20
Package Preparation			80	335	08-Apr-20	28-Jul-20
DP:	TX-3CD	Area 3C3 Develop Final Roadway Design Package	80	335	08-Apr-20	28-Jul-20
QA/QC Review			5	335	10-Aug-20	14-Aug-20
DP:	TX-3CD	Area 3C3 Final Roadway Design Package and QA/QC Review	5	335	10-Aug-20	14-Aug-20
Submittal			0	471	15-Aug-20	15-Aug-20
DP:	TX-3CD	Area 3C3 Submit Final Roadway Design Package for TxDOT/IE Review	0	471	15-Aug-20	15-Aug-20
TXDOT/IE Reviews			10	471	15-Aug-20	24-Aug-20
DP:	TX-3CD	Area 3C3 TxDOT/IE Review Final Roadway Design Package	10	471	15-Aug-20	24-Aug-20
Comment Resolution			11	337	25-Aug-20	08-Sep-20
DP:	TX-3CD	Area 3C3 Final Roadway Design Package - Clear Comments	10	337	25-Aug-20	07-Sep-20
DP:	TX-3CD	Area 3C3 Final Roadway Design Package - IFC	1	337	08-Sep-20	08-Sep-20
IH 820 Design Package 30%			113	91	01-Aug-19	06-Jan-20
DP82(	TX-3CD	IH 820 Ramp Survey & Develop Preliminary Roadway Horizontal and Vertical Alignment	10	91	01-Aug-19	14-Aug-19
DP82(	TX-3CD	IH 820 Ramp Geotech and Geopack Analysis	10	91	15-Aug-19	28-Aug-19
DP82(	TX-3CD	IH 820 Ramp Develop Preliminary Roadway Horizontal and Vertical Alignment for ML	10	91	29-Aug-19	11-Sep-19
DP82(	TX-3CD	IH 820 Ramp Preliminary Roadway Plans (Plan and Profile 30%)	10	91	12-Sep-19	25-Sep-19
DP82(	TX-3CD	IH 820 Ramp Submit Preliminary Road Plans to TxDOT/IE for Review and Comments	0	91	26-Sep-19	26-Sep-19
DP82(	TX-3CD	IH 820 Ramp TxDOT/IE Review and Comments Preliminary Road Plans	10	127	27-Sep-19	06-Oct-19
DP82(	TX-3CD	IH 820 Ramp Preliminary Road Plans (Plan and Profile 30%) - Clear Comments	5	91	07-Oct-19	11-Oct-19
DP82(	TX-3CD	IH 820 Ramp 30% Design Packages Complete	1	91	14-Oct-19	14-Oct-19
IH 820 Design Package 60 %			25	91	15-Oct-19	18-Nov-19
DP(	TX-3CD	IH 820 Ramp Develop Complete Roadway Design Package (Plan and Profile 60%)	5	91	15-Oct-19	21-Oct-19
DP(	TX-3CD	IH 820 Ramp Roadway Design Package Complete and QA/QC Review	5	91	25-Oct-19	31-Oct-19
DP(	TX-3CD	IH 820 Ramp Submit Complete Roadway Design Package for TxDOT/IE Review	0	127	01-Nov-19	01-Nov-19
DP(	TX-3CD	IH 820 Ramp TxDOT/IE Review Roadway Design Package	10	127	01-Nov-19	10-Nov-19
DP(	TX-3CD	IH 820 Ramp Complete Roadway Design Package - Clear Comments	5	91	11-Nov-19	15-Nov-19
DP(	TX-3CD	IH 820 Ramp Complete Roadway Design Package - (Plan and Profile 60%)	1	91	18-Nov-19	18-Nov-19
IH 820 Design Roadway Package			35	91	19-Nov-19	06-Jan-20
Package Preparation			10	91	19-Nov-19	02-Dec-19
[	TX-3CD	IH 820 Ramp Develop Final Roadway Design Package	10	91	19-Nov-19	02-Dec-19
QA/QC Review			5	91	13-Dec-19	19-Dec-19
[	TX-3CD	IH 820 Ramp Roadway Design Package Final and QA/QC Review	5	91	13-Dec-19	19-Dec-19
Submittal			0	127	20-Dec-19	20-Dec-19
[	TX-3CD	IH 820 Ramp Submit Final Roadway Design Package for TxDOT/IE Review	0	127	20-Dec-19	20-Dec-19
TXDOT/IE Reviews			10	127	20-Dec-19	29-Dec-19
[	TX-3CD	IH 820 Ramp TxDOT/IE Review Final Roadway Design Package	10	127	20-Dec-19	29-Dec-19
Comment Resolutions			6	91	30-Dec-19	06-Jan-20
[	TX-3CD	IH 820 Ramp Final Roadway Design Package - Clear Comments	5	91	30-Dec-19	03-Jan-20
[	TX-3CD	IH 820 Ramp Final Roadway Design Package - IFC	1	91	06-Jan-20	06-Jan-20
3C Construction Sta 1028+00 to 1401+00			1163	64	18-Mar-19	31-Aug-23
General Sta 1028+00 to 1401+00			81	306	18-Mar-19	09-Jul-19
W010PL(	TX-3CD	Project Signage Procurment Sta 1028+00 to 1401+00	20	306	18-Mar-19	12-Apr-19
W010PL(	TX-3CD	Project Signage Submittal Sta 1028+00 to 1401+00	1	306	15-Apr-19	15-Apr-19
W010PL1	TX-3CD	TXDOT Review of Project Signage Sta 1028+00 to 1401+00	15	306	16-Apr-19	06-May-19

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
W010PL1	TX-3CD	Project Signage - Clear Comments Sta 1028+00 to 1401+00	5	306	07-May-19	13-May-19
E010PL0	TX-3CD	Project Signage Procurment Sta 1028+00 to 1401+00	20	306	14-May-19	10-Jun-19
E010PL0	TX-3CD	Project Signage Install Sta 1028+00 to 1401+00	20	306	11-Jun-19	08-Jul-19
W010PL0	TX-3CD	Project Signage Completed Sta 1028+00 to 1401+00	0	306	09-Jul-19	09-Jul-19
Segment 3C Sta 1028+00 to 1401+00			796	64	12-Aug-20	31-Aug-23
3C1 - Eagle Pwky to SH 170 STA 1028 to 1176			776	64	09-Sep-20	31-Aug-23
Northbound Frontage Road STA 1028 to 1176			71	491	06-Jul-21	13-Oct-21
C30	TX-3CD	Area 3C1 - NB FR, Start Sta 1028+00 to 1176+00	0	491	06-Jul-21	06-Jul-21
C30	TX-3CD	Area 3C1 - NB FR, FF Start Sta 1028+00 to 1176+00	0	530	14-Jul-21	14-Jul-21
C30	TX-3CD	Area 3C1 - NB FR, Finish Sta 1028+00 to 1176+00	0	491	13-Oct-21	13-Oct-21
Traffic Control and Temporary Work			6	491	06-Jul-21	13-Jul-21
Barricades, Signs & Traffic Handling			1	491	13-Jul-21	13-Jul-21
	TX-3CD	Area 3C1 - NB FR, Move Traffic Sta 1028+00 to 1176+00	1	491	13-Jul-21	13-Jul-21
Portable Traffic Barrier			5	491	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - NB FR, Place Temp Conc Barrier Sta 1028+00 to 1176+00	5	491	06-Jul-21	12-Jul-21
Workzone Pavement Marking			5	491	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - NB FR, Place Temp Marking & Signing Sta 1028+00 to 1176+00	5	491	06-Jul-21	12-Jul-21
Erosion Control			5	491	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - NB FR, Place Temp Erosion Control Sta 1028+00 to 1176+00	5	491	06-Jul-21	12-Jul-21
Earthwork			45	491	14-Jul-21	14-Sep-21
Excavation			25	491	14-Jul-21	17-Aug-21
	TX-3CD	Area 3C1 - NB FR, Excavate Cut Areas Sta 1028+00 to 1176+00	25	491	14-Jul-21	17-Aug-21
Embankment			20	491	18-Aug-21	14-Sep-21
	TX-3CD	Area 3C1 - NB FR, Place Embankment Sta 1028+00 to 1176+00	20	491	18-Aug-21	14-Sep-21
Drainage			40	491	18-Aug-21	12-Oct-21
Culverts			20	501	18-Aug-21	14-Sep-21
	TX-3CD	Area 3C1 - NB FR, CLV05 Install Culvert Sta 1028+00 to 1176+00	20	501	18-Aug-21	14-Sep-21
Riprap			20	491	15-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - NB FR, Install Riprap Sta 1028+00 to 1176+00	20	491	15-Sep-21	12-Oct-21
Headwall			10	501	15-Sep-21	28-Sep-21
	TX-3CD	Area 3C1 - NB FR, Place Conc Headwall Sta 1028+00 to 1176+00	10	501	15-Sep-21	28-Sep-21
Pavement			15	496	15-Sep-21	05-Oct-21
Asphalt Pavement			15	496	15-Sep-21	05-Oct-21
HMA Paving			10	496	15-Sep-21	28-Sep-21
	TX-3CD	Area 3C1 - NB FR, Patch & Repair HMA Sta 1028+00 to 1176+00	10	496	15-Sep-21	28-Sep-21
SMA Paving			5	496	29-Sep-21	05-Oct-21
	TX-3CD	Area 3C1 - NB FR, Patch & Repair SMA Sta 1028+00 to 1176+00	5	496	29-Sep-21	05-Oct-21
BR 205 Henrietta CR.			13	549	06-Jul-21	23-Jul-21
(	TX-3CD	Area 3C1 - CR BR RH, BR 205 Start Sta 1113+78 to 1116+88	2	549	06-Jul-21	07-Jul-21
(	TX-3CD	Area 3C1 - CR BR RH, BR 205 Finish Sta 1113+78 to 1116+88	0	549	23-Jul-21	23-Jul-21
BR Demolition			5	549	09-Jul-21	15-Jul-21
	TX-3CD	Area 3C1 - CR BR RH, BR 205, Concrete Removal Sta 1113+78 to 1116+88	5	549	09-Jul-21	15-Jul-21
Concret Repairs			5	549	16-Jul-21	22-Jul-21
	TX-3CD	Area 3C1 - NB ML, BR 205 Concrete Repairs Sta 1113+78 to 1116+88	5	549	16-Jul-21	22-Jul-21
Replace Exspansion Joint			10	550	08-Jul-21	21-Jul-21
	TX-3CD	Area 3C1 - NB ML, BR 205 Install Exp Joints Sta 1113+78 to 1116+88	10	550	08-Jul-21	21-Jul-21
Aesthetic Finishes			10	550	08-Jul-21	21-Jul-21
	TX-3CD	Area 3C1 - NB ML, BR 205 Install Aethetics Finishes Sta 1113+78 to 1116+88	10	550	08-Jul-21	21-Jul-21
Permanent Barriers			10	545	15-Jul-21	28-Jul-21
Concrete Barriers			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - NB FR, Place Conc Rail Sta 1028+00 to 1176+00	10	545	15-Jul-21	28-Jul-21
Metal Beam Guardrails			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install MBGF Sta 1028+00 to 1176+00	10	545	15-Jul-21	28-Jul-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Signals and Illumination			25	530	15-Jul-21	18-Aug-21
Roadway Illumination			25	530	15-Jul-21	18-Aug-21
	TX-3CD	Area 3C1 - NB FR, Install Illumination Pole Bases Sta 1028+00 to 1176+00	5	530	15-Jul-21	21-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install Illumination Poles/Fixtures Sta 1028+00 to 1176+00	10	530	22-Jul-21	04-Aug-21
	TX-3CD	Area 3C1 - NB FR, Install Illumination Energize Fixtures Sta 1028+00 to 1176+00	10	530	05-Aug-21	18-Aug-21
Signing and Marking			11	545	14-Jul-21	28-Jul-21
Overhead Sign Structures			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install Overhead Signage Sta 1028+00 to 1176+00	10	545	15-Jul-21	28-Jul-21
Small Signage			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install Small Signage Sta 1028+00 to 1176+00	10	545	15-Jul-21	28-Jul-21
Pavement Marking			2	554	14-Jul-21	15-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install Permt Markings Sta 1028+00 to 1176+00	2	554	14-Jul-21	15-Jul-21
Landscaping			10	545	15-Jul-21	28-Jul-21
Seeding & Sodding			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install Topsoil Sta 1028+00 to 1176+00	10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - NB FR, Install Seeding/Sodding Sta 1028+00 to 1176+00	10	545	15-Jul-21	28-Jul-21
Northbound Entry Ramp STA 1080 to 1095			133	449	08-Jun-21	10-Dec-21
C3(	TX-3CD	Area 3C1 - NB ENR RWP-35N, Start Sta 1080+00 to 1096+40	0	449	08-Jun-21	08-Jun-21
C3(	TX-3CD	Area 3C1 - NB ENR RWP-35N, Interim - Finish Sta 1080+00 to 1096+40	0	449	03-Nov-21	03-Nov-21
C3(	TX-3CD	Area 3C1 - NB ENR RWP-35N, FF Start Sta 1080+00 to 1096+40	0	449	04-Nov-21	04-Nov-21
C3(	TX-3CD	Area 3C1 - NB ENR RWP-35N, Finish Sta 1080+00 to 1096+40	0	449	10-Dec-21	10-Dec-21
Traffic Control and Temporary Work			6	449	08-Jun-21	15-Jun-21
Barricades, Signs & Traffic Handling			1	449	15-Jun-21	15-Jun-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Move Traffic Sta 1080+00 to 1096+40	1	449	15-Jun-21	15-Jun-21
Portable Traffic Barrier			5	449	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Temp Conc Barrier Sta 1080+00 to 1096+40	5	449	08-Jun-21	14-Jun-21
Workzone Pavement Marking			5	449	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Temp Marking & Signing Sta 1080+00 to 1096+40	5	449	08-Jun-21	14-Jun-21
Erosion Control			5	449	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Temp Erosion Control Sta 1080+00 to 1096+40	5	449	08-Jun-21	14-Jun-21
Earthwork			50	449	16-Jun-21	24-Aug-21
Clear & Grub			5	449	16-Jun-21	22-Jun-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Clear and Grub Sta 1080+00 to 1096+40	5	449	16-Jun-21	22-Jun-21
Excavation			25	449	23-Jun-21	27-Jul-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Excavate Cut Areas Sta 1080+00 to 1096+40	25	449	23-Jun-21	27-Jul-21
Embankment			20	449	28-Jul-21	24-Aug-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Embankment Sta 1080+00 to 1096+40	20	449	28-Jul-21	24-Aug-21
Subgrade Treatment and Base			30	449	25-Aug-21	05-Oct-21
Lime Treatment			20	449	25-Aug-21	21-Sep-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Lime Treat Subgrade Sta 1080+00 to 1096+40	20	449	25-Aug-21	21-Sep-21
Flexbase			10	449	22-Sep-21	05-Oct-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Flexbase Sta 1080+00 to 1096+40	10	449	22-Sep-21	05-Oct-21
Pavement			26	470	06-Oct-21	10-Nov-21
Asphalt Pavement			16	470	20-Oct-21	10-Nov-21
HMA Paving			10	449	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place HMA Sta 1080+00 to 1096+40	10	449	20-Oct-21	02-Nov-21
SMA Paving			5	470	04-Nov-21	10-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place SMA Sta 1080+00 to 1096+40	5	470	04-Nov-21	10-Nov-21
Curb & Gutter			10	449	06-Oct-21	19-Oct-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Curb & Gutter Sta 1080+00 to 1096+40	10	449	06-Oct-21	19-Oct-21
Permanent Barriers			10	464	05-Nov-21	18-Nov-21
Concrete Barriers			10	464	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Place Conc Rail Sta 1080+00 to 1096+40	10	464	05-Nov-21	18-Nov-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Metal Beam Guardrails	10	464	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install MBGF Sta 1080+00 to 1096+40	10	464	05-Nov-21	18-Nov-21
		Crash Attenuators	5	469	05-Nov-21	11-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Attenuator Sta 1080+00 to 1096+40	5	469	05-Nov-21	11-Nov-21
		Signals and Illumination	25	449	05-Nov-21	09-Dec-21
		Roadway Illumination	25	449	05-Nov-21	09-Dec-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Illumination Pole Bases Sta 1080+00 to 1096+40	5	449	05-Nov-21	11-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Illumination Poles/Fixtures Sta 1080+00 to 1096+40	10	449	12-Nov-21	25-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Illumination Energize Fixtures Sta 1080+00 to 1096+40	10	449	26-Nov-21	09-Dec-21
		Signing and Marking	11	464	04-Nov-21	18-Nov-21
		Overhead Sign Structures	10	464	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Overhead Signage Sta 1080+00 to 1096+40	10	464	05-Nov-21	18-Nov-21
		Small Signage	10	464	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Small Signage Sta 1080+00 to 1096+40	10	464	05-Nov-21	18-Nov-21
		Pavement Marking	2	473	04-Nov-21	05-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Permt Markings Sta 1080+00 to 1096+40	2	473	04-Nov-21	05-Nov-21
		Landscaping	10	464	05-Nov-21	18-Nov-21
		Seeding & Sodding	10	464	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Topsoil Sta 1080+00 to 1096+40	10	464	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB ENR RWP-35N, Install Seeding/Sodding Sta 1080+00 to 1096+40	10	464	05-Nov-21	18-Nov-21
		Northbound Exit Ramp STA 1115 to 1130	221	361	08-Jun-21	13-Apr-22
C3(	TX-3CD	Area 3C1 - NB EXR, Start STA 1115 to 1130	0	361	08-Jun-21	08-Jun-21
		Traffic Control and Temporary Work	6	434	08-Jun-21	15-Jun-21
		Barricades, Signs & Traffic Handling	1	434	15-Jun-21	15-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Move Traffic	1	434	15-Jun-21	15-Jun-21
		Portable Traffic Barrier	5	434	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Place Temp Conc Barrier	5	434	08-Jun-21	14-Jun-21
		Workzone Pavement Marking	5	434	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Place Temp Marking & Signing	5	434	08-Jun-21	14-Jun-21
		Erosion Control	5	434	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Place Temp Erosion Control	5	434	08-Jun-21	14-Jun-21
		Earthwork	40	434	16-Jun-21	10-Aug-21
		Clear & Grub	5	434	16-Jun-21	22-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Clear and Grub	5	434	16-Jun-21	22-Jun-21
		Excavation	15	434	23-Jun-21	13-Jul-21
	TX-3CD	Area 3C1 - NB EXR, Excavate Cut Areas	15	434	23-Jun-21	13-Jul-21
		Embankment	20	434	14-Jul-21	10-Aug-21
	TX-3CD	Area 3C1 - NB EXR, Place Embankment	20	434	14-Jul-21	10-Aug-21
		Subgrade Treatment and Base	35	434	11-Aug-21	28-Sep-21
		Lime Treatment	20	434	11-Aug-21	07-Sep-21
	TX-3CD	Area 3C1 - NB EXR, Lime Treat Subgrade	20	434	11-Aug-21	07-Sep-21
		Flexbase	15	434	08-Sep-21	28-Sep-21
	TX-3CD	Area 3C1 - NB EXR, Place Flexbase	15	434	08-Sep-21	28-Sep-21
		Pavement	114	361	29-Sep-21	08-Mar-22
(	TX-3CD	Area 3C1 - NB EXR, FF Start STA 1115 to 1130	0	361	08-Mar-22	08-Mar-22
		Asphalt Pavement	103	361	13-Oct-21	07-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Sec 1 Interim - Finish STA 1115 to 1130	0	361	07-Mar-22	07-Mar-22
		HMA Paving	10	434	13-Oct-21	26-Oct-21
	TX-3CD	Area 3C1 - NB EXR, Place HMA	10	434	13-Oct-21	26-Oct-21
		SMA Paving	20	434	27-Oct-21	23-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Place SMA	20	434	27-Oct-21	23-Nov-21
		Curb & Gutter	10	434	29-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - NB EXR, Place Curb & Gutter	10	434	29-Sep-21	12-Oct-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
BR 102.1 Henrietta Creek			194	361	08-Jun-21	07-Mar-22
(	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Start	20	361	08-Jun-21	05-Jul-21
(	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Finish	0	361	07-Mar-22	07-Mar-22
BR Demolition			10	380	07-Jul-21	20-Jul-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Bridge Demo Existing BR	10	380	07-Jul-21	20-Jul-21
Drill Shafts			20	380	21-Jul-21	17-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Drill Shafts Abutment 1	5	380	21-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Drill Shafts Bent 2-3	5	380	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Drill Shafts Bent 4-5	5	380	04-Aug-21	10-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Drill Shafts Abutment 6	5	380	11-Aug-21	17-Aug-21
Columns			20	380	28-Jul-21	24-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Columns Abutment 1	5	392	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Columns Bent 2-3	5	387	04-Aug-21	10-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Columns Bent 4-5	5	382	11-Aug-21	17-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Columns Abutment 6	5	380	18-Aug-21	24-Aug-21
Bent Caps			15	382	11-Aug-21	31-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Cap Bent 2-3	10	387	11-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Cap Bent 4-5	10	382	18-Aug-21	31-Aug-21
Beams			63	361	07-Jul-21	01-Oct-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Beam Procurement	20	361	07-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Forward Precast Beams Shopdrawings to TxDOT	1	361	04-Aug-21	04-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Precast Beam Fabrication & Delivery Leadtime	40	361	05-Aug-21	29-Sep-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Conc Beams	2	361	30-Sep-21	01-Oct-21
BR Place CTB Embankment			20	462	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Place Stabilized Fill	20	462	03-Sep-21	30-Sep-21
Abutments			22	380	04-Aug-21	02-Sep-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Abutment 1	10	392	04-Aug-21	17-Aug-21
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Abutment 6	7	380	25-Aug-21	02-Sep-21
Approach Slab			10	361	21-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Apprch Slab Abutment 1	10	361	21-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Apprch Slab Abutment 6	10	361	21-Feb-22	04-Mar-22
Exspansion Joint			80	361	04-Oct-21	21-Jan-22
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Exp Joints	80	361	04-Oct-21	21-Jan-22
Deck			100	361	04-Oct-21	18-Feb-22
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Deck Slab	80	361	04-Oct-21	21-Jan-22
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Cure Deck Slab	20	361	24-Jan-22	18-Feb-22
Railings			5	366	21-Feb-22	25-Feb-22
	TX-3CD	Area 3C1 - NB EXR, BR 102.1 Install Conc Rail	5	366	21-Feb-22	25-Feb-22
Permanent Barriers			10	376	09-Mar-22	22-Mar-22
Concrete Barriers			10	376	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Place Conc Rail	10	376	09-Mar-22	22-Mar-22
Metal Beam Guardrails			10	376	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install MBGF	10	376	09-Mar-22	22-Mar-22
Crash Attenuators			5	381	09-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Attenuator	5	381	09-Mar-22	15-Mar-22
Signals and Illumination			25	361	09-Mar-22	12-Apr-22
Roadway Illumination			25	361	09-Mar-22	12-Apr-22
	TX-3CD	Area 3C1 - NB EXR, Install Illumination Pole Bases	5	361	09-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Illumination Poles/Fixtures	10	361	16-Mar-22	29-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Illumination Energize Fixtures	10	361	30-Mar-22	12-Apr-22
Signing and Marking			26	361	08-Mar-22	13-Apr-22
Overhead Sign Structures			10	376	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Overhead Signage	10	376	09-Mar-22	22-Mar-22

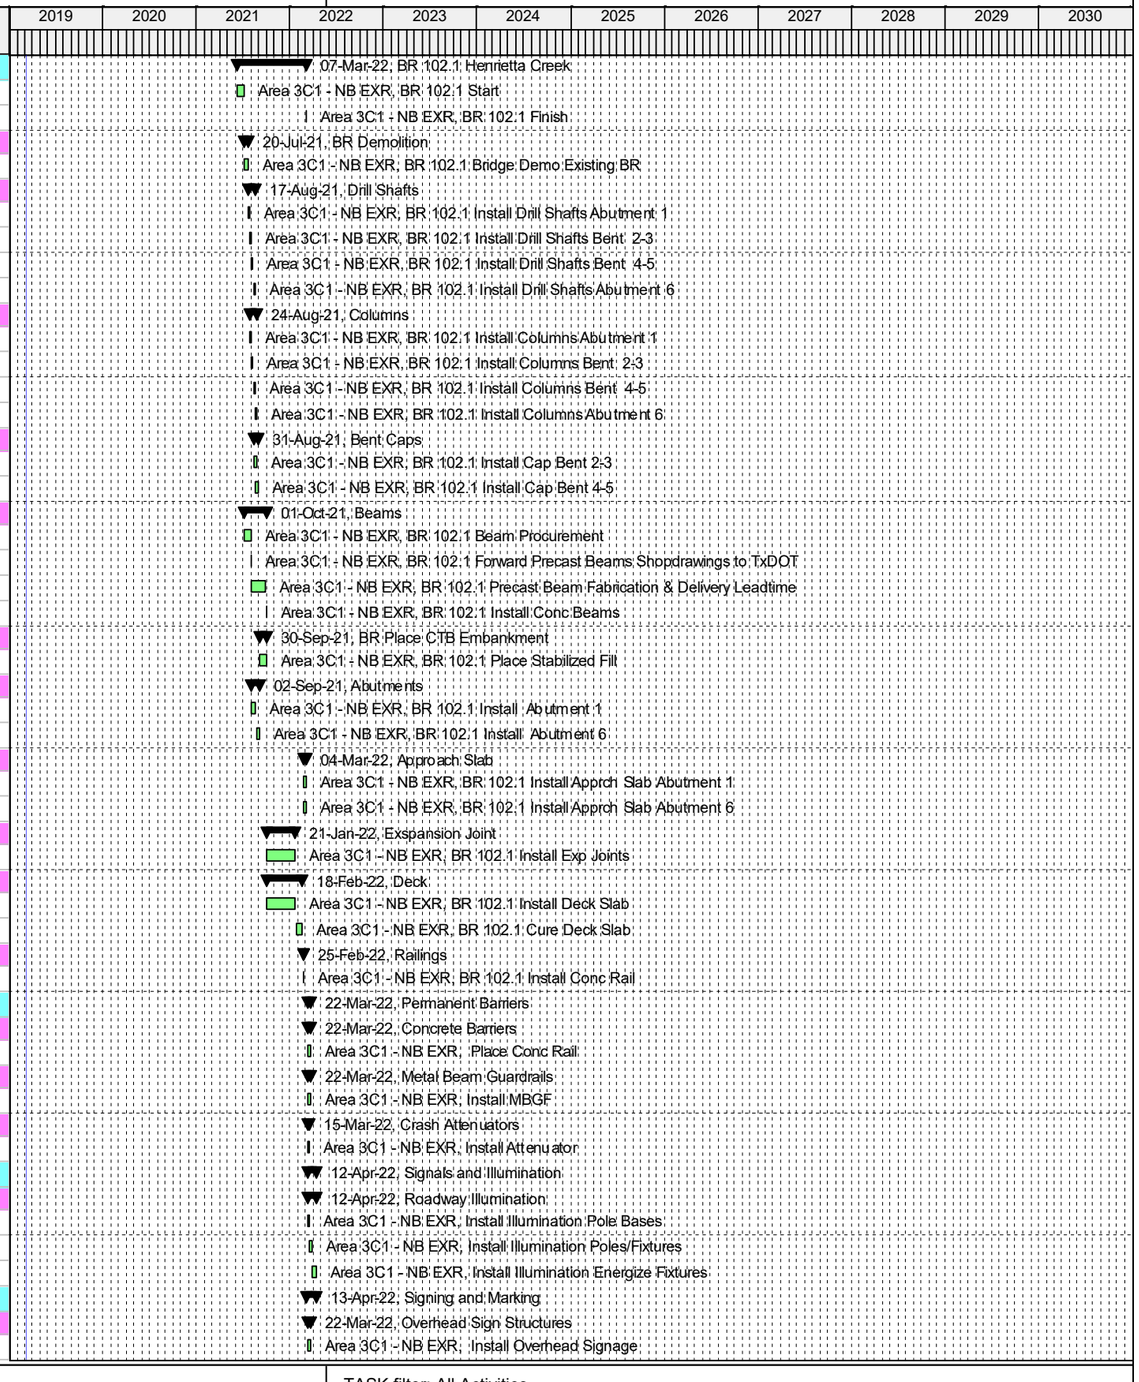

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Small Signage	10	376	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Small Signage	10	376	09-Mar-22	22-Mar-22
		Pavement Marking	26	361	08-Mar-22	13-Apr-22
	TX-3CD	Area 3C1 - NB EXR, Install Permt Markings	2	385	08-Mar-22	09-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Finish STA 1115 to 1130	0	361	13-Apr-22	13-Apr-22
		Landscaping	10	376	09-Mar-22	22-Mar-22
		Seeding & Sodding	10	376	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Topsoil	10	376	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - NB EXR, Install Seeding/Sodding	10	376	09-Mar-22	22-Mar-22
		ITS/TCS	20	454	29-Sep-21	26-Oct-21
		Duct Bank System	20	454	29-Sep-21	26-Oct-21
	TX-3CD	Area 3C1 - NB EXR, ITS &TCS Civil Work Install Coduit	20	454	29-Sep-21	26-Oct-21
		Northbound Exit Ramp STA 1156 to 1175	128	454	08-Jun-21	03-Dec-21
N-2	TX-3CD	Area 3C1 - NB EXR, Start STA 1156 to 1175	0	454	08-Jun-21	08-Jun-21
		Traffic Control and Temporary Work	6	454	08-Jun-21	15-Jun-21
		Barricades, Signs & Traffic Handling	1	454	15-Jun-21	15-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Move Traffic	1	454	15-Jun-21	15-Jun-21
		Portable Traffic Barrier	5	454	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Place Temp Conc Barrier	5	454	08-Jun-21	14-Jun-21
		Workzone Pavement Marking	5	454	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Place Temp Marking & Signing	5	454	08-Jun-21	14-Jun-21
		Erosion Control	5	454	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Place Temp Erosion Control	5	454	08-Jun-21	14-Jun-21
		Earthwork	40	454	16-Jun-21	10-Aug-21
		Clear & Grub	5	454	16-Jun-21	22-Jun-21
	TX-3CD	Area 3C1 - NB EXR, Clear and Grub	5	454	16-Jun-21	22-Jun-21
		Excavation	15	454	23-Jun-21	13-Jul-21
	TX-3CD	Area 3C1 - NB EXR, Excavate Cut Areas	15	454	23-Jun-21	13-Jul-21
		Embankment	20	454	14-Jul-21	10-Aug-21
	TX-3CD	Area 3C1 - NB EXR, Place Embankment	20	454	14-Jul-21	10-Aug-21
		Subgrade Treatment and Base	35	454	11-Aug-21	28-Sep-21
		Lime Treatment	20	454	11-Aug-21	07-Sep-21
	TX-3CD	Area 3C1 - NB EXR, Lime Treat Subgrade	20	454	11-Aug-21	07-Sep-21
		Flexbase	15	454	08-Sep-21	28-Sep-21
	TX-3CD	Area 3C1 - NB EXR, Place Flexbase	15	454	08-Sep-21	28-Sep-21
		Pavement	26	475	29-Sep-21	03-Nov-21
(	TX-3CD	Area 3C1 - NB EXR, FF Start STA 1156 to 1175	0	454	28-Oct-21	28-Oct-21
		Asphalt Pavement	16	475	13-Oct-21	03-Nov-21
TPV	TX-3CD	Area 3C1 - NB EXR, Interim - Finish STA 1156 to 1175	0	454	27-Oct-21	27-Oct-21
		HMA Paving	10	454	13-Oct-21	26-Oct-21
	TX-3CD	Area 3C1 - NB EXR, Place HMA	10	454	13-Oct-21	26-Oct-21
		SMA Paving	5	475	28-Oct-21	03-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Place SMA	5	475	28-Oct-21	03-Nov-21
		Curb & Gutter	10	454	29-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - NB EXR, Place Curb & Gutter	10	454	29-Sep-21	12-Oct-21
		Permanent Barriers	10	469	29-Oct-21	11-Nov-21
		Concrete Barriers	10	469	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Place Conc Rail	10	469	29-Oct-21	11-Nov-21
		Metal Beam Guardrails	10	469	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install MBGF	10	469	29-Oct-21	11-Nov-21
		Crash Attenuators	5	474	29-Oct-21	04-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Attenuator	5	474	29-Oct-21	04-Nov-21
		Signals and Illumination	25	454	29-Oct-21	02-Dec-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Roadway Illumination	25	454	29-Oct-21	02-Dec-21
	TX-3CD	Area 3C1 - NB EXR, Install Illumination Pole Bases	5	454	29-Oct-21	04-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Illumination Poles/Fixtures	10	454	05-Nov-21	18-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Illumination Energize Fixtures	10	454	19-Nov-21	02-Dec-21
		Signing and Marking	26	454	28-Oct-21	03-Dec-21
		Overhead Sign Structures	10	469	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Overhead Signage	10	469	29-Oct-21	11-Nov-21
		Small Signage	10	469	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Small Signage	10	469	29-Oct-21	11-Nov-21
		Pavement Marking	26	454	28-Oct-21	03-Dec-21
	TX-3CD	Area 3C1 - NB EXR, Install Permt Markings	2	478	28-Oct-21	29-Oct-21
	TX-3CD	Area 3C1 - NB EXR, Finish STA 1156 to 1175	0	454	03-Dec-21	03-Dec-21
		Landscaping	10	469	29-Oct-21	11-Nov-21
		Seeding & Sodding	10	469	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Topsoil	10	469	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C1 - NB EXR, Install Seeding/Sodding	10	469	29-Oct-21	11-Nov-21
		ITS/TCS	20	454	29-Sep-21	26-Oct-21
		Duct Bank System	20	454	29-Sep-21	26-Oct-21
	TX-3CD	Area 3C1 - NB EXR, ITS &TCS Civil Work Install Coduit	20	454	29-Sep-21	26-Oct-21
		Northbound GP Lane STA 1045 to 1176	294	288	08-Jun-21	25-Jul-22
C3(	TX-3CD	Area 3C1 - NB GP, Start STA 1045 to 1176	0	0	08-Jun-21	08-Jun-21
C3(	TX-3CD	Area 3C1 - NB GP, BR 103.1 ACM (Asbestos) and LCP (Lead) Testing	1	31	08-Jun-21	08-Jun-21
C3(	TX-3CD	Area 3C1 - NB GP, Interim - Finish STA 1045 to 1176	0	0	16-Jun-22	16-Jun-22
C3(	TX-3CD	Area 3C1 - NB GP, FF Start STA 1045 to 1176	0	288	17-Jun-22	17-Jun-22
C3(	TX-3CD	Area 3C1 - NB GP, Finish STA 1045 to 1176	0	288	25-Jul-22	25-Jul-22
		Traffic Control and Temporary Work	6	71	08-Jun-21	15-Jun-21
		Barricades, Signs & Traffic Handling	1	71	15-Jun-21	15-Jun-21
	TX-3CD	Area 3C1 - NB GP, Move Traffic	1	71	15-Jun-21	15-Jun-21
		Portable Traffic Barrier	5	71	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB GP, Place Temp Conc Barrier	5	71	08-Jun-21	14-Jun-21
		Workzone Pavement Marking	5	71	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB GP, Place Temp Marking & Signing	5	71	08-Jun-21	14-Jun-21
		Erosion Control	5	71	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB GP, Place Temp Erosion Control	5	71	08-Jun-21	14-Jun-21
		Earthwork	106	71	08-Jun-21	02-Nov-21
		Clear & Grub	5	71	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB GP, Clear and Grub	5	71	08-Jun-21	14-Jun-21
		Excavation	50	71	16-Jun-21	24-Aug-21
	TX-3CD	Area 3C1 - NB GP, Excavate Cut Areas	50	71	16-Jun-21	24-Aug-21
		Embankment	50	71	25-Aug-21	02-Nov-21
	TX-3CD	Area 3C1 - NB GP, Place Embankment	50	71	25-Aug-21	02-Nov-21
		Removals & Demo	5	71	08-Jun-21	14-Jun-21
		Pavement Removal	5	71	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 - NB GP, Remove Pavement	5	71	08-Jun-21	14-Jun-21
		Drainage	40	81	16-Jun-21	10-Aug-21
		Culverts	40	81	16-Jun-21	10-Aug-21
	TX-3CD	Area 3C1 - NB GP,CLV05 Install Culvert	40	81	16-Jun-21	10-Aug-21
		Subgrade Treatment and Base	70	71	03-Nov-21	08-Feb-22
		Lime Treatment	60	71	03-Nov-21	25-Jan-22
	TX-3CD	Area 3C1 - NB GP, Lime Treat Subgrade	60	71	03-Nov-21	25-Jan-22
		Flexbase	10	71	26-Jan-22	08-Feb-22
	TX-3CD	Area 3C1 - NB GP, Place Flexbase	10	71	26-Jan-22	08-Feb-22
		Pavement	11	309	09-Jun-22	23-Jun-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Asphalt Pavement			11	309	09-Jun-22	23-Jun-22
HMA Paving			5	0	09-Jun-22	15-Jun-22
	TX-3CD	Area 3C1 - NB GP, Place HMA	5	0	09-Jun-22	15-Jun-22
SMA Paving			5	309	17-Jun-22	23-Jun-22
	TX-3CD	Area 3C1 - NB GP, Place SMA Topping	5	309	17-Jun-22	23-Jun-22
Retaining Walls			75	181	16-Jun-21	28-Sep-21
RT-3C -N2			75	156	16-Jun-21	28-Sep-21
	TX-3CD	Area 3C1 - NB GP, Install Wall RT-3C -N2	60	156	16-Jun-21	07-Sep-21
	TX-3CD	Area 3C1 - NB GP, Install Coping Cap RT-3C-N2	15	156	08-Sep-21	28-Sep-21
RT-3C -N3			55	201	16-Jun-21	31-Aug-21
	TX-3CD	Area 3C1 - NB GP, Install Wall RT-3C -N3	40	201	16-Jun-21	10-Aug-21
	TX-3CD	Area 3C1 - NB GP, Install Coping Cap RT-3C-N3	15	201	11-Aug-21	31-Aug-21
RT-3C -N1			75	181	16-Jun-21	28-Sep-21
	TX-3CD	Area 3C1 - NB GP, Install Wall RT-3C -N1	60	181	16-Jun-21	07-Sep-21
	TX-3CD	Area 3C1 - NB GP, Install Coping Cap RT-3C-N1	15	181	08-Sep-21	28-Sep-21
BR 102.2 Henrietta Creek			262	5	08-Jun-21	09-Jun-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Start	20	0	08-Jun-21	05-Jul-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Finish	0	5	09-Jun-22	09-Jun-22
BR Excavation			10	1	07-Jul-21	20-Jul-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Bridge Excavation	10	1	07-Jul-21	20-Jul-21
Drill Shafts			30	9	21-Jul-21	31-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Drill Shafts Abutment 1	5	1	21-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Drill Shafts Bent 2-3	10	1	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Drill Shafts Bent 4-5	10	1	11-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Drill Shafts Abutment 6	5	9	25-Aug-21	31-Aug-21
Columns			30	9	28-Jul-21	07-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Columns Abutment 1	5	31	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Columns Bent 2-3	10	11	11-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Columns Bent 4-5	10	1	25-Aug-21	07-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Columns Abutment 6	5	9	01-Sep-21	07-Sep-21
Bent Caps			25	1	25-Aug-21	28-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Cap Bent 2-3	15	11	25-Aug-21	14-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Cap Bent 4-5	15	1	08-Sep-21	28-Sep-21
Beams			63	0	07-Jul-21	01-Oct-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Beam Procurement	20	0	07-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Forward Precast Beams Shopdrawings to TxDOT	1	0	04-Aug-21	04-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Precast Beam Fabrication & Delivery Leadtime	40	0	05-Aug-21	29-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Conc Beams	2	0	30-Sep-21	01-Oct-21
BR Place CTB Embankment			20	154	17-Sep-21	14-Oct-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Place Stabilized Backfill	20	154	17-Sep-21	14-Oct-21
Abutments			32	9	04-Aug-21	16-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Abutment 1	10	31	04-Aug-21	17-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Abutment 6	7	9	08-Sep-21	16-Sep-21
Approach Slab			15	0	19-May-22	08-Jun-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Apprch Slab Abutment 1	15	0	19-May-22	08-Jun-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Apprch Slab Abutment 6	15	0	19-May-22	08-Jun-22
Exspansion Joint			143	0	04-Oct-21	20-Apr-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Exp Joints	143	0	04-Oct-21	20-Apr-22
Deck			163	0	04-Oct-21	18-May-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Deck Slab	140	3	04-Oct-21	15-Apr-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Cure Deck Slab	20	0	21-Apr-22	18-May-22
Railings			10	10	19-May-22	01-Jun-22
	TX-3CD	Area 3C1 - NB GP, BR 102.2 Install Conc Rail	10	10	19-May-22	01-Jun-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
BR 103.1 Westport Pkwy			267	0	08-Jun-21	16-Jun-22
(	TX-3CD	Area 3C1 - NB GP, BR 103.1 Start	20	0	08-Jun-21	05-Jul-21
(	TX-3CD	Area 3C1 - NB GP, BR 103.1 Finish	0	0	16-Jun-22	16-Jun-22
BR Demolition			25	16	09-Jun-21	13-Jul-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	31	09-Jun-21	15-Jun-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Bridge Demolition	5	16	07-Jul-21	13-Jul-21
BR Excavation			10	11	07-Jul-21	20-Jul-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Bridge Excavation	10	11	07-Jul-21	20-Jul-21
Drill Shafts			20	11	21-Jul-21	17-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Drill Shafts Abutment 1	5	11	21-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Drill Shafts Bent 2	5	11	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Drill Shafts Bent 3	5	11	04-Aug-21	10-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Drill Shafts Abutment 4	5	11	11-Aug-21	17-Aug-21
Columns			20	16	28-Jul-21	24-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Columns Abutment 1	5	26	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Columns Bent 2	5	26	04-Aug-21	10-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Columns Bent 3	5	21	11-Aug-21	17-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Columns Abutment 4	5	11	18-Aug-21	24-Aug-21
Bent Caps			15	21	11-Aug-21	31-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Cap Bent 2	10	26	11-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Cap Bent 3	10	21	18-Aug-21	31-Aug-21
Beams			63	0	07-Jul-21	01-Oct-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Beam Procurement	20	0	07-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Forward Precast Beams Shopdrawings to TxDOT	1	0	04-Aug-21	04-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Precast Beam Fabrication & Delivery Leadtime	40	0	05-Aug-21	29-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Conc Beams	2	0	30-Sep-21	01-Oct-21
BR Place CTB Embankment			20	156	15-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Place Embankment	20	156	15-Sep-21	12-Oct-21
Abutments			30	11	04-Aug-21	14-Sep-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Abutment 1	15	26	04-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Abutment 4	15	11	25-Aug-21	14-Sep-21
Approach Slab			20	0	19-May-22	15-Jun-22
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Apprch Slab Abutment 1	10	0	19-May-22	01-Jun-22
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Apprch Slab Abutment 4	10	0	02-Jun-22	15-Jun-22
Exspansion Joint			143	0	04-Oct-21	20-Apr-22
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Exp Joints	143	0	04-Oct-21	20-Apr-22
Deck			163	0	04-Oct-21	18-May-22
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Deck Slab	140	3	04-Oct-21	15-Apr-22
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Cure Deck Slab	20	0	21-Apr-22	18-May-22
Railings			5	15	19-May-22	25-May-22
	TX-3CD	Area 3C1 - NB GP, BR 103.1 Install Conc Rail	5	15	19-May-22	25-May-22
Permanent Barriers			10	303	20-Jun-22	01-Jul-22
Concrete Barriers			10	303	20-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Place Conc Rail	10	303	20-Jun-22	01-Jul-22
Metal Beam Guardrails			10	303	20-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install MBGF	10	303	20-Jun-22	01-Jul-22
Signals and Illumination			25	288	20-Jun-22	22-Jul-22
Roadway Illumination			25	288	20-Jun-22	22-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install Illumination Pole Bases	5	288	20-Jun-22	24-Jun-22
	TX-3CD	Area 3C1 - NB GP, Install Illumination Poles/Fixtures	10	288	27-Jun-22	08-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install Illumination Energize Fixtures	10	288	11-Jul-22	22-Jul-22
High Mast Illumination			15	298	20-Jun-22	08-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install High Mast Illumination Pole Bases	5	298	20-Jun-22	24-Jun-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - NB GP, Install High Mast Illumination Poles/Fixtures	5	298	27-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install High Mast Illumination Energize Fixtures	5	298	04-Jul-22	08-Jul-22
Signing and Marking			11	303	17-Jun-22	01-Jul-22
Overhead Sign Structures			10	303	20-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install Overhead Signage	10	303	20-Jun-22	01-Jul-22
Small Signage			10	303	20-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install Small Signage	10	303	20-Jun-22	01-Jul-22
Pavement Marking			2	312	17-Jun-22	20-Jun-22
	TX-3CD	Area 3C1 - NB GP, Install Permt Markings	2	312	17-Jun-22	20-Jun-22
Landscaping			10	303	20-Jun-22	01-Jul-22
Seeding & Sodding			10	303	20-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install Topsoil	10	303	20-Jun-22	01-Jul-22
	TX-3CD	Area 3C1 - NB GP, Install Seeding/Sodding	10	303	20-Jun-22	01-Jul-22
ITS/TCS			20	71	09-Feb-22	08-Mar-22
Duct Bank System			20	71	09-Feb-22	08-Mar-22
	TX-3CD	Area 3C1 - NB GP, ITS &TCS Civil Work Install Coduit	20	71	09-Feb-22	08-Mar-22
Northbound ML Lane STA 1059 to 1176			315	0	16-Jun-22	31-Aug-23
C3(	TX-3CD	Area 3C1 - NB ML Start STA 1059 to 1176	10	0	16-Jun-22	29-Jun-22
C3(	TX-3CD	Area 3C1 - NB ML, BR 102.4 ACM (Asbestos) and LCP (Lead) Testing	1	26	30-Jun-22	30-Jun-22
C3(	TX-3CD	Area 3C1 - NB ML, Interim - Finish STA 1059 to 1176	0	0	19-Apr-23	19-Apr-23
C3(	TX-3CD	Area 3C1 - NB ML, FF Start STA 1059 to 1176	0	0	20-Apr-23	20-Apr-23
C3(	TX-3CD	Area 3C1 - NB ML, Finish STA 1059 to 1176	0	0	31-Aug-23	31-Aug-23
Traffic Control and Temporary Work			8	0	30-Jun-22	11-Jul-22
Barricades, Signs & Traffic Handling			1	0	11-Jul-22	11-Jul-22
	TX-3CD	Area 3C1 - NB ML, Move Traffic	1	0	11-Jul-22	11-Jul-22
Portable Traffic Barrier			5	2	30-Jun-22	06-Jul-22
	TX-3CD	Area 3C1 - NB ML, Place Temp Conc Barrier	5	2	30-Jun-22	06-Jul-22
Workzone Pavement Marking			5	2	30-Jun-22	06-Jul-22
	TX-3CD	Area 3C1 - NB ML, Place Temp Marking & Signing	5	2	30-Jun-22	06-Jul-22
Erosion Control			5	2	30-Jun-22	06-Jul-22
	TX-3CD	Area 3C1 - NB ML, Place Temp Erosion Control	5	2	30-Jun-22	06-Jul-22
Removals & Demo			7	0	30-Jun-22	08-Jul-22
Pavement Removal			7	0	30-Jun-22	08-Jul-22
	TX-3CD	Area 3C1 - NB ML, Remove Pavement	7	0	30-Jun-22	08-Jul-22
Earthwork			139	0	30-Jun-22	10-Jan-23
Clear & Grub			5	2	30-Jun-22	06-Jul-22
	TX-3CD	Area 3C1 - NB ML, Clear and Grub	5	2	30-Jun-22	06-Jul-22
Excavation			62	0	12-Jul-22	05-Oct-22
	TX-3CD	Area 3C1 - NB ML, Excavate Cut Areas	62	0	12-Jul-22	05-Oct-22
Embankment			69	0	06-Oct-22	10-Jan-23
	TX-3CD	Area 3C1 - NB ML, Place Embankment	69	0	06-Oct-22	10-Jan-23
Drainage			40	22	12-Jul-22	05-Sep-22
Culverts			40	22	12-Jul-22	05-Sep-22
	TX-3CD	Area 3C1 - NB ML, CLV05 Install Culvert	40	22	12-Jul-22	05-Sep-22
Subgrade Treatment and Base			65	0	11-Jan-23	11-Apr-23
Lime Treatment			40	0	11-Jan-23	07-Mar-23
	TX-3CD	Area 3C1 - NB ML, Lime Treat Subgrade	40	0	11-Jan-23	07-Mar-23
Flexbase			25	0	08-Mar-23	11-Apr-23
	TX-3CD	Area 3C1 - NB ML, Place Flexbase	25	0	08-Mar-23	11-Apr-23
Pavement			8	93	12-Apr-23	21-Apr-23
Asphalt Pavement			8	93	12-Apr-23	21-Apr-23
HMA Paving			5	0	12-Apr-23	18-Apr-23

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - NB ML, Place HMA	5	0	12-Apr-23	18-Apr-23
SMA Paving			2	93	20-Apr-23	21-Apr-23
	TX-3CD	Area 3C1 - NB ML, Place SMA	2	93	20-Apr-23	21-Apr-23
BR 102.4 Henrietta Creek			202	7	30-Jun-22	10-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Start	10	7	30-Jun-22	13-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Finish	0	7	10-Apr-23	10-Apr-23
BR Demolition			15	21	01-Jul-22	21-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	26	01-Jul-22	07-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Bridge Demolition	5	21	15-Jul-22	21-Jul-22
BR Excavation			5	21	15-Jul-22	21-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Bridge Excavation	5	21	15-Jul-22	21-Jul-22
Drill Shafts			20	21	22-Jul-22	18-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Drill Shafts Abutment 1	5	21	22-Jul-22	28-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Drill Shafts Bent 2-3	5	21	29-Jul-22	04-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Drill Shafts Bent 4-5	5	21	05-Aug-22	11-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Drill Shafts Abutment 6	5	21	12-Aug-22	18-Aug-22
Columns			20	26	29-Jul-22	25-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Columns Abutment 1	5	36	29-Jul-22	04-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Columns Bent 2-3	10	31	05-Aug-22	18-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Columns Bent 4-5	10	26	12-Aug-22	25-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Columns Abutment 6	5	21	19-Aug-22	25-Aug-22
Bent Caps			15	26	19-Aug-22	08-Sep-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Cap Bent 2-3	10	31	19-Aug-22	01-Sep-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Cap Bent 4-5	10	26	26-Aug-22	08-Sep-22
Beams			61	7	15-Jul-22	07-Oct-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Beam Procurement	18	7	15-Jul-22	09-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Forward Precast Beams Shopdrawings to TxDOT	1	7	10-Aug-22	10-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Precast Beam Fabrication & Delivery Leadtime	40	7	11-Aug-22	05-Oct-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Conc Beams	2	7	06-Oct-22	07-Oct-22
BR Place CTB Embankment			20	118	16-Sep-22	13-Oct-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Place Stabilized Backfill	20	118	16-Sep-22	13-Oct-22
Abutments			30	21	05-Aug-22	15-Sep-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Abutment 1	15	36	05-Aug-22	25-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Abutment 6	15	21	26-Aug-22	15-Sep-22
Approach Slab			15	7	20-Mar-23	07-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Apprch Slab Abutment 1	15	7	20-Mar-23	07-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Apprch Slab Abutment 6	15	7	20-Mar-23	07-Apr-23
Exspansion Joint			70	32	10-Oct-22	13-Jan-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Exp Joints	70	32	10-Oct-22	13-Jan-23
Railings			10	12	20-Mar-23	31-Mar-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Conc Rail	10	12	20-Mar-23	31-Mar-23
Deck			115	7	10-Oct-22	17-Mar-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Install Deck Slab	95	7	10-Oct-22	17-Feb-23
	TX-3CD	Area 3C1 - NB ML, BR 102.4 Cure Deck Slab	20	7	20-Feb-23	17-Mar-23
BR 103.2 Westport Pkwy			204	5	30-Jun-22	12-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Start	5	5	30-Jun-22	06-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Finish	0	5	12-Apr-23	12-Apr-23
BR Excavation			10	21	08-Jul-22	21-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Bridge Excavation	10	21	08-Jul-22	21-Jul-22
Drill Shafts			20	21	22-Jul-22	18-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Drill Shafts Abutment 1	5	21	22-Jul-22	28-Jul-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Drill Shafts Bent 2	5	21	29-Jul-22	04-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Drill Shafts Bent 3	5	21	05-Aug-22	11-Aug-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Drill Shafts Abutment 4	5	21	12-Aug-22	18-Aug-22
Columns			20	21	29-Jul-22	25-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Columns Abutment 1	5	36	29-Jul-22	04-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Columns Bent 2	5	31	05-Aug-22	11-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Columns Bent 3	5	26	12-Aug-22	18-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Columns Abutment 4	5	21	19-Aug-22	25-Aug-22
Bent Caps			15	26	12-Aug-22	01-Sep-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Cap Bent 2	10	31	12-Aug-22	25-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Cap Bent 3	10	26	19-Aug-22	01-Sep-22
Beams			66	5	08-Jul-22	07-Oct-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Beam Procurement	20	5	08-Jul-22	04-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Forward Precast Beams Shopdrawings to TxDOT	1	5	05-Aug-22	05-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Precast Beam Fabrication & Delivery Leadtime	40	5	08-Aug-22	30-Sep-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Conc Beams	5	5	03-Oct-22	07-Oct-22
BR Place CTB Embankment			20	122	09-Sep-22	06-Oct-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Place Stabilized Backfill	20	122	09-Sep-22	06-Oct-22
Abutments			25	21	05-Aug-22	08-Sep-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Abutment 1	10	36	05-Aug-22	18-Aug-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Abutment 4	10	21	26-Aug-22	08-Sep-22
Approach Slab			16	6	20-Mar-23	10-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Apprch Slab Abutment 1	16	6	20-Mar-23	10-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Apprch Slab Abutment 4	16	6	20-Mar-23	10-Apr-23
Exspansion Joint			60	40	10-Oct-22	30-Dec-22
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Exp Joints	60	40	10-Oct-22	30-Dec-22
Deck			115	5	10-Oct-22	17-Mar-23
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Deck Slab	95	5	10-Oct-22	17-Feb-23
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Cure Deck Slab	20	5	20-Feb-23	17-Mar-23
Railings			17	5	20-Mar-23	11-Apr-23
	TX-3CD	Area 3C1 - NB ML, BR 103.2 Install Conc Rail	17	5	20-Mar-23	11-Apr-23
Permanent Barriers			10	84	21-Apr-23	04-May-23
Concrete Barriers			10	84	21-Apr-23	04-May-23
	TX-3CD	Area 3C1 - NB ML, Place Conc Rail	10	84	21-Apr-23	04-May-23
Metal Beam Guardrails			10	84	21-Apr-23	04-May-23
	TX-3CD	Area 3C1 - NB ML, Install MBGF	10	84	21-Apr-23	04-May-23
Signals and Illumination			25	69	21-Apr-23	25-May-23
Roadway Illumination			25	69	21-Apr-23	25-May-23
	TX-3CD	Area 3C1 - NB ML, Install Illumination Pole Bases	5	69	21-Apr-23	27-Apr-23
	TX-3CD	Area 3C1 - NB ML, Install Illumination Poles/Fixtures	10	69	28-Apr-23	11-May-23
	TX-3CD	Area 3C1 - NB ML, Install Illumination Energize Fixtures	10	69	12-May-23	25-May-23
High Mast Illumination			15	79	21-Apr-23	11-May-23
	TX-3CD	Area 3C1 - NB ML, Install High Mast Illumination Pole Bases	5	79	21-Apr-23	27-Apr-23
	TX-3CD	Area 3C1 - NB ML, Install High Mast Illumination Poles/Fixtures	5	79	28-Apr-23	04-May-23
	TX-3CD	Area 3C1 - NB ML, Install High Mast Illumination Energize Fixtures	5	79	05-May-23	11-May-23
Signing and Marking			11	84	20-Apr-23	04-May-23
Overhead Sign Structures			10	84	21-Apr-23	04-May-23
	TX-3CD	Area 3C1 - NB ML, Install Overhead Signage	10	84	21-Apr-23	04-May-23
Small Signage			10	84	21-Apr-23	04-May-23
	TX-3CD	Area 3C1 - NB ML, Install Small Signage	10	84	21-Apr-23	04-May-23
Pavement Marking			2	93	20-Apr-23	21-Apr-23
	TX-3CD	Area 3C1 - NB ML, Install Permt Markings	2	93	20-Apr-23	21-Apr-23
Landscaping			10	84	21-Apr-23	04-May-23
Seeding & Sodding			10	84	21-Apr-23	04-May-23
	TX-3CD	Area 3C1 - NB ML, Install Seeding/Sodding	10	84	21-Apr-23	04-May-23

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - NB ML, Install Topsoil	10	84	21-Apr-23	04-May-23
ITS/TCS			126	0	08-Mar-23	31-Aug-23
(	TX-3CD	Area 3C1 - NB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	0	20-Apr-23	20-Apr-23
(	TX-3CD	Area 3C1 - NB ML, ITS &TCS Testing Complete	0	0	31-Aug-23	31-Aug-23
Duct Bank System			20	11	08-Mar-23	04-Apr-23
	TX-3CD	Area 3C1 - NB ML, ITS &TCS Civil Work Install Conduit	20	11	08-Mar-23	04-Apr-23
Equipment Foundations			25	0	20-Apr-23	24-May-23
	TX-3CD	Area 3C1 - NB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	25	0	20-Apr-23	24-May-23
Equipment			50	0	20-Apr-23	29-Jun-23
	TX-3CD	Area 3C1 - NB ML, ITS &TCS Fiber Install fiber	10	10	20-Apr-23	03-May-23
	TX-3CD	Area 3C1 - NB ML, ITS &TCS Fiber Cut and splice	20	10	04-May-23	31-May-23
	TX-3CD	Area 3C1 - NB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	25	0	25-May-23	28-Jun-23
	TX-3CD	Area 3C1 - NB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	0	29-Jun-23	29-Jun-23
Testing & Certification			65	0	01-Jun-23	30-Aug-23
	TX-3CD	Area 3C1 - NB ML, ITS &TCS Fiber Local Site Test	10	10	01-Jun-23	14-Jun-23
	TX-3CD	Area 3C1 - NB ML, ITS &TCS Fiber Fiber Complete	0	10	15-Jun-23	15-Jun-23
	TX-3CD	Area 3C1 - NB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	1	29-Jun-23	26-Jul-23
	TX-3CD	Area 3C1 - NB ML, ITS &TCS Testing Start	0	0	30-Jun-23	30-Jun-23
	TX-3CD	Area 3C1 - NB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	0	30-Jun-23	27-Jul-23
	TX-3CD	Area 3C1 - NB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	24	0	28-Jul-23	30-Aug-23
Crossroad Alliance Bridge Rehab Level 8 STA 1080			16	760	09-Sep-20	01-Oct-20
C3(	TX-3CD	Area 3C1 - CR BR RH, Start STA 1080	0	760	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			6	760	09-Sep-20	16-Sep-20
Barricades, Signs & Traffic Handling			1	760	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Move Traffic	1	760	16-Sep-20	16-Sep-20
Portable Traffic Barrier			5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Place Temp Conc Barrier	5	760	09-Sep-20	15-Sep-20
Workzone Pavement Marking			5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Place Temp Marking & Signing	5	760	09-Sep-20	15-Sep-20
Erosion Control			5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Place Temp Erosion Control	5	760	09-Sep-20	15-Sep-20
BR 201 Alliance Blvd			16	760	09-Sep-20	01-Oct-20
(	TX-3CD	Area 3C1 - CR BR RH, BR 201 Start STA 1080	2	763	09-Sep-20	10-Sep-20
(	TX-3CD	Area 3C1 - CR BR RH, BR 201 Finish STA 1080	0	760	01-Oct-20	01-Oct-20
BR Demolition			5	760	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, BR 201, Concrete Deck Removal	5	760	17-Sep-20	23-Sep-20
Rip Rap Removal			5	764	11-Sep-20	17-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 201 Remove Rip Rap	5	764	11-Sep-20	17-Sep-20
Rip Rap Replacement			5	764	18-Sep-20	24-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 201 Install Rip Rap	5	764	18-Sep-20	24-Sep-20
Concret Repairs			5	760	24-Sep-20	30-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 201 Concrete Repairs	5	760	24-Sep-20	30-Sep-20
Replace Exspansion Joint			10	764	11-Sep-20	24-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 201 Install Exp Joints	10	764	11-Sep-20	24-Sep-20
Crossroad Westport Pkwy STA 1132			299	298	18-May-21	11-Jul-22
Crossroad Westport Pkwy STA 1132 PH1			95	502	18-May-21	28-Sep-21
(	TX-3CD	Area 3C1 - CR WP, Start STA 1132	0	298	18-May-21	18-May-21
Traffic Control and Temporary Work			6	298	18-May-21	25-May-21
Barricades, Signs & Traffic Handling			1	298	25-May-21	25-May-21
	TX-3CD	Area 3C1 - CR WP, Move Traffic	1	298	25-May-21	25-May-21
Portable Traffic Barrier			5	298	18-May-21	24-May-21
	TX-3CD	Area 3C1 - CR WP, Place Temp Conc Barrier	5	298	18-May-21	24-May-21
Workzone Pavement Marking			5	298	18-May-21	24-May-21

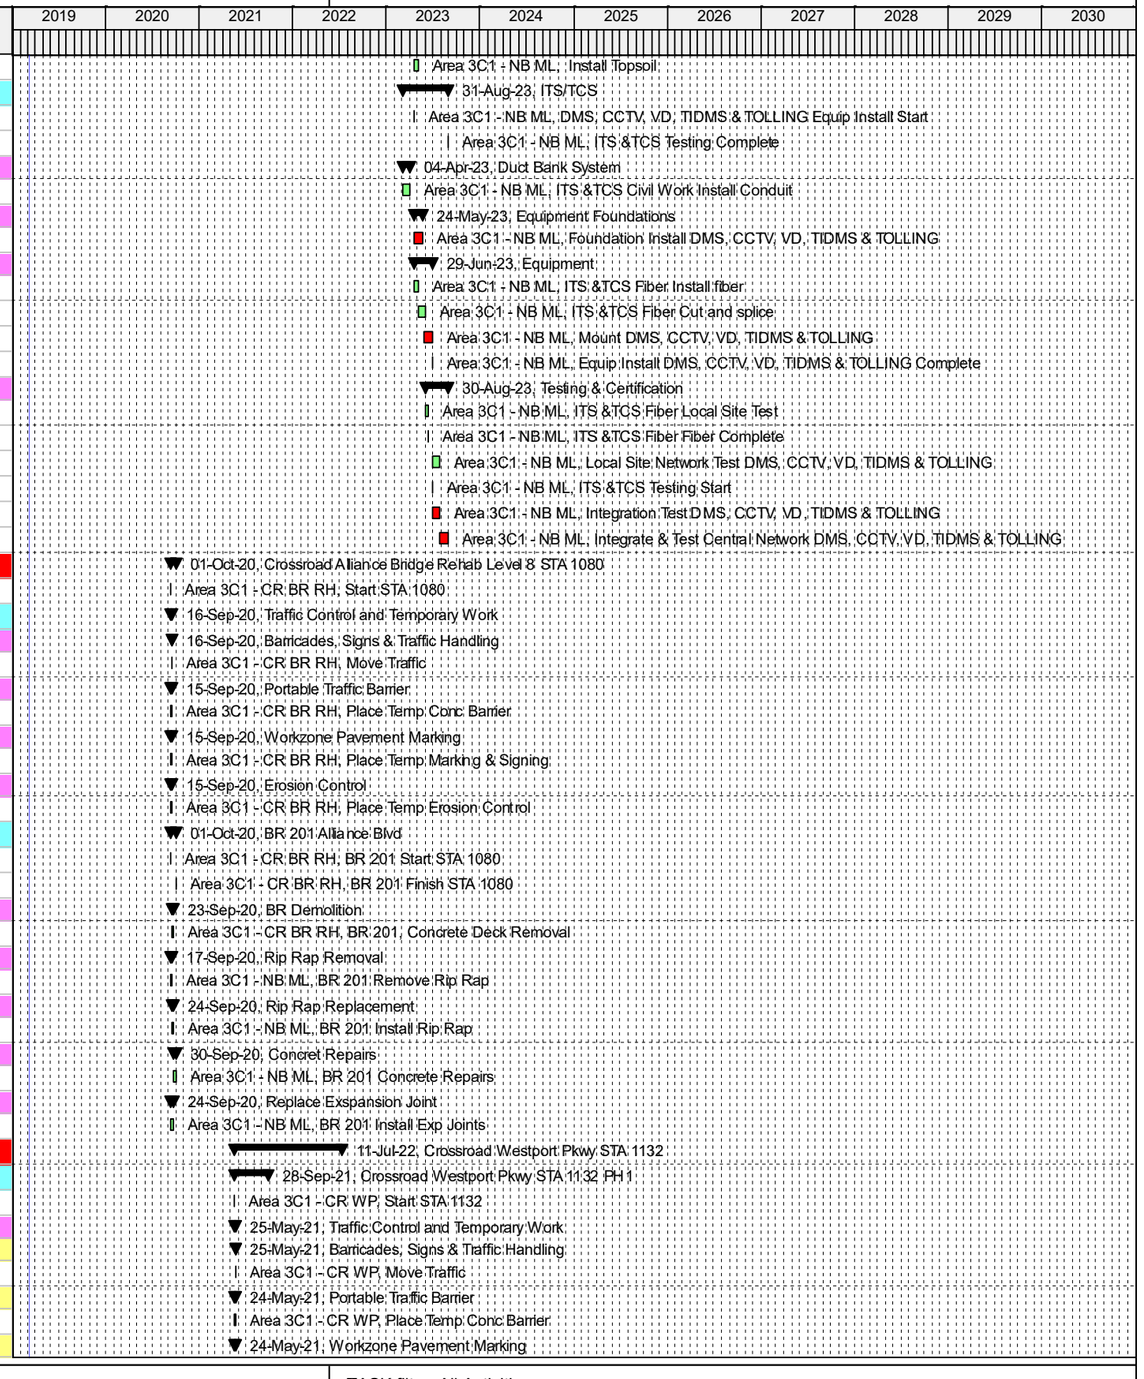

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - CR WP, Place Temp Marking & Signing	5	298	18-May-21	24-May-21
	Erosion Control		5	298	18-May-21	24-May-21
	TX-3CD	Area 3C1 - CR WP, Place Temp Erosion Control	5	298	18-May-21	24-May-21
	Removals & Demo		5	298	18-May-21	24-May-21
	Pavement Removal		5	298	18-May-21	24-May-21
	TX-3CD	Area 3C1 - CR WP, Remove Pavement	5	298	18-May-21	24-May-21
	Earthwork		41	298	18-May-21	13-Jul-21
	Clear & Grub		5	298	18-May-21	24-May-21
	TX-3CD	Area 3C1 - CR WP, Clear and Grub	5	298	18-May-21	24-May-21
	Excavation		15	298	26-May-21	15-Jun-21
	TX-3CD	Area 3C1 - CR WP, Excavate Cut Areas	15	298	26-May-21	15-Jun-21
	Embankment		20	298	16-Jun-21	13-Jul-21
	TX-3CD	Area 3C1 - CR WP, Place Embankment	20	298	16-Jun-21	13-Jul-21
	Subgrade Treatment and Base		10	298	14-Jul-21	27-Jul-21
	Lime Treatment		5	298	14-Jul-21	20-Jul-21
	TX-3CD	Area 3C1 - CR WP, Lime Treat Subgrade	5	298	14-Jul-21	20-Jul-21
	Flexbase		5	298	21-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 - CR WP, Place Flexbase	5	298	21-Jul-21	27-Jul-21
	Pavement		29	517	28-Jul-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, FF Start	0	502	23-Aug-21	23-Aug-21
	Asphalt Pavement		7	298	11-Aug-21	20-Aug-21
	TX-3CD	Area 3C1 - CR WP, Sec 1 Interim - Finish	0	298	20-Aug-21	20-Aug-21
	HMA Paving		2	298	11-Aug-21	12-Aug-21
	TX-3CD	Area 3C1 - CR WP, Place HMA	2	298	11-Aug-21	12-Aug-21
	SMA Paving		5	298	13-Aug-21	19-Aug-21
	TX-3CD	Area 3C1 - CR WP, Place SMA	5	298	13-Aug-21	19-Aug-21
	Curb & Gutter		10	298	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C1 - CR WP, Place Curb & Gutter	10	298	28-Jul-21	10-Aug-21
	Driveways		10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Place Driveways	10	517	24-Aug-21	06-Sep-21
	Sidewalks & Median		10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Place Sidewalks/Pathways	10	517	24-Aug-21	06-Sep-21
	Permanent Barriers		10	517	24-Aug-21	06-Sep-21
	Concrete Barriers		10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Place Conc Rail	10	517	24-Aug-21	06-Sep-21
	Metal Beam Guardrails		10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install MBGF	10	517	24-Aug-21	06-Sep-21
	Signals and Illumination		25	502	24-Aug-21	27-Sep-21
	Roadway Illumination		25	502	24-Aug-21	27-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install Illumination Pole Bases	5	502	24-Aug-21	30-Aug-21
	TX-3CD	Area 3C1 - CR WP, Install Illumination Poles/Fixtures	10	502	31-Aug-21	13-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install Illumination Energize Fixtures	10	502	14-Sep-21	27-Sep-21
	Signing and Marking		26	502	23-Aug-21	28-Sep-21
	Small Signage		10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install Small Signage	10	517	24-Aug-21	06-Sep-21
	Pavement Marking		26	502	23-Aug-21	28-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install Permt Markings	2	526	23-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - CR WP, Finish	0	502	28-Sep-21	28-Sep-21
	Landscaping		10	517	24-Aug-21	06-Sep-21
	Seeding & Sodding		10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install Topsoil	10	517	24-Aug-21	06-Sep-21
	TX-3CD	Area 3C1 - CR WP, Install Seeding/Sodding	10	517	24-Aug-21	06-Sep-21
	Crossroad Westport Pkwy STA 1132 PH2		95	434	20-Aug-21	31-Dec-21
	TX-3CD	Area 3C1 - CR WP, Start	0	298	20-Aug-21	20-Aug-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Traffic Control and Temporary Work			6	298	20-Aug-21	27-Aug-21
Barricades, Signs & Traffic Handling			1	298	27-Aug-21	27-Aug-21
TX-3CD		Area 3C1 - CR WP, Move Traffic	1	298	27-Aug-21	27-Aug-21
Portable Traffic Barrier			5	298	20-Aug-21	26-Aug-21
TX-3CD		Area 3C1 - CR WP, Place Temp Conc Barrier	5	298	20-Aug-21	26-Aug-21
Workzone Pavement Marking			5	298	20-Aug-21	26-Aug-21
TX-3CD		Area 3C1 - CR WP, Place Temp Marking & Signing	5	298	20-Aug-21	26-Aug-21
Erosion Control			5	298	20-Aug-21	26-Aug-21
TX-3CD		Area 3C1 - CR WP, Place Temp Erosion Control	5	298	20-Aug-21	26-Aug-21
Removals & Demo			5	298	20-Aug-21	26-Aug-21
Pavement Removal			5	298	20-Aug-21	26-Aug-21
TX-3CD		Area 3C1 - CR WP, Remove Pavement	5	298	20-Aug-21	26-Aug-21
Earthwork			41	298	20-Aug-21	15-Oct-21
Clear & Grub			5	298	20-Aug-21	26-Aug-21
TX-3CD		Area 3C1 - CR WP, Clear and Grub	5	298	20-Aug-21	26-Aug-21
Excavation			15	298	30-Aug-21	17-Sep-21
TX-3CD		Area 3C1 - CR WP, Excavate Cut Areas	15	298	30-Aug-21	17-Sep-21
Embankment			20	298	20-Sep-21	15-Oct-21
TX-3CD		Area 3C1 - CR WP, Place Embankment	20	298	20-Sep-21	15-Oct-21
Subgrade Treatment and Base			10	298	18-Oct-21	29-Oct-21
Lime Treatment			5	298	18-Oct-21	22-Oct-21
TX-3CD		Area 3C1 - CR WP, Lime Treat Subgrade	5	298	18-Oct-21	22-Oct-21
Flexbase			5	298	25-Oct-21	29-Oct-21
TX-3CD		Area 3C1 - CR WP, Place Flexbase	5	298	25-Oct-21	29-Oct-21
Pavement			29	449	01-Nov-21	09-Dec-21
TX-3CD		Area 3C1 - CR WP, FF Start	0	434	25-Nov-21	25-Nov-21
Asphalt Pavement			7	298	15-Nov-21	24-Nov-21
TX-3CD		Area 3C1 - CR WP, Sec 1 Interim - Finish	0	298	24-Nov-21	24-Nov-21
HMA Paving			2	298	15-Nov-21	16-Nov-21
TX-3CD		Area 3C1 - CR WP, Place HMA	2	298	15-Nov-21	16-Nov-21
SMA Paving			5	298	17-Nov-21	23-Nov-21
TX-3CD		Area 3C1 - CR WP, Place SMA	5	298	17-Nov-21	23-Nov-21
Curb & Gutter			10	298	01-Nov-21	12-Nov-21
TX-3CD		Area 3C1 - CR WP, Place Curb & Gutter	10	298	01-Nov-21	12-Nov-21
Driveways			10	305	01-Nov-21	12-Nov-21
TX-3CD		Area 3C1 - CR WP, Place Driveways	10	305	01-Nov-21	12-Nov-21
Sidewalks & Median			10	449	26-Nov-21	09-Dec-21
TX-3CD		Area 3C1 - CR WP, Place Sidewalks/Pathways	10	449	26-Nov-21	09-Dec-21
Permanent Barriers			10	449	26-Nov-21	09-Dec-21
Concrete Barriers			10	449	26-Nov-21	09-Dec-21
TX-3CD		Area 3C1 - CR WP, Place Conc Rail	10	449	26-Nov-21	09-Dec-21
Metal Beam Guardrails			10	449	26-Nov-21	09-Dec-21
TX-3CD		Area 3C1 - CR WP, Install MBGF	10	449	26-Nov-21	09-Dec-21
Signals and Illumination			25	434	26-Nov-21	30-Dec-21
Roadway Illumination			25	434	26-Nov-21	30-Dec-21
TX-3CD		Area 3C1 - CR WP, Install Illumination Pole Bases	5	434	26-Nov-21	02-Dec-21
TX-3CD		Area 3C1 - CR WP, Install Illumination Poles/Fixtures	10	434	03-Dec-21	16-Dec-21
TX-3CD		Area 3C1 - CR WP, Install Illumination Energize Fixtures	10	434	17-Dec-21	30-Dec-21
Signing and Marking			26	434	25-Nov-21	31-Dec-21
Small Signage			10	449	26-Nov-21	09-Dec-21
TX-3CD		Area 3C1 - CR WP, Install Small Signage	10	449	26-Nov-21	09-Dec-21
Pavement Marking			26	434	25-Nov-21	31-Dec-21
TX-3CD		Area 3C1 - CR WP, Install Permt Markings	2	458	25-Nov-21	26-Nov-21
TX-3CD		Area 3C1 - CR WP, Finish	0	434	31-Dec-21	31-Dec-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Landscaping	10	449	26-Nov-21	09-Dec-21
		Seeding & Sodding	10	449	26-Nov-21	09-Dec-21
	TX-3CD	Area 3C1 - CR WP, Install Topsoil	10	449	26-Nov-21	09-Dec-21
	TX-3CD	Area 3C1 - CR WP, Install Seeding/Sodding	10	449	26-Nov-21	09-Dec-21
		Crossroad Westport Pkwy STA 1132 PH3	95	366	24-Nov-21	06-Apr-22
	TX-3CD	Area 3C1 - CR WP, Start	0	298	24-Nov-21	24-Nov-21
		Traffic Control and Temporary Work	6	298	24-Nov-21	01-Dec-21
		Barricades, Signs & Traffic Handling	1	298	01-Dec-21	01-Dec-21
	TX-3CD	Area 3C1 - CR WP, Move Traffic	1	298	01-Dec-21	01-Dec-21
		Portable Traffic Barrier	5	298	24-Nov-21	30-Nov-21
	TX-3CD	Area 3C1 - CR WP, Place Temp Conc Barrier	5	298	24-Nov-21	30-Nov-21
		Workzone Pavement Marking	5	298	24-Nov-21	30-Nov-21
	TX-3CD	Area 3C1 - CR WP, Place Temp Marking & Signing	5	298	24-Nov-21	30-Nov-21
		Erosion Control	5	298	24-Nov-21	30-Nov-21
	TX-3CD	Area 3C1 - CR WP, Place Temp Erosion Control	5	298	24-Nov-21	30-Nov-21
		Removals & Demo	5	298	24-Nov-21	30-Nov-21
		Pavement Removal	5	298	24-Nov-21	30-Nov-21
	TX-3CD	Area 3C1 - CR WP, Remove Pavement	5	298	24-Nov-21	30-Nov-21
		Earthwork	41	298	24-Nov-21	19-Jan-22
		Clear & Grub	5	298	24-Nov-21	30-Nov-21
	TX-3CD	Area 3C1 - CR WP, Clear and Grub	5	298	24-Nov-21	30-Nov-21
		Excavation	15	298	02-Dec-21	22-Dec-21
	TX-3CD	Area 3C1 - CR WP, Excavate Cut Areas	15	298	02-Dec-21	22-Dec-21
		Embankment	20	298	23-Dec-21	19-Jan-22
	TX-3CD	Area 3C1 - CR WP, Place Embankment	20	298	23-Dec-21	19-Jan-22
		Subgrade Treatment and Base	10	298	20-Jan-22	02-Feb-22
		Lime Treatment	5	298	20-Jan-22	26-Jan-22
	TX-3CD	Area 3C1 - CR WP, Lime Treat Subgrade	5	298	20-Jan-22	26-Jan-22
		Flexbase	5	298	27-Jan-22	02-Feb-22
	TX-3CD	Area 3C1 - CR WP, Place Flexbase	5	298	27-Jan-22	02-Feb-22
		Pavement	29	381	03-Feb-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, FF Start	0	366	01-Mar-22	01-Mar-22
		Asphalt Pavement	7	298	17-Feb-22	28-Feb-22
	TX-3CD	Area 3C1 - CR WP, Sec 1 Interim - Finish	0	298	28-Feb-22	28-Feb-22
		HMA Paving	2	298	17-Feb-22	18-Feb-22
	TX-3CD	Area 3C1 - CR WP, Place HMA	2	298	17-Feb-22	18-Feb-22
		SMA Paving	5	298	21-Feb-22	25-Feb-22
	TX-3CD	Area 3C1 - CR WP, Place SMA	5	298	21-Feb-22	25-Feb-22
		Curb & Gutter	10	298	03-Feb-22	16-Feb-22
	TX-3CD	Area 3C1 - CR WP, Place Curb & Gutter	10	298	03-Feb-22	16-Feb-22
		Driveways	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Place Driveways	10	381	02-Mar-22	15-Mar-22
		Sidewalks & Median	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Place Sidewalks/Pathways	10	381	02-Mar-22	15-Mar-22
		Permanent Barriers	10	381	02-Mar-22	15-Mar-22
		Concrete Barriers	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Place Conc Rail	10	381	02-Mar-22	15-Mar-22
		Metal Beam Guardrails	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Install MBGF	10	381	02-Mar-22	15-Mar-22
		Signals and Illumination	25	366	02-Mar-22	05-Apr-22
		Roadway Illumination	25	366	02-Mar-22	05-Apr-22
	TX-3CD	Area 3C1 - CR WP, Install Illumination Pole Bases	5	366	02-Mar-22	08-Mar-22
	TX-3CD	Area 3C1 - CR WP, Install Illumination Poles/Fixtures	10	366	09-Mar-22	22-Mar-22
	TX-3CD	Area 3C1 - CR WP, Install Illumination Energize Fixtures	10	366	23-Mar-22	05-Apr-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Signing and Marking	25	366	02-Mar-22	06-Apr-22
		Small Signage	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Install Small Signage	10	381	02-Mar-22	15-Mar-22
		Pavement Marking	0	366	06-Apr-22	06-Apr-22
	TX-3CD	Area 3C1 - CR WP, Finish	0	366	06-Apr-22	06-Apr-22
		Landscaping	10	381	02-Mar-22	15-Mar-22
		Seeding & Sodding	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Install Topsoil	10	381	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C1 - CR WP, Install Seeding/Sodding	10	381	02-Mar-22	15-Mar-22
		Crossroad Westport Pkwy STA 1132 PH4	95	298	28-Feb-22	11-Jul-22
	TX-3CD	Area 3C1 - CR WP, Start	0	298	28-Feb-22	28-Feb-22
		Traffic Control and Temporary Work	6	298	28-Feb-22	07-Mar-22
		Barricades, Signs & Traffic Handling	1	298	07-Mar-22	07-Mar-22
	TX-3CD	Area 3C1 - CR WP, Move Traffic	1	298	07-Mar-22	07-Mar-22
		Portable Traffic Barrier	5	298	28-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - CR WP, Place Temp Conc Barrier	5	298	28-Feb-22	04-Mar-22
		Workzone Pavement Marking	5	298	28-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - CR WP, Place Temp Marking & Signing	5	298	28-Feb-22	04-Mar-22
		Erosion Control	5	298	28-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - CR WP, Place Temp Erosion Control	5	298	28-Feb-22	04-Mar-22
		Removals & Demo	5	298	28-Feb-22	04-Mar-22
		Pavement Removal	5	298	28-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - CR WP, Remove Pavement	5	298	28-Feb-22	04-Mar-22
		Earthwork	41	298	28-Feb-22	25-Apr-22
		Clear & Grub	5	298	28-Feb-22	04-Mar-22
	TX-3CD	Area 3C1 - CR WP, Clear and Grub	5	298	28-Feb-22	04-Mar-22
		Excavation	15	298	08-Mar-22	28-Mar-22
	TX-3CD	Area 3C1 - CR WP, Excavate Cut Areas	15	298	08-Mar-22	28-Mar-22
		Embankment	20	298	29-Mar-22	25-Apr-22
	TX-3CD	Area 3C1 - CR WP, Place Embankment	20	298	29-Mar-22	25-Apr-22
		Subgrade Treatment and Base	10	298	26-Apr-22	09-May-22
		Lime Treatment	5	298	26-Apr-22	02-May-22
	TX-3CD	Area 3C1 - CR WP, Lime Treat Subgrade	5	298	26-Apr-22	02-May-22
		Flexbase	5	298	03-May-22	09-May-22
	TX-3CD	Area 3C1 - CR WP, Place Flexbase	5	298	03-May-22	09-May-22
		Pavement	29	313	10-May-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, FF Start	0	298	03-Jun-22	03-Jun-22
		Asphalt Pavement	7	298	24-May-22	02-Jun-22
	TX-3CD	Area 3C1 - CR WP, Sec 1 Interim - Finish	0	298	02-Jun-22	02-Jun-22
		HMA Paving	2	298	24-May-22	25-May-22
	TX-3CD	Area 3C1 - CR WP, Place HMA	2	298	24-May-22	25-May-22
		SMA Paving	5	298	26-May-22	01-Jun-22
	TX-3CD	Area 3C1 - CR WP, Place SMA	5	298	26-May-22	01-Jun-22
		Curb & Gutter	10	298	10-May-22	23-May-22
	TX-3CD	Area 3C1 - CR WP, Place Curb & Gutter	10	298	10-May-22	23-May-22
		Driveways	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Place Driveways	10	313	06-Jun-22	17-Jun-22
		Sidewalks & Median	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Place Sidewalks/Pathways	10	313	06-Jun-22	17-Jun-22
		Permanent Barriers	10	313	06-Jun-22	17-Jun-22
		Concrete Barriers	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Place Conc Rail	10	313	06-Jun-22	17-Jun-22
		Metal Beam Guardrails	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Install MBGF	10	313	06-Jun-22	17-Jun-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Signals and Illumination	25	298	06-Jun-22	08-Jul-22
		Roadway Illumination	25	298	06-Jun-22	08-Jul-22
	TX-3CD	Area 3C1 - CR WP, Install Illumination Pole Bases	5	298	06-Jun-22	10-Jun-22
	TX-3CD	Area 3C1 - CR WP, Install Illumination Poles/Fixtures	10	298	13-Jun-22	24-Jun-22
	TX-3CD	Area 3C1 - CR WP, Install Illumination Energize Fixtures	10	298	27-Jun-22	08-Jul-22
		Signing and Marking	26	298	03-Jun-22	11-Jul-22
		Small Signage	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Install Small Signage	10	313	06-Jun-22	17-Jun-22
		Pavement Marking	26	298	03-Jun-22	11-Jul-22
	TX-3CD	Area 3C1 - CR WP, Install Permt Markings	2	322	03-Jun-22	06-Jun-22
	TX-3CD	Area 3C1 - CR WP, Finish	0	298	11-Jul-22	11-Jul-22
		Landscaping	10	313	06-Jun-22	17-Jun-22
		Seeding & Sodding	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Install Topsoil	10	313	06-Jun-22	17-Jun-22
	TX-3CD	Area 3C1 - CR WP, Install Seeding/Sodding	10	313	06-Jun-22	17-Jun-22
		Southbound ML Lane PH1 Sta 1099+75 to 1165+30	264	571	16-Sep-20	21-Sep-21
C3(	TX-3CD	Area 3C1 -SB ML, Start STA 1059 to 1176	0	567	16-Sep-20	16-Sep-20
		Traffic Control and Temporary Work	6	588	16-Sep-20	23-Sep-20
		Barricades, Signs & Traffic Handling	1	588	23-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 -SB ML, Move Traffic	1	588	23-Sep-20	23-Sep-20
		Portable Traffic Barrier	5	588	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 -SB ML, Place Temp Conc Barrier	5	588	16-Sep-20	22-Sep-20
		Workzone Pavement Marking	5	588	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 -SB ML, Place Temp Marking & Signing	5	588	16-Sep-20	22-Sep-20
		Erosion Control	5	588	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 -SB ML, Place Temp Erosion Control	5	588	16-Sep-20	22-Sep-20
		Earthwork	76	588	16-Sep-20	30-Dec-20
		Clear & Grub	5	588	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 -SB ML, Clear and Grub	5	588	16-Sep-20	22-Sep-20
		Excavation	30	588	24-Sep-20	04-Nov-20
	TX-3CD	Area 3C1 -SB ML, Excavate Cut Areas	30	588	24-Sep-20	04-Nov-20
		Embankment	20	588	03-Dec-20	30-Dec-20
	TX-3CD	Area 3C1 -SB ML, Place Embankment	20	588	03-Dec-20	30-Dec-20
		Drainage	20	588	05-Nov-20	02-Dec-20
		Culverts	20	588	05-Nov-20	02-Dec-20
	TX-3CD	Area 3C1 - NB FR, CLV05 Install Culvert	20	588	05-Nov-20	02-Dec-20
		Subgrade Treatment and Base	60	588	31-Dec-20	24-Mar-21
		Lime Treatment	40	588	31-Dec-20	24-Feb-21
	TX-3CD	Area 3C1 -SB ML, Lime Treat Subgrade	40	588	31-Dec-20	24-Feb-21
		Flexbase	20	588	25-Feb-21	24-Mar-21
	TX-3CD	Area 3C1 -SB ML, Place Flexbase	20	588	25-Feb-21	24-Mar-21
		Pavement	52	583	25-Mar-21	04-Jun-21
(	TX-3CD	Area 3C1 -SB ML, FF Start STA 1059 to 1176	0	567	24-May-21	24-May-21
		Asphalt Pavement	52	583	25-Mar-21	04-Jun-21
	TX-3CD	Area 3C1 - SB ML, Interim - Finish STA 1059 to 1176	0	567	21-May-21	21-May-21
		HMA Paving	10	598	25-Mar-21	07-Apr-21
	TX-3CD	Area 3C1 -SB ML, Place HMA	10	598	25-Mar-21	07-Apr-21
		SMA Paving	10	583	24-May-21	04-Jun-21
	TX-3CD	Area 3C1 -SB ML, Place SMA	10	583	24-May-21	04-Jun-21
		BR 102.3 Henrietta Creek	177	567	16-Sep-20	21-May-21
(	TX-3CD	Area 3C1 -SB ML, BR 102.3 Start	20	567	16-Sep-20	13-Oct-20
(	TX-3CD	Area 3C1 - SB ML, BR 102.3 Finish	0	567	21-May-21	21-May-21
		BR Excavation	5	573	15-Oct-20	21-Oct-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Bridge Excavation	5	573	15-Oct-20	21-Oct-20
Drill Shafts			20	583	22-Oct-20	18-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Drill Shafts Abutment 1	5	573	22-Oct-20	28-Oct-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Drill Shafts Bent 2-3	5	573	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Drill Shafts Bent 4-5	5	573	05-Nov-20	11-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Drill Shafts Abutment 6	5	583	12-Nov-20	18-Nov-20
Columns			25	583	29-Oct-20	02-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Columns Abutment 1	10	598	29-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Columns Bent 2-3	15	578	05-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Columns Bent 4-5	15	573	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Columns Abutment 6	10	583	19-Nov-20	02-Dec-20
Bent Caps			25	573	26-Nov-20	30-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Cap Bent 2-3	20	578	26-Nov-20	23-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Cap Bent 4-5	20	573	03-Dec-20	30-Dec-20
Beams			66	567	15-Oct-20	14-Jan-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Beam Procurement	20	567	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Forward Precast Beams Shopdrawings to TxDOT	1	567	12-Nov-20	12-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Precast Beam Fabrication & Delivery Leadtime	40	567	13-Nov-20	07-Jan-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Conc Beams	5	567	08-Jan-21	14-Jan-21
BR Place CTB Embankment			20	648	17-Dec-20	13-Jan-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Place Stabilized Backfill	20	648	17-Dec-20	13-Jan-21
Abutments			25	583	12-Nov-20	16-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Abutment 1	10	598	12-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Abutment 6	10	583	03-Dec-20	16-Dec-20
Approach Slab			10	567	07-May-21	20-May-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Apprch Slab Abutment 1	10	567	07-May-21	20-May-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Apprch Slab Abutment 6	10	567	07-May-21	20-May-21
Exspansion Joint			60	567	15-Jan-21	08-Apr-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Exp Joints	60	567	15-Jan-21	08-Apr-21
Deck			80	567	15-Jan-21	06-May-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Deck Slab	60	567	15-Jan-21	08-Apr-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Cure Deck Slab	20	567	09-Apr-21	06-May-21
Railings			10	567	07-May-21	20-May-21
	TX-3CD	Area 3C1 -SB ML, BR 102.3 Install Conc Rail	10	567	07-May-21	20-May-21
BR 103.2 Westport Pkwy			174	570	16-Sep-20	18-May-21
(	TX-3CD	Area 3C1 -SB ML, BR 103.2 Start	20	570	16-Sep-20	13-Oct-20
(	TX-3CD	Area 3C1 - SB ML, BR 103.2 Finish	0	570	18-May-21	18-May-21
BR Excavation			5	594	15-Oct-20	21-Oct-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Bridge Excavation	5	594	15-Oct-20	21-Oct-20
Drill Shafts			20	594	22-Oct-20	18-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Drill Shafts Abutment 1	5	594	22-Oct-20	28-Oct-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Drill Shafts Bent 2	5	594	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Drill Shafts Bent 3	5	594	05-Nov-20	11-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Drill Shafts Abutment4	5	594	12-Nov-20	18-Nov-20
Columns			20	594	29-Oct-20	25-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Columns Abutment 1	5	606	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Columns Bent 2	5	601	05-Nov-20	11-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Columns Bent 3	5	596	12-Nov-20	18-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Columns Abutment 4	5	594	19-Nov-20	25-Nov-20
Bent Caps			15	596	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Cap Bent 2	10	601	12-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Cap Bent 3	10	596	19-Nov-20	02-Dec-20
Beams			63	570	15-Oct-20	11-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Beam Procurement	20	570	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Forward Precast Beams Shopdrawings to TxDOT	1	570	12-Nov-20	12-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Precast Beam Fabrication & Delivery Leadtime	40	570	13-Nov-20	07-Jan-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Conc Beams	2	570	08-Jan-21	11-Jan-21
BR Place CTB Embankment			20	656	07-Dec-20	01-Jan-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Place Stabilized Backfill	20	656	07-Dec-20	01-Jan-21
Abutments			22	594	05-Nov-20	04-Dec-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Abutment 1	10	606	05-Nov-20	18-Nov-20
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Abutment 4	7	594	26-Nov-20	04-Dec-20
Approach Slab			10	570	04-May-21	17-May-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Apprch Slab Abutment 1	10	570	04-May-21	17-May-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Apprch Slab Abutment 4	10	570	04-May-21	17-May-21
Exspansion Joint			60	570	12-Jan-21	05-Apr-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Exp Joints	60	570	12-Jan-21	05-Apr-21
Deck			80	570	12-Jan-21	03-May-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Deck Slab	60	570	12-Jan-21	05-Apr-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Cure Deck Slab	20	570	06-Apr-21	03-May-21
Railings			5	575	04-May-21	10-May-21
	TX-3CD	Area 3C1 -SB ML, BR 103.2 Install Conc Rail	5	575	04-May-21	10-May-21
Permanent Barriers			10	582	25-May-21	07-Jun-21
Concrete Barriers			10	582	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Place Conc Rail	10	582	25-May-21	07-Jun-21
Metal Beam Guardrails			10	582	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install MBGF	10	582	25-May-21	07-Jun-21
Signals and Illumination			25	567	25-May-21	28-Jun-21
Roadway Illumination			25	567	25-May-21	28-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Illumination Pole Bases	5	567	25-May-21	31-May-21
	TX-3CD	Area 3C1 -SB ML, Install Illumination Poles/Fixtures	10	567	01-Jun-21	14-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Illumination Energize Fixtures	10	567	15-Jun-21	28-Jun-21
High Mast Illumination			15	577	25-May-21	14-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install High Mast Illumination Pole Bases	5	577	25-May-21	31-May-21
	TX-3CD	Area 3C1 -SB ML, Install High Mast Illumination Poles/Fixtures	5	577	01-Jun-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install High Mast Illumination Energize Fixtures	5	577	08-Jun-21	14-Jun-21
Signing and Marking			26	567	24-May-21	29-Jun-21
Overhead Sign Structures			10	582	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Overhead Signage	10	582	25-May-21	07-Jun-21
Small Signage			10	582	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Small Signage	10	582	25-May-21	07-Jun-21
Pavement Marking			26	567	24-May-21	29-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Permt Markings	2	591	24-May-21	25-May-21
	TX-3CD	Area 3C1 - SB ML, Finish STA 1059 to 1176	0	567	29-Jun-21	29-Jun-21
Landscaping			10	582	25-May-21	07-Jun-21
Seeding & Sodding			10	582	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Topsoil	10	582	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 -SB ML, Install Seeding/Sodding	10	582	25-May-21	07-Jun-21
ITS/TCS			128	571	25-Mar-21	21-Sep-21
Duct Bank System			20	588	25-Mar-21	21-Apr-21
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Civil Work Install Conduit	20	588	25-Mar-21	21-Apr-21
Equipment Foundations			20	571	24-May-21	18-Jun-21
	TX-3CD	Area 3C1 -SB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	20	571	24-May-21	18-Jun-21
Equipment			45	571	24-May-21	26-Jul-21
	TX-3CD	Area 3C1 -SB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	571	24-May-21	24-May-21
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Install fiber	10	576	24-May-21	04-Jun-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Cut and splice	20	576	07-Jun-21	02-Jul-21
	TX-3CD	Area 3C1 -SB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	25	571	21-Jun-21	23-Jul-21
	TX-3CD	Area 3C1 -SB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	571	26-Jul-21	26-Jul-21
Testing & Certification			56	571	05-Jul-21	21-Sep-21
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Local Site Test	10	576	05-Jul-21	16-Jul-21
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Fiber Complete	0	576	19-Jul-21	19-Jul-21
	TX-3CD	Area 3C1 -SB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	572	26-Jul-21	20-Aug-21
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Testing Start	0	571	27-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 -SB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	571	27-Jul-21	23-Aug-21
	TX-3CD	Area 3C1 -SB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	20	571	24-Aug-21	20-Sep-21
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Testing Complete	0	571	21-Sep-21	21-Sep-21
Southbound ML Lane PH2 STA 1048+00 to 1099+75			243	136	16-Jun-22	23-May-23
C3(	TX-3CD	Area 3C1 -SB ML, Start STA 1059 to 1176	0	132	16-Jun-22	16-Jun-22
Traffic Control and Temporary Work			6	132	16-Jun-22	23-Jun-22
Barricades, Signs & Traffic Handling			1	132	23-Jun-22	23-Jun-22
	TX-3CD	Area 3C1 -SB ML, Move Traffic	1	132	23-Jun-22	23-Jun-22
Portable Traffic Barrier			5	132	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 -SB ML, Place Temp Conc Barrier	5	132	16-Jun-22	22-Jun-22
Workzone Pavement Marking			5	132	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 -SB ML, Place Temp Marking & Signing	5	132	16-Jun-22	22-Jun-22
Erosion Control			5	132	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 -SB ML, Place Temp Erosion Control	5	132	16-Jun-22	22-Jun-22
Earthwork			76	132	16-Jun-22	29-Sep-22
Clear & Grub			5	132	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 -SB ML, Clear and Grub	5	132	16-Jun-22	22-Jun-22
Excavation			30	132	24-Jun-22	04-Aug-22
	TX-3CD	Area 3C1 -SB ML, Excavate Cut Areas	30	132	24-Jun-22	04-Aug-22
Embankment			20	132	02-Sep-22	29-Sep-22
	TX-3CD	Area 3C1 -SB ML, Place Embankment	20	132	02-Sep-22	29-Sep-22
Drainage			20	132	05-Aug-22	01-Sep-22
Culverts			20	132	05-Aug-22	01-Sep-22
	TX-3CD	Area 3C1 - NB FR, CLV05 Install Culvert	20	132	05-Aug-22	01-Sep-22
Subgrade Treatment and Base			60	132	30-Sep-22	22-Dec-22
Lime Treatment			40	132	30-Sep-22	24-Nov-22
	TX-3CD	Area 3C1 -SB ML, Lime Treat Subgrade	40	132	30-Sep-22	24-Nov-22
Flexbase			20	132	25-Nov-22	22-Dec-22
	TX-3CD	Area 3C1 -SB ML, Place Flexbase	20	132	25-Nov-22	22-Dec-22
Pavement			31	148	23-Dec-22	03-Feb-23
(	TX-3CD	Area 3C1 -SB ML, FF Start STA 1059 to 1176	0	132	23-Jan-23	23-Jan-23
Asphalt Pavement			31	148	23-Dec-22	03-Feb-23
	TX-3CD	Area 3C1 - SB ML, Interim - Finish STA 1059 to 1176	0	132	20-Jan-23	20-Jan-23
HMA Paving			10	142	23-Dec-22	05-Jan-23
	TX-3CD	Area 3C1 -SB ML, Place HMA	10	142	23-Dec-22	05-Jan-23
SMA Paving			10	148	23-Jan-23	03-Feb-23
	TX-3CD	Area 3C1 -SB ML, Place SMA	10	148	23-Jan-23	03-Feb-23
Permanent Barriers			10	147	24-Jan-23	06-Feb-23
Concrete Barriers			10	147	24-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Place Conc Rail	10	147	24-Jan-23	06-Feb-23
Metal Beam Guardrails			10	147	24-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install MBGF	10	147	24-Jan-23	06-Feb-23
Signals and Illumination			25	132	24-Jan-23	27-Feb-23
Roadway Illumination			25	132	24-Jan-23	27-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Illumination Pole Bases	5	132	24-Jan-23	30-Jan-23

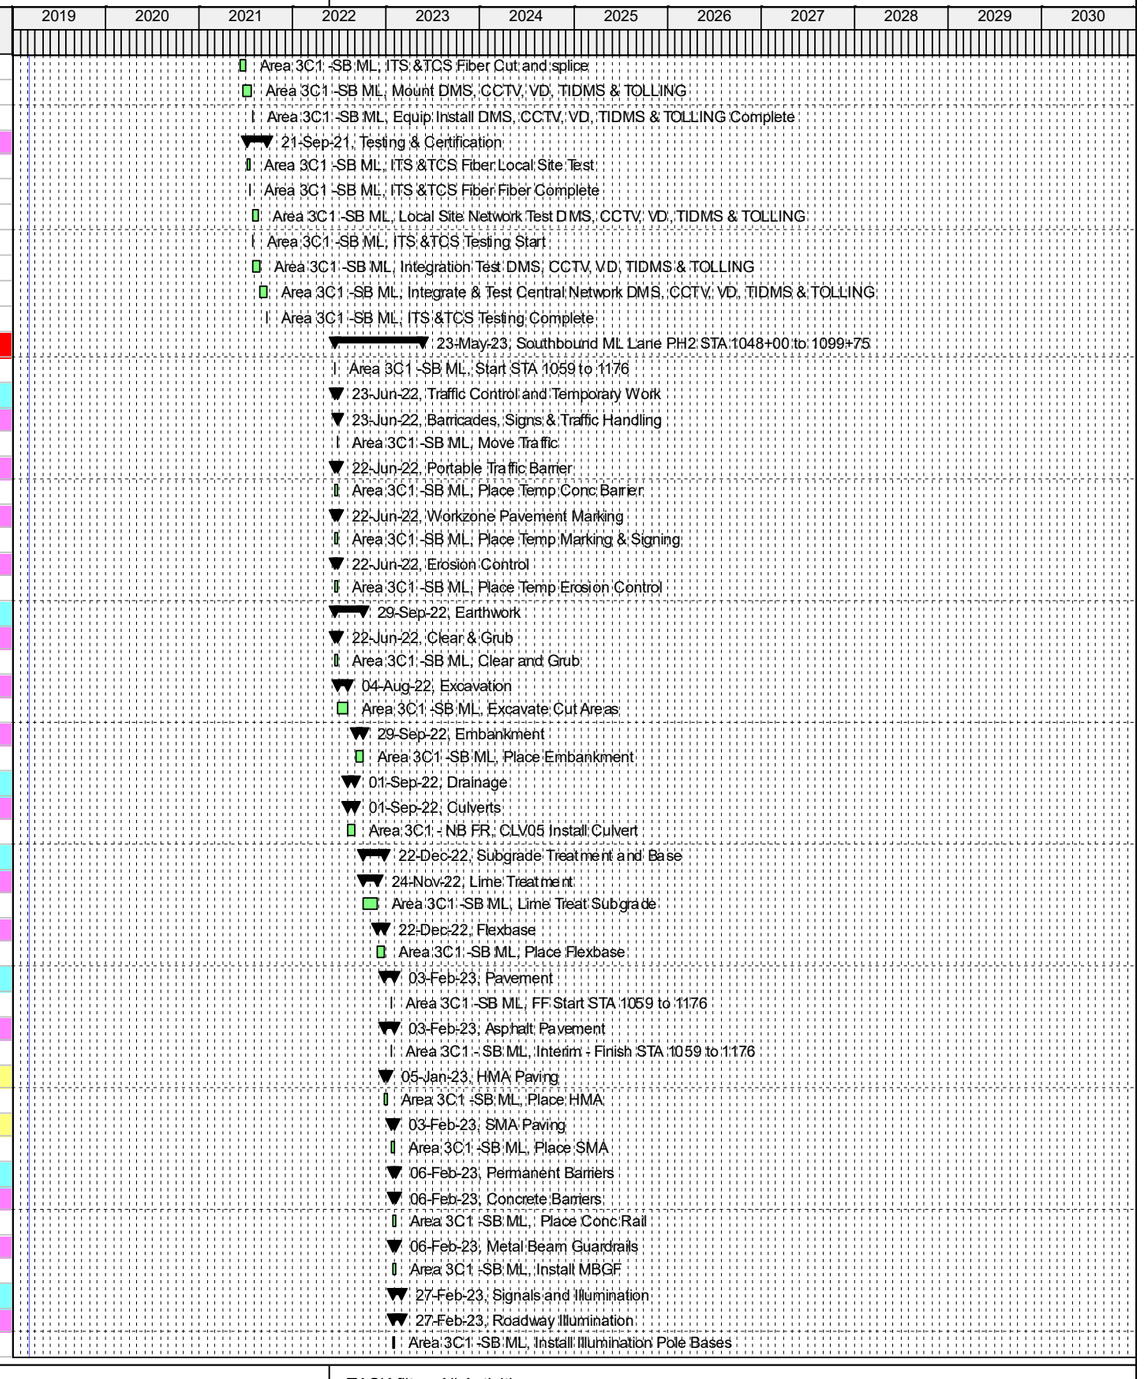

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 -SB ML, Install Illumination Poles/Fixtures	10	132	31-Jan-23	13-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Illumination Energize Fixtures	10	132	14-Feb-23	27-Feb-23
High Mast Illumination			15	142	24-Jan-23	13-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install High Mast Illumination Pole Bases	5	142	24-Jan-23	30-Jan-23
	TX-3CD	Area 3C1 -SB ML, Install High Mast Illumination Poles/Fixtures	5	142	31-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install High Mast Illumination Energize Fixtures	5	142	07-Feb-23	13-Feb-23
Signing and Marking			26	132	23-Jan-23	28-Feb-23
Overhead Sign Structures			10	147	24-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Overhead Signage	10	147	24-Jan-23	06-Feb-23
Small Signage			10	147	24-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Small Signage	10	147	24-Jan-23	06-Feb-23
Pavement Marking			26	132	23-Jan-23	28-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Permt Markings	2	156	23-Jan-23	24-Jan-23
	TX-3CD	Area 3C1 - SB ML, Finish STA 1059 to 1176	0	132	28-Feb-23	28-Feb-23
Landscaping			10	147	24-Jan-23	06-Feb-23
Seeding & Sodding			10	147	24-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Topsoil	10	147	24-Jan-23	06-Feb-23
	TX-3CD	Area 3C1 -SB ML, Install Seeding/Sodding	10	147	24-Jan-23	06-Feb-23
ITS/TCS			107	136	23-Dec-22	23-May-23
Duct Bank System			20	132	23-Dec-22	19-Jan-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Civil Work Install Conduit	20	132	23-Dec-22	19-Jan-23
Equipment Foundations			20	136	23-Jan-23	17-Feb-23
	TX-3CD	Area 3C1 -SB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	20	136	23-Jan-23	17-Feb-23
Equipment			45	136	23-Jan-23	27-Mar-23
	TX-3CD	Area 3C1 -SB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	136	23-Jan-23	23-Jan-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Install fiber	10	141	23-Jan-23	03-Feb-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Cut and splice	20	141	06-Feb-23	03-Mar-23
	TX-3CD	Area 3C1 -SB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	25	136	20-Feb-23	24-Mar-23
	TX-3CD	Area 3C1 -SB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	136	27-Mar-23	27-Mar-23
Testing & Certification			56	136	06-Mar-23	23-May-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Local Site Test	10	141	06-Mar-23	17-Mar-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Fiber Fiber Complete	0	141	20-Mar-23	20-Mar-23
	TX-3CD	Area 3C1 -SB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	137	27-Mar-23	21-Apr-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Testing Start	0	136	28-Mar-23	28-Mar-23
	TX-3CD	Area 3C1 -SB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	136	28-Mar-23	24-Apr-23
	TX-3CD	Area 3C1 -SB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	20	136	25-Apr-23	22-May-23
	TX-3CD	Area 3C1 -SB ML, ITS &TCS Testing Complete	0	136	23-May-23	23-May-23
Southbound ML Entry Ramp STA 1050 to 1059			118	197	16-Jun-22	29-Nov-22
C3(	TX-3CD	Area 3C1 - SB ENR ML, Start STA 1059 to 1059	0	197	16-Jun-22	16-Jun-22
Traffic Control and Temporary Work			6	197	16-Jun-22	23-Jun-22
Barricades, Signs & Traffic Handling			1	197	23-Jun-22	23-Jun-22
	TX-3CD	Area 3C1 - SB ENR ML, Move Traffic	1	197	23-Jun-22	23-Jun-22
Portable Traffic Barrier			5	197	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Temp Conc Barrier	5	197	16-Jun-22	22-Jun-22
Workzone Pavement Marking			5	197	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Temp Marking & Signing	5	197	16-Jun-22	22-Jun-22
Erosion Control			5	197	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Temp Erosion Control	5	197	16-Jun-22	22-Jun-22
Earthwork			41	197	16-Jun-22	11-Aug-22
Clear & Grub			5	197	16-Jun-22	22-Jun-22
	TX-3CD	Area 3C1 - SB ENR ML, Clear and Grub	5	197	16-Jun-22	22-Jun-22
Excavation			15	197	24-Jun-22	14-Jul-22
	TX-3CD	Area 3C1 - SB ENR ML, Excavate Cut Areas	15	197	24-Jun-22	14-Jul-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Embankment	20	197	15-Jul-22	11-Aug-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Embankment	20	197	15-Jul-22	11-Aug-22
		Subgrade Treatment and Base	30	197	12-Aug-22	22-Sep-22
		Lime Treatment	20	197	12-Aug-22	08-Sep-22
	TX-3CD	Area 3C1 - SB ENR ML, Lime Treat Subgrade	20	197	12-Aug-22	08-Sep-22
		Flexbase	10	197	09-Sep-22	22-Sep-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Flexbase	10	197	09-Sep-22	22-Sep-22
		Pavement	26	218	23-Sep-22	28-Oct-22
C	TX-3CD	Area 3C1 - SB ENR ML, FF Start STA 1059 to 1059	0	197	24-Oct-22	24-Oct-22
		Asphalt Pavement	16	218	07-Oct-22	28-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, Interim - Finish STA 1059 to 1059	0	197	21-Oct-22	21-Oct-22
		HMA Paving	2	205	07-Oct-22	10-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, Place HMA	2	205	07-Oct-22	10-Oct-22
		SMA Paving	5	218	24-Oct-22	28-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, Place SMA	5	218	24-Oct-22	28-Oct-22
		Curb & Gutter	10	205	23-Sep-22	06-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Curb & Gutter	10	205	23-Sep-22	06-Oct-22
		Permanent Barriers	10	212	25-Oct-22	07-Nov-22
		Concrete Barriers	10	212	25-Oct-22	07-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Place Conc Rail	10	212	25-Oct-22	07-Nov-22
		Metal Beam Guardrails	10	212	25-Oct-22	07-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install MBGF	10	212	25-Oct-22	07-Nov-22
		Signals and Illumination	25	197	25-Oct-22	28-Nov-22
		Roadway Illumination	25	197	25-Oct-22	28-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Illumination Pole Bases	5	197	25-Oct-22	31-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Illumination Poles/Fixtures	10	197	01-Nov-22	14-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Illumination Energize Fixtures	10	197	15-Nov-22	28-Nov-22
		Signing and Marking	26	197	24-Oct-22	29-Nov-22
		Overhead Sign Structures	10	212	25-Oct-22	07-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Overhead Signage	10	212	25-Oct-22	07-Nov-22
		Small Signage	10	212	25-Oct-22	07-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Small Signage	10	212	25-Oct-22	07-Nov-22
		Pavement Marking	26	197	24-Oct-22	29-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Permt Markings	2	221	24-Oct-22	25-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, Finish STA 1059 to 1059	0	197	29-Nov-22	29-Nov-22
		Landscaping	10	212	25-Oct-22	07-Nov-22
		Seeding & Sodding	10	212	25-Oct-22	07-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Topsoil	10	212	25-Oct-22	07-Nov-22
	TX-3CD	Area 3C1 - SB ENR ML, Install Seeding/Sodding	10	212	25-Oct-22	07-Nov-22
		ITS/TCS	20	197	23-Sep-22	20-Oct-22
		Duct Bank System	20	197	23-Sep-22	20-Oct-22
	TX-3CD	Area 3C1 - SB ENR ML, ITS &TCS Civil Work Install Coduit	20	197	23-Sep-22	20-Oct-22
		Southbound GP Lane STA 1045 to 1176	221	555	09-Sep-20	15-Jul-21
C3(	TX-3CD	Area 3C1 - SB GP, Start STA 1045+50 to 1176+00	5	0	09-Sep-20	15-Sep-20
C3(	TX-3CD	Area 3C1 - SB GP, BR 102.5 ACM (Asbestos) and LCP (Lead) Testing	1	36	16-Sep-20	16-Sep-20
C3(	TX-3CD	Area 3C1 - SB GP, BR 103.3 ACM (Asbestos) and LCP (Lead) Testing	1	39	16-Sep-20	16-Sep-20
C3(	TX-3CD	Area 3C1 - SB GP, Interim - Finish STA 1045 to 1176	0	0	08-Jun-21	08-Jun-21
C3(	TX-3CD	Area 3C1 - SB GP, FF Start STA 1045 to 1176	0	555	09-Jun-21	09-Jun-21
C3(	TX-3CD	Area 3C1 - SB GP, Finish STA 1045 to 1176	0	555	15-Jul-21	15-Jul-21
		Traffic Control and Temporary Work	8	0	16-Sep-20	25-Sep-20
		Barricades, Signs & Traffic Handling	1	0	25-Sep-20	25-Sep-20
	TX-3CD	Area 3C1 - SB GP, Move Traffic Sta 1045+50 to 1176+00	1	0	25-Sep-20	25-Sep-20
		Detour Construction/Removal	5	2	16-Sep-20	22-Sep-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP, Place Temp Paving Sta 1028+00 to 1052+00	5	2	16-Sep-20	22-Sep-20
Portable Traffic Barrier			5	2	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP, Place Temp Conc Barrier Sta 1045+50 to 1176+00	5	2	16-Sep-20	22-Sep-20
Workzone Pavement Marking			5	2	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP, Place Temp Marking & Signing Sta 1045+50 to 1176+00	5	2	16-Sep-20	22-Sep-20
Erosion Control			5	2	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP, Place Temp Erosion Control Sta 1045+50 to 1176+00	5	2	16-Sep-20	22-Sep-20
Removals & Demo			7	0	16-Sep-20	24-Sep-20
Pavement Removal			7	0	16-Sep-20	24-Sep-20
	TX-3CD	Area 3C1 - SB GP, Remove Pavement Sta 1045+50 to 1176+00	7	0	16-Sep-20	24-Sep-20
Earthwork			148	0	16-Sep-20	09-Apr-21
Clear & Grub			5	2	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP, Clear and Grub Sta 1045+50 to 1176+00	5	2	16-Sep-20	22-Sep-20
Excavation			40	0	28-Sep-20	20-Nov-20
	TX-3CD	Area 3C1 - SB GP, Excavate Cut Areas	40	0	28-Sep-20	20-Nov-20
Embankment			40	0	15-Feb-21	09-Apr-21
	TX-3CD	Area 3C1 - SB GP, Place Embankment	40	0	15-Feb-21	09-Apr-21
Drainage			100	0	28-Sep-20	12-Feb-21
Culverts			20	80	28-Sep-20	23-Oct-20
	TX-3CD	Area 3C1 - SB GP, CLV05 Install Culvert	20	80	28-Sep-20	23-Oct-20
Storm Sewer			30	0	23-Nov-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, Install Small RCP	30	0	23-Nov-20	01-Jan-21
Inlets			30	0	04-Jan-21	12-Feb-21
	TX-3CD	Area 3C1 - SB GP, Install MHs and Inlets	30	0	04-Jan-21	12-Feb-21
Subgrade Treatment and Base			20	0	12-Apr-21	07-May-21
Lime Treatment			15	0	12-Apr-21	30-Apr-21
	TX-3CD	Area 3C1 - SB GP, Lime Treat Subgrade	15	0	12-Apr-21	30-Apr-21
Flexbase			5	0	03-May-21	07-May-21
	TX-3CD	Area 3C1 - SB GP, Place Flexbase	5	0	03-May-21	07-May-21
Pavement			32	571	10-May-21	22-Jun-21
Asphalt Pavement			32	571	10-May-21	22-Jun-21
HMA Paving			21	0	10-May-21	07-Jun-21
	TX-3CD	Area 3C1 - SB GP, Place HMA	21	0	10-May-21	07-Jun-21
SMA Paving			10	571	09-Jun-21	22-Jun-21
	TX-3CD	Area 3C1 - SB GP, Place SMA	10	571	09-Jun-21	22-Jun-21
Retaining Walls			40	75	23-Nov-20	15-Jan-21
RT-3C -1A			30	85	23-Nov-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, Install Wall RT-3C-1A	20	85	23-Nov-20	18-Dec-20
	TX-3CD	Area 3C1 - SB GP, Install Coping Cap RT-3C-2A	10	85	21-Dec-20	01-Jan-21
RT-3C -S2			40	75	23-Nov-20	15-Jan-21
	TX-3CD	Area 3C1 - SB GP, Install Wall RT-3C-S2	30	75	23-Nov-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, Install Coping Cap RT-3C-S2	10	75	04-Jan-21	15-Jan-21
RT-3C -2A			30	85	23-Nov-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, Install Wall RT-3C-2A	20	85	23-Nov-20	18-Dec-20
	TX-3CD	Area 3C1 - SB GP, Install Coping Cap RT-3C-1A	10	85	21-Dec-20	01-Jan-21
RT-3C -S1			30	85	23-Nov-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, Install Wall RT-3C-S1	20	85	23-Nov-20	18-Dec-20
	TX-3CD	Area 3C1 - SB GP, Install Coping Cap RT-3C-S1	10	85	21-Dec-20	01-Jan-21
BR 102.5 Henrietta Creek			189	0	16-Sep-20	08-Jun-21
(	TX-3CD	Area 3C1 - SB GP, BR 102.5 Start	20	0	16-Sep-20	13-Oct-20
(	TX-3CD	Area 3C1 - SB GP, BR 102.5 Finish	0	0	08-Jun-21	08-Jun-21
BR Demolition			25	21	17-Sep-20	21-Oct-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	36	17-Sep-20	23-Sep-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Bridge Demolition	5	21	15-Oct-20	21-Oct-20
BR Excavation			5	21	15-Oct-20	21-Oct-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Bridge Excavation	5	21	15-Oct-20	21-Oct-20
Drill Shafts			20	24	22-Oct-20	18-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Drill Shafts Abutment 1	5	21	22-Oct-20	28-Oct-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Drill Shafts Bent 2-3	5	21	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Drill Shafts Bent 4-5	5	21	05-Nov-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Drill Shafts Abutment 6	5	24	12-Nov-20	18-Nov-20
Columns			20	24	29-Oct-20	25-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Columns Abutment 1	5	36	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Columns Bent 2-3	10	26	05-Nov-20	18-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Columns Bent 4-5	10	21	12-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Columns Abutment 6	5	24	19-Nov-20	25-Nov-20
Bent Caps			15	21	19-Nov-20	09-Dec-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Cap Bent 2-3	10	26	19-Nov-20	02-Dec-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Cap Bent 4-5	10	21	26-Nov-20	09-Dec-20
Beams			63	0	15-Oct-20	11-Jan-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Beam Procurement	20	0	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Forward Precast Beams Shopdrawings to TxDOT	1	0	12-Nov-20	12-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Precast Beam Fabrication & Delivery Leadtime	40	0	13-Nov-20	07-Jan-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Conc Beams	2	0	08-Jan-21	11-Jan-21
BR Place CTB Embankment			20	101	07-Dec-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Place Stabilized Backfill	20	101	07-Dec-20	01-Jan-21
Abutments			22	24	05-Nov-20	04-Dec-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Abutment 1	10	36	05-Nov-20	18-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Abutment 6	7	24	26-Nov-20	04-Dec-20
Approach Slab			10	0	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Apprch Slab Abutment 1	10	0	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Apprch Slab Abutment 6	10	0	25-May-21	07-Jun-21
Exspansion Joint			60	15	12-Jan-21	05-Apr-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Exp Joints	60	15	12-Jan-21	05-Apr-21
Railings			10	0	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Conc Rail	10	0	25-May-21	07-Jun-21
Deck			95	0	12-Jan-21	24-May-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Install Deck Slab	75	0	12-Jan-21	26-Apr-21
	TX-3CD	Area 3C1 - SB GP, BR 102.5 Cure Deck Slab	20	0	27-Apr-21	24-May-21
BR 103.3 Westport Pkwy			189	0	16-Sep-20	08-Jun-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Start	20	0	16-Sep-20	13-Oct-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Finish	0	0	08-Jun-21	08-Jun-21
BR Demolition			25	24	17-Sep-20	21-Oct-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	39	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Bridge Demolition	5	24	15-Oct-20	21-Oct-20
BR Excavation			5	24	15-Oct-20	21-Oct-20
	TX-3CD	Area 3C1 - SB GP,BR 12 Bridge Excavation	5	24	15-Oct-20	21-Oct-20
Drill Shafts			20	24	22-Oct-20	18-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Drill Shafts Abutment 1	5	24	22-Oct-20	28-Oct-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Drill Shafts Bent 2	5	24	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Drill Shafts Bent 3	5	24	05-Nov-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Drill Shafts Abutment 4	5	24	12-Nov-20	18-Nov-20
Columns			20	24	29-Oct-20	25-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Columns Abutment 1	5	36	29-Oct-20	04-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Columns Bent 2	5	31	05-Nov-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Columns Bent 3	5	26	12-Nov-20	18-Nov-20

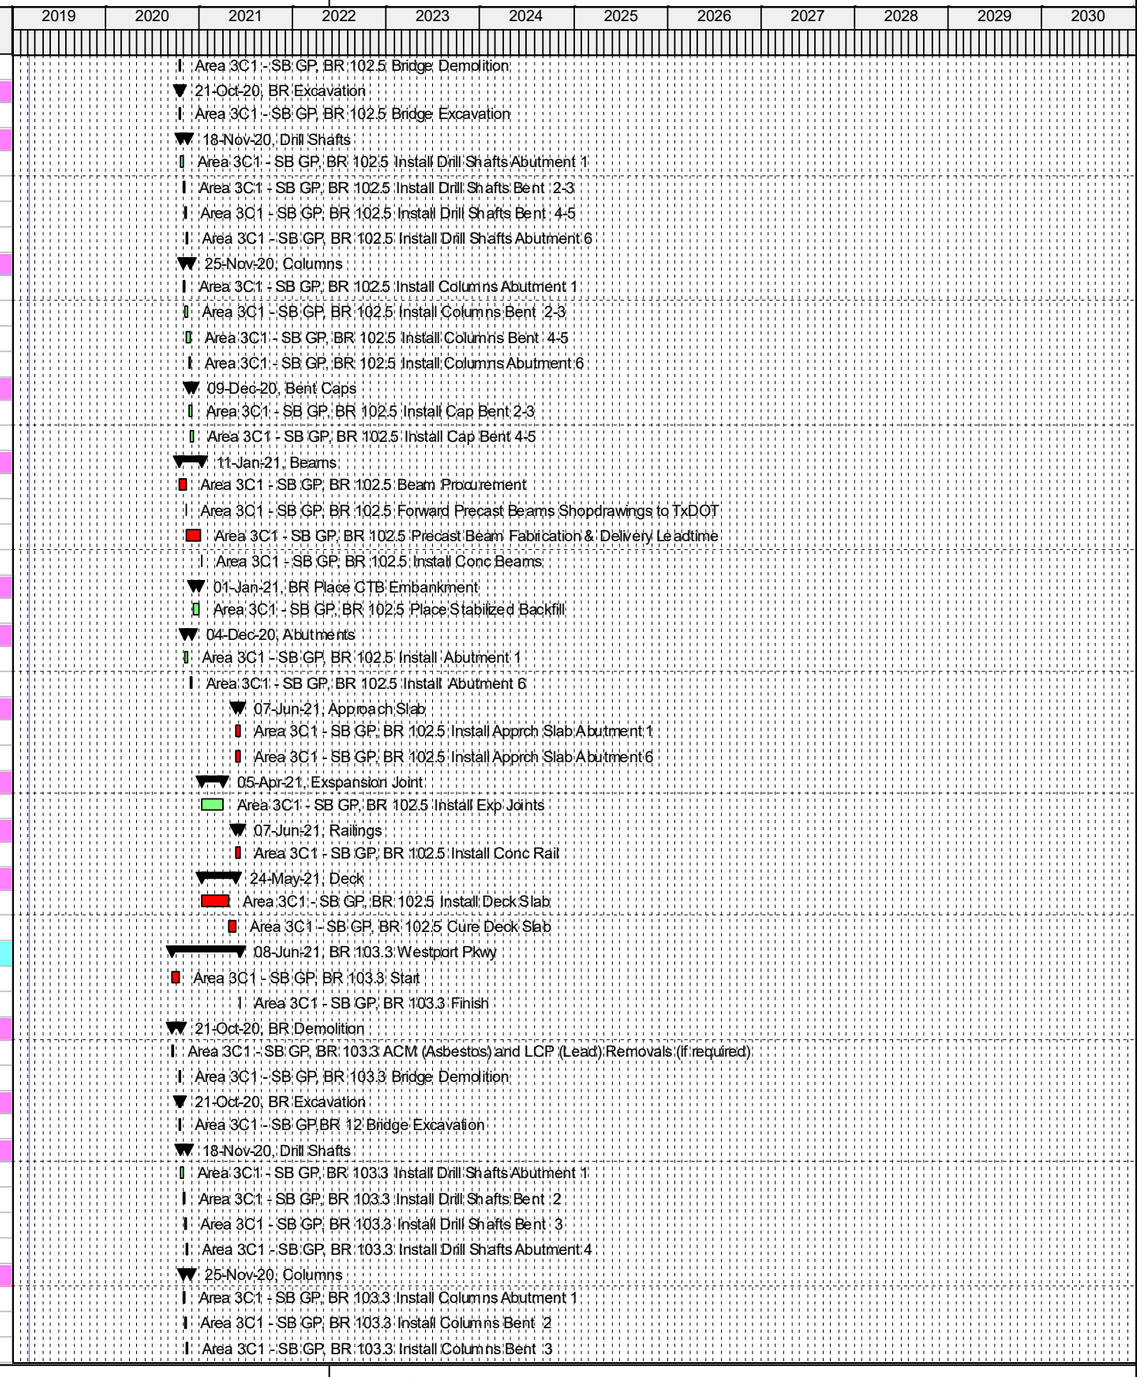

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Columns Abutment 4	5	24	19-Nov-20	25-Nov-20
Bent Caps			15	26	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Cap Bent 2	10	31	12-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Cap Bent 3	10	26	19-Nov-20	02-Dec-20
Beams			63	0	15-Oct-20	11-Jan-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Beam Procurement	20	0	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Forward Precast Beams Shopdrawings to TxDOT	1	0	12-Nov-20	12-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Precast Beam Fabrication & Delivery Leadtime	40	0	13-Nov-20	07-Jan-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Conc Beams	2	0	08-Jan-21	11-Jan-21
BR Place CTB Embankment			20	101	07-Dec-20	01-Jan-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Place Stabilized Backfull	20	101	07-Dec-20	01-Jan-21
Abutments			22	24	05-Nov-20	04-Dec-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Abutment 1	10	36	05-Nov-20	18-Nov-20
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Abutment 4	7	24	26-Nov-20	04-Dec-20
Approach Slab			10	0	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Apprch Slab Abutment 1	10	0	25-May-21	07-Jun-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Apprch Slab Abutment 4	10	0	25-May-21	07-Jun-21
Exspansion Joint			60	15	12-Jan-21	05-Apr-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Exp Joints	60	15	12-Jan-21	05-Apr-21
Deck			95	0	12-Jan-21	24-May-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Deck Slab	75	0	12-Jan-21	26-Apr-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Cure Deck Slab	20	0	27-Apr-21	24-May-21
Railings			5	5	25-May-21	31-May-21
	TX-3CD	Area 3C1 - SB GP, BR 103.3 Install Conc Rail	5	5	25-May-21	31-May-21
Permanent Barriers			10	570	10-Jun-21	23-Jun-21
Concrete Barriers			10	570	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Place Conc Rail	10	570	10-Jun-21	23-Jun-21
Metal Beam Guardrails			10	570	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install MBGF	10	570	10-Jun-21	23-Jun-21
Signals and Illumination			25	555	10-Jun-21	14-Jul-21
Roadway Illumination			25	555	10-Jun-21	14-Jul-21
	TX-3CD	Area 3C1 - SB GP, Install Illumination Pole Bases	5	555	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Illumination Poles/Fixtures	10	555	17-Jun-21	30-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Illumination Energize Fixtures	10	555	01-Jul-21	14-Jul-21
High Mast Illumination			15	565	10-Jun-21	30-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install High Mast Illumination Pole Bases	5	565	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install High Mast Illumination Poles/Fixtures	5	565	17-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install High Mast Illumination Energize Fixtures	5	565	24-Jun-21	30-Jun-21
Signing and Marking			11	570	09-Jun-21	23-Jun-21
Overhead Sign Structures			10	570	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Overhead Signage	10	570	10-Jun-21	23-Jun-21
Small Signage			10	570	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Small Signage	10	570	10-Jun-21	23-Jun-21
Pavement Marking			2	579	09-Jun-21	10-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Permt Markings	2	579	09-Jun-21	10-Jun-21
Landscaping			10	570	10-Jun-21	23-Jun-21
Seeding & Sodding			10	570	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Topsoil	10	570	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C1 - SB GP, Install Seeding/Sodding	10	570	10-Jun-21	23-Jun-21
ITS/TCS			0	21	10-May-21	10-May-21
Duct Bank System			0	21	10-May-21	10-May-21
	TX-3CD	Area 3C1 - SB GP, ITS &TCS Civil Work Install Conduit	0	21	10-May-21	10-May-21
Southbound GP Entry Ramp STA 1049 to 1059			118	653	16-Sep-20	01-Mar-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3(	TX-3CD	Area 3C1 - SB GP ENR, Start STA 1049 to 1059	0	653	16-Sep-20	16-Sep-20
C3(	TX-3CD	Area 3C1 - SB GP ENR, Interim - Finish STA 1049 to 1059	0	653	21-Jan-21	21-Jan-21
C3(	TX-3CD	Area 3C1 - SB GP ENR, FF Start STA 1049 to 1059	0	653	22-Jan-21	22-Jan-21
C3(	TX-3CD	Area 3C1 - SB GP ENR, Finish STA 1049 to 1059	0	653	01-Mar-21	01-Mar-21
Traffic Control and Temporary Work			6	653	16-Sep-20	23-Sep-20
Barricades, Signs & Traffic Handling			1	653	23-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Move Traffic	1	653	23-Sep-20	23-Sep-20
Portable Traffic Barrier			5	653	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Conc Barrier	5	653	16-Sep-20	22-Sep-20
Workzone Pavement Marking			5	653	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Marking & Signing	5	653	16-Sep-20	22-Sep-20
Erosion Control			5	653	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Erosion Control	5	653	16-Sep-20	22-Sep-20
Earthwork			41	653	16-Sep-20	11-Nov-20
Clear & Grub			5	653	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Clear and Grub	5	653	16-Sep-20	22-Sep-20
Excavation			15	653	24-Sep-20	14-Oct-20
	TX-3CD	Area 3C1 - SB GP ENR, Excavate Cut Areas	15	653	24-Sep-20	14-Oct-20
Embankment			20	653	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Embankment	20	653	15-Oct-20	11-Nov-20
Subgrade Treatment and Base			30	653	12-Nov-20	23-Dec-20
Lime Treatment			20	653	12-Nov-20	09-Dec-20
	TX-3CD	Area 3C1 - SB GP ENR, Lime Treat Subgrade	20	653	12-Nov-20	09-Dec-20
Flexbase			10	653	10-Dec-20	23-Dec-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Flexbase	10	653	10-Dec-20	23-Dec-20
Pavement			26	674	24-Dec-20	28-Jan-21
Asphalt Pavement			16	674	07-Jan-21	28-Jan-21
HMA Paving			10	653	07-Jan-21	20-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Place HMA	10	653	07-Jan-21	20-Jan-21
SMA Paving			5	674	22-Jan-21	28-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Place SMA	5	674	22-Jan-21	28-Jan-21
Curb & Gutter			10	653	24-Dec-20	06-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Curb & Gutter	10	653	24-Dec-20	06-Jan-21
Permanent Barriers			10	668	25-Jan-21	05-Feb-21
Concrete Barriers			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Conc Rail	10	668	25-Jan-21	05-Feb-21
Metal Beam Guardrails			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install MBGF	10	668	25-Jan-21	05-Feb-21
Signals and Illumination			25	653	25-Jan-21	26-Feb-21
Roadway Illumination			25	653	25-Jan-21	26-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Pole Bases	5	653	25-Jan-21	29-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Poles/Fixtures	10	653	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Energize Fixtures	10	653	15-Feb-21	26-Feb-21
Signing and Marking			11	668	22-Jan-21	05-Feb-21
Overhead Sign Structures			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Overhead Signage	10	668	25-Jan-21	05-Feb-21
Small Signage			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Small Signage	10	668	25-Jan-21	05-Feb-21
Pavement Marking			2	677	22-Jan-21	25-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Permt Markings	2	677	22-Jan-21	25-Jan-21
Landscaping			10	668	25-Jan-21	05-Feb-21
Seeding & Sodding			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Topsoil	10	668	25-Jan-21	05-Feb-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP ENR, Install Seeding/Sodding	10	668	25-Jan-21	05-Feb-21
ITS/TCS			20	653	24-Dec-20	20-Jan-21
Duct Bank System			20	653	24-Dec-20	20-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, ITS &TCS Civil Work Install Coduit	20	653	24-Dec-20	20-Jan-21
Southbound GP Exit Ramp STA 1080 to 1095			98	673	16-Sep-20	01-Feb-21
C3(	TX-3CD	Area 3C1 - SB EXR, Start STA 1080 to 1095	0	673	16-Sep-20	16-Sep-20
Traffic Control and Temporary Work			6	673	16-Sep-20	23-Sep-20
Barricades, Signs & Traffic Handling			1	673	23-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - SB EXR, Move Traffic	1	673	23-Sep-20	23-Sep-20
Portable Traffic Barrier			5	673	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB EXR, Place Temp Conc Barrier	5	673	16-Sep-20	22-Sep-20
Workzone Pavement Marking			5	673	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB EXR, Place Temp Marking & Signing	5	673	16-Sep-20	22-Sep-20
Erosion Control			5	673	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB EXR, Place Temp Erosion Control	5	673	16-Sep-20	22-Sep-20
Earthwork			41	673	16-Sep-20	11-Nov-20
Clear & Grub			5	673	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB EXR, Clear and Grub	5	673	16-Sep-20	22-Sep-20
Excavation			15	673	24-Sep-20	14-Oct-20
	TX-3CD	Area 3C1 - SB EXR, Excavate Cut Areas	15	673	24-Sep-20	14-Oct-20
Embankment			20	673	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 - SB EXR, Place Embankment	20	673	15-Oct-20	11-Nov-20
Subgrade Treatment and Base			10	673	12-Nov-20	25-Nov-20
Lime Treatment			5	673	12-Nov-20	18-Nov-20
	TX-3CD	Area 3C1 - SB EXR, Lime Treat Subgrade	5	673	12-Nov-20	18-Nov-20
Flexbase			5	673	19-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 - SB EXR, Place Flexbase	5	673	19-Nov-20	25-Nov-20
Pavement			26	694	26-Nov-20	31-Dec-20
(	TX-3CD	Area 3C1 - SB EXR, FF Start STA 1080 to 1095	19-Feb-	673	25-Dec-20	25-Dec-20
Asphalt Pavement			16	694	10-Dec-20	31-Dec-20
	TX-3CD	Area 3C1 - SB EXR, Interim - Finish STA 1080 to 1095	0	673	24-Dec-20	24-Dec-20
HMA Paving			2	681	10-Dec-20	11-Dec-20
	TX-3CD	Area 3C1 - SB EXR, Place HMA	2	681	10-Dec-20	11-Dec-20
SMA Paving			5	694	25-Dec-20	31-Dec-20
	TX-3CD	Area 3C1 - SB EXR, Place SMA	5	694	25-Dec-20	31-Dec-20
Curb & Gutter			10	681	26-Nov-20	09-Dec-20
	TX-3CD	Area 3C1 - SB EXR, Place Curb & Gutter	10	681	26-Nov-20	09-Dec-20
Permanent Barriers			10	688	28-Dec-20	08-Jan-21
Concrete Barriers			10	688	28-Dec-20	08-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Place Conc Rail	10	688	28-Dec-20	08-Jan-21
Metal Beam Guardrails			10	688	28-Dec-20	08-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install MBGF	10	688	28-Dec-20	08-Jan-21
Crash Attenuators			5	693	28-Dec-20	01-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Attenuator	5	693	28-Dec-20	01-Jan-21
Signals and Illumination			25	673	28-Dec-20	29-Jan-21
Roadway Illumination			25	673	28-Dec-20	29-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Illumination Pole Bases	5	673	28-Dec-20	01-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Illumination Poles/Fixtures	10	673	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Illumination Energize Fixtures	10	673	18-Jan-21	29-Jan-21
Signing and Marking			26	673	25-Dec-20	01-Feb-21
Overhead Sign Structures			10	688	28-Dec-20	08-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Overhead Signage	10	688	28-Dec-20	08-Jan-21
Small Signage			10	688	28-Dec-20	08-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB EXR, Install Small Signage	10	688	28-Dec-20	08-Jan-21
Pavement Marking			26	673	25-Dec-20	01-Feb-21
	TX-3CD	Area 3C1 - SB EXR, Install Permt Markings	2	697	25-Dec-20	28-Dec-20
	TX-3CD	Area 3C1 - SB EXR, Finish STA 1080 to 1095	0	673	01-Feb-21	01-Feb-21
Landscaping			10	688	28-Dec-20	08-Jan-21
Seeding & Sodding			10	688	28-Dec-20	08-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Topsoil	10	688	28-Dec-20	08-Jan-21
	TX-3CD	Area 3C1 - SB EXR, Install Seeding/Sodding	10	688	28-Dec-20	08-Jan-21
ITS/TCS			20	673	26-Nov-20	23-Dec-20
Duct Bank System			20	673	26-Nov-20	23-Dec-20
	TX-3CD	Area 3C1 - SB EXR, ITS &TCS Civil Work Install Coduit	20	673	26-Nov-20	23-Dec-20
Southbound GP Entry Ramp STA 1110 to 1120			103	668	16-Sep-20	08-Feb-21
C3(	TX-3CD	Area 3C1 - SB GP ENR, Start STA 1110 to 1120	0	668	16-Sep-20	16-Sep-20
Traffic Control and Temporary Work			6	668	16-Sep-20	23-Sep-20
Barricades, Signs & Traffic Handling			1	668	23-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Move Traffic	1	668	23-Sep-20	23-Sep-20
Portable Traffic Barrier			5	668	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Conc Barrier	5	668	16-Sep-20	22-Sep-20
Workzone Pavement Marking			5	668	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Marking & Signing	5	668	16-Sep-20	22-Sep-20
Erosion Control			5	668	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Erosion Control	5	668	16-Sep-20	22-Sep-20
Earthwork			41	668	16-Sep-20	11-Nov-20
Clear & Grub			5	668	16-Sep-20	22-Sep-20
	TX-3CD	Area 3C1 - SB GP ENR, Clear and Grub	5	668	16-Sep-20	22-Sep-20
Excavation			15	668	24-Sep-20	14-Oct-20
	TX-3CD	Area 3C1 - SB GP ENR, Excavate Cut Areas	15	668	24-Sep-20	14-Oct-20
Embankment			20	668	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Embankment	20	668	15-Oct-20	11-Nov-20
Subgrade Treatment and Base			15	668	12-Nov-20	02-Dec-20
Lime Treatment			10	668	12-Nov-20	25-Nov-20
	TX-3CD	Area 3C1 - SB GP ENR, Lime Treat Subgrade	10	668	12-Nov-20	25-Nov-20
Flexbase			5	668	26-Nov-20	02-Dec-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Flexbase	5	668	26-Nov-20	02-Dec-20
Pavement			26	689	03-Dec-20	07-Jan-21
(	TX-3CD	Area 3C1 - SB GP ENR, FF Start STA 1110 to 1120	0	668	01-Jan-21	01-Jan-21
Asphalt Pavement			11	689	24-Dec-20	07-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Interim - Finish STA 1110 to 1120	0	668	31-Dec-20	31-Dec-20
HMA Paving			2	671	24-Dec-20	25-Dec-20
	TX-3CD	Area 3C1 - SB GP ENR, Place HMA	2	671	24-Dec-20	25-Dec-20
SMA Paving			5	689	01-Jan-21	07-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Place SMA	5	689	01-Jan-21	07-Jan-21
Curb & Gutter			15	671	03-Dec-20	23-Dec-20
	TX-3CD	Area 3C1 - SB GP ENR, Place Curb & Gutter	15	671	03-Dec-20	23-Dec-20
Permanent Barriers			10	683	04-Jan-21	15-Jan-21
Concrete Barriers			10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Conc Rail	10	683	04-Jan-21	15-Jan-21
Metal Beam Guardrails			10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install MBGF	10	683	04-Jan-21	15-Jan-21
Crash Attenuators			5	688	04-Jan-21	08-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Attenuator	5	688	04-Jan-21	08-Jan-21
Signals and Illumination			25	668	04-Jan-21	05-Feb-21
Roadway Illumination			25	668	04-Jan-21	05-Feb-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Pole Bases	5	668	04-Jan-21	08-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Poles/Fixtures	10	668	11-Jan-21	22-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Energize Fixtures	10	668	25-Jan-21	05-Feb-21
Signing and Marking			26	668	01-Jan-21	08-Feb-21
Overhead Sign Structures			10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Overhead Signage	10	683	04-Jan-21	15-Jan-21
Small Signage			10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Small Signage	10	683	04-Jan-21	15-Jan-21
Pavement Marking			26	668	01-Jan-21	08-Feb-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Permt Markings	2	692	01-Jan-21	04-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Finish STA 1110 to 1120	0	668	08-Feb-21	08-Feb-21
Landscaping			10	683	04-Jan-21	15-Jan-21
Seeding & Sodding			10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Topsoil	10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Seeding/Sodding	10	683	04-Jan-21	15-Jan-21
ITS/TCS			20	668	03-Dec-20	30-Dec-20
Duct Bank System			20	668	03-Dec-20	30-Dec-20
	TX-3CD	Area 3C1 - SB GP ENR, ITS &TCS Civil Work Install Coduit	20	668	03-Dec-20	30-Dec-20
Southbound GP Entry Ramp STA 1164 to 1176			98	464	06-Jul-21	19-Nov-21
C3(	TX-3CD	Area 3C1 - EB ENR, Start STA 1164 to 1176	0	464	06-Jul-21	06-Jul-21
Traffic Control and Temporary Work			6	464	06-Jul-21	13-Jul-21
Barricades, Signs & Traffic Handling			1	464	13-Jul-21	13-Jul-21
	TX-3CD	Area 3C1 - SB GP ENR, Move Traffic	1	464	13-Jul-21	13-Jul-21
Portable Traffic Barrier			5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Conc Barrier	5	464	06-Jul-21	12-Jul-21
Workzone Pavement Marking			5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Marking & Signing	5	464	06-Jul-21	12-Jul-21
Erosion Control			5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Temp Erosion Control	5	464	06-Jul-21	12-Jul-21
Earthwork			41	464	06-Jul-21	31-Aug-21
Clear & Grub			5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP ENR, Clear and Grub	5	464	06-Jul-21	12-Jul-21
Excavation			15	464	14-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - SB GP ENR, Excavate Cut Areas	15	464	14-Jul-21	03-Aug-21
Embankment			20	464	04-Aug-21	31-Aug-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Embankment	20	464	04-Aug-21	31-Aug-21
Subgrade Treatment and Base			10	464	01-Sep-21	14-Sep-21
Lime Treatment			5	464	01-Sep-21	07-Sep-21
	TX-3CD	Area 3C1 - SB GP ENR, Lime Treat Subgrade	5	464	01-Sep-21	07-Sep-21
Flexbase			5	464	08-Sep-21	14-Sep-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Flexbase	5	464	08-Sep-21	14-Sep-21
Pavement			26	485	15-Sep-21	20-Oct-21
(	TX-3CD	Area 3C1 - SB GP ENR, FF Start STA 1164 to 1176	0	464	14-Oct-21	14-Oct-21
Asphalt Pavement			16	485	29-Sep-21	20-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Interim - Finish STA 1164 to 1176	0	464	13-Oct-21	13-Oct-21
HMA Paving			2	472	29-Sep-21	30-Sep-21
	TX-3CD	Area 3C1 - SB GP ENR, Place HMA	2	472	29-Sep-21	30-Sep-21
SMA Paving			5	485	14-Oct-21	20-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Place SMA	5	485	14-Oct-21	20-Oct-21
Curb & Gutter			10	472	15-Sep-21	28-Sep-21
	TX-3CD	Area 3C1 - SB GP ENR, Place Curb & Gutter	10	472	15-Sep-21	28-Sep-21
Permanent Barriers			10	479	15-Oct-21	28-Oct-21
Concrete Barriers			10	479	15-Oct-21	28-Oct-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP ENR, Place Conc Rail	10	479	15-Oct-21	28-Oct-21
	Metal Beam Guardrails		10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install MBGF	10	479	15-Oct-21	28-Oct-21
	Crash Attenuators		5	484	15-Oct-21	21-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Attenuator	5	484	15-Oct-21	21-Oct-21
	Signals and Illumination		25	464	15-Oct-21	18-Nov-21
	Roadway Illumination		25	464	15-Oct-21	18-Nov-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Pole Bases	5	464	15-Oct-21	21-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Poles/Fixtures	10	464	22-Oct-21	04-Nov-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Illumination Energize Fixtures	10	464	05-Nov-21	18-Nov-21
	Signing and Marking		26	464	14-Oct-21	19-Nov-21
	Overhead Sign Structures		10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Overhead Signage	10	479	15-Oct-21	28-Oct-21
	Small Signage		10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Small Signage	10	479	15-Oct-21	28-Oct-21
	Pavement Marking		26	464	14-Oct-21	19-Nov-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Permt Markings	2	488	14-Oct-21	15-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Finish STA 1164 to 1176	0	464	19-Nov-21	19-Nov-21
	Landscaping		10	479	15-Oct-21	28-Oct-21
	Seeding & Sodding		10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Topsoil	10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, Install Seeding/Sodding	10	479	15-Oct-21	28-Oct-21
	ITS/TCS		20	464	15-Sep-21	12-Oct-21
	Duct Bank System		20	464	15-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - SB GP ENR, ITS &TCS Civil Work Install Coduit	20	464	15-Sep-21	12-Oct-21
	Southbound GP Exit Ramp STA 1134 to 1150		98	464	06-Jul-21	19-Nov-21
C3(	TX-3CD	Area 3C1 - SB GP EXR, Start STA 1134 to 1150	0	464	06-Jul-21	06-Jul-21
	Traffic Control and Temporary Work		6	464	06-Jul-21	13-Jul-21
	Barricades, Signs & Traffic Handling		1	464	13-Jul-21	13-Jul-21
	TX-3CD	Area 3C1 - SB GP EXR, Move Traffic	1	464	13-Jul-21	13-Jul-21
	Portable Traffic Barrier		5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Temp Conc Barrier	5	464	06-Jul-21	12-Jul-21
	Workzone Pavement Marking		5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Temp Marking & Signing	5	464	06-Jul-21	12-Jul-21
	Erosion Control		5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Temp Erosion Control	5	464	06-Jul-21	12-Jul-21
	Earthwork		41	464	06-Jul-21	31-Aug-21
	Clear & Grub		5	464	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB GP EXR, Clear and Grub	5	464	06-Jul-21	12-Jul-21
	Excavation		15	464	14-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - SB GP EXR, Excavate Cut Areas	15	464	14-Jul-21	03-Aug-21
	Embankment		20	464	04-Aug-21	31-Aug-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Embankment	20	464	04-Aug-21	31-Aug-21
	Subgrade Treatment and Base		10	464	01-Sep-21	14-Sep-21
	Lime Treatment		5	464	01-Sep-21	07-Sep-21
	TX-3CD	Area 3C1 - SB GP EXR, Lime Treat Subgrade	5	464	01-Sep-21	07-Sep-21
	Flexbase		5	464	08-Sep-21	14-Sep-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Flexbase	5	464	08-Sep-21	14-Sep-21
	Pavement		26	485	15-Sep-21	20-Oct-21
(	TX-3CD	Area 3C1 - SB GP EXR, FF Start STA 1134 to 1150	0	464	14-Oct-21	14-Oct-21
	Asphalt Pavement		16	485	29-Sep-21	20-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Interim - Finish STA 1134 to 1150	0	464	13-Oct-21	13-Oct-21
	HMA Paving		2	472	29-Sep-21	30-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C1 - SB GP EXR, Place HMA	2	472	29-Sep-21	30-Sep-21
SMA Paving			5	485	14-Oct-21	20-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Place SMA	5	485	14-Oct-21	20-Oct-21
Curb & Gutter			10	472	15-Sep-21	28-Sep-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Curb & Gutter	10	472	15-Sep-21	28-Sep-21
Permanent Barriers			10	479	15-Oct-21	28-Oct-21
Concrete Barriers			10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Place Conc Rail	10	479	15-Oct-21	28-Oct-21
Metal Beam Guardrails			10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Install MBGF	10	479	15-Oct-21	28-Oct-21
Signals and Illumination			25	464	15-Oct-21	18-Nov-21
Roadway Illumination			25	464	15-Oct-21	18-Nov-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Illumination Pole Bases	5	464	15-Oct-21	21-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Illumination Poles/Fixtures	10	464	22-Oct-21	04-Nov-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Illumination Energize Fixtures	10	464	05-Nov-21	18-Nov-21
Signing and Marking			26	464	14-Oct-21	19-Nov-21
Overhead Sign Structures			10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Overhead Signage	10	479	15-Oct-21	28-Oct-21
Small Signage			10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Small Signage	10	479	15-Oct-21	28-Oct-21
Pavement Marking			26	464	14-Oct-21	19-Nov-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Permt Markings	2	488	14-Oct-21	15-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Finish STA 1134 to 1150	0	464	19-Nov-21	19-Nov-21
Landscaping			10	479	15-Oct-21	28-Oct-21
Seeding & Sodding			10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Topsoil	10	479	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, Install Seeding/Sodding	10	479	15-Oct-21	28-Oct-21
ITS/TCS			20	464	15-Sep-21	12-Oct-21
Duct Bank System			20	464	15-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - SB GP EXR, ITS &TCS Civil Work Install Coduit	20	464	15-Sep-21	12-Oct-21
Southbound Frontage Road STA 1028 to 1176			71	491	06-Jul-21	13-Oct-21
C3(	TX-3CD	Area 3C1 - SB FR, Start STA 1028 to 1176	0	464	06-Jul-21	06-Jul-21
Traffic Control 19-Feb-20			6	491	06-Jul-21	13-Jul-21
Barricades, Signs & Traffic Handling			1	491	13-Jul-21	13-Jul-21
	TX-3CD	Area 3C1 - SB FR, Move Traffic	1	491	13-Jul-21	13-Jul-21
Portable Traffic Barrier			5	491	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB FR, Place Temp Conc Barrier	5	491	06-Jul-21	12-Jul-21
Workzone Pavement Marking			5	491	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB FR, Place Temp Marking & Signing	5	491	06-Jul-21	12-Jul-21
Erosion Control			5	491	06-Jul-21	12-Jul-21
	TX-3CD	Area 3C1 - SB FR, Place Temp Erosion Control	5	491	06-Jul-21	12-Jul-21
Earthwork			45	491	14-Jul-21	14-Sep-21
Excavation			25	491	14-Jul-21	17-Aug-21
	TX-3CD	Area 3C1 - SB FR, Excavate Cut Areas	25	491	14-Jul-21	17-Aug-21
Embankment			20	491	18-Aug-21	14-Sep-21
	TX-3CD	Area 3C1 - SB FR, Place Embankment	20	491	18-Aug-21	14-Sep-21
Drainage			65	491	14-Jul-21	12-Oct-21
Culverts			20	496	14-Jul-21	10-Aug-21
	TX-3CD	Area 3C1 - SB FR, CLV05 Install Culvert	20	496	14-Jul-21	10-Aug-21
Riprap			20	491	15-Sep-21	12-Oct-21
	TX-3CD	Area 3C1 - SB FR, Install Riprap	20	491	15-Sep-21	12-Oct-21
Headwall			10	506	11-Aug-21	24-Aug-21
	TX-3CD	Area 3C1 - SB FR, Place Conc Headwall	10	506	11-Aug-21	24-Aug-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Pavement			65	491	14-Jul-21	13-Oct-21
(	TX-3CD	Area 3C1 - SB FR, Start STA 1028 to 1176	0	530	14-Jul-21	14-Jul-21
(	TX-3CD	Area 3C1 - SB FR, Finish STA 1028 to 1176	0	491	13-Oct-21	13-Oct-21
Asphalt Pavement			15	541	14-Jul-21	03-Aug-21
HMA Paving			10	541	14-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 - NB FR, Patch & Repair HMA	10	541	14-Jul-21	27-Jul-21
SMA Paving			5	541	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C1 - NB FR, Patch & Repair SMA	5	541	28-Jul-21	03-Aug-21
Curb & Gutter			20	536	14-Jul-21	10-Aug-21
	TX-3CD	Area 3C1 - SB FR, Place Curb & Gutter	20	536	14-Jul-21	10-Aug-21
Driveways			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Place Driveways	10	545	15-Jul-21	28-Jul-21
Sidewalks & Median			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Place Sidewalks/Pathways	10	545	15-Jul-21	28-Jul-21
BR 204 Henrietta CR.			13	549	06-Jul-21	23-Jul-21
(	TX-3CD	Area 3C1 - CR BR RH, BR 204 Start	2	549	06-Jul-21	07-Jul-21
(	TX-3CD	Area 3C1 - CR BR RH, BR 204 Finish	0	549	23-Jul-21	23-Jul-21
BR Demolition			5	549	09-Jul-21	15-Jul-21
	TX-3CD	Area 3C1 - CR BR RH, BR 204, Concrete Removal	5	549	09-Jul-21	15-Jul-21
Concret Repairs			5	549	16-Jul-21	22-Jul-21
	TX-3CD	Area 3C1 - NB ML, BR 204 Concrete Repairs	5	549	16-Jul-21	22-Jul-21
Replace Exspansion Joint			10	550	08-Jul-21	21-Jul-21
	TX-3CD	Area 3C1 - NB ML, BR 204 Install Exp Joints	10	550	08-Jul-21	21-Jul-21
Permanent Barriers			10	545	15-Jul-21	28-Jul-21
Concrete Barriers			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Place Conc Rail	10	545	15-Jul-21	28-Jul-21
Metal Beam Guardrails			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install MBGF	10	545	15-Jul-21	28-Jul-21
Signals and Illumination			26	530	14-Jul-21	18-Aug-21
Roadway Illumination			25	530	15-Jul-21	18-Aug-21
	TX-3CD	Area 3C1 - SB FR, Install Illumination Pole Bases	5	530	15-Jul-21	21-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Illumination Poles/Fixtures	10	530	22-Jul-21	04-Aug-21
	TX-3CD	Area 3C1 - SB FR, Install Illumination Energize Fixtures	10	530	05-Aug-21	18-Aug-21
Traffic Signals			10	546	14-Jul-21	27-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Traffic Light Poles/Fixtures	10	546	14-Jul-21	27-Jul-21
Signing and Marking			11	545	14-Jul-21	28-Jul-21
Overhead Sign Structures			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Overhead Signage	10	545	15-Jul-21	28-Jul-21
Small Signage			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Small Signage	10	545	15-Jul-21	28-Jul-21
Pavement Marking			2	554	14-Jul-21	15-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Permt Markings	2	554	14-Jul-21	15-Jul-21
Landscaping			10	545	15-Jul-21	28-Jul-21
Seeding & Sodding			10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Topsoil	10	545	15-Jul-21	28-Jul-21
	TX-3CD	Area 3C1 - SB FR, Install Seeding/Sodding	10	545	15-Jul-21	28-Jul-21
3C2 - SH 170 to N. Tarant Pkwy Sta 1176 to 1401			656	204	12-Aug-20	16-Feb-23
Northbound Frontage Road Sta-1176 to 1280			168	422	27-May-21	18-Jan-22
C3(	TX-3CD	Area 3C2 - NB FR, Start STA 1176 to 1280	0	300	27-May-21	27-May-21
Traffic Control and Temporary Work			6	422	27-May-21	03-Jun-21
Barricades, Signs & Traffic Handling			1	422	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB FR, Move Traffic	1	422	03-Jun-21	03-Jun-21
Portable Traffic Barrier			5	422	27-May-21	02-Jun-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB FR, Place Temp Conc Barrier	5	422	27-May-21	02-Jun-21
	Workzone Pavement Marking		5	422	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR, Place Temp Marking & Signing	5	422	27-May-21	02-Jun-21
	Erosion Control		5	422	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR, Place Temp Erosion Control	5	422	27-May-21	02-Jun-21
	Removals & Demo		5	422	27-May-21	02-Jun-21
	Pavement Removal		5	422	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR, Remove Pavement	5	422	27-May-21	02-Jun-21
	Earthwork		41	422	27-May-21	22-Jul-21
	Clear & Grub		5	422	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR, Clear and Grub	5	422	27-May-21	02-Jun-21
	Excavation		15	422	04-Jun-21	24-Jun-21
	TX-3CD	Area 3C2 - NB FR, Excavate Cut Areas	15	422	04-Jun-21	24-Jun-21
	Embankment		20	422	25-Jun-21	22-Jul-21
	TX-3CD	Area 3C2 - NB FR, Place Embankment	20	422	25-Jun-21	22-Jul-21
	Drainage		131	438	25-Jun-21	24-Dec-21
	Culverts		20	442	25-Jun-21	22-Jul-21
	TX-3CD	Area 3C2 - NB FR, CLV06 Install Culvert	20	442	25-Jun-21	22-Jul-21
	TX-3CD	Area 3C2 - NB FR, CLV08 Install Culvert	20	442	25-Jun-21	22-Jul-21
	Storm Sewer		20	442	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C2 - NB FR, Install Small RCP	20	442	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C2 - NB FR, CLV07 Install Medium RCP	20	442	23-Jul-21	19-Aug-21
	Riprap		10	438	13-Dec-21	24-Dec-21
	TX-3CD	Area 3C2 - NB FR, Place RipRap	10	438	13-Dec-21	24-Dec-21
	Inlets		20	442	20-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB FR, Install MHs and Inlets	20	442	20-Aug-21	16-Sep-21
	Headwall		10	512	23-Jul-21	05-Aug-21
	TX-3CD	Area 3C1 - SB FR, Place Conc Headwall	10	512	23-Jul-21	05-Aug-21
	Subgrade Treatment and Base		80	422	23-Jul-21	11-Nov-21
	Lime Treatment		60	422	23-Jul-21	14-Oct-21
	TX-3CD	Area 3C2 - NB FR, Lime Treat Subgrade	60	422	23-Jul-21	14-Oct-21
	Flexbase		20	422	15-Oct-21	11-Nov-21
	TX-3CD	Area 3C2 - NB FR, Place Flexbase	20	422	15-Oct-21	11-Nov-21
	Pavement		32	437	12-Nov-21	27-Dec-21
(	TX-3CD	Area 3C2 - NB FR, Interim - Finish STA 1176 to 1280	0	422	10-Dec-21	10-Dec-21
(	TX-3CD	Area 3C2 - NB FR, FF Start STA 1176 to 1280	0	422	13-Dec-21	13-Dec-21
	Asphalt Pavement		16	443	26-Nov-21	17-Dec-21
	HMA Paving		10	422	26-Nov-21	09-Dec-21
	TX-3CD	Area 3C2 - NB FR, Place HMA Paving	10	422	26-Nov-21	09-Dec-21
	SMA Paving		5	443	13-Dec-21	17-Dec-21
	TX-3CD	Area 3C2 - NB FR, Place SMA Paving	5	443	13-Dec-21	17-Dec-21
	Curb & Gutter		10	422	12-Nov-21	25-Nov-21
	TX-3CD	Area 3C2 - NB FR, Place Curb & Gutter	10	422	12-Nov-21	25-Nov-21
	Driveways		10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Place Driveways	10	437	14-Dec-21	27-Dec-21
	Sidewalks & Median		10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Place Sidewalks/Pathways	10	437	14-Dec-21	27-Dec-21
	Retaining Walls		75	442	04-Jun-21	16-Sep-21
	Wall RT-3C-N5		75	442	04-Jun-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N5	60	442	04-Jun-21	26-Aug-21
	Wall Coping RT-3C-N5		15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N5 Coping Cap	15	442	27-Aug-21	16-Sep-21
	Wall RT-3C-N6		75	442	04-Jun-21	16-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N6	60	442	04-Jun-21	26-Aug-21
Wall Coping RT-3C-N6			15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N6 Coping Cap	15	442	27-Aug-21	16-Sep-21
Wall RT-3C-N8			75	442	04-Jun-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N8	60	442	04-Jun-21	26-Aug-21
Wall Coping RT-3C-N8			15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N8 Coping Cap	15	442	27-Aug-21	16-Sep-21
Wall RT-3C-N9			75	442	04-Jun-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N9	60	442	04-Jun-21	26-Aug-21
Wall Coping RT-3C-N9			15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N9 Coping Cap	15	442	27-Aug-21	16-Sep-21
Wall RT-3C-N10			75	442	04-Jun-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N10	60	442	04-Jun-21	26-Aug-21
Wall Coping RT-3C-N10			15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N10 Coping Cap	15	442	27-Aug-21	16-Sep-21
Wall RT-3C-N11			75	442	04-Jun-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N11	60	442	04-Jun-21	26-Aug-21
Wall Coping RT-3C-N11			15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N11 Coping Cap	15	442	27-Aug-21	16-Sep-21
Wall RT-3C-N12			75	442	04-Jun-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N12	60	442	04-Jun-21	26-Aug-21
Wall Coping RT-3C-N12			15	442	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB GP, Install RT-3C-N12 Coping Cap	15	442	27-Aug-21	16-Sep-21
Permanent Barriers			10	437	14-Dec-21	27-Dec-21
Concrete Barriers			10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Place Conc Rail	10	437	14-Dec-21	27-Dec-21
Metal Beam Guardrails			10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install MBGF	10	437	14-Dec-21	27-Dec-21
Signals and Illumination			26	422	13-Dec-21	17-Jan-22
Roadway Illumination			25	422	14-Dec-21	17-Jan-22
	TX-3CD	Area 3C2 - NB FR, Install Illumination Pole Bases	5	422	14-Dec-21	20-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install Illumination Poles/Fixtures	10	422	21-Dec-21	03-Jan-22
	TX-3CD	Area 3C2 - NB FR, Install Illumination Energize Fixtures	10	422	04-Jan-22	17-Jan-22
Traffic Signals			10	438	13-Dec-21	24-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install Traffic Light Poles/Fixtures	10	438	13-Dec-21	24-Dec-21
Signing and Marking			26	422	13-Dec-21	18-Jan-22
Overhead Sign Structures			10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install Overhead Signage	10	437	14-Dec-21	27-Dec-21
Small Signage			10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install Small Signage	10	437	14-Dec-21	27-Dec-21
Pavement Marking			26	422	13-Dec-21	18-Jan-22
	TX-3CD	Area 3C2 - NB FR, Install Permt Markings	2	446	13-Dec-21	14-Dec-21
	TX-3CD	Area 3C2 - NB FR, Finish STA 1176 to 1280	0	422	18-Jan-22	18-Jan-22
Landscaping			10	437	14-Dec-21	27-Dec-21
Seeding & Sodding			10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install Topsoil	10	437	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - NB FR, Install Seeding/Sodding	10	437	14-Dec-21	27-Dec-21
ITS/TCS			20	422	12-Nov-21	09-Dec-21
Duct Bank System			20	422	12-Nov-21	09-Dec-21
	TX-3CD	Area 3C2 - NB FR, ITS &TCS Civil Work Install Coduit	20	422	12-Nov-21	09-Dec-21
Northbound Entry Ramp STA 1185 to 1200			133	457	27-May-21	30-Nov-21
C3(	TX-3CD	Area 3C2 - NB ENR, Start STA 1185 to 1200	0	457	27-May-21	27-May-21
C3(	TX-3CD	Area 3C2 - NB ENR, Interim - Finish STA 1185 to 1200	0	457	22-Oct-21	22-Oct-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3(	TX-3CD	Area 3C2 - NB ENR, FF Start STA 1185 to 1200	0	457	25-Oct-21	25-Oct-21
C3(	TX-3CD	Area 3C2 - NB ENR, Finish STA 1185 to 1200	0	457	30-Nov-21	30-Nov-21
Traffic Control and Temporary Work			6	457	27-May-21	03-Jun-21
Barricades, Signs & Traffic Handling			1	457	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB ENR, Move Traffic	1	457	03-Jun-21	03-Jun-21
Portable Traffic Barrier			5	457	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ENR, Place Temp Conc Barrier	5	457	27-May-21	02-Jun-21
Workzone Pavement Marking			5	457	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ENR, Place Temp Marking & Signing	5	457	27-May-21	02-Jun-21
Erosion Control			5	457	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ENR, Place Temp Erosion Control	5	457	27-May-21	02-Jun-21
Earthwork			45	457	04-Jun-21	05-Aug-21
Clear & Grub			5	457	04-Jun-21	10-Jun-21
	TX-3CD	Area 3C2 - NB ENR, Clear and Grub	5	457	04-Jun-21	10-Jun-21
Excavation			20	457	11-Jun-21	08-Jul-21
	TX-3CD	Area 3C2 - NB ENR, Excavate Cut Areas	20	457	11-Jun-21	08-Jul-21
Embankment			20	457	09-Jul-21	05-Aug-21
	TX-3CD	Area 3C2 - NB ENR, Place Embankment	20	457	09-Jul-21	05-Aug-21
Subgrade Treatment and Base			35	457	06-Aug-21	23-Sep-21
Lime Treatment			20	457	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - NB ENR, Lime Treat Subgrade	20	457	06-Aug-21	02-Sep-21
Flexbase			15	457	03-Sep-21	23-Sep-21
	TX-3CD	Area 3C2 - NB ENR, Place Flexbase	15	457	03-Sep-21	23-Sep-21
Pavement			26	478	24-Sep-21	29-Oct-21
Asphalt Pavement			16	478	08-Oct-21	29-Oct-21
HMA Paving			10	457	08-Oct-21	21-Oct-21
	TX-3CD	Area 3C2 - NB ENR, Place HMA	10	457	08-Oct-21	21-Oct-21
SMA Paving			5	478	25-Oct-21	29-Oct-21
	TX-3CD	Area 3C2 - NB ENR, Place SMA	5	478	25-Oct-21	29-Oct-21
Curb & Gutter			10	457	24-Sep-21	07-Oct-21
	TX-3CD	Area 3C2 - NB ENR, Place Curb & Gutter	10	457	24-Sep-21	07-Oct-21
Permanent Barriers			10	472	26-Oct-21	08-Nov-21
Concrete Barriers			10	472	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Place Conc Rail	10	472	26-Oct-21	08-Nov-21
Metal Beam Guardrails			10	472	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install MBGF	10	472	26-Oct-21	08-Nov-21
Signals and Illumination			25	457	26-Oct-21	29-Nov-21
Roadway Illumination			25	457	26-Oct-21	29-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Illumination Pole Bases	5	457	26-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Illumination Poles/Fixtures	10	457	02-Nov-21	15-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Illumination Energize Fixtures	10	457	16-Nov-21	29-Nov-21
Signing and Marking			11	472	25-Oct-21	08-Nov-21
Overhead Sign Structures			10	472	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Overhead Signage	10	472	26-Oct-21	08-Nov-21
Small Signage			10	472	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Small Signage	10	472	26-Oct-21	08-Nov-21
Pavement Marking			2	481	25-Oct-21	26-Oct-21
	TX-3CD	Area 3C2 - NB ENR, Install Permt Markings	2	481	25-Oct-21	26-Oct-21
Landscaping			10	472	26-Oct-21	08-Nov-21
Seeding & Sodding			10	472	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Topsoil	10	472	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ENR, Install Seeding/Sodding	10	472	26-Oct-21	08-Nov-21
ITS/TCS			20	457	24-Sep-21	21-Oct-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Duct Bank System	20	457	24-Sep-21	21-Oct-21
	TX-3CD	Area 3C2 - NB ENR, ITS &TCS Civil Work Install Coduit	20	457	24-Sep-21	21-Oct-21
		Northbound Exit Ramp NBML to NBFR STA 1130 to 1180 PH 3	319	140	26-Nov-21	16-Feb-23
C3(	TX-3CD	Area 3C2 - NB EXR, Start STA 1180 to 1220	0	140	26-Nov-21	26-Nov-21
		Traffic Control and Temporary Work	6	312	26-Nov-21	03-Dec-21
		Barricades, Signs & Traffic Handling	1	312	03-Dec-21	03-Dec-21
	TX-3CD	Area 3C2 - NB EXR, Move Traffic	1	312	03-Dec-21	03-Dec-21
		Portable Traffic Barrier	5	312	26-Nov-21	02-Dec-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Conc Barrier	5	312	26-Nov-21	02-Dec-21
		Workzone Pavement Marking	5	312	26-Nov-21	02-Dec-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Marking & Signing	5	312	26-Nov-21	02-Dec-21
		Erosion Control	5	312	26-Nov-21	02-Dec-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Erosion Control	5	312	26-Nov-21	02-Dec-21
		Earthwork	40	342	06-Dec-21	28-Jan-22
		Clear & Grub	5	312	06-Dec-21	10-Dec-21
	TX-3CD	Area 3C2 - NB EXR, Clear and Grub	5	312	06-Dec-21	10-Dec-21
		Excavation	15	312	13-Dec-21	31-Dec-21
	TX-3CD	Area 3C2 - NB EXR, Excavate Cut Areas	15	312	13-Dec-21	31-Dec-21
		Embankment	20	342	03-Jan-22	28-Jan-22
	TX-3CD	Area 3C2 - NB EXR, Place Embankment	20	342	03-Jan-22	28-Jan-22
		Drainage	40	342	03-Jan-22	25-Feb-22
		Storm Sewer	20	342	03-Jan-22	28-Jan-22
	TX-3CD	Area 3C2 - NB EXR, Install Small RCP	20	342	03-Jan-22	28-Jan-22
		Inlets	20	342	31-Jan-22	25-Feb-22
	TX-3CD	Area 3C2 - NB EXR, Install MHs and Inlets	20	342	31-Jan-22	25-Feb-22
		Subgrade Treatment and Base	65	312	31-Jan-22	29-Apr-22
		Lime Treatment	20	342	31-Jan-22	25-Feb-22
	TX-3CD	Area 3C2 - NB EXR, Lime Treat Subgrade	20	342	31-Jan-22	25-Feb-22
		Flexbase	15	312	11-Apr-22	29-Apr-22
	TX-3CD	Area 3C2 - NB EXR, Place Flexbase	15	312	11-Apr-22	29-Apr-22
		Pavement	198	150	02-May-22	01-Feb-23
(	TX-3CD	Area 3C2 - NB EXR, FF Start STA 1180 to 1220	0	140	26-Jan-23	26-Jan-23
		Asphalt Pavement	188	150	16-May-22	01-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Interim - Finish STA 1180 to 1220	0	140	25-Jan-23	25-Jan-23
		HMA Paving	10	312	16-May-22	27-May-22
	TX-3CD	Area 3C2 - NB EXR, Place HMA	10	312	16-May-22	27-May-22
		SMA Paving	5	150	26-Jan-23	01-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Place SMA	5	150	26-Jan-23	01-Feb-23
		Curb & Gutter	10	312	02-May-22	13-May-22
	TX-3CD	Area 3C2 - NB EXR, Place Curb & Gutter	10	312	02-May-22	13-May-22
		Retaining Walls	70	312	03-Jan-22	08-Apr-22
		Wall RT-3C-VI-3B	50	332	03-Jan-22	11-Mar-22
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-VI-3B	40	332	03-Jan-22	25-Feb-22
		Wall Coping RT-3C-S8	10	332	28-Feb-22	11-Mar-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-3B	10	332	28-Feb-22	11-Mar-22
		Wall RT-3C-VI-1B	35	347	03-Jan-22	18-Feb-22
	TX-3CD	Area 3C2 - SB GP, Install Wall Wall RT-3C-VI-1B	25	347	03-Jan-22	04-Feb-22
		Wall Coping RT-3C-S6	10	347	07-Feb-22	18-Feb-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-1B	10	347	07-Feb-22	18-Feb-22
		Wall RT-3C-VI-2B	35	347	03-Jan-22	18-Feb-22
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-VI-2B	25	347	03-Jan-22	04-Feb-22
		Wall Coping RT-3C-S7	10	347	07-Feb-22	18-Feb-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-2B	10	347	07-Feb-22	18-Feb-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Wall RT-3C-VI-2AB	30	352	03-Jan-22	11-Feb-22
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-VI-2AB	20	352	03-Jan-22	28-Jan-22
		Wall Coping RT-3C-S10	10	352	31-Jan-22	11-Feb-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-2AB	10	352	31-Jan-22	11-Feb-22
		Wall RT-3C-N7B	70	312	03-Jan-22	08-Apr-22
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-N7B	60	312	03-Jan-22	25-Mar-22
		Wall Coping RT-3C-S10	10	312	28-Mar-22	08-Apr-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-N7B	10	312	28-Mar-22	08-Apr-22
		3C2 NB EXR BR 114 Braided Ramp	303	140	26-Nov-21	25-Jan-23
(	TX-3CD	Area 3C2 - NB EXR, BR 114 Start	2	140	26-Nov-21	29-Nov-21
(	TX-3CD	Area 3C2 - NB EXR, BR 114 Finish	0	140	25-Jan-23	25-Jan-23
		BR Excavation	5	140	01-Dec-21	07-Dec-21
	TX-3CD	Area 3C2 - NB EXR, BR 114 Bridge Excavation	5	140	01-Dec-21	07-Dec-21
		Drill Shafts	60	200	08-Dec-21	01-Mar-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Drill Shafts Abutment 1	5	140	08-Dec-21	14-Dec-21
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Drill Shafts Bent 2-3	25	140	15-Dec-21	18-Jan-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Drill Shafts Bent 4-5	25	140	19-Feb-20	22-Feb-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Drill Shafts Abutment 6	5	200	23-Feb-22	01-Mar-22
		Footings	45	145	19-Jan-22	22-Mar-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Footings Bent 2-3	20	170	19-Jan-22	15-Feb-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Footings Bent 4-5	20	140	23-Feb-22	22-Mar-22
		Columns	95	170	15-Dec-21	26-Apr-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Columns Abutment 1	10	255	15-Dec-21	28-Dec-21
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Columns Bent 2-3	20	170	16-Feb-22	15-Mar-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Columns Abutment 6	10	200	02-Mar-22	15-Mar-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Columns Bent 4-5	25	140	23-Mar-22	26-Apr-22
		Bent Caps	70	140	16-Mar-22	21-Jun-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Cap Bent 2-3	40	170	16-Mar-22	10-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Cap Bent 4-5	40	140	27-Apr-22	21-Jun-22
		Beams	150	140	01-Dec-21	28-Jun-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Beam Procurement	20	224	01-Dec-21	28-Dec-21
	TX-3CD	Area 3C2 - NB EXR, BR 114 Forward Precast Beams Shopdrawings to TxDOT	1	224	29-Dec-21	29-Dec-21
	TX-3CD	Area 3C2 - NB EXR, BR 114 Precast Beam Fabrication & Delivery Leadtime	40	224	30-Dec-21	23-Feb-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Conc Beams	5	140	22-Jun-22	28-Jun-22
		BR Place CTB Embankment	20	325	30-Mar-22	26-Apr-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Place Stabilized Backfill	20	325	30-Mar-22	26-Apr-22
		Abutments	65	200	29-Dec-21	29-Mar-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Abutment 1	10	255	29-Dec-21	11-Jan-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Abutment 6	10	200	16-Mar-22	29-Mar-22
		Approach Slab	10	140	11-Jan-23	24-Jan-23
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Apprch Slab Abutment 6	10	140	11-Jan-23	24-Jan-23
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Apprch Slab Abutment 1	10	140	11-Jan-23	24-Jan-23
		Exspansion Joint	120	140	29-Jun-22	13-Dec-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Exp Joints	120	140	29-Jun-22	13-Dec-22
		Deck	140	140	29-Jun-22	10-Jan-23
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Deck Slab	120	140	29-Jun-22	13-Dec-22
	TX-3CD	Area 3C2 - NB EXR, BR 114 Cure Deck Slab	20	140	14-Dec-22	10-Jan-23
		Railings	10	140	11-Jan-23	24-Jan-23
	TX-3CD	Area 3C2 - NB EXR, BR 114 Install Conc Rail	10	140	11-Jan-23	24-Jan-23
		Permanent Barriers	10	144	27-Jan-23	09-Feb-23
		Concrete Barriers	10	144	27-Jan-23	09-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Place Conc Rail	10	144	27-Jan-23	09-Feb-23
		Metal Beam Guardrails	10	144	27-Jan-23	09-Feb-23

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB EXR, Install MBGF	10	144	27-Jan-23	09-Feb-23
Signals and Illumination			15	140	26-Jan-23	15-Feb-23
High Mast Illumination			15	140	26-Jan-23	15-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install High Mast Illumination Pole Bases	5	140	26-Jan-23	01-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install High Mast Illumination Poles/Fixtures	5	140	02-Feb-23	08-Feb-23
	TX-3CD	Area 3C2 - NB EXR,Install High Mast Illumination Energize Fixtures	5	140	09-Feb-23	15-Feb-23
Signing and Marking			15	140	26-Jan-23	16-Feb-23
Overhead Sign Structures			10	144	27-Jan-23	09-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install Overhead Signage	10	144	27-Jan-23	09-Feb-23
Small Signage			10	144	27-Jan-23	09-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install Small Signage	10	144	27-Jan-23	09-Feb-23
Pavement Marking			15	140	26-Jan-23	16-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install Permt Markings	2	153	26-Jan-23	27-Jan-23
	TX-3CD	Area 3C2 - NB EXR, Finish STA 1180 to 1220	0	140	16-Feb-23	16-Feb-23
Landscaping			10	144	27-Jan-23	09-Feb-23
Seeding & Sodding			10	144	27-Jan-23	09-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install Topsoil	10	144	27-Jan-23	09-Feb-23
	TX-3CD	Area 3C2 - NB EXR, Install Seeding/Sodding	10	144	27-Jan-23	09-Feb-23
ITS/TCS			20	312	02-May-22	27-May-22
Duct Bank System			20	312	02-May-22	27-May-22
	TX-3CD	Area 3C2 - NB EXR, ITS &TCS Civil Work Install Coduit	20	312	02-May-22	27-May-22
Northbound Exit Ramp NBML to SH 170 DC STA 1180 to 1220-1			290	300	27-May-21	07-Jul-22
C3(	TX-3CD	Area 3C2 - NB EXR, Start STA 1180 to 1220	0	300	27-May-21	27-May-21
Traffic Control and Temporary Work			6	462	27-May-21	03-Jun-21
Barricades, Signs & Traffic Handling			1	462	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Move Traffic	1	462	03-Jun-21	03-Jun-21
Portable Traffic Barrier			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Conc Barrier	5	462	27-May-21	02-Jun-21
Workzone Pavement Marking			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Marking & Signing	5	462	27-May-21	02-Jun-21
Erosion Control			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Erosion Control	5	462	27-May-21	02-Jun-21
Earthwork			40	462	04-Jun-21	29-Jul-21
Clear & Grub			5	462	04-Jun-21	10-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Clear and Grub	5	462	04-Jun-21	10-Jun-21
Excavation			15	462	11-Jun-21	01-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Excavate Cut Areas	15	462	11-Jun-21	01-Jul-21
Embankment			20	462	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Place Embankment	20	462	02-Jul-21	29-Jul-21
Subgrade Treatment and Base			35	462	30-Jul-21	16-Sep-21
Lime Treatment			20	462	30-Jul-21	26-Aug-21
	TX-3CD	Area 3C2 - NB EXR, Lime Treat Subgrade	20	462	30-Jul-21	26-Aug-21
Flexbase			15	462	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB EXR, Place Flexbase	15	462	27-Aug-21	16-Sep-21
Pavement			188	321	17-Sep-21	07-Jun-22
(	TX-3CD	Area 3C2 - NB EXR, FF Start STA 1180 to 1220	0	300	01-Jun-22	01-Jun-22
Asphalt Pavement			178	321	01-Oct-21	07-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Interim - Finish STA 1180 to 1220	0	300	31-May-22	31-May-22
HMA Paving			10	462	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - NB EXR, Place HMA	10	462	01-Oct-21	14-Oct-21
SMA Paving			5	321	01-Jun-22	07-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Place SMA	5	321	01-Jun-22	07-Jun-22
Curb & Gutter			10	462	17-Sep-21	30-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB EXR, Place Curb & Gutter	10	462	17-Sep-21	30-Sep-21
3C2 BR 122 Direct Connector Ramp NB EXR			263	300	27-May-21	31-May-22
(	TX-3CD	Area 3C2 - NB EXR, BR 122 Start	2	300	27-May-21	28-May-21
(	TX-3CD	Area 3C2 - NB EXR, BR 122 Finish	0	300	31-May-22	31-May-22
BR Excavation			5	300	01-Jun-21	07-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Bridge Excavation	5	300	01-Jun-21	07-Jun-21
Drill Shafts			30	350	08-Jun-21	19-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Abutment 1	5	300	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Bent 2-6	10	300	15-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Bent 7-11	10	300	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Abutment 12	5	350	13-Jul-21	19-Jul-21
Footings			20	305	29-Jun-21	26-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Footings Bent 2-6	10	315	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Footings Bent 7-11	10	300	13-Jul-21	26-Jul-21
Columns			55	330	15-Jun-21	30-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Abutment 1	10	375	15-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Bent 2-6	20	315	13-Jul-21	09-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Abutment 12	10	350	20-Jul-21	02-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Bent 7-11	25	300	27-Jul-21	30-Aug-21
Bent Caps			55	300	10-Aug-21	25-Oct-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Cap Bent 2-6	40	315	10-Aug-21	04-Oct-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Cap Bent 7-11	40	300	31-Aug-21	25-Oct-21
Beams			110	300	01-Jun-21	01-Nov-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Beam Procurement	20	344	01-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Forward Precast Beams Shopdrawings to TxDOT	1	344	29-Jun-21	29-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Precast Beam Fabrication & Delivery Leadtime	40	344	30-Jun-21	24-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Conc Beams	5	300	26-Oct-21	01-Nov-21
BR Place CTB Embankment			20	475	17-Aug-21	13-Sep-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Place Stabilized Backfill	20	475	17-Aug-21	13-Sep-21
Abutments			35	350	29-Jun-21	16-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Abutment 1	10	375	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Abutment 12	10	350	03-Aug-21	16-Aug-21
Approach Slab			10	300	17-May-22	30-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Apprch Slab Abutment 1	10	300	17-May-22	30-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Apprch Slab Abutment 12	10	300	17-May-22	30-May-22
Exspansion Joint			120	300	02-Nov-21	18-Apr-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Exp Joints	120	300	02-Nov-21	18-Apr-22
Deck			140	300	02-Nov-21	16-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Deck Slab	120	300	02-Nov-21	18-Apr-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Cure Deck Slab	20	300	19-Apr-22	16-May-22
Railings			10	300	17-May-22	30-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Conc Rail	10	300	17-May-22	30-May-22
Permanent Barriers			10	315	02-Jun-22	15-Jun-22
Concrete Barriers			10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Place Conc Rail	10	315	02-Jun-22	15-Jun-22
Metal Beam Guardrails			10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install MBGF	10	315	02-Jun-22	15-Jun-22
Signals and Illumination			25	300	02-Jun-22	06-Jul-22
Roadway Illumination			25	300	02-Jun-22	06-Jul-22
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Pole Bases	5	300	02-Jun-22	08-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Poles/Fixtures	10	300	09-Jun-22	22-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Energize Fixtures	10	300	23-Jun-22	06-Jul-22
Signing and Marking			26	300	01-Jun-22	07-Jul-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Overhead Sign Structures	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Overhead Signage	10	315	02-Jun-22	15-Jun-22
		Small Signage	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Small Signage	10	315	02-Jun-22	15-Jun-22
		Pavement Marking	26	300	01-Jun-22	07-Jul-22
	TX-3CD	Area 3C2 - NB EXR, Install Permt Markings	2	324	01-Jun-22	02-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Finish STA 1180 to 1220	0	300	07-Jul-22	07-Jul-22
		Landscaping	10	315	02-Jun-22	15-Jun-22
		Seeding & Sodding	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Topsoil	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Seeding/Sodding	10	315	02-Jun-22	15-Jun-22
		ITS/TCS	20	462	17-Sep-21	14-Oct-21
		Duct Bank System	20	462	17-Sep-21	14-Oct-21
	TX-3CD	Area 3C2 - NB EXR, ITS &TCS Civil Work Install Coduit	20	462	17-Sep-21	14-Oct-21
		Northbound Exit Ramp NBML to NBFR STA 1130 to 1180 PH 1	131	140	27-May-21	26-Nov-21
C3(	TX-3CD	Area 3C2 - NB EXR, Start STA 1180 to 1220	0	140	27-May-21	27-May-21
		Traffic Control and Temporary Work	6	140	27-May-21	03-Jun-21
		Barricades, Signs & Traffic Handling	1	140	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Move Traffic	1	140	03-Jun-21	03-Jun-21
		Portable Traffic Barrier	5	140	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Conc Barrier	5	140	27-May-21	02-Jun-21
		Workzone Pavement Marking	5	140	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Marking & Signing	5	140	27-May-21	02-Jun-21
		Erosion Control	5	140	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Erosion Control	5	140	27-May-21	02-Jun-21
		Earthwork	40	170	04-Jun-21	29-Jul-21
		Clear & Grub	5	140	04-Jun-21	10-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Clear and Grub	5	140	04-Jun-21	10-Jun-21
		Excavation	15	140	11-Jun-21	01-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Excavate Cut Areas	15	140	11-Jun-21	01-Jul-21
		Embankment	20	170	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Place Embankment	20	170	02-Jul-21	29-Jul-21
		Drainage	40	170	02-Jul-21	26-Aug-21
		Storm Sewer	20	170	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Install Small RCP	20	170	02-Jul-21	29-Jul-21
		Inlets	20	170	30-Jul-21	26-Aug-21
	TX-3CD	Area 3C2 - NB EXR, Install MHs and Inlets	20	170	30-Jul-21	26-Aug-21
		Subgrade Treatment and Base	65	140	30-Jul-21	28-Oct-21
		Lime Treatment	20	170	30-Jul-21	26-Aug-21
	TX-3CD	Area 3C2 - NB EXR, Lime Treat Subgrade	20	170	30-Jul-21	26-Aug-21
		Flexbase	15	140	08-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 - NB EXR, Place Flexbase	15	140	08-Oct-21	28-Oct-21
		Pavement	20	140	29-Oct-21	26-Nov-21
		Asphalt Pavement	10	140	12-Nov-21	26-Nov-21
	TX-3CD	Area 3C2 - NB EXR, Interim - Finish STA 1180 to 1220	0	140	26-Nov-21	26-Nov-21
		HMA Paving	10	140	12-Nov-21	25-Nov-21
	TX-3CD	Area 3C2 - NB EXR, Place HMA	10	140	12-Nov-21	25-Nov-21
		Curb & Gutter	10	140	29-Oct-21	11-Nov-21
	TX-3CD	Area 3C2 - NB EXR, Place Curb & Gutter	10	140	29-Oct-21	11-Nov-21
		Retaining Walls	70	140	02-Jul-21	07-Oct-21
		Wall RT-3C-VI-3B	50	160	02-Jul-21	09-Sep-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-VI-3B	40	160	02-Jul-21	26-Aug-21
		Wall Coping RT-3C-S8	10	160	27-Aug-21	09-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-3B	10	160	27-Aug-21	09-Sep-21
	Wall RT-3C-VI-1B		35	175	02-Jul-21	19-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Wall Wall RT-3C-VI-1B	25	175	02-Jul-21	05-Aug-21
	Wall Coping RT-3C-S6		10	175	06-Aug-21	19-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-1B	10	175	06-Aug-21	19-Aug-21
	Wall RT-3C-VI-2B		35	175	02-Jul-21	19-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-VI-2B	25	175	02-Jul-21	05-Aug-21
	Wall Coping RT-3C-S7		10	175	06-Aug-21	19-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-2B	10	175	06-Aug-21	19-Aug-21
	Wall RT-3C-VI-2AB		30	180	02-Jul-21	12-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-VI-2AB	20	180	02-Jul-21	29-Jul-21
	Wall Coping RT-3C-S10		10	180	30-Jul-21	12-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-VI-2AB	10	180	30-Jul-21	12-Aug-21
	Wall RT-3C-N7B		70	140	02-Jul-21	07-Oct-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-N7B	60	140	02-Jul-21	23-Sep-21
	Wall Coping RT-3C-S10		10	140	24-Sep-21	07-Oct-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-N7B	10	140	24-Sep-21	07-Oct-21
Northbound Exit Ramp NBGP to NBFR STA 1220 to 1240			128	668	12-Aug-20	08-Feb-21
C3(	TX-3CD	Area 3C2 - NB EXR, Start STA 1220 to 1240	0	668	12-Aug-20	12-Aug-20
Traffic Control and Temporary Work			6	668	12-Aug-20	19-Aug-20
	Barricades, Signs & Traffic Handling		1	668	19-Aug-20	19-Aug-20
	TX-3CD	Area 3C2 - NB EXR, Move Traffic	1	668	19-Aug-20	19-Aug-20
	Portable Traffic Barrier		5	668	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - NB EXR, Place Temp Conc Barrier	5	668	12-Aug-20	18-Aug-20
	Workzone Pavement Marking		5	668	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - NB EXR, Place Temp Marking & Signing	5	668	12-Aug-20	18-Aug-20
	Erosion Control		5	668	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - NB EXR, Place Temp Erosion Control	5	668	12-Aug-20	18-Aug-20
Earthwork			40	668	20-Aug-20	14-Oct-20
	Clear & Grub		5	668	20-Aug-20	26-Aug-20
	TX-3CD	Area 3C2 - NB EXR, Clear and Grub	5	668	20-Aug-20	26-Aug-20
	Excavation		15	668	27-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 - NB EXR, Excavate Cut Areas	15	668	27-Aug-20	16-Sep-20
	Embankment		20	668	17-Sep-20	14-Oct-20
	TX-3CD	Area 3C2 - NB EXR, Place Embankment	20	668	17-Sep-20	14-Oct-20
Subgrade Treatment and Base			35	668	15-Oct-20	02-Dec-20
	Lime Treatment		20	668	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C2 - NB EXR, Lime Treat Subgrade	20	668	15-Oct-20	11-Nov-20
	Flexbase		15	668	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - NB EXR, Place Flexbase	15	668	12-Nov-20	02-Dec-20
Pavement			26	689	03-Dec-20	07-Jan-21
(	TX-3CD	Area 3C2 - NB EXR, FF Start STA 1220 to 1240	0	668	01-Jan-21	01-Jan-21
TP\	**Asphalt Pavement**		16	689	17-Dec-20	07-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Interim - Finish STA 1220 to 1240	0	668	31-Dec-20	31-Dec-20
	HMA Paving		10	668	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C2 - NB EXR, Place HMA	10	668	17-Dec-20	30-Dec-20
	SMA Paving		5	689	01-Jan-21	07-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Place SMA	5	689	01-Jan-21	07-Jan-21
	Curb & Gutter		10	668	03-Dec-20	16-Dec-20
	TX-3CD	Area 3C2 - NB EXR, Place Curb & Gutter	10	668	03-Dec-20	16-Dec-20
Permanent Barriers			10	683	04-Jan-21	15-Jan-21
	Concrete Barriers		10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Place Conc Rail	10	683	04-Jan-21	15-Jan-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Metal Beam Guardrails	10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install MBGF	10	683	04-Jan-21	15-Jan-21
		Signals and Illumination	25	668	04-Jan-21	05-Feb-21
		Roadway Illumination	25	668	04-Jan-21	05-Feb-21
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Pole Bases	5	668	04-Jan-21	08-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Poles/Fixtures	10	668	11-Jan-21	22-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Energize Fixtures	10	668	25-Jan-21	05-Feb-21
		Signing and Marking	26	668	01-Jan-21	08-Feb-21
		Overhead Sign Structures	10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install Overhead Signage	10	683	04-Jan-21	15-Jan-21
		Small Signage	10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install Small Signage	10	683	04-Jan-21	15-Jan-21
		Pavement Marking	26	668	01-Jan-21	08-Feb-21
	TX-3CD	Area 3C2 - NB EXR, Install Permt Markings	2	692	01-Jan-21	04-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Finish STA 1220 to 1240	0	668	08-Feb-21	08-Feb-21
		Landscaping	10	683	04-Jan-21	15-Jan-21
		Seeding & Sodding	10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install Topsoil	10	683	04-Jan-21	15-Jan-21
	TX-3CD	Area 3C2 - NB EXR, Install Seeding/Sodding	10	683	04-Jan-21	15-Jan-21
		ITS/TCS	20	668	03-Dec-20	30-Dec-20
		Duct Bank System	20	668	03-Dec-20	30-Dec-20
	TX-3CD	Area 3C2 - NB EXR, ITS &TCS Civil Work Install Coduit	20	668	03-Dec-20	30-Dec-20
		Northbound GP Lane STA 1176 to 1280	233	563	12-Aug-20	05-Jul-21
C3(	TX-3CD	Area 3C2 NB GP, Start STA 1176 to 1280	0	140	12-Aug-20	12-Aug-20
C3(	TX-3CD	Area 3C2 -NB GP BR 111.1 ACM (Asbestos) and LCP (Lead) Testing	1	143	12-Aug-20	12-Aug-20
C3(	TX-3CD	Area 3C2 -NB GP BR 108.1 ACM (Asbestos) and LCP (Lead) Testing	1	143	12-Aug-20	12-Aug-20
		Traffic Control and Temporary Work	6	225	12-Aug-20	19-Aug-20
		Barricades, Signs & Traffic Handling	1	225	19-Aug-20	19-Aug-20
	TX-3CD	Area 3C2 NB GP, Move Traffic	1	225	19-Aug-20	19-Aug-20
		Erosion Control	5	225	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 NB GP, Place Temp Erosion Control	5	225	12-Aug-20	18-Aug-20
		Removals & Demo	5	225	12-Aug-20	18-Aug-20
		Pavement Removal	5	225	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 NB GP, Remove Pavement	5	225	12-Aug-20	18-Aug-20
		Earthwork	66	225	12-Aug-20	11-Nov-20
		Clear & Grub	5	225	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 NB GP, Clear and Grub	5	225	12-Aug-20	18-Aug-20
		Excavation	15	225	20-Aug-20	09-Sep-20
	TX-3CD	Area 3C2 NB GP, Excavate Cut Areas	15	225	20-Aug-20	09-Sep-20
		Embankment	20	225	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C2 NB GP, Place Embankment	20	225	15-Oct-20	11-Nov-20
		Drainage	40	225	20-Aug-20	14-Oct-20
		Culverts	20	245	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 - NB GP, CLV08 Install Culvert	20	245	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 - NB GP, CLV06 Install Culvert	20	245	20-Aug-20	16-Sep-20
		Storm Sewer	20	225	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 NB GP, CLV07 Install Medium RCP	20	225	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 NB GP, Install Small RCP	20	225	20-Aug-20	16-Sep-20
		Inlets	20	225	17-Sep-20	14-Oct-20
	TX-3CD	Area 3C2 NB GP, Install MHs and Inlets	20	225	17-Sep-20	14-Oct-20
		Subgrade Treatment and Base	35	225	12-Nov-20	30-Dec-20
		Lime Treatment	20	225	12-Nov-20	09-Dec-20
	TX-3CD	Area 3C2 NB GP, Lime Treat Subgrade	20	225	12-Nov-20	09-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Flexbase	15	225	10-Dec-20	30-Dec-20
	TX-3CD	Area 3C2 NB GP, Place Flexbase	15	225	10-Dec-20	30-Dec-20
		Pavement	111	584	31-Dec-20	03-Jun-21
(	TX-3CD	Area 3C2 NB GP, FF Start STA 1176 to 1280	0	563	28-May-21	28-May-21
		Asphalt Pavement	111	584	31-Dec-20	03-Jun-21
	TX-3CD	Area 3C2 - NB GP, Interim - Finish STA 1176 to 1280	0	140	27-May-21	27-May-21
		HMA Paving	10	235	31-Dec-20	13-Jan-21
	TX-3CD	Area 3C2 NB GP, Place HMA	10	235	31-Dec-20	13-Jan-21
		SMA Paving	5	584	28-May-21	03-Jun-21
	TX-3CD	Area 3C2 NB GP, Place SMA	5	584	28-May-21	03-Jun-21
		Retaining Walls	75	230	20-Aug-20	02-Dec-20
		Wall RT-3C-8A	75	230	20-Aug-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-8A	60	230	20-Aug-20	11-Nov-20
		Wall Coping RT-3C-8A	15	230	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Coping Cap RT-3C-8A	15	230	12-Nov-20	02-Dec-20
		Wall RT-3C-N4	75	230	20-Aug-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N4	60	230	20-Aug-20	11-Nov-20
		Wall Coping RT-3C-N4	15	230	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Coping Cap RT-3C-N4	15	230	12-Nov-20	02-Dec-20
		Wall RT-3C-N7	75	230	20-Aug-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-N7	60	230	20-Aug-20	11-Nov-20
		Wall Coping RT-3C-N7	15	230	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Coping Cap RT-3C-N7	15	230	12-Nov-20	02-Dec-20
		Wall RT-3C-6A	75	230	20-Aug-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-6A	60	230	20-Aug-20	11-Nov-20
		Wall Coping RT-3C-6A	15	230	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Coping Cap RT-3C-6A	15	230	12-Nov-20	02-Dec-20
		Wall RT-3C-W1	75	230	20-Aug-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Wall RT-3C-W1	60	230	20-Aug-20	11-Nov-20
		Wall Coping RT-3C-W1	15	230	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - NB GP, Install Coping Cap RT-3C-W1	15	230	12-Nov-20	02-Dec-20
		3C2 BR 108.1 NB GP Keller-Hicks Rd	206	140	12-Aug-20	27-May-21
(	TX-3CD	Area 3C2 -NB GP BR 108.1 Start	3	140	12-Aug-20	14-Aug-20
(	TX-3CD	Area 3C2 - NB GP BR 108.1 Finish	0	140	27-May-21	27-May-21
		BR Demolition	7	140	18-Aug-20	26-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	140	18-Aug-20	24-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Bridge Demolition	2	140	25-Aug-20	26-Aug-20
		BR Excavation	4	143	18-Aug-20	21-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Bridge Excavation	4	143	18-Aug-20	21-Aug-20
		Drill Shafts	20	160	27-Aug-20	23-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Drill Shafts Abutment 1	5	140	27-Aug-20	02-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Drill Shafts Bent 2	5	140	03-Sep-20	09-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Drill Shafts Bent 3	5	140	10-Sep-20	16-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Drill Shafts Abutment 4	5	160	17-Sep-20	23-Sep-20
		Columns	35	150	03-Sep-20	21-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Columns Abutment 1	10	175	03-Sep-20	16-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Columns Bent 2	20	150	10-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Columns Bent 3	25	140	17-Sep-20	21-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Columns Abutment 4	10	160	24-Sep-20	07-Oct-20
		Bent Caps	30	140	08-Oct-20	18-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Cap Bent 2	20	150	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Cap Bent 3	20	140	22-Oct-20	18-Nov-20
		Beams	72	140	18-Aug-20	25-Nov-20

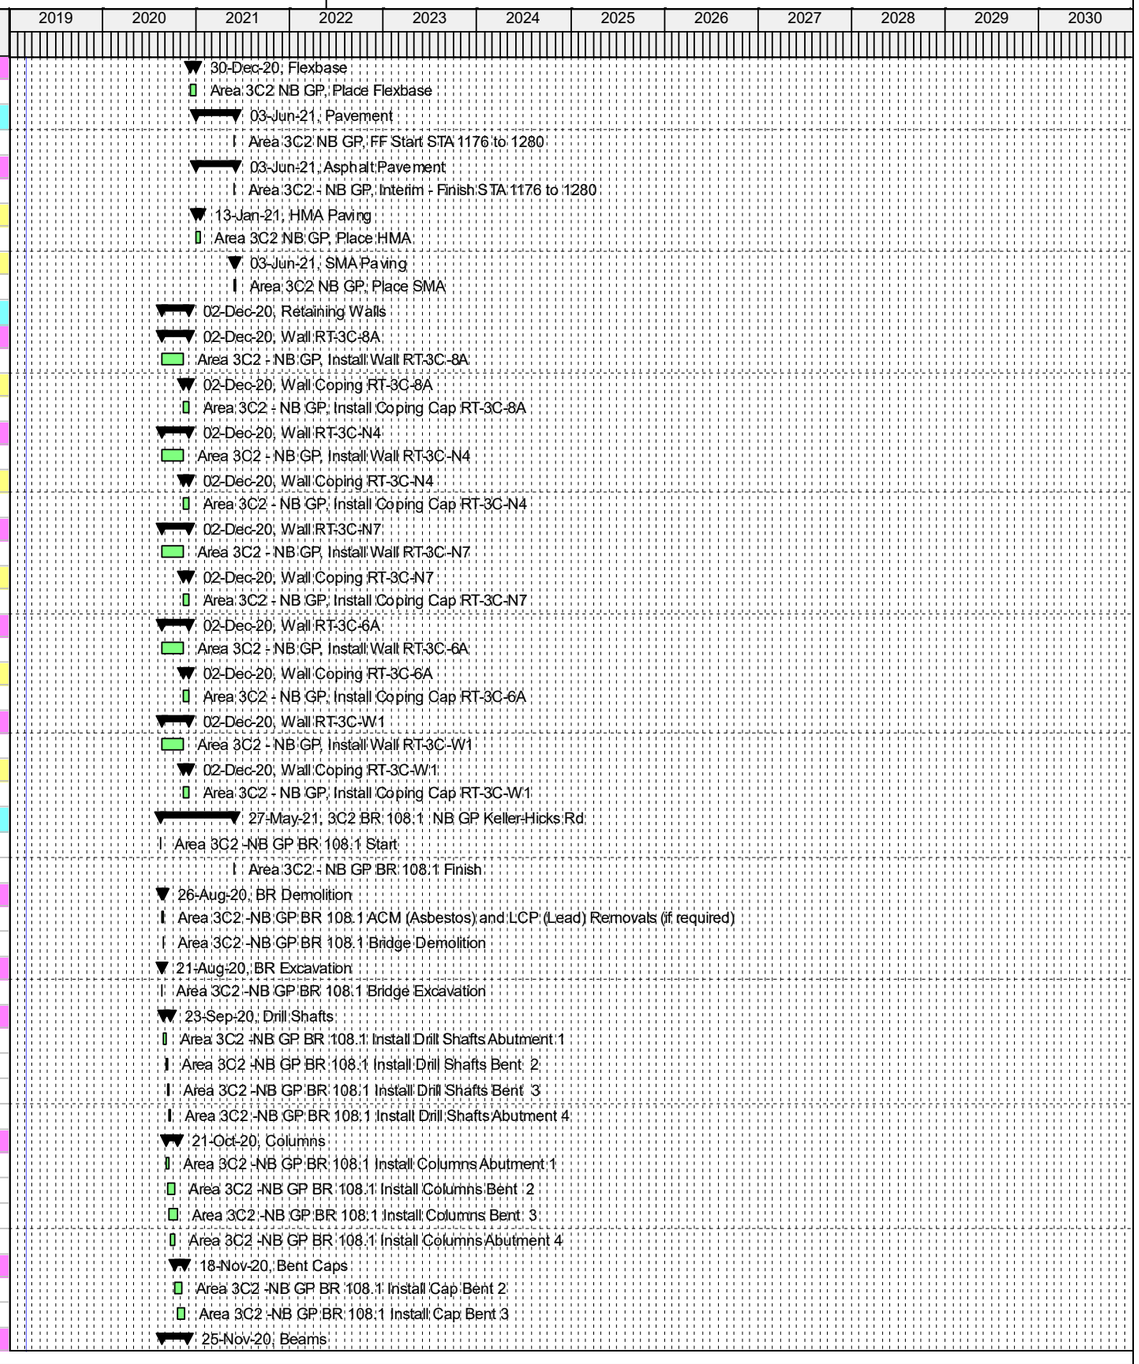

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 -NB GP BR 108.1 Beam Procurement	20	146	18-Aug-20	14-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Forward Precast Beams Shopdrawings to TxDOT	1	146	15-Sep-20	15-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Precast Beam Fabrication & Delivery Leadtime	40	146	16-Sep-20	10-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Conc Beams	5	140	19-Nov-20	25-Nov-20
BR Place CTB Embankment			20	265	22-Oct-20	18-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Place Stabilized Backfill	20	265	22-Oct-20	18-Nov-20
Abutments			25	160	17-Sep-20	21-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Abutment 1	10	175	17-Sep-20	30-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Abutment 4	10	160	08-Oct-20	21-Oct-20
Approach Slab			10	140	13-May-21	26-May-21
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Apprch Slab Abutment 1	10	140	13-May-21	26-May-21
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Apprch Slab Abutment 4	10	140	13-May-21	26-May-21
Deck			120	140	26-Nov-20	12-May-21
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Deck Slab	100	140	26-Nov-20	14-Apr-21
	TX-3CD	Area 3C2 -NB GP BR 108.1 Cure Deck Slab	20	140	15-Apr-21	12-May-21
Exspansion Joint			100	140	26-Nov-20	14-Apr-21
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Exp Joints	100	140	26-Nov-20	14-Apr-21
Railings			10	140	13-May-21	26-May-21
	TX-3CD	Area 3C2 -NB GP BR 108.1 Install Conc Rail	10	140	13-May-21	26-May-21
3C2 BR 111.1 NB GP Golden Triangle Blvd			203	143	12-Aug-20	24-May-21
(	TX-3CD	Area 3C2 -NB GP BR 111.1 Start	3	143	12-Aug-20	14-Aug-20
(	TX-3CD	Area 3C2 - NB GP BR 111.1 Finish	0	143	24-May-21	24-May-21
BR Demolition			7	143	13-Aug-20	21-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	143	13-Aug-20	19-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Bridge Demolition	2	143	20-Aug-20	21-Aug-20
BR Excavation			4	143	18-Aug-20	21-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Bridge Excavation	4	143	18-Aug-20	21-Aug-20
Drill Shafts			20	163	24-Aug-20	18-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Drill Shafts Abutment 1	5	143	24-Aug-20	28-Aug-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Drill Shafts Bent 2	5	143	31-Aug-20	04-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Drill Shafts Bent 3	5	143	07-Sep-20	11-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Drill Shafts Abutment 4	5	163	14-Sep-20	18-Sep-20
Columns			35	153	31-Aug-20	16-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Columns Abutment 1	10	178	31-Aug-20	11-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Columns Bent 2	20	153	07-Sep-20	02-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Columns Bent 3	25	143	14-Sep-20	16-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Columns Abutment 4	10	163	21-Sep-20	02-Oct-20
Bent Caps			30	143	05-Oct-20	13-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Cap Bent 2	20	153	05-Oct-20	30-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Cap Bent 3	20	143	19-Oct-20	13-Nov-20
Beams			69	143	18-Aug-20	20-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Beam Procurement	20	146	18-Aug-20	14-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Forward Precast Beams Shopdrawings to TxDOT	1	146	15-Sep-20	15-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Precast Beam Fabrication & Delivery Leadtime	40	146	16-Sep-20	10-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Conc Beams	5	143	16-Nov-20	20-Nov-20
BR Place CTB Embankment			20	268	19-Oct-20	13-Nov-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Place Embankment	20	268	19-Oct-20	13-Nov-20
Abutments			25	163	14-Sep-20	16-Oct-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Abutment 1	10	178	14-Sep-20	25-Sep-20
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Abutment 4	10	163	05-Oct-20	16-Oct-20
Approach Slab			10	143	10-May-21	21-May-21
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Apprch Slab Abutment 1	10	143	10-May-21	21-May-21
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Apprch Slab Abutment 4	10	143	10-May-21	21-May-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Exspansion Joint	100	143	23-Nov-20	09-Apr-21
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Exp Joints	100	143	23-Nov-20	09-Apr-21
		Deck	120	143	23-Nov-20	07-May-21
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Deck Slab	100	143	23-Nov-20	09-Apr-21
	TX-3CD	Area 3C2 -NB GP BR 111.1 Cure Deck Slab	20	143	12-Apr-21	07-May-21
		Railings	10	143	10-May-21	21-May-21
	TX-3CD	Area 3C2 -NB GP BR 111.1 Install Conc Rail	10	143	10-May-21	21-May-21
		Permanent Barriers	10	578	31-May-21	11-Jun-21
		Concrete Barriers	10	578	31-May-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Place Conc Rail	10	578	31-May-21	11-Jun-21
		Metal Beam Guardrails	10	578	31-May-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Install MBGF	10	578	31-May-21	11-Jun-21
		Signals and Illumination	25	563	31-May-21	02-Jul-21
		Roadway Illumination	25	563	31-May-21	02-Jul-21
	TX-3CD	Area 3C2 NB GP, Install Illumination Pole Bases	5	563	31-May-21	04-Jun-21
	TX-3CD	Area 3C2 NB GP, Install Illumination Poles/Fixtures	10	563	07-Jun-21	18-Jun-21
	TX-3CD	Area 3C2 NB GP, Install Illumination Energize Fixtures	10	563	21-Jun-21	02-Jul-21
		High Mast Illumination	15	573	31-May-21	18-Jun-21
	TX-3CD	Area 3C2 NB GP, Install High Mast Illumination Pole Bases	5	573	31-May-21	04-Jun-21
	TX-3CD	Area 3C2 NB GP, Install High Mast Illumination Poles/Fixtures	5	573	07-Jun-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Install High Mast Illumination Energize Fixtures	5	573	14-Jun-21	18-Jun-21
		Signing and Marking	26	563	28-May-21	05-Jul-21
		Overhead Sign Structures	10	578	31-May-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Install Overhead Signage	10	578	31-May-21	11-Jun-21
		Small Signage	10	578	31-May-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Install Small Signage	10	578	31-May-21	11-Jun-21
		Pavement Marking	26	563	28-May-21	05-Jul-21
	TX-3CD	Area 3C2 NB GP, Install Permt Markings	2	587	28-May-21	31-May-21
	TX-3CD	Area 3C2 - NB GP, Finish STA 1176 to 1280	0	563	05-Jul-21	05-Jul-21
		Landscaping	10	578	31-May-21	11-Jun-21
		Seeding & Sodding	10	578	31-May-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Install Seeding/Sodding	10	578	31-May-21	11-Jun-21
	TX-3CD	Area 3C2 NB GP, Install Topsoil	10	578	31-May-21	11-Jun-21
		ITS/TCS	20	225	31-Dec-20	27-Jan-21
		Duct Bank System	20	225	31-Dec-20	27-Jan-21
	TX-3CD	Area 3C2 NB GP, ITS &TCS Civil Work Install Coduit	20	225	31-Dec-20	27-Jan-21
		Northbound U-Turn SH 170 STA 1183	241	349	27-May-21	29-Apr-22
C3(	TX-3CD	Area 3C2 - NB FR U-Turn, Start STA 1183	0	349	27-May-21	27-May-21
C3(	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 ACM (Asbestos) and LCP (Lead) Testing	1	366	27-May-21	27-May-21
		Traffic Control and Temporary Work	6	473	27-May-21	03-Jun-21
		Barricades, Signs & Traffic Handling	1	473	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Move Traffic	1	473	03-Jun-21	03-Jun-21
		Portable Traffic Barrier	5	473	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Temp Conc Barrier	5	473	27-May-21	02-Jun-21
		Workzone Pavement Marking	5	473	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Temp Marking & Signing	5	473	27-May-21	02-Jun-21
		Erosion Control	5	473	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Temp Erosion Control	5	473	27-May-21	02-Jun-21
		Earthwork	35	473	04-Jun-21	22-Jul-21
		Excavation	15	473	04-Jun-21	24-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Excavate Cut Areas	15	473	04-Jun-21	24-Jun-21
		Embankment	20	473	25-Jun-21	22-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Embankment	20	473	25-Jun-21	22-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Subgrade Treatment and Base			35	473	23-Jul-21	09-Sep-21
Lime Treatment			20	473	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Lime Treat Subgrade	20	473	23-Jul-21	19-Aug-21
Flexbase			15	473	20-Aug-21	09-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Flexbase	15	473	20-Aug-21	09-Sep-21
Pavement			165	349	10-Sep-21	28-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, FF Start STA 1183	0	349	01-Apr-22	01-Apr-22
Asphalt Pavement			155	349	24-Sep-21	28-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Interim - Finish STA 1183	0	349	31-Mar-22	31-Mar-22
HMA Paving			10	473	24-Sep-21	07-Oct-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place HMA	10	473	24-Sep-21	07-Oct-21
SMA Paving			20	349	01-Apr-22	28-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place SMA	20	349	01-Apr-22	28-Apr-22
Curb & Gutter			10	473	10-Sep-21	23-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Curb & Gutter	10	473	10-Sep-21	23-Sep-21
3C2 BR 120 NB FR U-Turn			220	349	27-May-21	31-Mar-22
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Start	20	349	27-May-21	23-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Finish	0	349	31-Mar-22	31-Mar-22
BR Demolition			22	351	28-May-21	28-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 ACM (Asbestos) and LCP (Lead) Removals (if required)	5	366	28-May-21	03-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Bridge Demolition	2	351	25-Jun-21	28-Jun-21
BR Excavation			4	349	25-Jun-21	30-Jun-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Bridge Excavation	4	349	25-Jun-21	30-Jun-21
Drill Shafts			20	369	01-Jul-21	28-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Drill Shafts Abutment 1	5	349	01-Jul-21	07-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Drill Shafts Bent 2	5	349	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Drill Shafts Bent 3	5	349	15-Jul-21	21-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Drill Shafts Abutment 4	5	369	22-Jul-21	28-Jul-21
Columns			35	359	08-Jul-21	25-Aug-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Columns Abutment 1	10	384	08-Jul-21	21-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Columns Bent 2	20	359	15-Jul-21	11-Aug-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Columns Bent 3	25	349	22-Jul-21	25-Aug-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Columns Abutment 4	10	369	29-Jul-21	11-Aug-21
Bent Caps			30	349	12-Aug-21	22-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Cap Bent 2	20	359	12-Aug-21	08-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Cap Bent 3	20	349	26-Aug-21	22-Sep-21
Beams			69	349	25-Jun-21	29-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Beam Procurement	20	352	25-Jun-21	22-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Forward Precast Beams Shopdrawings to TxDOT	1	352	23-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Precast Beam Fabrication & Delivery Leadtime	40	352	26-Jul-21	17-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Conc Beams	5	349	23-Sep-21	29-Sep-21
BR Place CTB Embankment			20	474	26-Aug-21	22-Sep-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Place Stabilized Backfill	20	474	26-Aug-21	22-Sep-21
Abutments			25	369	22-Jul-21	25-Aug-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Abutment 1	10	384	22-Jul-21	04-Aug-21
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Abutment 4	10	369	12-Aug-21	25-Aug-21
Approach Slab			10	349	17-Mar-22	30-Mar-22
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Apprch Slab Abutment 1	10	349	17-Mar-22	30-Mar-22
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Apprch Slab Abutment 4	10	349	17-Mar-22	30-Mar-22
Deck			120	349	30-Sep-21	16-Mar-22
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Deck Slab	100	349	30-Sep-21	16-Feb-22
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Cure Deck Slab	20	349	17-Feb-22	16-Mar-22
Exspansion Joint			100	349	30-Sep-21	16-Feb-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Exp Joints	100	349	30-Sep-21	16-Feb-22
Railings			10	349	17-Mar-22	30-Mar-22
	TX-3CD	Area 3C2 - NB FR U-Turn, BR 120 Install Conc Rail	10	349	17-Mar-22	30-Mar-22
Permanent Barriers			10	358	04-Apr-22	15-Apr-22
Concrete Barriers			10	358	04-Apr-22	15-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Place Conc Rail	10	358	04-Apr-22	15-Apr-22
Metal Beam Guardrails			10	358	04-Apr-22	15-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Install MBGF	10	358	04-Apr-22	15-Apr-22
Signing and Marking			20	349	01-Apr-22	29-Apr-22
Small Signage			10	358	04-Apr-22	15-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Install Small Signage	10	358	04-Apr-22	15-Apr-22
Pavement Marking			20	349	01-Apr-22	29-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Install Permt Markings	2	367	01-Apr-22	04-Apr-22
	TX-3CD	Area 3C2 - NB FR U-Turn,, Finish STA 1183	0	349	29-Apr-22	29-Apr-22
Northbound Exit Ramp NBML to NBGP STA 1257 to 1270			128	462	27-May-21	23-Nov-21
C3(	TX-3CD	Area 3C2 - NB ML EXR, Start STA 1257 to 1270	0	462	27-May-21	27-May-21
Traffic Control and Temporary Work			6	462	27-May-21	03-Jun-21
Barricades, Signs & Traffic Handling			1	462	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB ML EXR, Move Traffic	1	462	03-Jun-21	03-Jun-21
Portable Traffic Barrier			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Temp Conc Barrier	5	462	27-May-21	02-Jun-21
Workzone Pavement Marking			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Temp Marking & Signing	5	462	27-May-21	02-Jun-21
Erosion Control			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Temp Erosion Control	5	462	27-May-21	02-Jun-21
Earthwork			40	462	04-Jun-21	29-Jul-21
Clear & Grub			5	462	04-Jun-21	10-Jun-21
	TX-3CD	Area 3C2 - NB ML EXR, Clear and Grub	5	462	04-Jun-21	10-Jun-21
Excavation			15	462	11-Jun-21	01-Jul-21
	TX-3CD	Area 3C2 - NB ML EXR, Excavate Cut Areas	15	462	11-Jun-21	01-Jul-21
Embankment			20	462	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Embankment	20	462	02-Jul-21	29-Jul-21
Subgrade Treatment and Base			35	462	30-Jul-21	16-Sep-21
Lime Treatment			20	462	30-Jul-21	26-Aug-21
	TX-3CD	Area 3C2 - NB ML EXR, Lime Treat Subgrade	20	462	30-Jul-21	26-Aug-21
Flexbase			15	462	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Flexbase	15	462	27-Aug-21	16-Sep-21
Pavement			41	468	17-Sep-21	12-Nov-21
(	TX-3CD	Area 3C2 - NB ML EXR, FF Start STA 1257 to 1270	0	462	18-Oct-21	18-Oct-21
Asphalt Pavement			31	468	01-Oct-21	12-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Interim - Finish STA 1257 to 1270	0	462	15-Oct-21	15-Oct-21
HMA Paving			10	462	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - NB ML EXR, Place HMA	10	462	01-Oct-21	14-Oct-21
SMA Paving			20	468	18-Oct-21	12-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Place SMA	20	468	18-Oct-21	12-Nov-21
Curb & Gutter			10	462	17-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Curb & Gutter	10	462	17-Sep-21	30-Sep-21
Permanent Barriers			10	477	19-Oct-21	01-Nov-21
Concrete Barriers			10	477	19-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Place Conc Rail	10	477	19-Oct-21	01-Nov-21
Metal Beam Guardrails			10	477	19-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install MBGF	10	477	19-Oct-21	01-Nov-21
Crash Attenuators			5	482	19-Oct-21	25-Oct-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB ML EXR, Install Attenuator	5	482	19-Oct-21	25-Oct-21
Signals and Illumination			25	462	19-Oct-21	22-Nov-21
Roadway Illumination			25	462	19-Oct-21	22-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Illumination Pole Bases	5	462	19-Oct-21	25-Oct-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Illumination Poles/Fixtures	10	462	26-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Illumination Energize Fixtures	10	462	09-Nov-21	22-Nov-21
Signing and Marking			26	462	18-Oct-21	23-Nov-21
Overhead Sign Structures			10	477	19-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Overhead Signage	10	477	19-Oct-21	01-Nov-21
Small Signage			10	477	19-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Small Signage	10	477	19-Oct-21	01-Nov-21
Pavement Marking			26	462	18-Oct-21	23-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Permt Markings	2	486	18-Oct-21	19-Oct-21
	TX-3CD	Area 3C2 - NB ML EXR, Finish STA 1257 to 1270	0	462	23-Nov-21	23-Nov-21
Landscaping			10	477	19-Oct-21	01-Nov-21
Seeding & Sodding			10	477	19-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Topsoil	10	477	19-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB ML EXR, Install Seeding/Sodding	10	477	19-Oct-21	01-Nov-21
ITS/TCS			20	462	17-Sep-21	14-Oct-21
Duct Bank System			20	462	17-Sep-21	14-Oct-21
	TX-3CD	Area 3C2 - NB ML EXR, ITS &TCS Civil Work Install Coduit	20	462	17-Sep-21	14-Oct-21
Northbound Exit Ramp NBGP to SH 170 DC STA 1180 to 1220			290	300	27-May-21	07-Jul-22
C3(	TX-3CD	Area 3C2 - NB EXR, Start STA 1180 to 1220	0	300	27-May-21	27-May-21
Traffic Control and Temporary Work			6	462	27-May-21	03-Jun-21
Barricades, Signs & Traffic Handling			1	462	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Move Traffic	1	462	03-Jun-21	03-Jun-21
Portable Traffic Barrier			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Conc Barrier	5	462	27-May-21	02-Jun-21
Workzone Pavement Marking			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Marking & Signing	5	462	27-May-21	02-Jun-21
Erosion Control			5	462	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Place Temp Erosion Control	5	462	27-May-21	02-Jun-21
Earthwork			40	462	04-Jun-21	29-Jul-21
Clear & Grub			5	462	04-Jun-21	10-Jun-21
	TX-3CD	Area 3C2 - NB EXR, Clear and Grub	5	462	04-Jun-21	10-Jun-21
Excavation			15	462	11-Jun-21	01-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Excavate Cut Areas	15	462	11-Jun-21	01-Jul-21
Embankment			20	462	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB EXR, Place Embankment	20	462	02-Jul-21	29-Jul-21
Subgrade Treatment and Base			35	462	30-Jul-21	16-Sep-21
Lime Treatment			20	462	30-Jul-21	26-Aug-21
	TX-3CD	Area 3C2 - NB EXR, Lime Treat Subgrade	20	462	30-Jul-21	26-Aug-21
Flexbase			15	462	27-Aug-21	16-Sep-21
	TX-3CD	Area 3C2 - NB EXR, Place Flexbase	15	462	27-Aug-21	16-Sep-21
Pavement			188	321	17-Sep-21	07-Jun-22
(	TX-3CD	Area 3C2 - NB EXR, FF Start STA 1180 to 1220	0	300	01-Jun-22	01-Jun-22
Asphalt Pavement			178	321	01-Oct-21	07-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Interim - Finish STA 1180 to 1220	0	300	31-May-22	31-May-22
HMA Paving			10	462	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - NB EXR, Place HMA	10	462	01-Oct-21	14-Oct-21
SMA Paving			5	321	01-Jun-22	07-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Place SMA	5	321	01-Jun-22	07-Jun-22
Curb & Gutter			10	462	17-Sep-21	30-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - NB EXR, Place Curb & Gutter	10	462	17-Sep-21	30-Sep-21
3C2 BR 122 Direct Connector Ramp NB EXR			263	300	27-May-21	31-May-22
(	TX-3CD	Area 3C2 - NB EXR, BR 122 Start	2	300	27-May-21	28-May-21
(	TX-3CD	Area 3C2 - NB EXR, BR 122 Finish	0	300	31-May-22	31-May-22
BR Excavation			5	300	01-Jun-21	07-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Bridge Excavation	5	300	01-Jun-21	07-Jun-21
Drill Shafts			30	350	08-Jun-21	19-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Abutment 1	5	300	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Bent 2-6	10	300	15-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Bent 7-11	10	300	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Drill Shafts Abutment 12	5	350	13-Jul-21	19-Jul-21
Footings			20	305	29-Jun-21	26-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Footings Bent 2-6	10	315	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Footings Bent 7-11	10	300	13-Jul-21	26-Jul-21
Columns			55	330	15-Jun-21	30-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Abutment 1	10	375	15-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Bent 2-6	20	315	13-Jul-21	09-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Abutment 12	10	350	20-Jul-21	02-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Columns Bent 7-11	25	300	27-Jul-21	30-Aug-21
Bent Caps			55	300	10-Aug-21	25-Oct-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Cap Bent 2-6	40	315	10-Aug-21	04-Oct-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Cap Bent 7-11	40	300	31-Aug-21	25-Oct-21
Beams			110	300	01-Jun-21	01-Nov-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Beam Procurement	20	344	01-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Forward Precast Beams Shopdrawings to TxDOT	1	344	29-Jun-21	29-Jun-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Precast Beam Fabrication & Delivery Leadtime	40	344	30-Jun-21	24-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Conc Beams	5	300	26-Oct-21	01-Nov-21
BR Place CTB Embankment			20	475	17-Aug-21	13-Sep-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Place Stabilized Backfill	20	475	17-Aug-21	13-Sep-21
Abutments			35	350	29-Jun-21	16-Aug-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Abutment 1	10	375	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Abutment 12	10	350	03-Aug-21	16-Aug-21
Approach Slab			10	300	17-May-22	30-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Apprch Slab Abutment 1	10	300	17-May-22	30-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Apprch Slab Abutment 12	10	300	17-May-22	30-May-22
Exspansion Joint			120	300	02-Nov-21	18-Apr-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Exp Joints	120	300	02-Nov-21	18-Apr-22
Deck			140	300	02-Nov-21	16-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Deck Slab	120	300	02-Nov-21	18-Apr-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Cure Deck Slab	20	300	19-Apr-22	16-May-22
Railings			10	300	17-May-22	30-May-22
	TX-3CD	Area 3C2 - NB EXR, BR 122 Install Conc Rail	10	300	17-May-22	30-May-22
Permanent Barriers			10	315	02-Jun-22	15-Jun-22
Concrete Barriers			10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Place Conc Rail	10	315	02-Jun-22	15-Jun-22
Metal Beam Guardrails			10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install MBGF	10	315	02-Jun-22	15-Jun-22
Signals and Illumination			25	300	02-Jun-22	06-Jul-22
Roadway Illumination			25	300	02-Jun-22	06-Jul-22
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Pole Bases	5	300	02-Jun-22	08-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Poles/Fixtures	10	300	09-Jun-22	22-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Illumination Energize Fixtures	10	300	23-Jun-22	06-Jul-22
Signing and Marking			26	300	01-Jun-22	07-Jul-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Overhead Sign Structures	10	315	02-Jun-22	15-Jun-22
TPW	TX-3CD	Area 3C2 - NB EXR, Install Overhead Signage	10	315	02-Jun-22	15-Jun-22
		Small Signage	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Small Signage	10	315	02-Jun-22	15-Jun-22
		Pavement Marking	26	300	01-Jun-22	07-Jul-22
	TX-3CD	Area 3C2 - NB EXR, Install Permt Markings	2	324	01-Jun-22	02-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Finish STA 1180 to 1220	0	300	07-Jul-22	07-Jul-22
		Landscaping	10	315	02-Jun-22	15-Jun-22
		Seeding & Sodding	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Topsoi	10	315	02-Jun-22	15-Jun-22
	TX-3CD	Area 3C2 - NB EXR, Install Seeding/Sodding	10	315	02-Jun-22	15-Jun-22
		ITS/TCS	20	462	17-Sep-21	14-Oct-21
		Duct Bank System	20	462	17-Sep-21	14-Oct-21
	TX-3CD	Area 3C2 - NB EXR, ITS &TCS Civil Work Install Coduit	20	462	17-Sep-21	14-Oct-21
		Northbound ML Lane STA 1176 to 1280	275	379	27-May-21	16-Jun-22
C3(	TX-3CD	Area 3C2 - NB ML, Start STA 1176 to 1280	0	140	27-May-21	27-May-21
		Traffic Control and Temporary Work	6	377	27-May-21	03-Jun-21
		Barricades, Signs & Traffic Handling	1	377	03-Jun-21	03-Jun-21
	TX-3CD	Area 3C2 - NB ML, Move Traffic	1	377	03-Jun-21	03-Jun-21
		Erosion Control	5	377	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ML, Place Temp Erosion Control	5	377	27-May-21	02-Jun-21
		Removals & Demo	5	377	27-May-21	02-Jun-21
		Pavement Removal	5	377	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ML, Remove Pavement	5	377	27-May-21	02-Jun-21
		Earthwork	86	377	27-May-21	23-Sep-21
		Clear & Grub	5	377	27-May-21	02-Jun-21
	TX-3CD	Area 3C2 - NB ML, Clear and Grub	5	377	27-May-21	02-Jun-21
		Excavation	15	377	04-Jun-21	24-Jun-21
	TX-3CD	Area 3C2 - NB ML, Excavate Cut Areas	15	377	04-Jun-21	24-Jun-21
		Embankment	20	377	27-Aug-21	23-Sep-21
	TX-3CD	Area 3C2 - NB ML, Place Embankment	20	377	27-Aug-21	23-Sep-21
		Drainage	60	377	04-Jun-21	26-Aug-21
		Culverts	20	377	04-Jun-21	01-Jul-21
	TX-3CD	Area 3C2 - NB ML, CLV06 Install Culvert	20	377	04-Jun-21	01-Jul-21
	TX-3CD	Area 3C2 - NB ML, CLV08 Install Culvert	20	377	04-Jun-21	01-Jul-21
		Storm Sewer	20	377	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB ML, Install Small RCP	20	377	02-Jul-21	29-Jul-21
	TX-3CD	Area 3C2 - NB ML, CLV07 Install Medium RCP	20	377	02-Jul-21	29-Jul-21
		Inlets	20	377	30-Jul-21	26-Aug-21
	TX-3CD	Area 3C2 - NB ML, Install MHs and Inlets	20	377	30-Jul-21	26-Aug-21
		Subgrade Treatment and Base	80	377	24-Sep-21	13-Jan-22
		Lime Treatment	60	377	24-Sep-21	16-Dec-21
	TX-3CD	Area 3C2 - NB ML, Lime Treat Subgrade	60	377	24-Sep-21	16-Dec-21
		Flexbase	20	377	17-Dec-21	13-Jan-22
	TX-3CD	Area 3C2 - NB ML, Place Flexbase	20	377	17-Dec-21	13-Jan-22
		Pavement	38	386	14-Jan-22	08-Mar-22
(	TX-3CD	Area 3C2 - NB ML, FF Start STA 1176 to 1280	0	370	23-Feb-22	23-Feb-22
		Asphalt Pavement	38	386	14-Jan-22	08-Mar-22
	TX-3CD	Area 3C2 - NB ML, Interim - Finish STA 1176 to 1280	0	370	22-Feb-22	22-Feb-22
		HMA Paving	10	387	14-Jan-22	27-Jan-22
	TX-3CD	Area 3C2 - NB ML, Place HMA	10	387	14-Jan-22	27-Jan-22
		SMA Paving	10	386	23-Feb-22	08-Mar-22
	TX-3CD	Area 3C2 - NB ML, Place SMA	10	386	23-Feb-22	08-Mar-22

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
3C2 BR 108.2 NB ML Keller-Hicks Rd			193	370	27-May-21	22-Feb-22
(	TX-3CD	Area 3C2 NB ML BR 108.2 Start	3	370	27-May-21	31-May-21
(	TX-3CD	Area 3C2 NB ML BR 108.2 Finish	0	370	22-Feb-22	22-Feb-22
BR Excavation			4	370	02-Jun-21	07-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Bridge Excavation	4	370	02-Jun-21	07-Jun-21
Drill Shafts			20	390	08-Jun-21	05-Jul-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Drill Shafts Abutment 1	5	370	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Drill Shafts Bent 2	5	370	15-Jun-21	21-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Drill Shafts Bent 3	5	370	22-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Drill Shafts Abutment 4	5	390	29-Jun-21	05-Jul-21
Columns			35	380	15-Jun-21	02-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Columns Abutment 1	10	405	15-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Columns Bent 2	20	380	22-Jun-21	19-Jul-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Columns Bent 3	25	370	29-Jun-21	02-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Columns Abutment 4	10	390	06-Jul-21	19-Jul-21
Bent Caps			30	370	20-Jul-21	30-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Cap Bent 2	20	380	20-Jul-21	16-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Cap Bent 3	20	370	03-Aug-21	30-Aug-21
Beams			69	370	02-Jun-21	06-Sep-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Beam Procurement	20	373	02-Jun-21	29-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Forward Precast Beams Shopdrawings to TxDOT	1	373	30-Jun-21	30-Jun-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Precast Beam Fabrication & Delivery Leadtime	40	373	01-Jul-21	25-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Conc Beams	5	370	31-Aug-21	06-Sep-21
BR Place CTB Embankment			20	485	03-Aug-21	30-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Place Stabilized Backfill	20	485	03-Aug-21	30-Aug-21
Abutments			25	390	29-Jun-21	02-Aug-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Abutment 1	10	405	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Abutment 4	10	390	20-Jul-21	02-Aug-21
Approach Slab			10	370	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Apprch Slab Abutment 1	10	370	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Apprch Slab Abutment 4	10	370	08-Feb-22	21-Feb-22
Exspansion Joint			90	370	07-Sep-21	10-Jan-22
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Exp Joints	90	370	07-Sep-21	10-Jan-22
Deck			110	370	07-Sep-21	07-Feb-22
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Deck Slab	90	370	07-Sep-21	10-Jan-22
	TX-3CD	Area 3C2 NB ML BR 108.2 Cure Deck Slab	20	370	11-Jan-22	07-Feb-22
Railings			10	370	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 NB ML BR 108.2 Install Conc Rail	10	370	08-Feb-22	21-Feb-22
3C2 BR 111.2 NB ML Golden Triangle Blvd			193	370	27-May-21	22-Feb-22
(	TX-3CD	Area 3C2 NB ML BR 111.2 Start	3	370	27-May-21	31-May-21
(	TX-3CD	Area 3C2 NB ML BR 111.2 Finish	0	370	22-Feb-22	22-Feb-22
BR Excavation			4	370	02-Jun-21	07-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Bridge Excavation	4	370	02-Jun-21	07-Jun-21
Drill Shafts			20	390	08-Jun-21	05-Jul-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Drill Shafts Abutment 1	5	370	08-Jun-21	14-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Drill Shafts Bent 2	5	370	15-Jun-21	21-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Drill Shafts Bent 3	5	370	22-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Drill Shafts Abutment 4	5	390	29-Jun-21	05-Jul-21
Columns			35	380	15-Jun-21	02-Aug-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Columns Abutment 1	10	405	15-Jun-21	28-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Columns Bent 2	20	380	22-Jun-21	19-Jul-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Columns Bent 3	25	370	29-Jun-21	02-Aug-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Columns Abutment 4	10	390	06-Jul-21	19-Jul-21
Bent Caps			30	370	20-Jul-21	30-Aug-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Cap Bent 2	20	380	20-Jul-21	16-Aug-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Cap Bent 3	20	370	03-Aug-21	30-Aug-21
Beams			69	370	02-Jun-21	06-Sep-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Beam Procurement	20	373	02-Jun-21	29-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Forward Precast Beams Shopdrawings to TxDOT	1	373	30-Jun-21	30-Jun-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Precast Beam Fabrication & Delivery Leadtime	40	373	01-Jul-21	25-Aug-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Conc Beams	5	370	31-Aug-21	06-Sep-21
BR Place CTB Embankment			20	485	03-Aug-21	30-Aug-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Place Stabilized Backfill	20	485	03-Aug-21	30-Aug-21
Abutments			25	390	29-Jun-21	02-Aug-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Abutment 1	10	405	29-Jun-21	12-Jul-21
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Abutment 4	10	390	20-Jul-21	02-Aug-21
Approach Slab			10	370	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Apprch Slab Abutment 1	10	370	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Apprch Slab Abutment 4	10	370	08-Feb-22	21-Feb-22
Exspansion Joint			90	370	07-Sep-21	10-Jan-22
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Exp Joints	90	370	07-Sep-21	10-Jan-22
Deck			110	370	07-Sep-21	07-Feb-22
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Deck Slab	90	370	07-Sep-21	10-Jan-22
	TX-3CD	Area 3C2 NB ML BR 111.2 Cure Deck Slab	20	370	11-Jan-22	07-Feb-22
Railings			10	370	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 NB ML BR 111.2 Install Conc Rail	10	370	08-Feb-22	21-Feb-22
Permanent Barriers			10	385	24-Feb-22	09-Mar-22
Concrete Barriers			10	385	24-Feb-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Place Conc Rail	10	385	24-Feb-22	09-Mar-22
Metal Beam Guardrails			10	385	24-Feb-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install MBGF	10	385	24-Feb-22	09-Mar-22
Signals and Illumination			25	370	24-Feb-22	30-Mar-22
Roadway Illumination			25	370	24-Feb-22	30-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Illumination Pole Bases	5	370	24-Feb-22	02-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Illumination Poles/Fixtures	10	370	03-Mar-22	16-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Illumination Energize Fixtures	10	370	17-Mar-22	30-Mar-22
High Mast Illumination			15	380	24-Feb-22	16-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install High Mast Illumination Pole Bases	5	380	24-Feb-22	02-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install High Mast Illumination Poles/Fixtures	5	380	03-Mar-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install High Mast Illumination Energize Fixtures	5	380	10-Mar-22	16-Mar-22
Signing and Marking			26	370	23-Feb-22	31-Mar-22
Overhead Sign Structures			10	385	24-Feb-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Overhead Signage	10	385	24-Feb-22	09-Mar-22
Small Signage			10	385	24-Feb-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Small Signage	10	385	24-Feb-22	09-Mar-22
Pavement Marking			26	370	23-Feb-22	31-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Permt Markings	2	394	23-Feb-22	24-Feb-22
	TX-3CD	Area 3C2 - NB ML, Finish STA 1176 to 1280	0	370	31-Mar-22	31-Mar-22
Landscaping			10	385	24-Feb-22	09-Mar-22
Seeding & Sodding			10	385	24-Feb-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Topsoil	10	385	24-Feb-22	09-Mar-22
	TX-3CD	Area 3C2 - NB ML, Install Seeding/Sodding	10	385	24-Feb-22	09-Mar-22
ITS/TCS			109	379	14-Jan-22	16-Jun-22
Duct Bank System			20	377	14-Jan-22	10-Feb-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Civil Work Install Coduit	20	377	14-Jan-22	10-Feb-22

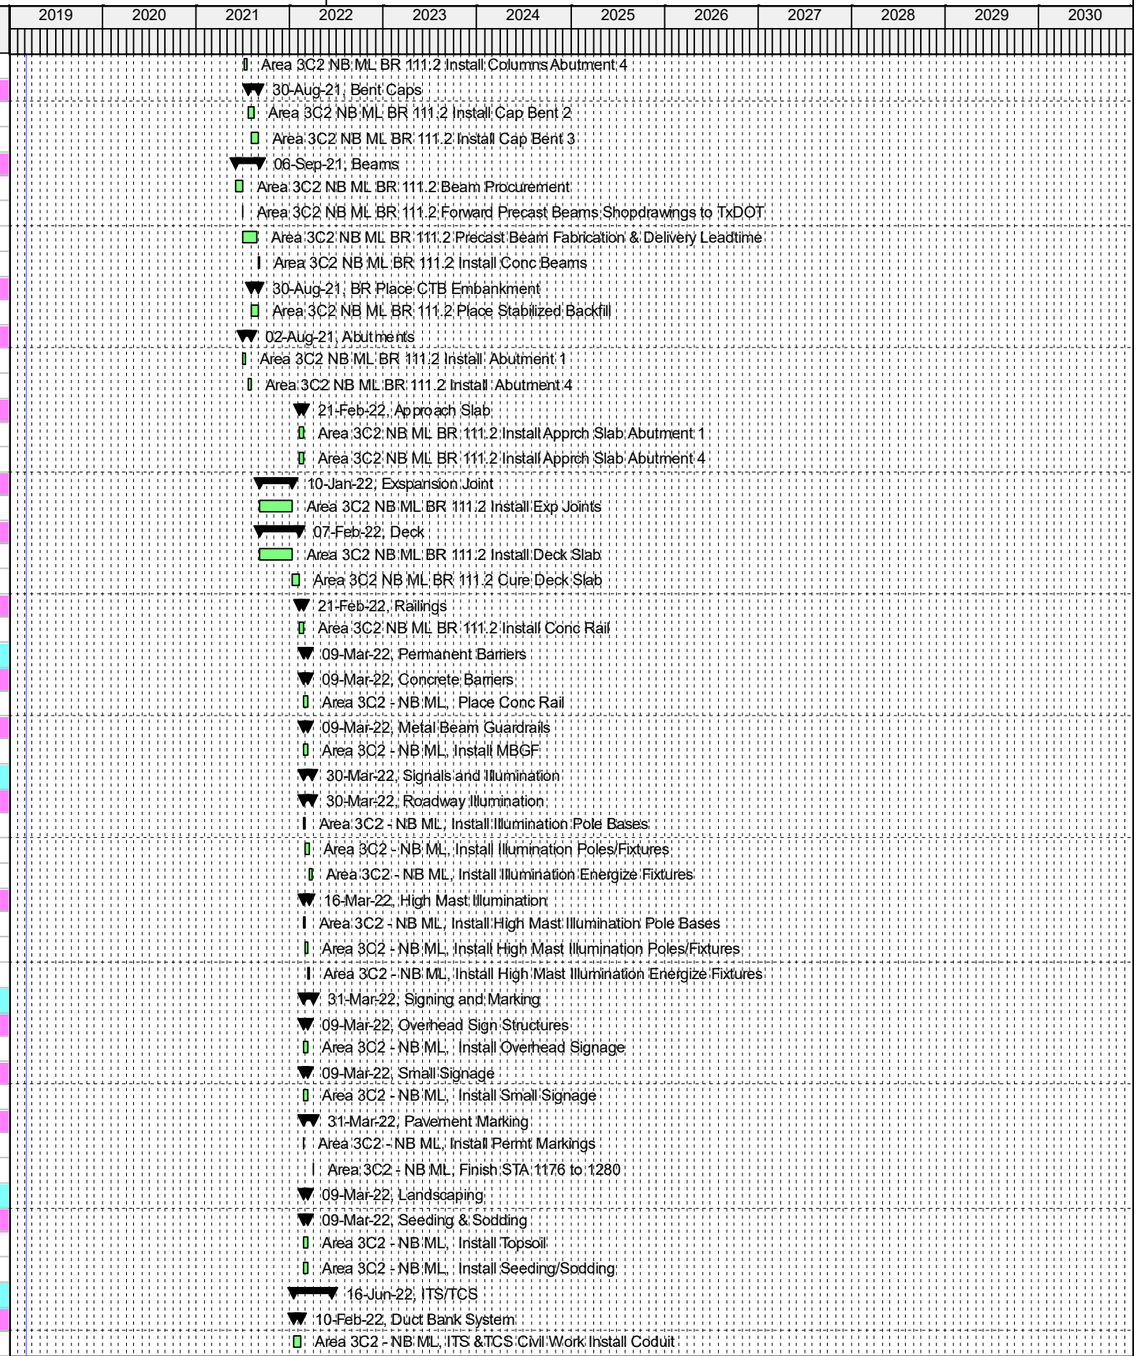

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Equipment Foundations			20	379	23-Feb-22	22-Mar-22
	TX-3CD	Area 3C2 - NB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	20	379	23-Feb-22	22-Mar-22
Equipment			60	380	23-Feb-22	17-May-22
	TX-3CD	Area 3C2 - NB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	379	23-Feb-22	23-Feb-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Fiber Install fiber	10	384	23-Feb-22	08-Mar-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Fiber Cut and splice	20	384	09-Mar-22	05-Apr-22
	TX-3CD	Area 3C2 - NB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	20	379	23-Mar-22	19-Apr-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Fiber Fiber Complete	0	384	13-Apr-22	13-Apr-22
	TX-3CD	Area 3C2 - NB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	380	20-Apr-22	17-May-22
	TX-3CD	Area 3C2 - NB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	379	20-Apr-22	20-Apr-22
Testing & Certification			51	379	06-Apr-22	16-Jun-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Fiber Local Site Test	5	384	06-Apr-22	12-Apr-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Testing Start	0	379	21-Apr-22	21-Apr-22
	TX-3CD	Area 3C2 - NB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	379	21-Apr-22	18-May-22
	TX-3CD	Area 3C2 - NB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	20	379	19-May-22	15-Jun-22
	TX-3CD	Area 3C2 - NB ML, ITS &TCS Testing Complete	0	379	16-Jun-22	16-Jun-22
Crossroad Alliance Blvd Bridge Rehab Level 8 STA 1080			16	760	09-Sep-20	01-Oct-20
C3(	TX-3CD	Area 3C1 - CR BR RH, Start STA 1080	0	760	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			6	760	09-Sep-20	16-Sep-20
Barricades, Signs & Traffic Handling			1	760	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Move Traffic	1	760	16-Sep-20	16-Sep-20
Portable Traffic Barrier			5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Place Temp Conc Barrier	5	760	09-Sep-20	15-Sep-20
Workzone Pavement Marking			5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Place Temp Marking & Signing	5	760	09-Sep-20	15-Sep-20
Erosion Control			5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, Place Temp Erosion Control	5	760	09-Sep-20	15-Sep-20
BR 206 Alliance Blvd			16	760	09-Sep-20	01-Oct-20
(	TX-3CD	Area 3C1 - CR BR RH, BR 206 Start	2	763	09-Sep-20	10-Sep-20
(	TX-3CD	Area 3C1 - CR BR RH, BR 206 Finish STA 1080	0	760	01-Oct-20	01-Oct-20
BR Demolition			5	760	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, BR 206, Concrete Removal	5	760	17-Sep-20	23-Sep-20
Concret Repairs			5	760	24-Sep-20	30-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 206, Concrete Repairs	5	760	24-Sep-20	30-Sep-20
Replace Exspansion Joint			10	764	11-Sep-20	24-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 206, Install Exp Joints	10	764	11-Sep-20	24-Sep-20
BR 207 Alliance Blvd			16	760	09-Sep-20	01-Oct-20
(	TX-3CD	Area 3C1 - CR BR RH, BR 207 Start	2	763	09-Sep-20	10-Sep-20
(	TX-3CD	Area 3C1 - CR BR RH, BR 207 Finish STA 1080	0	760	01-Oct-20	01-Oct-20
BR Demolition			5	760	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C1 - CR BR RH, BR 207 Concrete Removal	5	760	17-Sep-20	23-Sep-20
Rip Rap Removal			5	764	11-Sep-20	17-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR 207 Remove Rip Rap	5	764	11-Sep-20	17-Sep-20
Rip Rap Replacement			5	764	18-Sep-20	24-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR BR 207 Install Rip Rap	5	764	18-Sep-20	24-Sep-20
Concret Repairs			5	760	24-Sep-20	30-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR BR 207 BR Concrete Repairs	5	760	24-Sep-20	30-Sep-20
Replace Exspansion Joint			10	764	11-Sep-20	24-Sep-20
	TX-3CD	Area 3C1 - NB ML, BR BR 207 Install Exp Joints	10	764	11-Sep-20	24-Sep-20
Southbound ML Lane STA 1176 to 1280			308	316	08-Jul-21	13-Sep-22
C3(	TX-3CD	Area 3C2 - SB ML, Start STA 1176 to 1280	0	307	08-Jul-21	08-Jul-21
Traffic Control and Temporary Work			6	357	08-Jul-21	15-Jul-21
Barricades, Signs & Traffic Handling			1	357	15-Jul-21	15-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB ML, Move Traffic	1	357	15-Jul-21	15-Jul-21
Portable Traffic Barrier			5	357	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML, Place Temp Conc Barrier	5	357	08-Jul-21	14-Jul-21
Workzone Pavement Marking			5	357	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML, Place Temp Marking & Signing	5	357	08-Jul-21	14-Jul-21
Erosion Control			5	357	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML, Place Temp Erosion Control	5	357	08-Jul-21	14-Jul-21
Removals & Demo			5	357	08-Jul-21	14-Jul-21
Pavement Removal			5	19-Fet	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML, Remove Pavement	5	357	08-Jul-21	14-Jul-21
Earthwork			76	357	08-Jul-21	21-Oct-21
Clear & Grub			5	357	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML, Clear and Grub	5	357	08-Jul-21	14-Jul-21
Excavation			40	357	16-Jul-21	09-Sep-21
	TX-3CD	Area 3C2 - SB ML, Excavate Cut Areas	40	357	16-Jul-21	09-Sep-21
Embankment			30	357	10-Sep-21	21-Oct-21
	TX-3CD	Area 3C2 - SB ML, Place Embankment,	30	357	10-Sep-21	21-Oct-21
Drainage			60	367	16-Jul-21	07-Oct-21
Culverts			20	367	16-Jul-21	12-Aug-21
	TX-3CD	Area 3C2 - SB ML, CLV06 Install Culvert	20	367	16-Jul-21	12-Aug-21
	TX-3CD	Area 3C2 - SB ML, CLV08 Install Culvert	20	367	16-Jul-21	12-Aug-21
Storm Sewer			20	367	13-Aug-21	09-Sep-21
	TX-3CD	Area 3C2 - SB ML, Install Small RCP	20	367	13-Aug-21	09-Sep-21
	TX-3CD	Area 3C2 - SB ML, CLV07 Install Medium RCP	20	367	13-Aug-21	09-Sep-21
Inlets			20	367	10-Sep-21	07-Oct-21
	TX-3CD	Area 3C2 - SB ML, Install MHs and Inlets	20	367	10-Sep-21	07-Oct-21
Subgrade Treatment and Base			80	357	22-Oct-21	10-Feb-22
Lime Treatment			60	357	22-Oct-21	13-Jan-22
	TX-3CD	Area 3C2 - SB ML, Lime Treat Subgrade	60	357	22-Oct-21	13-Jan-22
Flexbase			20	357	14-Jan-22	10-Feb-22
	TX-3CD	Area 3C2 - SB ML, Place Flexbase	20	357	14-Jan-22	10-Feb-22
Pavement			76	328	11-Feb-22	27-May-22
	TX-3CD	Area 3C2 - SB ML, FF Start STA 1176 to 1280	0	307	23-May-22	23-May-22
Asphalt Pavement			76	328	11-Feb-22	27-May-22
	TX-3CD	Area 3C2 - SB ML, Interim - Finish STA 1176 to 1280	0	307	20-May-22	20-May-22
HMA Paving			10	367	11-Feb-22	24-Feb-22
	TX-3CD	Area 3C2 - SB ML, Place HMA	10	367	11-Feb-22	24-Feb-22
SMA Paving			5	328	23-May-22	27-May-22
	TX-3CD	Area 3C2 - SB ML, Place SMA	5	328	23-May-22	27-May-22
3C2 BR 108.2 SB ML Keller-Hicks Rd			226	307	08-Jul-21	20-May-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Start	20	307	08-Jul-21	04-Aug-21
	TX-3CD	Area 3C2 - SB ML, BR 108.2 Finish	0	307	20-May-22	20-May-22
BR Excavation			5	307	06-Aug-21	12-Aug-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Bridge Excavation	5	307	06-Aug-21	12-Aug-21
Drill Shafts			30	332	13-Aug-21	23-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Drill Shafts Abutment 1	5	307	13-Aug-21	19-Aug-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Drill Shafts Bent 2	10	307	20-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Drill Shafts Bent 3	10	307	03-Sep-21	16-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Drill Shafts Abutment 4	5	332	17-Sep-21	23-Sep-21
Columns			45	322	20-Aug-21	21-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Columns Abutment 1	10	357	20-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Columns Bent 2	20	327	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Columns Bent 3	25	307	17-Sep-21	21-Oct-21

Actual Work | Critical Remaining Work | Summary
Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Columns Abutment 4	10	332	24-Sep-21	07-Oct-21
Bent Caps			40	307	01-Oct-21	25-Nov-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Cap Bent 2	20	327	01-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Cap Bent 3	25	307	22-Oct-21	25-Nov-21
Beams			85	307	06-Aug-21	02-Dec-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Beam Procurement	20	326	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Forward Precast Beams Shopdrawings to TxDOT	1	326	03-Sep-21	03-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Precast Beam Fabrication & Delivery Leadtime	40	326	06-Sep-21	29-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Conc Beams	5	307	26-Nov-21	02-Dec-21
BR Place CTB Embankment			20	427	22-Oct-21	18-Nov-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Place Stabilized Backfill	20	427	22-Oct-21	18-Nov-21
Abutments			35	332	03-Sep-21	21-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Abutment 1	10	357	03-Sep-21	16-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Abutment 4	10	332	08-Oct-21	21-Oct-21
Approach Slab			10	307	06-May-22	19-May-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Apprch Slab Abutment 1	10	307	06-May-22	19-May-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Apprch Slab Abutment 4	10	307	06-May-22	19-May-22
Exspansion Joint			90	307	03-Dec-21	07-Apr-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Exp Joints	90	307	03-Dec-21	07-Apr-22
Deck			110	307	03-Dec-21	05-May-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Deck Slab	90	307	03-Dec-21	07-Apr-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Cure Deck Slab	20	307	08-Apr-22	05-May-22
Railings			10	307	06-May-22	19-May-22
	TX-3CD	Area 3C2 SB ML, BR 108.2 Install Conc Rail	10	307	06-May-22	19-May-22
3C2 BR 111.2 SB ML Golden Triangle Blvd			226	307	08-Jul-21	20-May-22
(	TX-3CD	Area 3C2 SB ML, BR 111.2 Start	20	307	08-Jul-21	04-Aug-21
(	TX-3CD	Area 3C2 - SB ML, BR 111.2 Finish	0	307	20-May-22	20-May-22
BR Excavation			5	307	06-Aug-21	12-Aug-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Bridge Excavation	5	307	06-Aug-21	12-Aug-21
Drill Shafts			30	332	13-Aug-21	23-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Drill Shafts Abutment 1	5	307	13-Aug-21	19-Aug-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Drill Shafts Bent 2	10	307	20-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Drill Shafts Bent 3	10	307	03-Sep-21	16-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Drill Shafts Abutment 4	5	332	17-Sep-21	23-Sep-21
Columns			45	322	20-Aug-21	21-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Columns Abutment 1	10	357	20-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Columns Bent 2	20	327	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Columns Bent 3	25	307	17-Sep-21	21-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Columns Abutment 4	10	332	24-Sep-21	07-Oct-21
Bent Caps			40	307	01-Oct-21	25-Nov-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Cap Bent 2-4	20	327	01-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Cap Bent 5-8	25	307	22-Oct-21	25-Nov-21
Beams			85	307	06-Aug-21	02-Dec-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Beam Procurement	20	326	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Forward Precast Beams Shopdrawings to TxDOT	1	326	03-Sep-21	03-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Precast Beam Fabrication & Delivery Leadtime	40	326	06-Sep-21	29-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Conc Beams	5	307	26-Nov-21	02-Dec-21
BR Place CTB Embankment			20	427	22-Oct-21	18-Nov-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Place Stabilized Backfill	20	427	22-Oct-21	18-Nov-21
Abutments			35	332	03-Sep-21	21-Oct-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Abutment 1	10	357	03-Sep-21	16-Sep-21
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Abutment 8	10	332	08-Oct-21	21-Oct-21
Approach Slab			10	307	06-May-22	19-May-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Apprch Slab Abutment 1	10	307	06-May-22	19-May-22
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Apprch Slab Abutment 4	10	307	06-May-22	19-May-22
Exspansion Joint			90	307	03-Dec-21	07-Apr-22
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Exp Joints	90	307	03-Dec-21	07-Apr-22
Deck			110	307	03-Dec-21	05-May-22
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Deck Slab	90	307	03-Dec-21	07-Apr-22
	TX-3CD	Area 3C2 SB ML, BR 111.2 Cure Deck Slab	20	307	08-Apr-22	05-May-22
Railings			10	307	06-May-22	19-May-22
	TX-3CD	Area 3C2 SB ML, BR 111.2 Install Conc Rail	10	307	06-May-22	19-May-22
Permanent Barriers			10	322	24-May-22	06-Jun-22
Concrete Barriers			10	322	24-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Place Conc Rail	10	322	24-May-22	06-Jun-22
Metal Beam Guardrails			10	322	24-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install MBGF	10	322	24-May-22	06-Jun-22
Signals and Illumination			25	307	24-May-22	27-Jun-22
Roadway Illumination			25	307	24-May-22	27-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Illumination Pole Bases	5	307	24-May-22	30-May-22
	TX-3CD	Area 3C2 - SB ML, Install Illumination Poles/Fixtures	10	307	31-May-22	13-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Illumination Energize Fixtures	10	307	14-Jun-22	27-Jun-22
High Mast Illumination			15	317	24-May-22	13-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install High Mast Illumination Pole Bases	5	317	24-May-22	30-May-22
	TX-3CD	Area 3C2 - SB ML, Install High Mast Illumination Poles/Fixtures	5	317	31-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install High Mast Illumination Energize Fixtures	5	317	07-Jun-22	13-Jun-22
Signing and Marking			26	307	23-May-22	28-Jun-22
Overhead Sign Structures			10	322	24-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Overhead Signage	10	322	24-May-22	06-Jun-22
Small Signage			10	322	24-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Small Signage	10	322	24-May-22	06-Jun-22
Pavement Marking			26	307	23-May-22	28-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Permt Markings	2	331	23-May-22	24-May-22
	TX-3CD	Area 3C2 - SB ML, Finish STA 1176 to 1280	0	307	28-Jun-22	28-Jun-22
Landscaping			10	322	24-May-22	06-Jun-22
Seeding & Sodding			10	322	24-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Topsoil	10	322	24-May-22	06-Jun-22
	TX-3CD	Area 3C2 - SB ML, Install Seeding/Sodding	10	322	24-May-22	06-Jun-22
ITS/TCS			152	316	11-Feb-22	13-Sep-22
Duct Bank System			20	357	11-Feb-22	10-Mar-22
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Civil Work Install Coduit	20	357	11-Feb-22	10-Mar-22
Equipment Foundations			20	316	23-May-22	17-Jun-22
	TX-3CD	Area 3C2 - SB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	20	316	23-May-22	17-Jun-22
Equipment			40	316	23-May-22	18-Jul-22
	TX-3CD	Area 3C2 - SB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	316	23-May-22	23-May-22
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Fiber Install fiber	10	321	23-May-22	03-Jun-22
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Fiber Cut and splice	20	321	06-Jun-22	01-Jul-22
	TX-3CD	Area 3C2 - SB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	20	316	20-Jun-22	15-Jul-22
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Fiber Local Site Test	5	321	04-Jul-22	08-Jul-22
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Fiber Fiber Complete	0	321	11-Jul-22	11-Jul-22
	TX-3CD	Area 3C2 - SB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	316	18-Jul-22	18-Jul-22
Testing & Certification			41	316	18-Jul-22	13-Sep-22
	TX-3CD	Area 3C2 - SB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	317	18-Jul-22	12-Aug-22
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Testing Start	0	316	19-Jul-22	19-Jul-22
	TX-3CD	Area 3C2 - SB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	316	19-Jul-22	15-Aug-22
	TX-3CD	Area 3C2 - SB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	20	316	16-Aug-22	12-Sep-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB ML, ITS &TCS Testing Complete	0	316	13-Sep-22	13-Sep-22
Southbound Entry Ramp SBGP to SBML STA 1253 to 1270			118	442	08-Jul-21	21-Dec-21
C3(	TX-3CD	Area 3C2 - SB ML ENR, Start STA 1253 to 1270	0	442	08-Jul-21	08-Jul-21
Traffic Control and Temporary Work			6	442	08-Jul-21	15-Jul-21
Barricades, Signs & Traffic Handling			1	442	15-Jul-21	15-Jul-21
	TX-3CD	Area 3C2 - SB ML ENR, Move Traffic	1	442	15-Jul-21	15-Jul-21
Portable Traffic Barrier			5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Temp Conc Barrier	5	442	08-Jul-21	14-Jul-21
Workzone Pavement Marking			5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Temp Marking & Signing	5	442	08-Jul-21	14-Jul-21
Erosion Control			5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Temp Erosion Control	5	442	08-Jul-21	14-Jul-21
Earthwork			41	442	08-Jul-21	02-Sep-21
Clear & Grub			5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ML ENR, Clear and Grub	5	442	08-Jul-21	14-Jul-21
Excavation			15	442	16-Jul-21	05-Aug-21
	TX-3CD	Area 3C2 - SB ML ENR, Excavate Cut Areas	15	442	16-Jul-21	05-Aug-21
Embankment			20	442	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Embankment	20	442	06-Aug-21	02-Sep-21
Subgrade Treatment and Base			30	442	03-Sep-21	14-Oct-21
Lime Treatment			20	442	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - SB ML ENR, Lime Treat Subgrade	20	442	03-Sep-21	30-Sep-21
Flexbase			10	442	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Flexbase	10	442	01-Oct-21	14-Oct-21
Pavement			26	463	15-Oct-21	19-Nov-21
(	TX-3CD	Area 3C2 - SB ML ENR, FF Start STA 1253 to 1270	0	442	15-Nov-21	15-Nov-21
Asphalt Pavement			16	463	29-Oct-21	19-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Interim - Finish STA 1253 to 1270	0	442	12-Nov-21	12-Nov-21
HMA Paving			5	447	29-Oct-21	04-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Place HMA	5	447	29-Oct-21	04-Nov-21
SMA Paving			5	463	15-Nov-21	19-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Place SMA	5	463	15-Nov-21	19-Nov-21
Curb & Gutter			10	447	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Curb & Gutter	10	447	15-Oct-21	28-Oct-21
Permanent Barriers			10	457	16-Nov-21	29-Nov-21
Concrete Barriers			10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Place Conc Rail	10	457	16-Nov-21	29-Nov-21
Metal Beam Guardrails			10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install MBGF	10	457	16-Nov-21	29-Nov-21
Crash Attenuators			5	462	16-Nov-21	22-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Attenuator	5	462	16-Nov-21	22-Nov-21
Signals and Illumination			25	442	16-Nov-21	20-Dec-21
Roadway Illumination			25	442	16-Nov-21	20-Dec-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Illumination Pole Bases	5	442	16-Nov-21	22-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Illumination Poles/Fixtures	10	442	23-Nov-21	06-Dec-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Illumination Energize Fixtures	10	442	07-Dec-21	20-Dec-21
Signing and Marking			26	442	15-Nov-21	21-Dec-21
Overhead Sign Structures			10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Overhead Signage	10	457	16-Nov-21	29-Nov-21
Small Signage			10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Small Signage	10	457	16-Nov-21	29-Nov-21
Pavement Marking			26	442	15-Nov-21	21-Dec-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Permt Markings	2	466	15-Nov-21	16-Nov-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB ML ENR, Finish STA 1253 to 1270	0	442	21-Dec-21	21-Dec-21
Landscaping			10	457	16-Nov-21	29-Nov-21
Seeding & Sodding			10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Seeding/Sodding	10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, Install Topsoil	10	457	16-Nov-21	29-Nov-21
ITS/TCS			20	442	15-Oct-21	11-Nov-21
Duct Bank System			20	442	15-Oct-21	11-Nov-21
	TX-3CD	Area 3C2 - SB ML ENR, ITS &TCS Civil Work Install Coduit	20	442	15-Oct-21	11-Nov-21
Southbound GP Lane SBGP to SBFR STA 1176 to 1280			263	533	12-Aug-20	16-Aug-21
C3(	TX-3CD	Area 3C2 - SB GP, Start STA 1176 to 1280	0	270	12-Aug-20	12-Aug-20
Traffic Control and Temporary Work			6	320	12-Aug-20	19-Aug-20
Barricades, Signs & Traffic Handling			1	320	19-Aug-20	19-Aug-20
	TX-3CD	Area 3C2 - SB GP, Move Traffic	1	320	19-Aug-20	19-Aug-20
Portable Traffic Barrier			5	320	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB GP, Place Temp Conc Barrier	5	320	12-Aug-20	18-Aug-20
Workzone Pavement Marking			5	320	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB GP, Place Temp Marking & Signing	5	320	12-Aug-20	18-Aug-20
Erosion Control			5	320	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB GP, Place Temp Erosion Control	5	320	12-Aug-20	18-Aug-20
Removals & Demo			5	320	12-Aug-20	18-Aug-20
Pavement Removal			5	320	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB GP, Remove Pavement	5	320	12-Aug-20	18-Aug-20
Earthwork			86	320	12-Aug-20	09-Dec-20
Clear & Grub			5	320	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB GP, Clear and Grub	5	320	12-Aug-20	18-Aug-20
Excavation			40	320	20-Aug-20	14-Oct-20
	TX-3CD	Area 3C2 - SB GP, Excavate Cut Areas	40	320	20-Aug-20	14-Oct-20
Embankment			40	320	15-Oct-20	09-Dec-20
	TX-3CD	Area 3C2 - SB GP, Place Embankment,	40	320	15-Oct-20	09-Dec-20
Drainage			60	340	20-Aug-20	11-Nov-20
Culverts			20	340	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 - SB GP, CLV06 Install Culvert	20	340	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 - SB GP, CLV08 Install Culvert	20	340	20-Aug-20	16-Sep-20
Storm Sewer			20	340	17-Sep-20	14-Oct-20
	TX-3CD	Area 3C2 - SB GP, CLV07 Install Medium RCP	20	340	17-Sep-20	14-Oct-20
	TX-3CD	Area 3C2 - SB GP, Install Small RCP	20	340	17-Sep-20	14-Oct-20
Inlets			20	340	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C2 - SB GP, Install MHs and Inlets	20	340	15-Oct-20	11-Nov-20
Subgrade Treatment and Base			80	320	10-Dec-20	31-Mar-21
Lime Treatment			60	320	10-Dec-20	03-Mar-21
	TX-3CD	Area 3C2 - SB GP, Lime Treat Subgrade	60	320	10-Dec-20	03-Mar-21
Flexbase			20	320	04-Mar-21	31-Mar-21
	TX-3CD	Area 3C2 - SB GP, Place Flexbase	20	320	04-Mar-21	31-Mar-21
Pavement			76	554	01-Apr-21	15-Jul-21
(	TX-3CD	Area 3C2 - SB GP, FF Start STA 1176 to 1280	0	533	09-Jul-21	09-Jul-21
Asphalt Pavement			76	554	01-Apr-21	15-Jul-21
	TX-3CD	Area 3C2 - SB GP, Interim - Finish STA 1176 to 1280	0	270	08-Jul-21	08-Jul-21
HMA Paving			10	330	01-Apr-21	14-Apr-21
	TX-3CD	Area 3C2 - SB GP, Place HMA	10	330	01-Apr-21	14-Apr-21
SMA Paving			5	554	09-Jul-21	15-Jul-21
	TX-3CD	Area 3C2 - SB GP, Place SMA	5	554	09-Jul-21	15-Jul-21
Retaining Walls			55	365	15-Oct-20	30-Dec-20
Wall RT-3C-7A			35	385	15-Oct-20	02-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-7A	20	385	15-Oct-20	11-Nov-20
Wall Coping RT-3C-7A			15	385	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-7A	15	385	12-Nov-20	02-Dec-20
Wall RT-3C-E1			35	385	15-Oct-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-E1	20	385	15-Oct-20	11-Nov-20
Wall Coping RT-3C-E1			15	385	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-E1	15	385	12-Nov-20	02-Dec-20
Wall RT-3C-S3			35	385	15-Oct-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S3	20	385	15-Oct-20	11-Nov-20
Wall Coping RT-3C-S3			15	385	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S3	15	385	12-Nov-20	02-Dec-20
Wall RT-3C-S4			35	385	15-Oct-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S4	20	385	15-Oct-20	11-Nov-20
Wall Coping RT-3C-S4			15	385	12-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Coping CapRT-3C-S4	15	385	12-Nov-20	02-Dec-20
Wall RT-3C-9A			55	365	15-Oct-20	30-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-9A	40	365	15-Oct-20	09-Dec-20
Wall Coping RT-3C-9A			15	365	10-Dec-20	30-Dec-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-9A	15	365	10-Dec-20	30-Dec-20
3C2 BR 108.3 SB GP Keller-Hicks Rd			236	270	12-Aug-20	08-Jul-21
(	TX-3CD	Area 3C2 - SB GP, BR 108.3 Start	20	270	12-Aug-20	08-Sep-20
(	TX-3CD	Area 3C2 - SB GP, BR 108.3 Finish	0	270	08-Jul-21	08-Jul-21
BR Excavation			5	270	10-Sep-20	16-Sep-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Bridge Excavation	5	270	10-Sep-20	16-Sep-20
Drill Shafts			30	295	17-Sep-20	28-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Drill Shafts Abutment 1	5	270	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Drill Shafts Bent 2	10	270	24-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Drill Shafts Bent 3	10	270	08-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Drill Shafts Abutment 4	5	295	22-Oct-20	28-Oct-20
Columns			45	285	24-Sep-20	25-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Columns Abutment 1	10	320	24-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Columns Bent 2	20	290	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Columns Bent 3	25	270	22-Oct-20	25-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Columns Abutment 4	10	295	29-Oct-20	11-Nov-20
Bent Caps			40	270	05-Nov-20	30-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Cap Bent 2	20	290	05-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Cap Bent 3	25	270	26-Nov-20	30-Dec-20
Beams			85	270	10-Sep-20	06-Jan-21
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Beam Procurement	20	289	10-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Forward Precast Beams Shopdrawings to TxDOT	1	289	08-Oct-20	08-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Precast Beam Fabrication & Delivery Leadtime	40	289	09-Oct-20	03-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Conc Beams	5	270	31-Dec-20	06-Jan-21
BR Place CTB Embankment			20	400	26-Nov-20	23-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Place Embankment	20	400	26-Nov-20	23-Dec-20
Abutments			35	295	08-Oct-20	25-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Abutment 1	10	320	08-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Abutment 4	10	295	12-Nov-20	25-Nov-20
Approach Slab			10	270	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Apprch Slab Abutment 1	10	270	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Apprch Slab Abutment 4	10	270	24-Jun-21	07-Jul-21
Exspansion Joint			100	270	07-Jan-21	26-May-21
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Exp Joints	100	270	07-Jan-21	26-May-21
Deck			120	270	07-Jan-21	23-Jun-21

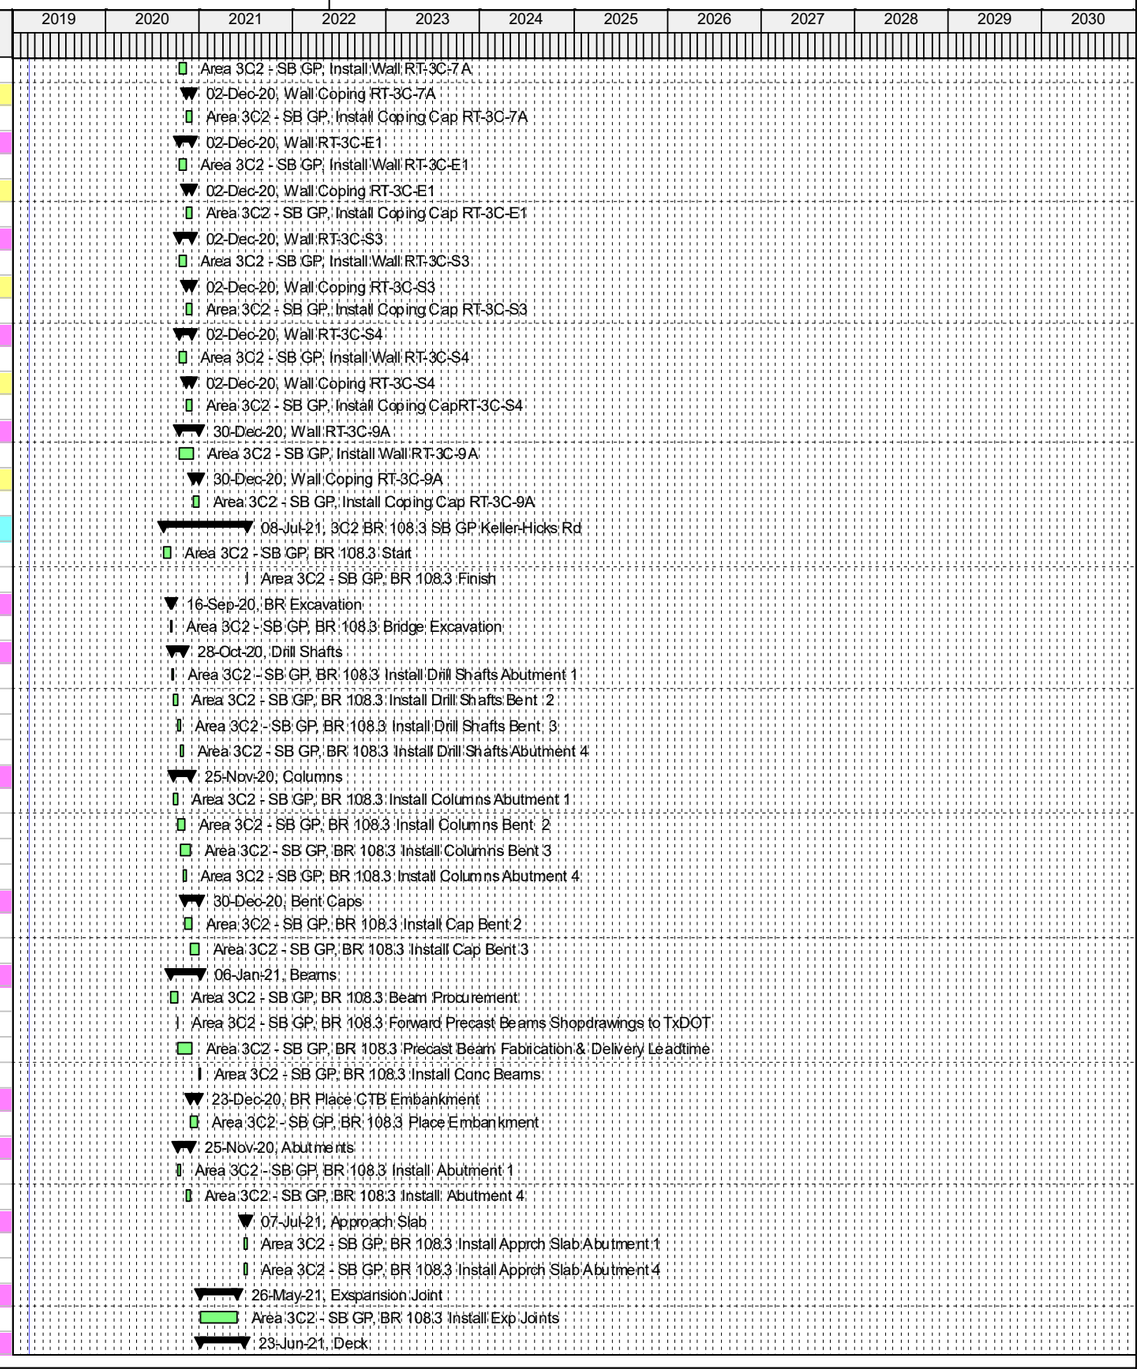

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Deck Slab	100	270	07-Jan-21	26-May-21
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Cure Deck Slab	20	270	27-May-21	23-Jun-21
Railings			10	270	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C2 - SB GP, BR 108.3 Install Conc Rail	10	270	24-Jun-21	07-Jul-21
3C2 BR 111.3 SB GP Golden Triangle Blvd			236	270	12-Aug-20	08-Jul-21
(	TX-3CD	Area 3C2 - SB GP, BR 111.3 Start	20	270	12-Aug-20	08-Sep-20
(	TX-3CD	Area 3C2 - SB GP, BR 111.3 Finish	0	270	08-Jul-21	08-Jul-21
BR Excavation			5	270	10-Sep-20	16-Sep-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Bridge Excavation	5	270	10-Sep-20	16-Sep-20
Drill Shafts			30	295	17-Sep-20	28-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Drill Shafts Abutment 1	5	270	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Drill Shafts Bent 2	10	270	24-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Drill Shafts Bent 3	10	270	08-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Drill Shafts Abutment 4	5	295	22-Oct-20	28-Oct-20
Columns			45	285	24-Sep-20	25-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Columns Abutment 1	10	320	24-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Columns Bent 2	20	290	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Columns Bent 3	25	270	22-Oct-20	25-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Columns Abutment 4	10	295	29-Oct-20	11-Nov-20
Bent Caps			40	270	05-Nov-20	30-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Cap Bent 2	20	290	05-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Cap Bent 3	25	270	26-Nov-20	30-Dec-20
Beams			85	270	10-Sep-20	06-Jan-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Beam Procurement	20	289	10-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Forward Precast Beams Shopdrawings to TxDOT	1	289	08-Oct-20	08-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Precast Beam Fabrication & Delivery Leadtime	40	289	09-Oct-20	03-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Conc Beams	5	270	31-Dec-20	06-Jan-21
BR Place CTB Embankment			20	400	26-Nov-20	23-Dec-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Place Stabilized Backfill	20	400	26-Nov-20	23-Dec-20
Abutments			35	295	08-Oct-20	25-Nov-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Abutment 1	10	320	08-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Abutment 4	10	295	12-Nov-20	25-Nov-20
Approach Slab			10	270	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Apprch Slab Abutment 1	10	270	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Apprch Slab Abutment 4	10	270	24-Jun-21	07-Jul-21
Exspansion Joint			100	270	07-Jan-21	26-May-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Exp Joints	100	270	07-Jan-21	26-May-21
Deck			120	270	07-Jan-21	23-Jun-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Deck Slab	100	270	07-Jan-21	26-May-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Cure Deck Slab	20	270	27-May-21	23-Jun-21
Railings			10	270	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C2 - SB GP, BR 111.3 Install Conc Rail	10	270	24-Jun-21	07-Jul-21
Permanent Barriers			10	548	12-Jul-21	23-Jul-21
Concrete Barriers			10	548	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Place Conc Rail	10	548	12-Jul-21	23-Jul-21
Metal Beam Guardrails			10	548	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install MBGF	10	548	12-Jul-21	23-Jul-21
Signals and Illumination			25	533	12-Jul-21	13-Aug-21
Roadway Illumination			25	533	12-Jul-21	13-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Illumination Pole Bases	5	533	12-Jul-21	16-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install Illumination Poles/Fixtures	10	533	19-Jul-21	30-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install Illumination Energize Fixtures	10	533	02-Aug-21	13-Aug-21
High Mast Illumination			15	543	12-Jul-21	30-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB GP, Install High Mast Illumination Pole Bases	5	543	12-Jul-21	16-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install High Mast Illumination Poles/Fixtures	5	543	19-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install High Mast Illumination Energize Fixtures	5	543	26-Jul-21	30-Jul-21
Signing and Marking			26	533	09-Jul-21	16-Aug-21
Overhead Sign Structures			10	548	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install Overhead Signage	10	548	12-Jul-21	23-Jul-21
Small Signage			10	548	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install Small Signage	10	548	12-Jul-21	23-Jul-21
Pavement Marking			26	533	09-Jul-21	16-Aug-21
	TX-3CD	Area 3C2 - SB GP, Install Permt Markings	2	557	09-Jul-21	12-Jul-21
	TX-3CD	Area 3C2 - SB GP, Finish STA 1176 to 1280	0	533	16-Aug-21	16-Aug-21
Landscaping			10	548	12-Jul-21	23-Jul-21
Seeding & Sodding			10	548	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install Topsoil	10	548	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C2 - SB GP, Install Seeding/Sodding	10	548	12-Jul-21	23-Jul-21
ITS/TCS			20	320	01-Apr-21	28-Apr-21
Duct Bank System			20	320	01-Apr-21	28-Apr-21
	TX-3CD	Area 3C2 - SB GP, ITS &TCS Civil Work Install Coduit	20	320	01-Apr-21	28-Apr-21
Southbound Exit Ramp STA 1185 to 1205			98	698	12-Aug-20	28-Dec-20
C3(	TX-3CD	Area 3C2 - SB EXR, Start STA 1185 to 1205	0	698	12-Aug-20	12-Aug-20
Traffic Control and Temporary Work			6	698	12-Aug-20	19-Aug-20
Barricades, Signs & Traffic Handling			1	698	19-Aug-20	19-Aug-20
	TX-3CD	Area 3C2 - SB EXR, Move Traffic	1	698	19-Aug-20	19-Aug-20
Portable Traffic Barrier			5	698	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB EXR, Place Temp Conc Barrier	5	698	12-Aug-20	18-Aug-20
Workzone Pavement Marking			5	698	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB EXR, Place Temp Marking & Signing	5	698	12-Aug-20	18-Aug-20
Erosion Control			5	698	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB EXR, Place Temp Erosion Control	5	698	12-Aug-20	18-Aug-20
Earthwork			41	698	12-Aug-20	07-Oct-20
Clear & Grub			5	698	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB EXR, Clear and Grub	5	698	12-Aug-20	18-Aug-20
Excavation			15	698	20-Aug-20	09-Sep-20
	TX-3CD	Area 3C2 - SB EXR, Excavate Cut Areas	15	698	20-Aug-20	09-Sep-20
Embankment			20	698	10-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB EXR, Place Embankment	20	698	10-Sep-20	07-Oct-20
Subgrade Treatment and Base			10	698	08-Oct-20	21-Oct-20
Lime Treatment			5	698	08-Oct-20	14-Oct-20
	TX-3CD	Area 3C2 - SB EXR, Lime Treat Subgrade	5	698	08-Oct-20	14-Oct-20
Flexbase			5	698	15-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB EXR, Place Flexbase	5	698	15-Oct-20	21-Oct-20
Pavement			26	719	22-Oct-20	26-Nov-20
(	TX-3CD	Area 3C2 - SB EXR, FF Start STA 1185 to 1205	19-Feb-	698	20-Nov-20	20-Nov-20
Asphalt Pavement			16	719	05-Nov-20	26-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Interim - Finish STA 1185 to 1205	0	698	19-Nov-20	19-Nov-20
HMA Paving			2	706	05-Nov-20	06-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Place HMA	2	706	05-Nov-20	06-Nov-20
SMA Paving			5	719	20-Nov-20	26-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Place SMA	5	719	20-Nov-20	26-Nov-20
Curb & Gutter			10	706	22-Oct-20	04-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Place Curb & Gutter	10	706	22-Oct-20	04-Nov-20
Permanent Barriers			10	713	23-Nov-20	04-Dec-20
Concrete Barriers			10	713	23-Nov-20	04-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB EXR, Place Conc Rail	10	713	23-Nov-20	04-Dec-20
		Metal Beam Guardrails	10	713	23-Nov-20	04-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install MBGF	10	713	23-Nov-20	04-Dec-20
		Crash Attenuators	5	718	23-Nov-20	27-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Install Attenuator	5	718	23-Nov-20	27-Nov-20
		Signals and Illumination	25	698	23-Nov-20	25-Dec-20
		Roadway Illumination	25	698	23-Nov-20	25-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Illumination Pole Bases	5	698	23-Nov-20	27-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Install Illumination Poles/Fixtures	10	698	30-Nov-20	11-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Illumination Energize Fixtures	10	698	14-Dec-20	25-Dec-20
		Signing and Marking	26	698	20-Nov-20	28-Dec-20
		Overhead Sign Structures	10	713	23-Nov-20	04-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Overhead Signage	10	713	23-Nov-20	04-Dec-20
		Small Signage	10	713	23-Nov-20	04-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Small Signage	10	713	23-Nov-20	04-Dec-20
		Pavement Marking	26	698	20-Nov-20	28-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Permt Markings	2	722	20-Nov-20	23-Nov-20
	TX-3CD	Area 3C2 - SB EXR, Finish STA 1185 to 1205	0	698	28-Dec-20	28-Dec-20
		Landscaping	10	713	23-Nov-20	04-Dec-20
		Seeding & Sodding	10	713	23-Nov-20	04-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Topsoil	10	713	23-Nov-20	04-Dec-20
	TX-3CD	Area 3C2 - SB EXR, Install Seeding/Sodding	10	713	23-Nov-20	04-Dec-20
		ITS/TCS	20	698	22-Oct-20	18-Nov-20
		Duct Bank System	20	698	22-Oct-20	18-Nov-20
	TX-3CD	Area 3C2 - SB EXR, ITS &TCS Civil Work Install Coduit	20	698	22-Oct-20	18-Nov-20
		Southbound Entry Ramp STA 1210 to 1237	118	442	08-Jul-21	21-Dec-21
C3(	TX-3CD	Area 3C2 - SB ENR, Start STA 1210 to 1237	0	442	08-Jul-21	08-Jul-21
		Traffic Control and Temporary Work	6	442	08-Jul-21	15-Jul-21
		Barricades, Signs & Traffic Handling	1	442	15-Jul-21	15-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Move Traffic	1	442	15-Jul-21	15-Jul-21
		Portable Traffic Barrier	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Conc Barrier	5	442	08-Jul-21	14-Jul-21
		Workzone Pavement Marking	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Marking & Signing	5	442	08-Jul-21	14-Jul-21
		Erosion Control	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Erosion Control	5	442	08-Jul-21	14-Jul-21
		Earthwork	41	442	08-Jul-21	02-Sep-21
		Clear & Grub	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Clear and Grub	5	442	08-Jul-21	14-Jul-21
		Excavation	15	442	16-Jul-21	05-Aug-21
	TX-3CD	Area 3C2 - SB ENR, Excavate Cut Areas	15	442	16-Jul-21	05-Aug-21
		Embankment	20	442	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - SB ENR, Place Embankment	20	442	06-Aug-21	02-Sep-21
		Subgrade Treatment and Base	30	442	03-Sep-21	14-Oct-21
		Lime Treatment	20	442	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - SB ENR, Lime Treat Subgrade	20	442	03-Sep-21	30-Sep-21
		Flexbase	10	442	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Flexbase	10	442	01-Oct-21	14-Oct-21
		Pavement	23	466	15-Oct-21	16-Nov-21
(	TX-3CD	Area 3C2 - SB ENR, FF Start STA 1210 to 1237	0	442	15-Nov-21	15-Nov-21
		Asphalt Pavement	13	466	29-Oct-21	16-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Interim - Finish STA 1210 to 1237	0	442	12-Nov-21	12-Nov-21
		HMA Paving	5	447	29-Oct-21	04-Nov-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB ENR, Place HMA	5	447	29-Oct-21	04-Nov-21
	SMA Paving		2	466	15-Nov-21	16-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Place SMA	2	466	15-Nov-21	16-Nov-21
	Curb & Gutter		10	447	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Curb & Gutter	10	447	15-Oct-21	28-Oct-21
	Permanent Barriers		10	457	16-Nov-21	29-Nov-21
	Concrete Barriers		10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Place Conc Rail	10	457	16-Nov-21	29-Nov-21
	Metal Beam Guardrails		10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install MBGF	10	457	16-Nov-21	29-Nov-21
	Signals and Illumination		25	442	16-Nov-21	20-Dec-21
	Roadway Illumination		25	442	16-Nov-21	20-Dec-21
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Pole Bases	5	442	16-Nov-21	22-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Poles/Fixtures	10	442	23-Nov-21	06-Dec-21
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Energize Fixtures	10	442	07-Dec-21	20-Dec-21
	Signing and Marking		26	442	15-Nov-21	21-Dec-21
	Overhead Sign Structures		10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Overhead Signage	10	457	16-Nov-21	29-Nov-21
	Small Signage		10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Small Signage	10	457	16-Nov-21	29-Nov-21
	Pavement Marking		26	442	15-Nov-21	21-Dec-21
	TX-3CD	Area 3C2 - SB ENR, Install Permt Markings	2	466	15-Nov-21	16-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Finish STA 1210 to 1237	0	442	21-Dec-21	21-Dec-21
	Landscaping		10	457	16-Nov-21	29-Nov-21
	Seeding & Sodding		10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Topsoil	10	457	16-Nov-21	29-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Seeding/Sodding	10	457	16-Nov-21	29-Nov-21
	ITS/TCS		20	442	15-Oct-21	11-Nov-21
	Duct Bank System		20	442	15-Oct-21	11-Nov-21
	TX-3CD	Area 3C2 - SB ENR, ITS &TCS Civil Work Install Coduit	20	442	15-Oct-21	11-Nov-21
Southbound U-Turn SH 170 STA 1178			230	330	08-Jul-21	26-May-22
C3(	TX-3CD	Area 3C2 - SB FR U-Turn, Start STA 1178	0	330	08-Jul-21	08-Jul-21
	Traffic Control and Temporary Work		6	462	08-Jul-21	15-Jul-21
	Barricades, Signs & Traffic Handling		1	462	15-Jul-21	15-Jul-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Move Traffic	1	462	15-Jul-21	15-Jul-21
	Portable Traffic Barrier		5	462	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Place Temp Conc Barrier	5	462	08-Jul-21	14-Jul-21
	Workzone Pavement Marking		5	462	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Place Temp Marking & Signing	5	462	08-Jul-21	14-Jul-21
	Erosion Control		5	462	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Place Temp Erosion Control	5	462	08-Jul-21	14-Jul-21
	Earthwork		41	462	08-Jul-21	02-Sep-21
	Clear & Grub		5	462	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Clear and Grub	5	462	08-Jul-21	14-Jul-21
	Excavation		15	462	16-Jul-21	05-Aug-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Excavate Cut Areas	15	462	16-Jul-21	05-Aug-21
	Embankment		20	462	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Place Embankment	20	462	06-Aug-21	02-Sep-21
	Subgrade Treatment and Base		30	462	03-Sep-21	14-Oct-21
	Lime Treatment		20	462	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Lime Treat Subgrade	20	462	03-Sep-21	30-Sep-21
	Flexbase		10	462	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - SB FR U-Turn, Place Flexbase	10	462	01-Oct-21	14-Oct-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Pavement			150	339	15-Oct-21	12-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, FF Start STA 1178	0	330	11-May-22	11-May-22
Asphalt Pavement			140	339	29-Oct-21	12-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, Interim - Finish STA 1178	0	330	10-May-22	10-May-22
HMA Paving			5	462	29-Oct-21	04-Nov-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, Place HMA	5	462	29-Oct-21	04-Nov-21
SMA Paving			2	339	11-May-22	12-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, Place SMA	2	339	11-May-22	12-May-22
Curb & Gutter			10	462	15-Oct-21	28-Oct-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, Place Curb & Gutter	10	462	15-Oct-21	28-Oct-21
3C2 BR 121 SB FR U-Turn			218	330	08-Jul-21	10-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Start	2	330	08-Jul-21	09-Jul-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Finish	0	330	10-May-22	10-May-22
BR Excavation			5	330	13-Jul-21	19-Jul-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Bridge Excavation	5	330	13-Jul-21	19-Jul-21
Drill Shafts			30	355	20-Jul-21	30-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Drill Shafts Abutment 1	5	330	20-Jul-21	26-Jul-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Drill Shafts Bent 2	10	330	27-Jul-21	09-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Drill Shafts Bent 3	10	330	10-Aug-21	23-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Drill Shafts Abutment 4	5	355	24-Aug-21	30-Aug-21
Columns			45	345	27-Jul-21	27-Sep-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Columns Abutment 1	10	380	27-Jul-21	09-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Columns Bent 2	20	350	10-Aug-21	06-Sep-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Columns Bent 3	25	330	24-Aug-21	27-Sep-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Columns Abutment 4	10	355	31-Aug-21	13-Sep-21
Bent Caps			40	330	07-Sep-21	01-Nov-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Cap Bent 2	20	350	07-Sep-21	04-Oct-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Cap Bent 3	25	330	28-Sep-21	01-Nov-21
Beams			85	330	13-Jul-21	08-Nov-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Beam Procurement	20	349	13-Jul-21	09-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Forward Precast Beams Shopdrawings to TxDOT	1	349	10-Aug-21	10-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Precast Beam Fabrication & Delivery Leadtime	40	349	11-Aug-21	05-Oct-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Conc Beams	5	330	02-Nov-21	08-Nov-21
BR Place CTB Embankment			20	460	28-Sep-21	25-Oct-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Place Embankment	20	460	28-Sep-21	25-Oct-21
Abutments			35	355	10-Aug-21	27-Sep-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Abutment 1	10	380	10-Aug-21	23-Aug-21
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Abutment 4	10	355	14-Sep-21	27-Sep-21
Approach Slab			10	330	26-Apr-22	09-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Apprch Slab Abutment 1	10	330	26-Apr-22	09-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Apprch Slab Abutment 4	10	330	26-Apr-22	09-May-22
Exspansion Joint			100	330	09-Nov-21	28-Mar-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Exp Joints	100	330	09-Nov-21	28-Mar-22
Deck			120	330	09-Nov-21	25-Apr-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Deck Slab	100	330	09-Nov-21	28-Mar-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Cure Deck Slab	20	330	29-Mar-22	25-Apr-22
Railings			10	330	26-Apr-22	09-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, BR 121 Install Conc Rail	10	330	26-Apr-22	09-May-22
Permanent Barriers			10	330	12-May-22	25-May-22
Concrete Barriers			10	330	12-May-22	25-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, Place Conc Rail	10	330	12-May-22	25-May-22
Metal Beam Guardrails			10	330	12-May-22	25-May-22
A	TX-3CD	Area 3C2 - SB FR U-Turn, Install MBGF	10	330	12-May-22	25-May-22

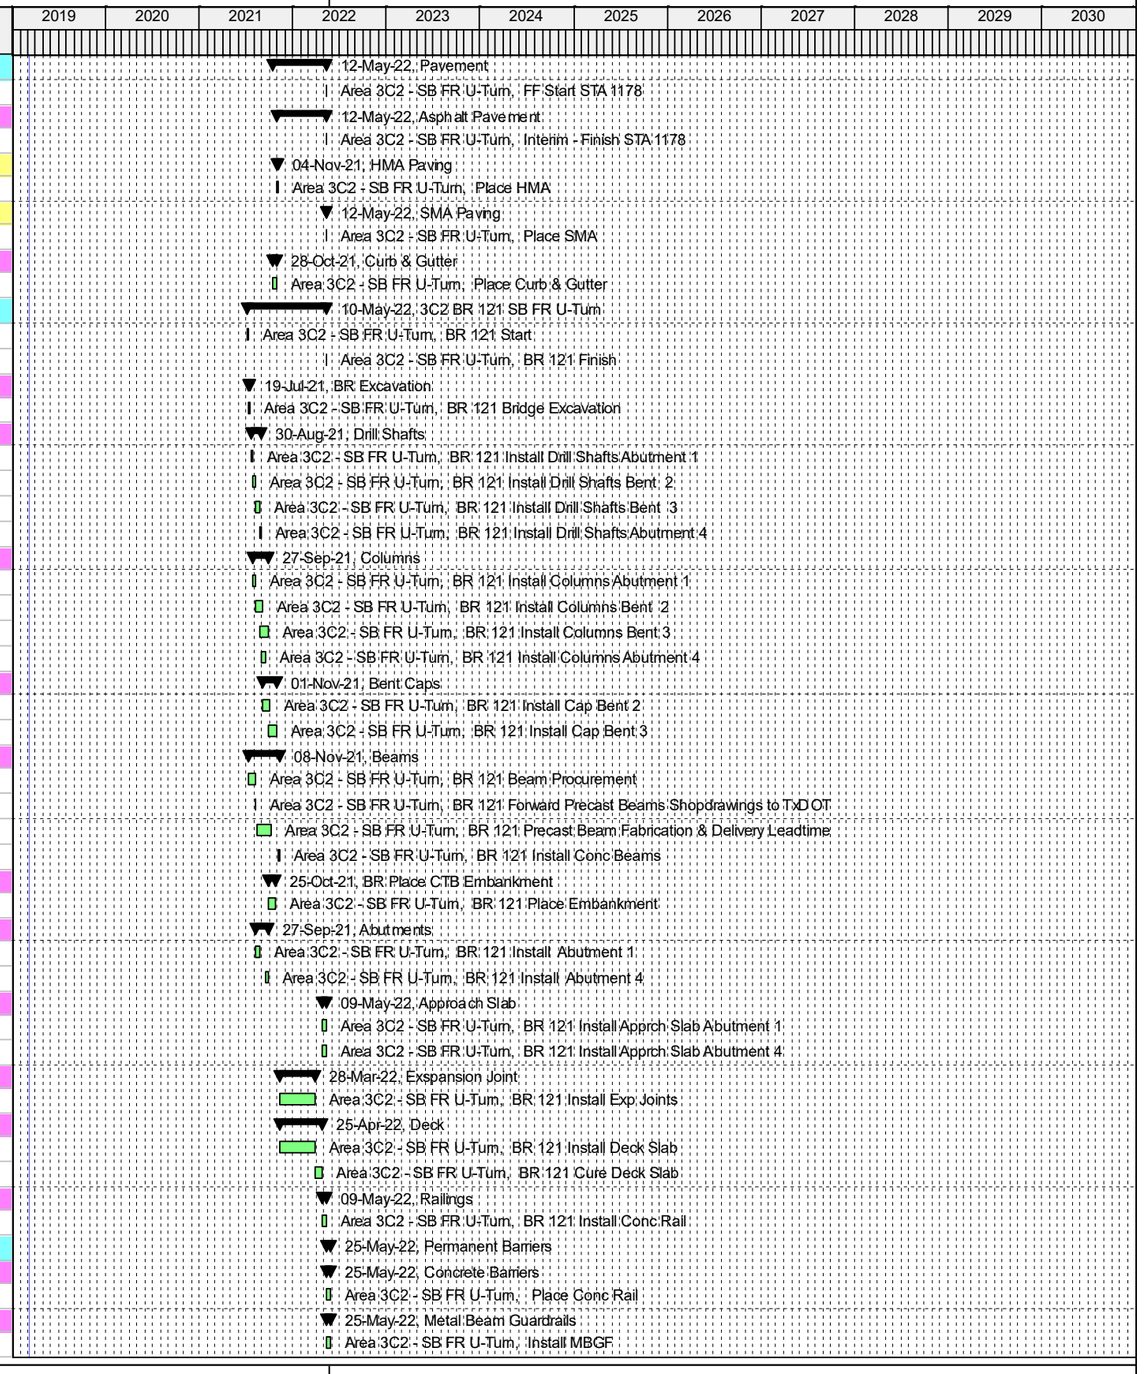

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Signing and Marking	11	330	11-May-22	26-May-22
		Small Signage	10	330	12-May-22	25-May-22
	TX-3CD	Area 3C2 - SB FR U-Turn, Install Small Signage	10	330	12-May-22	25-May-22
		Pavement Marking	11	330	11-May-22	26-May-22
	TX-3CD	Area 3C2 - SB FR U-Turn, Install Permt Markings	2	339	11-May-22	12-May-22
	TX-3CD	Area 3C2 - SB FR U-Turn, Finish STA 1178	0	330	26-May-22	26-May-22
		Southbound Entry Ramp SH 170 DC STA 1180 to 1240	290	270	08-Jul-21	18-Aug-22
C3(	TX-3CD	Area 3C2 - SB ENR, Start STA 1180 to 1240	0	270	08-Jul-21	08-Jul-21
		Traffic Control and Temporary Work	6	442	08-Jul-21	15-Jul-21
		Barricades, Signs & Traffic Handling	1	442	15-Jul-21	15-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Move Traffic	1	442	15-Jul-21	15-Jul-21
		Portable Traffic Barrier	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Conc Barrier	5	442	08-Jul-21	14-Jul-21
		Workzone Pavement Marking	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Marking & Signing	5	442	08-Jul-21	14-Jul-21
		Erosion Control	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Erosion Control	5	442	08-Jul-21	14-Jul-21
		Earthwork	41	442	08-Jul-21	02-Sep-21
		Clear & Grub	5	442	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB ENR, Clear and Grub	5	442	08-Jul-21	14-Jul-21
		Excavation	15	442	16-Jul-21	05-Aug-21
	TX-3CD	Area 3C2 - SB ENR, Excavate Cut Areas	15	442	16-Jul-21	05-Aug-21
		Embankment	20	442	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - SB ENR, Place Embankment	20	442	06-Aug-21	02-Sep-21
		Subgrade Treatment and Base	30	442	03-Sep-21	14-Oct-21
		Lime Treatment	20	442	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - SB ENR, Lime Treat Subgrade	20	442	03-Sep-21	30-Sep-21
		Flexbase	10	442	01-Oct-21	14-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Flexbase	10	442	01-Oct-21	14-Oct-21
		Pavement	195	294	15-Oct-21	14-Jul-22
(	TX-3CD	Area 3C2 - SB ENR, FF Start STA 1180 to 1240	0	270	13-Jul-22	13-Jul-22
		Asphalt Pavement	185	294	29-Oct-21	14-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Interim - Finish STA 1180 to 1240	0	270	12-Jul-22	12-Jul-22
		HMA Paving	5	447	29-Oct-21	04-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Place HMA	5	447	29-Oct-21	04-Nov-21
		SMA Paving	2	294	13-Jul-22	14-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Place SMA	2	294	13-Jul-22	14-Jul-22
		Curb & Gutter	10	447	15-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Curb & Gutter	10	447	15-Oct-21	28-Oct-21
		3C2 BR 123 Direct Connector Ramp SB ENR	263	270	08-Jul-21	12-Jul-22
(	TX-3CD	Area 3C2 - SB ENR, BR 123 Start	2	270	08-Jul-21	09-Jul-21
(	TX-3CD	Area 3C2 - SB ENR, BR 123 Finish	0	270	12-Jul-22	12-Jul-22
		BR Excavation	5	270	13-Jul-21	19-Jul-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Bridge Excavation	5	270	13-Jul-21	19-Jul-21
		Drill Shafts	30	320	20-Jul-21	30-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Drill Shafts Abutment 1	5	270	20-Jul-21	26-Jul-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Drill Shafts Bent 2-6	10	270	27-Jul-21	09-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Drill Shafts Bent 7-11	10	270	10-Aug-21	23-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Drill Shafts Abutment 12	5	320	24-Aug-21	30-Aug-21
		Footings	20	275	10-Aug-21	06-Sep-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Footings Bent 2-6	10	285	10-Aug-21	23-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Footings Bent 7-11	10	270	24-Aug-21	06-Sep-21
		Columns	55	300	27-Jul-21	11-Oct-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Columns Abutment 1	10	345	27-Jul-21	09-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Columns Bent 2-6	20	285	24-Aug-21	20-Sep-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Columns Abutment 12	10	320	31-Aug-21	13-Sep-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Columns Bent 7-11	25	270	07-Sep-21	11-Oct-21
Bent Caps			55	270	21-Sep-21	06-Dec-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Cap Bent 2-6	40	285	21-Sep-21	15-Nov-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Cap Bent 7-11	40	270	12-Oct-21	06-Dec-21
Beams			110	270	13-Jul-21	13-Dec-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Beam Procurement	20	314	13-Jul-21	09-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Forward Precast Beams Shopdrawings to TxDOT	1	314	10-Aug-21	10-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Precast Beam Fabrication & Delivery Leadtime	40	314	11-Aug-21	05-Oct-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Conc Beams	5	270	07-Dec-21	13-Dec-21
BR Place CTB Embankment			20	445	28-Sep-21	25-Oct-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Place Stabilized Backfill	20	445	28-Sep-21	25-Oct-21
Abutments			35	320	10-Aug-21	27-Sep-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Abutment 1	10	345	10-Aug-21	23-Aug-21
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Abutment 12	10	320	14-Sep-21	27-Sep-21
Approach Slab			10	270	28-Jun-22	11-Jul-22
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Apprch Slab Abutment 12	10	270	28-Jun-22	11-Jul-22
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Apprch Slab Abutment 1	10	270	28-Jun-22	11-Jul-22
Exspansion Joint			120	270	14-Dec-21	30-May-22
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Exp Joints	120	270	14-Dec-21	30-May-22
Deck			140	270	14-Dec-21	27-Jun-22
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Deck Slab	120	270	14-Dec-21	30-May-22
	TX-3CD	Area 3C2 - SB ENR, BR 123 Cure Deck Slab	20	270	31-May-22	27-Jun-22
Railings			10	270	28-Jun-22	11-Jul-22
	TX-3CD	Area 3C2 - SB ENR, BR 123 Install Conc Rail	10	270	28-Jun-22	11-Jul-22
Permanent Barriers			10	285	14-Jul-22	27-Jul-22
Concrete Barriers			10	285	14-Jul-22	27-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Place Conc Rail	10	285	14-Jul-22	27-Jul-22
Metal Beam Guardrails			10	285	14-Jul-22	27-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Install MBGF	10	285	14-Jul-22	27-Jul-22
Signals and Illumination			25	270	14-Jul-22	17-Aug-22
Roadway Illumination			25	270	14-Jul-22	17-Aug-22
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Pole Bases	5	270	14-Jul-22	20-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Poles/Fixtures	10	270	21-Jul-22	03-Aug-22
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Energize Fixtures	10	270	04-Aug-22	17-Aug-22
Signing and Marking			26	270	13-Jul-22	18-Aug-22
Overhead Sign Structures			10	285	14-Jul-22	27-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Install Overhead Signage	10	285	14-Jul-22	27-Jul-22
Small Signage			10	285	14-Jul-22	27-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Install Small Signage	10	285	14-Jul-22	27-Jul-22
Pavement Marking			26	270	13-Jul-22	18-Aug-22
	TX-3CD	Area 3C2 - SB ENR, Install Permt Markings	2	294	13-Jul-22	14-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Finish STA 1180 to 1240	0	270	18-Aug-22	18-Aug-22
Landscaping			10	285	14-Jul-22	27-Jul-22
Seeding & Sodding			10	285	14-Jul-22	27-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Install Topsoil	10	285	14-Jul-22	27-Jul-22
	TX-3CD	Area 3C2 - SB ENR, Install Seeding/Sodding	10	285	14-Jul-22	27-Jul-22
ITS/TCS			20	442	15-Oct-21	11-Nov-21
Duct Bank System			20	442	15-Oct-21	11-Nov-21
	TX-3CD	Area 3C2 - SB ENR, ITS &TCS Civil Work Install Coduit	20	442	15-Oct-21	11-Nov-21
Southbound Entry Ramp SH 170 DC STA 1130 to 1180 PH 2			128	360	18-Oct-21	14-Apr-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3(	TX-3CD	Area 3C2 - SB ENR, Start STA 1180 to 1240	0	360	18-Oct-21	18-Oct-21
Traffic Control and Temporary Work			6	360	18-Oct-21	25-Oct-21
Barricades, Signs & Traffic Handling			1	360	25-Oct-21	25-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Move Traffic	1	360	25-Oct-21	25-Oct-21
Portable Traffic Barrier			5	360	18-Oct-21	22-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Conc Barrier	5	360	18-Oct-21	22-Oct-21
Workzone Pavement Marking			5	360	18-Oct-21	22-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Marking & Signing	5	360	18-Oct-21	22-Oct-21
Erosion Control			5	360	18-Oct-21	22-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place Temp Erosion Control	5	360	18-Oct-21	22-Oct-21
Earthwork			41	370	18-Oct-21	13-Dec-21
Clear & Grub			5	360	18-Oct-21	22-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Clear and Grub	5	360	18-Oct-21	22-Oct-21
Excavation			15	360	26-Oct-21	15-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Excavate Cut Areas	15	360	26-Oct-21	15-Nov-21
Embankment			20	370	16-Nov-21	13-Dec-21
	TX-3CD	Area 3C2 - SB ENR, Place Embankment	20	370	16-Nov-21	13-Dec-21
Drainage			40	385	26-Oct-21	20-Dec-21
Storm Sewer			20	385	26-Oct-21	22-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Small RCP	20	385	26-Oct-21	22-Nov-21
Inlets			20	385	23-Nov-21	20-Dec-21
	TX-3CD	Area 3C2 - SB ENR, Install MHs and Inlets	20	385	23-Nov-21	20-Dec-21
Subgrade Treatment and Base			40	360	14-Dec-21	07-Feb-22
Lime Treatment			20	370	14-Dec-21	10-Jan-22
	TX-3CD	Area 3C2 - SB ENR, Lime Treat Subgrade	20	370	14-Dec-21	10-Jan-22
Flexbase			10	360	25-Jan-22	07-Feb-22
	TX-3CD	Area 3C2 - SB ENR, Place Flexbase	10	360	25-Jan-22	07-Feb-22
Pavement			23	384	08-Feb-22	10-Mar-22
(	TX-3CD	Area 3C2 - SB ENR, FF Start STA 1180 to 1240	0	360	09-Mar-22	09-Mar-22
Asphalt Pavement			13	384	22-Feb-22	10-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Interim - Finish STA 1180 to 1240	0	360	08-Mar-22	08-Mar-22
HMA Paving			5	365	22-Feb-22	28-Feb-22
	TX-3CD	Area 3C2 - SB ENR, Place HMA	5	365	22-Feb-22	28-Feb-22
SMA Paving			2	384	09-Mar-22	10-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Place SMA	2	384	09-Mar-22	10-Mar-22
Curb & Gutter			10	365	08-Feb-22	21-Feb-22
	TX-3CD	Area 3C2 - SB ENR, Place Curb & Gutter	10	365	08-Feb-22	21-Feb-22
Retaining Walls			50	360	16-Nov-21	24-Jan-22
Wall RT-3C-V-1B			50	360	16-Nov-21	24-Jan-22
	TX-3CD	Area 3C2 - SB GP, Install Wall Wall RT-3C-V-1B	40	360	16-Nov-21	10-Jan-22
Wall Coping RT-3C-S6			10	360	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-1B	10	360	11-Jan-22	24-Jan-22
Wall RT-3C-V-2B			30	380	16-Nov-21	27-Dec-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-V-2B	20	380	16-Nov-21	13-Dec-21
Wall Coping RT-3C-S7			10	380	14-Dec-21	27-Dec-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-2B	10	380	14-Dec-21	27-Dec-21
Wall RT-3C-V-3B			40	370	16-Nov-21	10-Jan-22
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-V-3B	30	370	16-Nov-21	27-Dec-21
Wall Coping RT-3C-S8			10	370	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-3B	10	370	28-Dec-21	10-Jan-22
Wall RT-3C-V-2AB			30	380	16-Nov-21	27-Dec-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-V-2AB	20	380	16-Nov-21	13-Dec-21
Wall Coping RT-3C-S10			10	380	14-Dec-21	27-Dec-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-2AB	10	380	14-Dec-21	27-Dec-21
Permanent Barriers			10	375	10-Mar-22	23-Mar-22
Concrete Barriers			10	375	10-Mar-22	23-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Place Conc Rail	10	375	10-Mar-22	23-Mar-22
Metal Beam Guardrails			10	375	10-Mar-22	23-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install MBGF	10	375	10-Mar-22	23-Mar-22
Signals and Illumination			26	360	09-Mar-22	13-Apr-22
Roadway Illumination			25	360	10-Mar-22	13-Apr-22
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Pole Bases	5	360	10-Mar-22	16-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Poles/Fixtures	10	360	17-Mar-22	30-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Energize Fixtures	10	360	31-Mar-22	13-Apr-22
High Mast Illumination			15	371	09-Mar-22	29-Mar-22
	TX-3CD	Area 3C2 - NB EXR, Install High Mast Illumination Pole Bases	5	371	09-Mar-22	15-Mar-22
	TX-3CD	Area 3C2 - NB EXR, Install High Mast Illumination Poles/Fixtures	5	371	16-Mar-22	22-Mar-22
	TX-3CD	Area 3C2 - NB EXR,Install High Mast Illumination Energize Fixtures	5	371	23-Mar-22	29-Mar-22
Signing and Marking			26	360	09-Mar-22	14-Apr-22
Overhead Sign Structures			10	375	10-Mar-22	23-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install Overhead Signage	10	375	10-Mar-22	23-Mar-22
Small Signage			10	375	10-Mar-22	23-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install Small Signage	10	375	10-Mar-22	23-Mar-22
Pavement Marking			26	360	09-Mar-22	14-Apr-22
	TX-3CD	Area 3C2 - SB ENR, Install Permt Markings	2	384	09-Mar-22	10-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Finish STA 1180 to 1240	0	360	14-Apr-22	14-Apr-22
Landscaping			10	375	10-Mar-22	23-Mar-22
Seeding & Sodding			10	375	10-Mar-22	23-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install Topsoi	10	375	10-Mar-22	23-Mar-22
	TX-3CD	Area 3C2 - SB ENR, Install Seeding/Sodding	10	375	10-Mar-22	23-Mar-22
ITS/TCS			20	360	08-Feb-22	07-Mar-22
Duct Bank System			20	360	08-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB ENR, ITS &TCS Civil Work Install Coduit	20	360	08-Feb-22	07-Mar-22
Southbound Entry Ramp SBFR to SBML STA 1130 to 1180 PH 1			335	461	12-Aug-20	24-Nov-21
C3(	TX-3CD	Area 3C2 - SB ENR, Start STA 1180 to 1240	0	360	12-Aug-20	12-Aug-20
Traffic Control and Temporary Work			6	567	12-Aug-20	19-Aug-20
Barricades, Signs & Traffic Handling			1	567	19-Aug-20	19-Aug-20
	TX-3CD	Area 3C2 - SB ENR, Move Traffic	1	567	19-Aug-20	19-Aug-20
Portable Traffic Barrier			5	567	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB ENR, Place Temp Conc Barrier	5	567	12-Aug-20	18-Aug-20
Workzone Pavement Marking			5	567	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB ENR, Place Temp Marking & Signing	5	567	12-Aug-20	18-Aug-20
Erosion Control			5	567	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB ENR, Place Temp Erosion Control	5	567	12-Aug-20	18-Aug-20
Earthwork			41	577	12-Aug-20	07-Oct-20
Clear & Grub			5	567	12-Aug-20	18-Aug-20
	TX-3CD	Area 3C2 - SB ENR, Clear and Grub	5	567	12-Aug-20	18-Aug-20
Excavation			15	567	20-Aug-20	09-Sep-20
	TX-3CD	Area 3C2 - SB ENR, Excavate Cut Areas	15	567	20-Aug-20	09-Sep-20
Embankment			20	577	10-Sep-20	07-Oct-20
	TX-3CD	Area 3C2 - SB ENR, Place Embankment	20	577	10-Sep-20	07-Oct-20
Drainage			40	592	20-Aug-20	14-Oct-20
Storm Sewer			20	592	20-Aug-20	16-Sep-20
	TX-3CD	Area 3C2 - SB ENR, Install Small RCP	20	592	20-Aug-20	16-Sep-20
Inlets			20	592	17-Sep-20	14-Oct-20
	TX-3CD	Area 3C2 - SB ENR, Install MHs and Inlets	20	592	17-Sep-20	14-Oct-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Subgrade Treatment and Base			40	567	08-Oct-20	02-Dec-20
Lime Treatment			20	577	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C2 - SB ENR, Lime Treat Subgrade	20	577	08-Oct-20	04-Nov-20
Flexbase			10	567	19-Nov-20	02-Dec-20
	TX-3CD	Area 3C2 - SB ENR, Place Flexbase	10	567	19-Nov-20	02-Dec-20
Pavement			230	485	03-Dec-20	20-Oct-21
(	TX-3CD	Area 3C2 - SB ENR, FF Start STA 1180 to 1240	0	461	19-Oct-21	19-Oct-21
Asphalt Pavement			220	485	17-Dec-20	20-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Interim - Finish STA 1180 to 1240	0	360	18-Oct-21	18-Oct-21
HMA Paving			5	572	17-Dec-20	23-Dec-20
	TX-3CD	Area 3C2 - SB ENR, Place HMA	5	572	17-Dec-20	23-Dec-20
SMA Paving			2	485	19-Oct-21	20-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Place SMA	2	485	19-Oct-21	20-Oct-21
Curb & Gutter			10	572	03-Dec-20	16-Dec-20
	TX-3CD	Area 3C2 - SB ENR, Place Curb & Gutter	10	572	03-Dec-20	16-Dec-20
Retaining Walls			50	567	10-Sep-20	18-Nov-20
Wall RT-3C-V-1B			50	567	10-Sep-20	18-Nov-20
	TX-3CD	Area 3C2 - SB GP, Install Wall Wall RT-3C-V-1B	40	567	10-Sep-20	04-Nov-20
Wall Coping RT-3C-S6			10	567	05-Nov-20	18-Nov-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-1B	10	567	05-Nov-20	18-Nov-20
Wall RT-3C-V-2B			30	587	10-Sep-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-V-2B	20	587	10-Sep-20	07-Oct-20
Wall Coping RT-3C-S7			10	587	08-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-2B	10	587	08-Oct-20	21-Oct-20
Wall RT-3C-V-3B			40	577	10-Sep-20	04-Nov-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-V-3B	30	577	10-Sep-20	21-Oct-20
Wall Coping RT-3C-S8			10	577	22-Oct-20	04-Nov-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-3B	10	577	22-Oct-20	04-Nov-20
Wall RT-3C-V-2AB			30	587	10-Sep-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-V-2AB	20	587	10-Sep-20	07-Oct-20
Wall Coping RT-3C-S10			10	587	08-Oct-20	21-Oct-20
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-V-2AB	10	587	08-Oct-20	21-Oct-20
3C2 SB ENR BR 115 Braided Ramp			308	360	12-Aug-20	18-Oct-21
(	TX-3CD	Area 3C2 - SB ENR, BR 115 Start	2	360	12-Aug-20	13-Aug-20
(	TX-3CD	Area 3C2 - SB ENR, BR 115 Finish	0	360	18-Oct-21	18-Oct-21
BR Excavation			5	360	17-Aug-20	21-Aug-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Bridge Excavation	5	360	17-Aug-20	21-Aug-20
Drill Shafts			60	425	24-Aug-20	13-Nov-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Drill Shafts Abutment 1	5	360	24-Aug-20	28-Aug-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Drill Shafts Bent 2-3	25	360	31-Aug-20	02-Oct-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Drill Shafts Bent 4-6	25	360	05-Oct-20	06-Nov-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Drill Shafts Abutment 7	5	425	09-Nov-20	13-Nov-20
Footings			35	360	05-Oct-20	20-Nov-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Footings Bent 2-3	10	385	05-Oct-20	16-Oct-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Footings Bent 4-6	10	360	09-Nov-20	20-Nov-20
Columns			90	400	31-Aug-20	01-Jan-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Columns Abutment 1	10	480	31-Aug-20	11-Sep-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Columns Bent 2-3	30	385	19-Oct-20	27-Nov-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Columns Abutment 7	10	425	16-Nov-20	27-Nov-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Columns Bent 4-6	30	360	23-Nov-20	01-Jan-21
Bent Caps			75	360	30-Nov-20	12-Mar-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Cap Bent 2-3	50	385	30-Nov-20	05-Feb-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Cap Bent 4-6	50	360	04-Jan-21	12-Mar-21

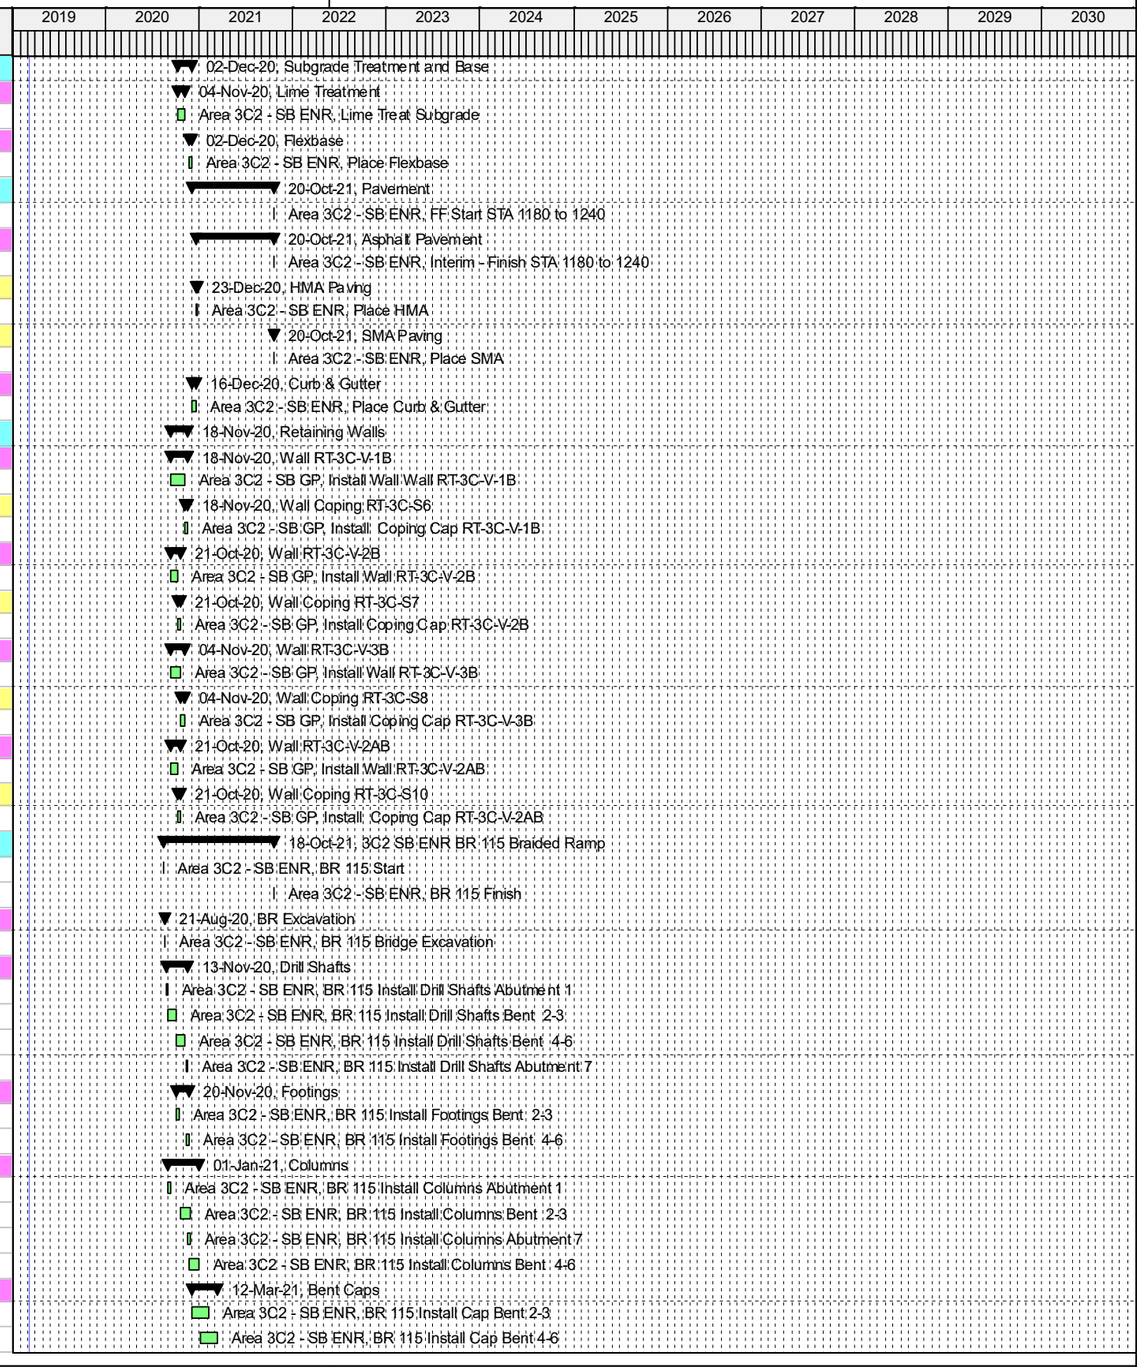

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Beams			155	360	17-Aug-20	19-Mar-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Beam Procurement	20	449	17-Aug-20	11-Sep-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Forward Precast Beams Shopdrawings to TxDOT	1	449	14-Sep-20	14-Sep-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Precast Beam Fabrication & Delivery Leadtime	40	449	15-Sep-20	09-Nov-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Conc Beams	5	360	15-Mar-21	19-Mar-21
BR Place CTB Embankment			20	550	14-Dec-20	08-Jan-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Place Stabilized Backfill	20	550	14-Dec-20	08-Jan-21
Abutments			65	425	14-Sep-20	11-Dec-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Abutment 1	10	480	14-Sep-20	25-Sep-20
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Abutment 7	10	425	30-Nov-20	11-Dec-20
Approach Slab			10	360	04-Oct-21	15-Oct-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Apprch Slab Abutment 7	10	360	04-Oct-21	15-Oct-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Apprch Slab Abutment 1	10	360	04-Oct-21	15-Oct-21
Exspansion Joint			120	360	22-Mar-21	03-Sep-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Exp Joints	120	360	22-Mar-21	03-Sep-21
Deck			140	360	22-Mar-21	01-Oct-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Deck Slab	120	360	22-Mar-21	03-Sep-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Cure Deck Slab	20	360	06-Sep-21	01-Oct-21
Railings			10	360	04-Oct-21	15-Oct-21
	TX-3CD	Area 3C2 - SB ENR, BR 115 Install Conc Rail	10	360	04-Oct-21	15-Oct-21
Permanent Barriers			10	476	20-Oct-21	02-Nov-21
Concrete Barriers			10	476	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Place Conc Rail	10	476	20-Oct-21	02-Nov-21
Metal Beam Guardrails			10	476	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install MBGF	10	476	20-Oct-21	02-Nov-21
Signals and Illumination			26	461	19-Oct-21	23-Nov-21
Roadway Illumination			25	461	20-Oct-21	23-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Pole Bases	5	461	20-Oct-21	26-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Poles/Fixtures	10	461	27-Oct-21	09-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Illumination Energize Fixtures	10	461	10-Nov-21	23-Nov-21
High Mast Illumination			15	472	19-Oct-21	08-Nov-21
	TX-3CD	Area 3C2 - NB EXR, Install High Mast Illumination Pole Bases	5	472	19-Oct-21	25-Oct-21
	TX-3CD	Area 3C2 - NB EXR, Install High Mast Illumination Poles/Fixtures	5	472	26-Oct-21	01-Nov-21
	TX-3CD	Area 3C2 - NB EXR,Install High Mast Illumination Energize Fixtures	5	472	02-Nov-21	08-Nov-21
Signing and Marking			26	461	19-Oct-21	24-Nov-21
Overhead Sign Structures			10	476	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Overhead Signage	10	476	20-Oct-21	02-Nov-21
Small Signage			10	476	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Small Signage	10	476	20-Oct-21	02-Nov-21
Pavement Marking			26	461	19-Oct-21	24-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Permt Markings	2	485	19-Oct-21	20-Oct-21
	TX-3CD	Area 3C2 - SB ENR, Finish STA 1180 to 1240	0	461	24-Nov-21	24-Nov-21
Landscaping			10	476	20-Oct-21	02-Nov-21
Seeding & Sodding			10	476	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Topsoil	10	476	20-Oct-21	02-Nov-21
	TX-3CD	Area 3C2 - SB ENR, Install Seeding/Sodding	10	476	20-Oct-21	02-Nov-21
ITS/TCS			20	567	03-Dec-20	30-Dec-20
Duct Bank System			20	567	03-Dec-20	30-Dec-20
	TX-3CD	Area 3C2 - SB ENR, ITS &TCS Civil Work Install Coduit	20	567	03-Dec-20	30-Dec-20
Southbound Frontage Road Sta-1176 to 1280			188	372	08-Jul-21	29-Mar-22
C3(	TX-3CD	Area 3C2 - SB FR, Start STA 1176 to 1280	0	270	08-Jul-21	08-Jul-21
Traffic Control and Temporary Work			6	372	08-Jul-21	15-Jul-21
Barricades, Signs & Traffic Handling			1	372	15-Jul-21	15-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB FR, Move Traffic	1	372	15-Jul-21	15-Jul-21
Portable Traffic Barrier			5	372	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR, Place Temp Conc Barrier	5	372	08-Jul-21	14-Jul-21
Workzone Pavement Marking			5	372	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR, Place Temp Marking & Signing	5	372	08-Jul-21	14-Jul-21
Erosion Control			5	372	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR, Place Temp Erosion Control	5	372	08-Jul-21	14-Jul-21
Removals & Demo			5	372	08-Jul-21	14-Jul-21
Pavement Removal			5	372	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR, Remove Pavement	5	372	08-Jul-21	14-Jul-21
Earthwork			26	417	08-Jul-21	12-Aug-21
Clear & Grub			5	372	08-Jul-21	14-Jul-21
	TX-3CD	Area 3C2 - SB FR, Clear and Grub	5	372	08-Jul-21	14-Jul-21
Excavation			15	372	16-Jul-21	05-Aug-21
	TX-3CD	Area 3C2 - SB FR, Excavate Cut Areas	15	372	16-Jul-21	05-Aug-21
Embankment			20	417	16-Jul-21	12-Aug-21
	TX-3CD	Area 3C2 - SB FR, Place Embankment	20	417	16-Jul-21	12-Aug-21
Drainage			151	388	06-Aug-21	04-Mar-22
Culverts			20	402	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - SB FR, CLV06 Install Culvert	20	402	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C2 - SB FR, CLV08 Install Culvert	20	402	06-Aug-21	02-Sep-21
Storm Sewer			20	402	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - SB FR, Install Small RCP	20	402	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C2 - SB FR, CLV07 Install Medium RCP	20	402	03-Sep-21	30-Sep-21
Riprap			10	388	21-Feb-22	04-Mar-22
	TX-3CD	Area 3C2 - SB FR, Place RipRap	10	388	21-Feb-22	04-Mar-22
Inlets			20	402	01-Oct-21	28-Oct-21
	TX-3CD	Area 3C2 - SB FR, Install MHs and Inlets	20	402	01-Oct-21	28-Oct-21
Subgrade Treatment and Base			105	372	13-Aug-21	06-Jan-22
Lime Treatment			40	417	13-Aug-21	07-Oct-21
	TX-3CD	Area 3C2 - SB FR, Lime Treat Subgrade	40	417	13-Aug-21	07-Oct-21
Flexbase			20	372	10-Dec-21	06-Jan-22
	TX-3CD	Area 3C2 - SB FR, Place Flexbase	20	372	10-Dec-21	06-Jan-22
Pavement			42	387	07-Jan-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, FF Start STA 1176 to 1280	0	372	21-Feb-22	21-Feb-22
Asphalt Pavement			16	393	04-Feb-22	25-Feb-22
	TX-3CD	Area 3C2 - SB FR, Sec 1 Interim - Finish STA 1176 to 1280	0	372	18-Feb-22	18-Feb-22
HMA Paving			10	372	04-Feb-22	17-Feb-22
	TX-3CD	Area 3C2 - SB FR, Place HMA	10	372	04-Feb-22	17-Feb-22
SMA Paving			5	393	21-Feb-22	25-Feb-22
	TX-3CD	Area 3C2 - SB FR, Place SMA	5	393	21-Feb-22	25-Feb-22
Curb & Gutter			20	372	07-Jan-22	03-Feb-22
	TX-3CD	Area 3C2 - SB FR, Place Curb & Gutter	20	372	07-Jan-22	03-Feb-22
Driveways			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Place Driveways	10	387	22-Feb-22	07-Mar-22
Sidewalks & Median			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Place Sidewalks/Pathways	10	387	22-Feb-22	07-Mar-22
Retaining Walls			90	372	06-Aug-21	09-Dec-21
Wall RT-3C-S6			75	387	06-Aug-21	18-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S6	60	387	06-Aug-21	28-Oct-21
Wall Coping RT-3C-S6			15	387	29-Oct-21	18-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S6	15	387	29-Oct-21	18-Nov-21
Wall RT-3C-S7			75	387	06-Aug-21	18-Nov-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S7	60	387	06-Aug-21	28-Oct-21
Wall Coping RT-3C-S7			15	387	29-Oct-21	18-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S7	15	387	29-Oct-21	18-Nov-21
Wall RT-3C-S8			90	372	06-Aug-21	09-Dec-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S8	75	372	06-Aug-21	18-Nov-21
Wall Coping RT-3C-S8			15	372	19-Nov-21	09-Dec-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S8	15	372	19-Nov-21	09-Dec-21
Wall RT-3C-S10			35	427	06-Aug-21	23-Sep-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S10	20	427	06-Aug-21	02-Sep-21
Wall Coping RT-3C-S10			15	427	03-Sep-21	23-Sep-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S10	15	427	03-Sep-21	23-Sep-21
Wall RT-3C-S5			77	385	06-Aug-21	22-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S5	62	385	06-Aug-21	01-Nov-21
Wall Coping RT-3C-S5			15	385	02-Nov-21	22-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S5	15	385	02-Nov-21	22-Nov-21
Wall RT-3C-S9			80	382	06-Aug-21	25-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Wall RT-3C-S9	65	382	06-Aug-21	04-Nov-21
Wall Coping RT-3C-S9			15	382	05-Nov-21	25-Nov-21
	TX-3CD	Area 3C2 - SB GP, Install Coping Cap RT-3C-S9	15	382	05-Nov-21	25-Nov-21
Permanent Barriers			10	387	22-Feb-22	07-Mar-22
Concrete Barriers			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Place Conc Rail	10	387	22-Feb-22	07-Mar-22
Metal Beam Guardrails			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install MBGF	10	387	22-Feb-22	07-Mar-22
Signals and Illumination			26	372	21-Feb-22	28-Mar-22
Roadway Illumination			25	372	22-Feb-22	28-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Illumination Pole Bases	5	372	22-Feb-22	28-Feb-22
	TX-3CD	Area 3C2 - SB FR, Install Illumination Poles/Fixtures	10	372	01-Mar-22	14-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Illumination Energize Fixtures	10	372	15-Mar-22	28-Mar-22
Traffic Signals			10	388	21-Feb-22	04-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Traffic Light Poles/Fixtures	10	388	21-Feb-22	04-Mar-22
Signing and Marking			26	372	21-Feb-22	29-Mar-22
Overhead Sign Structures			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Overhead Signage	10	387	22-Feb-22	07-Mar-22
Small Signage			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Small Signage	10	387	22-Feb-22	07-Mar-22
Pavement Marking			26	372	21-Feb-22	29-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Permt Markings	2	396	21-Feb-22	22-Feb-22
	TX-3CD	Area 3C2 - SB FR, Finish STA 1176 to 1280	0	372	29-Mar-22	29-Mar-22
Landscaping			10	387	22-Feb-22	07-Mar-22
Seeding & Sodding			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Topsoil	10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C2 - SB FR, Install Seeding/Sodding	10	387	22-Feb-22	07-Mar-22
ITS/TCS			20	382	07-Jan-22	03-Feb-22
Duct Bank System			20	382	07-Jan-22	03-Feb-22
	TX-3CD	Area 3C2 - SB FR, ITS &TCS Civil Work Install Coduit	20	382	07-Jan-22	03-Feb-22
3C3 - Golden Triangle Blvd to N. Tarant Pkwy Sta 1280 to 1401			494	346	09-Sep-20	02-Aug-22
Northbound Frontage Road Sta 1280 to 1401			208	372	10-Jun-21	29-Mar-22
C3(	TX-3CD	Area 3C3 - NB FR, Start STA 1280 to 1401	0	372	10-Jun-21	10-Jun-21
Traffic Control and Temporary Work			11	372	10-Jun-21	24-Jun-21
Barricades, Signs & Traffic Handling			1	372	24-Jun-21	24-Jun-21
	TX-3CD	Area 3C3 - NB FR, Move Traffic	1	372	24-Jun-21	24-Jun-21
Portable Traffic Barrier			10	372	10-Jun-21	23-Jun-21

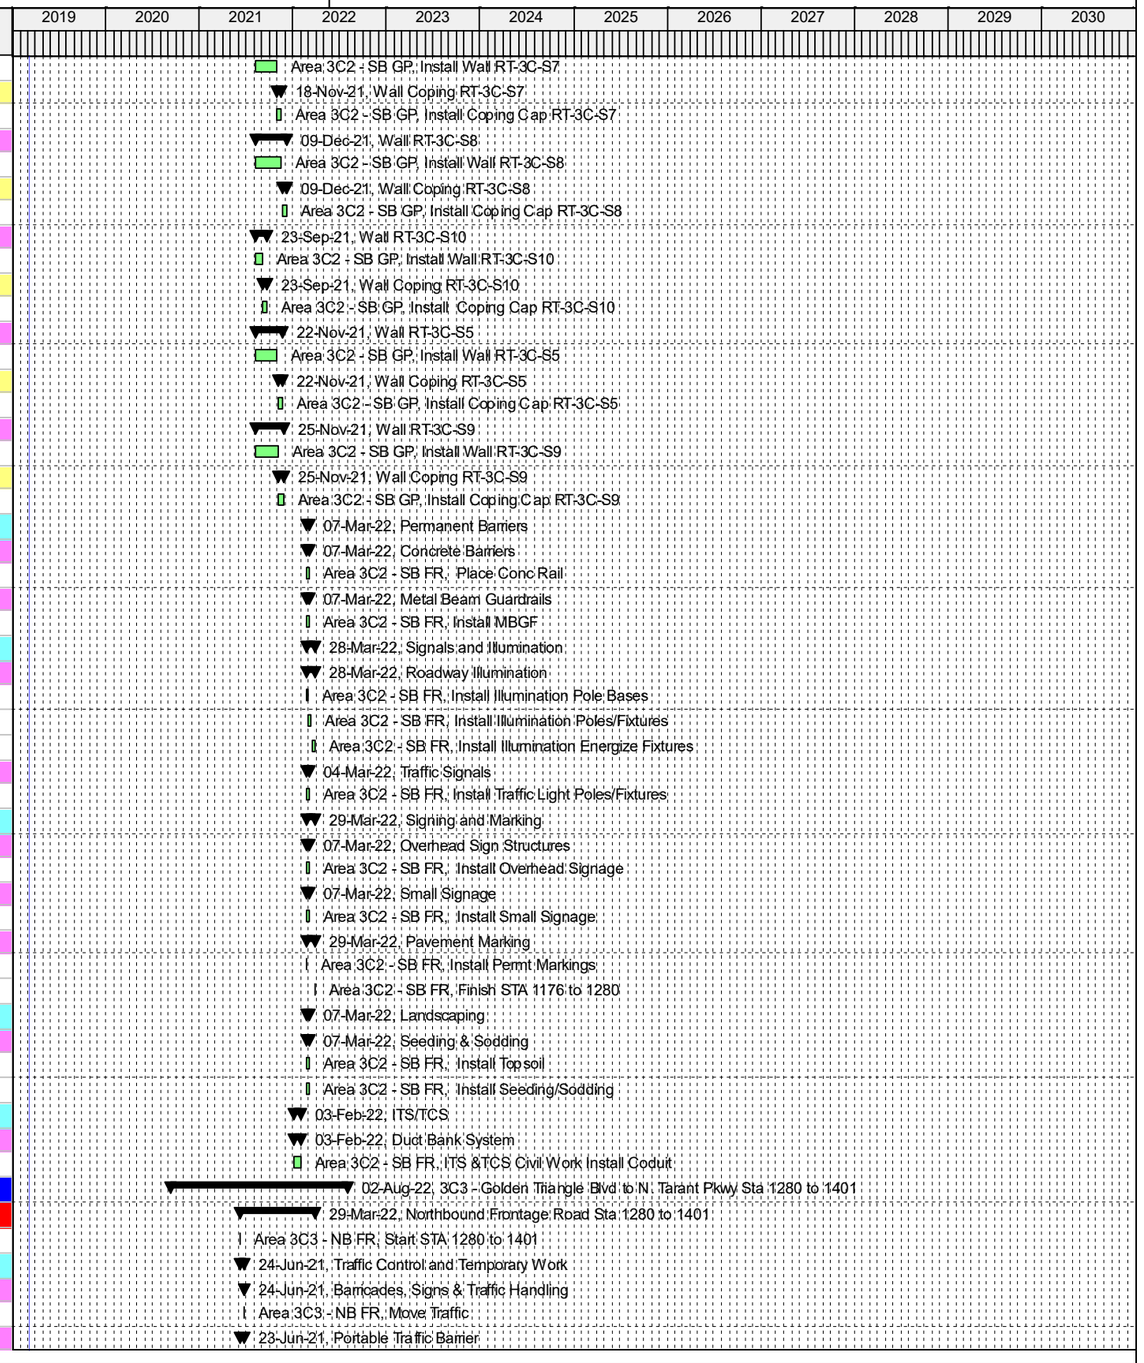

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - NB FR, Place Temp Conc Barrier	10	372	10-Jun-21	23-Jun-21
Workzone Pavement Marking			10	372	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB FR, Place Temp Marking & Signing	10	372	10-Jun-21	23-Jun-21
Erosion Control			5	377	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB FR, Place Temp Erosion Control	5	377	10-Jun-21	16-Jun-21
Removals & Demo			10	372	10-Jun-21	23-Jun-21
Pavement Removal			10	372	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB FR, Remove Pavement	10	372	10-Jun-21	23-Jun-21
Earthwork			71	372	10-Jun-21	16-Sep-21
Clear & Grub			10	372	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB FR, Clear and Grub	10	372	10-Jun-21	23-Jun-21
Excavation			30	372	25-Jun-21	05-Aug-21
	TX-3CD	Area 3C3 - NB FR, Excavate Cut Areas	30	372	25-Jun-21	05-Aug-21
Embankment			30	372	06-Aug-21	16-Sep-21
	TX-3CD	Area 3C3 - NB FR, Place Embankment	30	372	06-Aug-21	16-Sep-21
Drainage			151	388	06-Aug-21	04-Mar-22
Culverts			20	402	06-Aug-21	02-Sep-21
	TX-3CD	Area 3C3 - NB FR, CLV 10B Install Culvert	20	402	06-Aug-21	02-Sep-21
Storm Sewer			20	402	03-Sep-21	30-Sep-21
	TX-3CD	Area 3C3 - NB FR, Install Small RCP	20	402	03-Sep-21	30-Sep-21
Riprap			10	388	21-Feb-22	04-Mar-22
	TX-3CD	Area 3C3 - NB FR, Place RipRap	10	388	21-Feb-22	04-Mar-22
Inlets			20	402	01-Oct-21	28-Oct-21
	TX-3CD	Area 3C3 - NB FR, Install MHs and Inlets	20	402	01-Oct-21	28-Oct-21
Subgrade Treatment and Base			80	372	17-Sep-21	06-Jan-22
Lime Treatment			60	372	17-Sep-21	09-Dec-21
	TX-3CD	Area 3C3 - NB FR, Lime Treat Subgrade	60	372	17-Sep-21	09-Dec-21
Flexbase			20	372	10-Dec-21	06-Jan-22
	TX-3CD	Area 3C3 - NB FR, Place Flexbase	20	372	10-Dec-21	06-Jan-22
Pavement			52	377	07-Jan-22	21-Mar-22
(	TX-3CD	Area 3C3 - NB FR, FF Start STA 1280 to 1401	0	372	21-Feb-22	21-Feb-22
Asphalt Pavement			16	393	04-Feb-22	25-Feb-22
	TX-3CD	Area 3C3 - NB FR, Interim - Finish STA 1280 to 1401	0	372	18-Feb-22	18-Feb-22
HMA Paving			10	372	04-Feb-22	17-Feb-22
	TX-3CD	Area 3C3 - NB FR, Place HMA Paving	10	372	04-Feb-22	17-Feb-22
SMA Paving			5	393	21-Feb-22	25-Feb-22
	TX-3CD	Area 3C3 - NB FR, Place SMA Paving	5	393	21-Feb-22	25-Feb-22
Curb & Gutter			20	372	07-Jan-22	03-Feb-22
	TX-3CD	Area 3C3 - NB FR, Place Curb & Gutter	20	372	07-Jan-22	03-Feb-22
Driveways			20	377	22-Feb-22	21-Mar-22
	TX-3CD	Area 3C3 - NB FR, Place Driveways	20	377	22-Feb-22	21-Mar-22
Sidewalks & Median			20	377	22-Feb-22	21-Mar-22
	TX-3CD	Area 3C3 - NB FR, Place Sidewalks/Pathways	20	377	22-Feb-22	21-Mar-22
Permanent Barriers			10	387	22-Feb-22	07-Mar-22
Concrete Barriers			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C3 - NB FR, Place Conc Rail	10	387	22-Feb-22	07-Mar-22
Metal Beam Guardrails			10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install MBGF	10	387	22-Feb-22	07-Mar-22
Signals and Illumination			26	372	21-Feb-22	28-Mar-22
Roadway Illumination			25	372	22-Feb-22	28-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Illumination Pole Bases	5	372	22-Feb-22	28-Feb-22
	TX-3CD	Area 3C3 - NB FR, Install Illumination Poles/Fixtures	10	372	01-Mar-22	14-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Illumination Energize Fixtures	10	372	15-Mar-22	28-Mar-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Traffic Signals	10	388	21-Feb-22	04-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Traffic Light Poles/Fixtures	10	388	21-Feb-22	04-Mar-22
		Signing and Marking	26	372	21-Feb-22	29-Mar-22
		Overhead Sign Structures	10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Overhead Signage	10	387	22-Feb-22	07-Mar-22
		Small Signage	10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Small Signage	10	387	22-Feb-22	07-Mar-22
		Pavement Marking	26	372	21-Feb-22	29-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Permt Markings	2	396	21-Feb-22	22-Feb-22
	TX-3CD	Area 3C3 - NB FR, Finish STA 1280 to 1401	0	372	29-Mar-22	29-Mar-22
		Landscaping	10	387	22-Feb-22	07-Mar-22
		Seeding & Sodding	10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Topsoil	10	387	22-Feb-22	07-Mar-22
	TX-3CD	Area 3C3 - NB FR, Install Seeding/Sodding	10	387	22-Feb-22	07-Mar-22
		ITS/TCS	20	382	07-Jan-22	03-Feb-22
		Duct Bank System	20	382	07-Jan-22	03-Feb-22
	TX-3CD	Area 3C3 - NB FR, ITS &TCS Civil Work Install Coduit	20	382	07-Jan-22	03-Feb-22
		Northbound Entry Ramp NBFR to NBGP STA 1290 to 1303	103	477	10-Jun-21	02-Nov-21
C3(	TX-3CD	Area 3C3 - NB ENR, Start STA 1290 to 1303	0	477	10-Jun-21	10-Jun-21
		Traffic Control and Temporary Work	6	477	10-Jun-21	17-Jun-21
		Barricades, Signs & Traffic Handling	1	477	17-Jun-21	17-Jun-21
	TX-3CD	Area 3C3 - NB ENR, Move Traffic	1	477	17-Jun-21	17-Jun-21
		Portable Traffic Barrier	5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB ENR, Place Temp Conc Barrier	5	477	10-Jun-21	16-Jun-21
		Workzone Pavement Marking	5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB ENR, Place Temp Marking & Signing	5	477	10-Jun-21	16-Jun-21
		Erosion Control	5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB ENR, Place Temp Erosion Control	5	477	10-Jun-21	16-Jun-21
		Removals & Demo	5	477	10-Jun-21	16-Jun-21
		Pavement Removal	5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB ENR, Pavement Removal	5	477	10-Jun-21	16-Jun-21
		Earthwork	41	477	10-Jun-21	05-Aug-21
		Clear & Grub	5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB ENR, Clear and Grub	5	477	10-Jun-21	16-Jun-21
		Excavation	15	477	18-Jun-21	08-Jul-21
	TX-3CD	Area 3C3 - NB ENR, Excavate Cut Areas	15	477	18-Jun-21	08-Jul-21
		Embankment	20	477	09-Jul-21	05-Aug-21
	TX-3CD	Area 3C3 - NB ENR, Place Embankment	20	477	09-Jul-21	05-Aug-21
		Subgrade Treatment and Base	15	477	06-Aug-21	26-Aug-21
		Lime Treatment	10	477	06-Aug-21	19-Aug-21
	TX-3CD	Area 3C3 - NB ENR, Lime Treat Subgrade	10	477	06-Aug-21	19-Aug-21
		Flexbase	5	477	20-Aug-21	26-Aug-21
	TX-3CD	Area 3C3 - NB ENR, Place Flexbase	5	477	20-Aug-21	26-Aug-21
		Pavement	31	493	27-Aug-21	08-Oct-21
(	TX-3CD	Area 3C3 - NB ENR, FF Start STA 1290 to 1303	0	477	27-Sep-21	27-Sep-21
		Asphalt Pavement	21	493	10-Sep-21	08-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Sec 1 Interim STA 1290 to 1303	0	477	24-Sep-21	24-Sep-21
		HMA Paving	2	485	10-Sep-21	13-Sep-21
	TX-3CD	Area 3C3 - NB ENR, Place HMA	2	485	10-Sep-21	13-Sep-21
		SMA Paving	10	493	27-Sep-21	08-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Place SMA	10	493	27-Sep-21	08-Oct-21
		Curb & Gutter	10	485	27-Aug-21	09-Sep-21
	TX-3CD	Area 3C3 - NB ENR, Place Curb & Gutter	10	485	27-Aug-21	09-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Permanent Barriers			10	492	28-Sep-21	11-Oct-21
Concrete Barriers			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Place Conc Rail	10	492	28-Sep-21	11-Oct-21
Metal Beam Guardrails			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install MBGF	10	492	28-Sep-21	11-Oct-21
Crash Attenuators			5	497	28-Sep-21	04-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Attenuator	5	497	28-Sep-21	04-Oct-21
Signing and Marking			26	477	27-Sep-21	02-Nov-21
Overhead Sign Structures			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Overhead Signage	10	492	28-Sep-21	11-Oct-21
Small Signage			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Small Signage	10	492	28-Sep-21	11-Oct-21
Pavement Marking			26	477	27-Sep-21	02-Nov-21
	TX-3CD	Area 3C3 - NB ENR, Install Permt Markings	2	501	27-Sep-21	28-Sep-21
	TX-3CD	Area 3C3 - NB ENR, Finish STA 1290 to 1303	0	477	02-Nov-21	02-Nov-21
Landscaping			10	492	28-Sep-21	11-Oct-21
Seeding & Sodding			10	19-Fet	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Topsoil	10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Seeding/Sodding	10	492	28-Sep-21	11-Oct-21
ITS/TCS			20	477	27-Aug-21	23-Sep-21
Duct Bank System			20	477	27-Aug-21	23-Sep-21
	TX-3CD	Area 3C3 - NB ENR, ITS &TCS Civil Work Install Coduit	20	477	27-Aug-21	23-Sep-21
Signals and Illumination			25	477	28-Sep-21	01-Nov-21
Roadway Illumination			25	477	28-Sep-21	01-Nov-21
	TX-3CD	Area 3C3 - NB ENR, Install Illumination Pole Bases	5	477	28-Sep-21	04-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Illumination Poles/Fixtures	10	477	05-Oct-21	18-Oct-21
	TX-3CD	Area 3C3 - NB ENR, Install Illumination Energize Fixtures	10	477	19-Oct-21	01-Nov-21
Northbound Exit Ramp NBGP to NBFR STA 1322 to 1340			103	477	10-Jun-21	02-Nov-21
C3(	TX-3CD	Area 3C3 - NB EXR, Start STA 1322 to 1340	0	477	10-Jun-21	10-Jun-21
Traffic Control and Temporary Work			6	477	10-Jun-21	17-Jun-21
Barricades, Signs & Traffic Handling			1	477	17-Jun-21	17-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Move Traffic	1	477	17-Jun-21	17-Jun-21
Portable Traffic Barrier			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Place Temp Conc Barrier	5	477	10-Jun-21	16-Jun-21
Workzone Pavement Marking			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Place Temp Marking & Signing	5	477	10-Jun-21	16-Jun-21
Erosion Control			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Place Temp Erosion Control	5	477	10-Jun-21	16-Jun-21
Removals & Demo			5	477	10-Jun-21	16-Jun-21
Pavement Removal			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Pavement Removal	5	477	10-Jun-21	16-Jun-21
Earthwork			41	477	10-Jun-21	05-Aug-21
Clear & Grub			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Clear and Grub	5	477	10-Jun-21	16-Jun-21
Excavation			15	477	18-Jun-21	08-Jul-21
	TX-3CD	Area 3C3 - NB EXR, Excavate Cut Areas	15	477	18-Jun-21	08-Jul-21
Embankment			20	477	09-Jul-21	05-Aug-21
	TX-3CD	Area 3C3 - NB EXR, Place Embankment	20	477	09-Jul-21	05-Aug-21
Subgrade Treatment and Base			15	477	06-Aug-21	26-Aug-21
Lime Treatment			10	477	06-Aug-21	19-Aug-21
	TX-3CD	Area 3C3 - NB EXR, Lime Treat Subgrade	10	477	06-Aug-21	19-Aug-21
Flexbase			5	477	20-Aug-21	26-Aug-21
	TX-3CD	Area 3C3 - NB EXR, Place Flexbase	5	477	20-Aug-21	26-Aug-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Pavement			31	493	27-Aug-21	08-Oct-21
(	TX-3CD	Area 3C3 - NB EXR, FF Start STA 1322 to 1340	0	477	27-Sep-21	27-Sep-21
Asphalt Pavement			21	493	10-Sep-21	08-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Sec 1 Interim STA 1322 to 1340	0	477	24-Sep-21	24-Sep-21
HMA Paving			2	485	10-Sep-21	13-Sep-21
	TX-3CD	Area 3C3 - NB EXR, Place HMA	2	485	10-Sep-21	13-Sep-21
SMA Paving			10	493	27-Sep-21	08-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Place SMA	10	493	27-Sep-21	08-Oct-21
Curb & Gutter			10	485	27-Aug-21	09-Sep-21
	TX-3CD	Area 3C3 - NB EXR, Place Curb & Gutter	10	485	27-Aug-21	09-Sep-21
Permanent Barriers			10	492	28-Sep-21	11-Oct-21
Concrete Barriers			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Place Conc Rail	10	492	28-Sep-21	11-Oct-21
Metal Beam Guardrails			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install MBGF	10	492	28-Sep-21	11-Oct-21
Crash Attenuators			5	497	28-Sep-21	04-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Attenuator	5	497	28-Sep-21	04-Oct-21
Signals and Illumination			25	477	28-Sep-21	01-Nov-21
Roadway Illumination			25	477	28-Sep-21	01-Nov-21
	TX-3CD	Area 3C3 - NB EXR, Install Illumination Pole Bases	5	477	28-Sep-21	04-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Illumination Poles/Fixtures	10	477	05-Oct-21	18-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Illumination Energize Fixtures	10	477	19-Oct-21	01-Nov-21
Signing and Marking			26	477	27-Sep-21	02-Nov-21
Overhead Sign Structures			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Overhead Signage	10	492	28-Sep-21	11-Oct-21
Small Signage			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Small Signage	10	492	28-Sep-21	11-Oct-21
Pavement Marking			26	477	27-Sep-21	02-Nov-21
	TX-3CD	Area 3C3 - NB EXR, Install Permt Markings	2	501	27-Sep-21	28-Sep-21
	TX-3CD	Area 3C3 - NB EXR, Finish STA 1322 to 1340	0	477	02-Nov-21	02-Nov-21
Landscaping			10	492	28-Sep-21	11-Oct-21
Seeding & Sodding			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Topsoil	10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Seeding/Sodding	10	492	28-Sep-21	11-Oct-21
ITS/TCS			20	477	27-Aug-21	23-Sep-21
Duct Bank System			20	477	27-Aug-21	23-Sep-21
	TX-3CD	Area 3C3 - NB EXR, ITS &TCS Civil Work Install Coduit	20	477	27-Aug-21	23-Sep-21
Northbound Exit Ramp NBGP to NBFR STA 1383 to 1397			103	477	10-Jun-21	02-Nov-21
C3(	TX-3CD	Area 3C3 - NB EXR, Start STA 1383 to 1397	0	477	10-Jun-21	10-Jun-21
Traffic Control and Temporary Work			6	477	10-Jun-21	17-Jun-21
Barricades, Signs & Traffic Handling			1	477	17-Jun-21	17-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Move Traffic	1	477	17-Jun-21	17-Jun-21
Portable Traffic Barrier			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Place Temp Conc Barrier	5	477	10-Jun-21	16-Jun-21
Workzone Pavement Marking			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Place Temp Marking & Signing	5	477	10-Jun-21	16-Jun-21
Erosion Control			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Place Temp Erosion Control	5	477	10-Jun-21	16-Jun-21
Removals & Demo			5	477	10-Jun-21	16-Jun-21
Pavement Removal			5	477	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB EXR, Clear and Grub	5	477	10-Jun-21	16-Jun-21
Earthwork			41	477	10-Jun-21	05-Aug-21
Clear & Grub			5	477	10-Jun-21	16-Jun-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - NB EXR, Clear and Grub	5	477	10-Jun-21	16-Jun-21
Excavation			15	477	18-Jun-21	08-Jul-21
	TX-3CD	Area 3C3 - NB EXR, Excavate Cut Areas	15	477	18-Jun-21	08-Jul-21
Embankment			20	477	09-Jul-21	05-Aug-21
	TX-3CD	Area 3C3 - NB EXR, Place Embankment	20	477	09-Jul-21	05-Aug-21
Subgrade Treatment and Base			15	477	06-Aug-21	26-Aug-21
Lime Treatment			10	477	06-Aug-21	19-Aug-21
	TX-3CD	Area 3C3 - NB EXR, Lime Treat Subgrade	10	477	06-Aug-21	19-Aug-21
Flexbase			5	477	20-Aug-21	26-Aug-21
	TX-3CD	Area 3C3 - NB EXR, Place Flexbase	5	477	20-Aug-21	26-Aug-21
Pavement			26	498	27-Aug-21	01-Oct-21
(	TX-3CD	Area 3C3 - NB EXR, FF Start STA 1383 to 1397	0	477	27-Sep-21	27-Sep-21
Asphalt Pavement			16	498	10-Sep-21	01-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Interim Finish STA 1383 to 1397	0	477	24-Sep-21	24-Sep-21
HMA Paving			5	482	10-Sep-21	16-Sep-21
	TX-3CD	Area 3C3 - NB EXR, Place HMA	5	482	10-Sep-21	16-Sep-21
SMA Paving			5	498	27-Sep-21	01-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Place SMA	5	498	27-Sep-21	01-Oct-21
Curb & Gutter			10	482	27-Aug-21	09-Sep-21
	TX-3CD	Area 3C3 - NB EXR, Place Curb & Gutter	10	482	27-Aug-21	09-Sep-21
Permanent Barriers			10	492	28-Sep-21	11-Oct-21
Concrete Barriers			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Place Conc Rail	10	492	28-Sep-21	11-Oct-21
Metal Beam Guardrails			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install MBGF	10	492	28-Sep-21	11-Oct-21
Signals and Illumination			25	477	28-Sep-21	01-Nov-21
Roadway Illumination			25	477	28-Sep-21	01-Nov-21
	TX-3CD	Area 3C3 - NB EXR, Install Illumination Pole Bases	5	477	28-Sep-21	04-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Illumination Poles/Fixtures	10	477	05-Oct-21	18-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Illumination Energize Fixtures	10	477	19-Oct-21	01-Nov-21
Signing and Marking			26	477	27-Sep-21	02-Nov-21
Overhead Sign Structures			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Overhead Signage	10	492	28-Sep-21	11-Oct-21
Small Signage			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Small Signage	10	492	28-Sep-21	11-Oct-21
Pavement Marking			26	477	27-Sep-21	02-Nov-21
	TX-3CD	Area 3C3 - NB EXR, Install Permt Markings	2	501	27-Sep-21	28-Sep-21
	TX-3CD	Area 3C3 - NB EXR, Finish STA 1383 to 1397	0	477	02-Nov-21	02-Nov-21
Landscaping			10	492	28-Sep-21	11-Oct-21
Seeding & Sodding			10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Topsoil	10	492	28-Sep-21	11-Oct-21
	TX-3CD	Area 3C3 - NB EXR, Install Seeding/Sodding	10	492	28-Sep-21	11-Oct-21
ITS/TCS			20	477	27-Aug-21	23-Sep-21
Duct Bank System			20	477	27-Aug-21	23-Sep-21
	TX-3CD	Area 3C3 - NB EXR, ITS &TCS Civil Work Install Coduit	20	477	27-Aug-21	23-Sep-21
Northbound GP Sta 1280 to 1401			223	553	09-Sep-20	19-Jul-21
C3(	TX-3CD	Area 3C3 - NB GP, Start STA 1280 to 1401	0	362	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			11	362	09-Sep-20	23-Sep-20
Barricades, Signs & Traffic Handling			1	362	23-Sep-20	23-Sep-20
	TX-3CD	Area 3C3 - NB GP, Move Traffic	1	362	23-Sep-20	23-Sep-20
Portable Traffic Barrier			10	362	09-Sep-20	22-Sep-20
	TX-3CD	Area 3C3 - NB GP, Place Temp Conc Barrier	10	362	09-Sep-20	22-Sep-20
Workzone Pavement Marking			10	362	09-Sep-20	22-Sep-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - NB GP, Place Temp Marking & Signing	10	362	09-Sep-20	22-Sep-20
Erosion Control			5	367	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB GP, Place Temp Erosion Control	5	367	09-Sep-20	15-Sep-20
Removals & Demo			10	362	09-Sep-20	22-Sep-20
Pavement Removal			10	362	09-Sep-20	22-Sep-20
	TX-3CD	Area 3C3 - NB GP, Remove Pavement	10	362	09-Sep-20	22-Sep-20
Earthwork			56	402	09-Sep-20	25-Nov-20
Clear & Grub			5	367	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB GP, Clear and Grub	5	367	09-Sep-20	15-Sep-20
Excavation			25	362	24-Sep-20	28-Oct-20
	TX-3CD	Area 3C3 - NB GP, Excavate Cut Areas	25	362	24-Sep-20	28-Oct-20
Embankment			20	402	29-Oct-20	25-Nov-20
	TX-3CD	Area 3C3 - NB GP, Place Embankment,	20	402	29-Oct-20	25-Nov-20
Drainage			172	568	29-Oct-20	25-Jun-21
Culverts			20	422	29-Oct-20	25-Nov-20
	TX-3CD	Area 3C3 - NB GP, CLV 11 Install Culvert	20	422	29-Oct-20	25-Nov-20
	TX-3CD	Area 3C3 - NB GP, CLV 10B Install Culvert	20	422	29-Oct-20	25-Nov-20
Storm Sewer			20	422	26-Nov-20	23-Dec-20
	TX-3CD	Area 3C3 - NB GP, Install Small RCP	20	422	26-Nov-20	23-Dec-20
Riprap			10	568	14-Jun-21	25-Jun-21
	TX-3CD	Area 3C3 - NB GP, Place RipRap	10	568	14-Jun-21	25-Jun-21
Inlets			20	422	24-Dec-20	20-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install MHs and Inlets	20	422	24-Dec-20	20-Jan-21
Subgrade Treatment and Base			120	362	26-Nov-20	12-May-21
Lime Treatment			60	402	26-Nov-20	17-Feb-21
	TX-3CD	Area 3C3 - NB GP, Lime Treat Subgrade	60	402	26-Nov-20	17-Feb-21
Flexbase			20	362	15-Apr-21	12-May-21
	TX-3CD	Area 3C3 - NB GP, Place Flexbase	20	362	15-Apr-21	12-May-21
Pavement			28	572	13-May-21	21-Jun-21
(	TX-3CD	Area 3C3 - NB GP, FF Start STA 1280 to 1401	0	553	11-Jun-21	11-Jun-21
Asphalt Pavement			28	572	13-May-21	21-Jun-21
	TX-3CD	Area 3C3 - NB GP, Interim - Finish STA 1280 to 1401	0	362	10-Jun-21	10-Jun-21
HMA Paving			10	372	13-May-21	26-May-21
	TX-3CD	Area 3C3 - NB GP, Place HMA	10	372	13-May-21	26-May-21
SMA Paving			7	572	11-Jun-21	21-Jun-21
	TX-3CD	Area 3C3 - NB GP, Place SMA	7	572	11-Jun-21	21-Jun-21
Retaining Walls			120	362	29-Oct-20	14-Apr-21
Wall RT-3C-N13			50	432	29-Oct-20	06-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N13	30	432	29-Oct-20	09-Dec-20
Wall Coping RT-3C-N13			20	432	10-Dec-20	06-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N13 Coping Cap	20	432	10-Dec-20	06-Jan-21
Wall RT-3C-N14			30	452	29-Oct-20	09-Dec-20
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N14	20	452	29-Oct-20	25-Nov-20
Wall Coping RT-3C-N14			10	452	26-Nov-20	09-Dec-20
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N14 Coping Cap	10	452	26-Nov-20	09-Dec-20
Wall RT-3C-N15			45	437	29-Oct-20	30-Dec-20
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N15	25	437	29-Oct-20	02-Dec-20
Wall Coping RT-3C-N15			20	437	03-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N15 Coping Cap	20	437	03-Dec-20	30-Dec-20
Wall RT-3C-N16			120	362	29-Oct-20	14-Apr-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N16	80	362	29-Oct-20	17-Feb-21
Wall Coping RT-3C-N16			40	362	18-Feb-21	14-Apr-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N16 Coping Cap	40	362	18-Feb-21	14-Apr-21

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Wall RT-3C-N17	60	422	29-Oct-20	20-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N17	40	422	29-Oct-20	23-Dec-20
		Wall Coping RT-3C-N17	20	422	24-Dec-20	20-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N17 Coping Cap	20	422	24-Dec-20	20-Jan-21
		Wall RT-3C-N18	80	402	29-Oct-20	17-Feb-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N18	60	402	29-Oct-20	20-Jan-21
		Wall Coping RT-3C-N18	20	402	21-Jan-21	17-Feb-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N18 Coping Cap	20	402	21-Jan-21	17-Feb-21
		Wall RT-3C-N19	105	377	29-Oct-20	24-Mar-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N19	80	377	29-Oct-20	17-Feb-21
		Wall Coping RT-3C-N19	25	377	18-Feb-21	24-Mar-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N19 Coping Cap	25	377	18-Feb-21	24-Mar-21
		Wall RT-3C-N20	105	377	29-Oct-20	24-Mar-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N20	80	377	29-Oct-20	17-Feb-21
		Wall Coping RT-3C-N20	25	377	18-Feb-21	24-Mar-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N20 Coping Cap	25	377	18-Feb-21	24-Mar-21
		Wall RT-3C-N21	50	432	29-Oct-20	06-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install Wall RT-3C-N21	20	432	29-Oct-20	25-Nov-20
		Wall Coping RT-3C-N21	30	432	26-Nov-20	06-Jan-21
	TX-3CD	Area 3C3 - NB GP, Install RT-3C-N21 Coping Cap	30	432	26-Nov-20	06-Jan-21
		Permanent Barriers	10	568	14-Jun-21	25-Jun-21
		Concrete Barriers	10	568	14-Jun-21	25-Jun-21
	TX-3CD	Area 3C3 - NB GP, Place Conc Rail	10	568	14-Jun-21	25-Jun-21
		Metal Beam Guardrails	10	568	14-Jun-21	25-Jun-21
	TX-3CD	Area 3C3 - NB GP, Install MBGF	10	568	14-Jun-21	25-Jun-21
		Signals and Illumination	25	553	14-Jun-21	16-Jul-21
		Roadway Illumination	25	553	14-Jun-21	16-Jul-21
	TX-3CD	Area 3C3 - NB GP, Install Illumination Pole Bases	5	553	14-Jun-21	18-Jun-21
	TX-3CD	Area 3C3 - NB GP, Install Illumination Poles/Fixtures	10	553	21-Jun-21	02-Jul-21
	TX-3CD	Area 3C3 - NB GP, Install Illumination Energize Fixtures	10	553	05-Jul-21	16-Jul-21
		High Mast Illumination	15	563	14-Jun-21	02-Jul-21
	TX-3CD	Area 3C3 - NB GP, Install High Mast Illumination Pole Bases	5	563	14-Jun-21	18-Jun-21
	TX-3CD	Area 3C3 - NB GP, Install High Mast Illumination Poles/Fixtures	5	563	21-Jun-21	25-Jun-21
	TX-3CD	Area 3C3 - NB GP, Install High Mast Illumination Energize Fixtures	5	563	28-Jun-21	02-Jul-21
		Signing and Marking	26	553	11-Jun-21	19-Jul-21
		Overhead Sign Structures	10	568	14-Jun-21	25-Jun-21
	TX-3CD	Area 3C3 - NB GP, Install Overhead Signage	10	568	14-Jun-21	25-Jun-21
		Small Signage	10	568	14-Jun-21	25-Jun-21
	TX-3CD	Area 3C3 - NB GP, Install Small Signage	10	568	14-Jun-21	25-Jun-21
		Pavement Marking	26	553	11-Jun-21	19-Jul-21
	TX-3CD	Area 3C3 - NB GP, Install Permt Markings	2	577	11-Jun-21	14-Jun-21
	TX-3CD	Area 3C3 - NB GP, Finish STA 1280 to 1401	0	553	19-Jul-21	19-Jul-21
		Landscaping	20	558	14-Jun-21	09-Jul-21
		Seeding & Sodding	20	558	14-Jun-21	09-Jul-21
	TX-3CD	Area 3C3 - NB GP, Install Topsoil	20	558	14-Jun-21	09-Jul-21
	TX-3CD	Area 3C3 - NB GP, Install Seeding/Sodding	20	558	14-Jun-21	09-Jul-21
		ITS/TCS	20	362	13-May-21	09-Jun-21
(	TX-3CD	Area 3C3 - NB GP, ITS &TCS Civil Work Install Coduit	20	362	13-May-21	09-Jun-21
		Northbound Exit Ramp NBML to NBFR STA 1334 to 1390	270	506	09-Sep-20	22-Sep-21
C3(	TX-3CD	Area 3C3 - NB ML EXR, Start STA 1334 to 1390	0	506	09-Sep-20	09-Sep-20
		Traffic Control and Temporary Work	6	673	09-Sep-20	16-Sep-20
		Barricades, Signs & Traffic Handling	1	673	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, Move Traffic	1	673	16-Sep-20	16-Sep-20

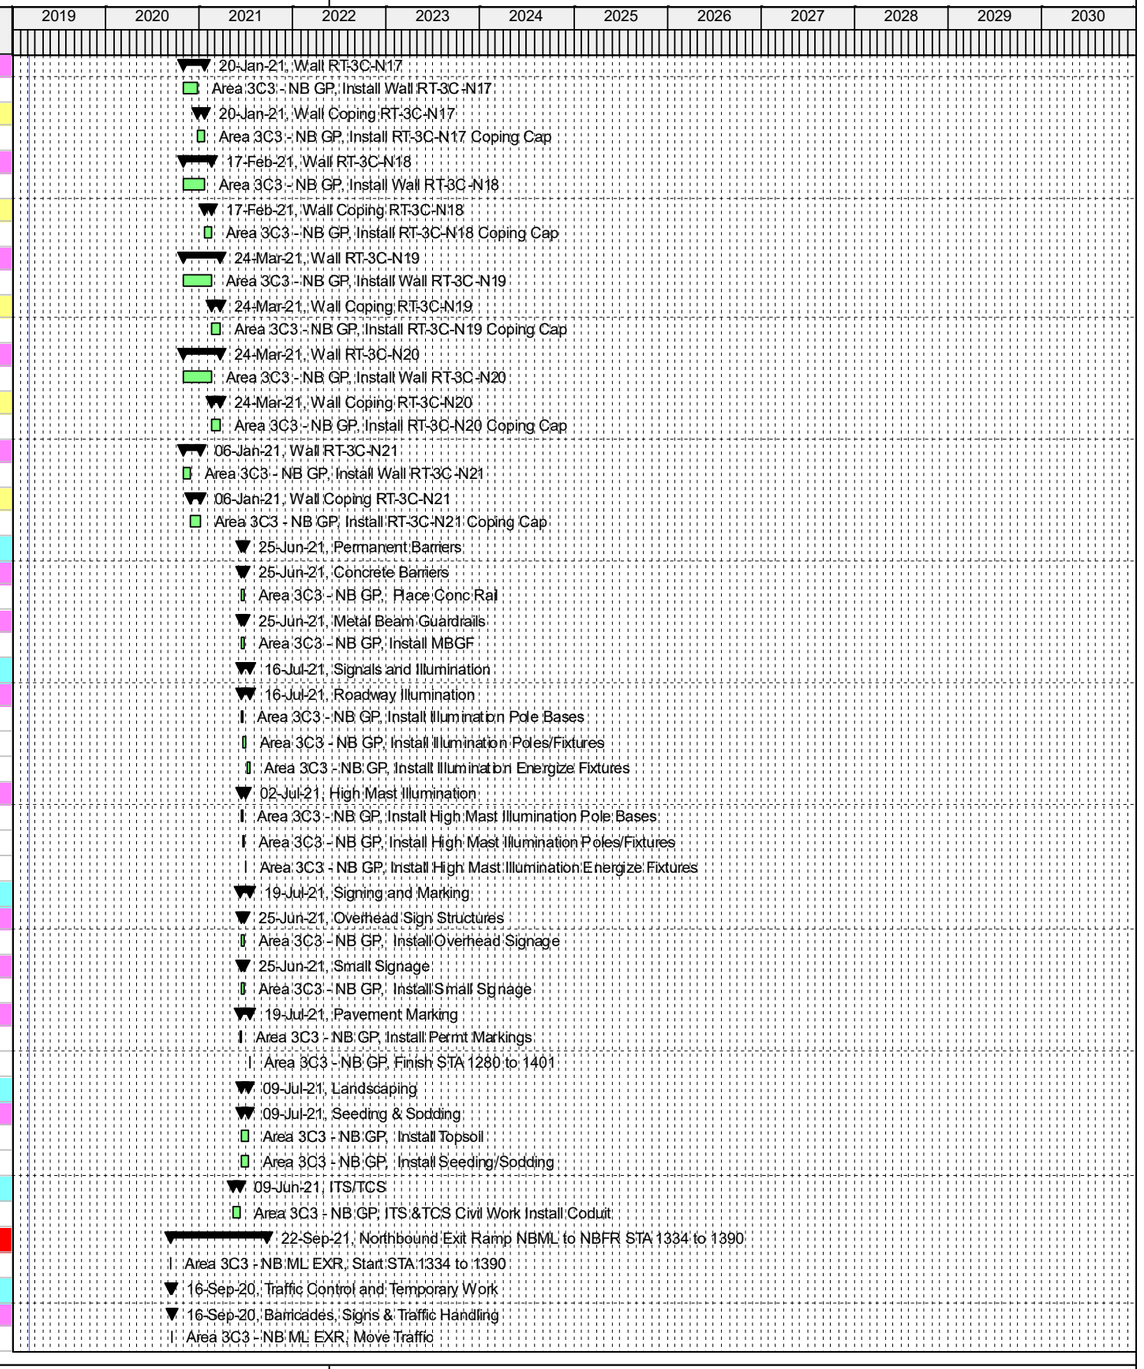

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Portable Traffic Barrier	5	673	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, Place Temp Conc Barrier	5	673	09-Sep-20	15-Sep-20
		Workzone Pavement Marking	5	673	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, Place Temp Marking & Signing	5	673	09-Sep-20	15-Sep-20
		Erosion Control	5	673	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, Place Temp Erosion Control	5	673	09-Sep-20	15-Sep-20
		Removals & Demo	5	673	09-Sep-20	15-Sep-20
		Pavement Removal	5	673	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, Pavement Removal	5	673	09-Sep-20	15-Sep-20
		Earthwork	41	673	09-Sep-20	04-Nov-20
		Clear & Grub	5	673	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, Clear and Grub	5	673	09-Sep-20	15-Sep-20
		Excavation	15	673	17-Sep-20	07-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, Excavate Cut Areas	15	673	17-Sep-20	07-Oct-20
		Embankment	20	673	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, Place Embankment	20	673	08-Oct-20	04-Nov-20
		Subgrade Treatment and Base	15	673	05-Nov-20	25-Nov-20
		Lime Treatment	10	673	05-Nov-20	18-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, Lime Treat Subgrade	10	673	05-Nov-20	18-Nov-20
		Flexbase	5	673	19-Nov-20	25-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, Place Flexbase	5	673	19-Nov-20	25-Nov-20
		Pavement	198	522	26-Nov-20	30-Aug-21
(	TX-3CD	Area 3C3 - NB ML EXR, FF Start STA 1334 to 1390	0	506	17-Aug-21	17-Aug-21
		Asphalt Pavement	188	522	10-Dec-20	30-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Interim - Finish STA 1334 to 1390	0	506	16-Aug-21	16-Aug-21
		HMA Paving	2	681	10-Dec-20	11-Dec-20
	TX-3CD	Area 3C3 - NB ML EXR, Place HMA	2	681	10-Dec-20	11-Dec-20
		SMA Paving	10	522	17-Aug-21	30-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Place SMA	10	522	17-Aug-21	30-Aug-21
		Curb & Gutter	10	681	26-Nov-20	09-Dec-20
	TX-3CD	Area 3C3 - NB ML EXR, Place Curb & Gutter	10	681	26-Nov-20	09-Dec-20
		3C3 BR 113.1 Braided Ramp NB ML EXR	243	506	09-Sep-20	16-Aug-21
(	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Start	2	506	09-Sep-20	10-Sep-20
(	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Finish	0	506	16-Aug-21	16-Aug-21
		BR Excavation	5	506	14-Sep-20	18-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Bridge Excavation	5	506	14-Sep-20	18-Sep-20
		Drill Shafts	30	556	21-Sep-20	30-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Drill Shafts Abutment 1	5	506	21-Sep-20	25-Sep-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Drill Shafts Bent 2-3	10	506	28-Sep-20	09-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Drill Shafts Bent 4-5	10	506	12-Oct-20	23-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Drill Shafts Abutment 6	5	556	26-Oct-20	30-Oct-20
		Footings	20	511	12-Oct-20	06-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Footings Bent 2-3	10	521	12-Oct-20	23-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Footings Bent 4-5	10	506	26-Oct-20	06-Nov-20
		Columns	55	536	28-Sep-20	11-Dec-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Columns Abutment 1	10	581	28-Sep-20	09-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Columns Bent 2-3	20	521	26-Oct-20	20-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Columns Abutment 6	10	556	02-Nov-20	13-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Columns Bent 4-5	25	506	09-Nov-20	11-Dec-20
		Bent Caps	55	506	23-Nov-20	05-Feb-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Cap Bent 2-3	40	521	23-Nov-20	15-Jan-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Cap Bent 4-5	40	506	14-Dec-20	05-Feb-21
		Beams	110	506	14-Sep-20	12-Feb-21

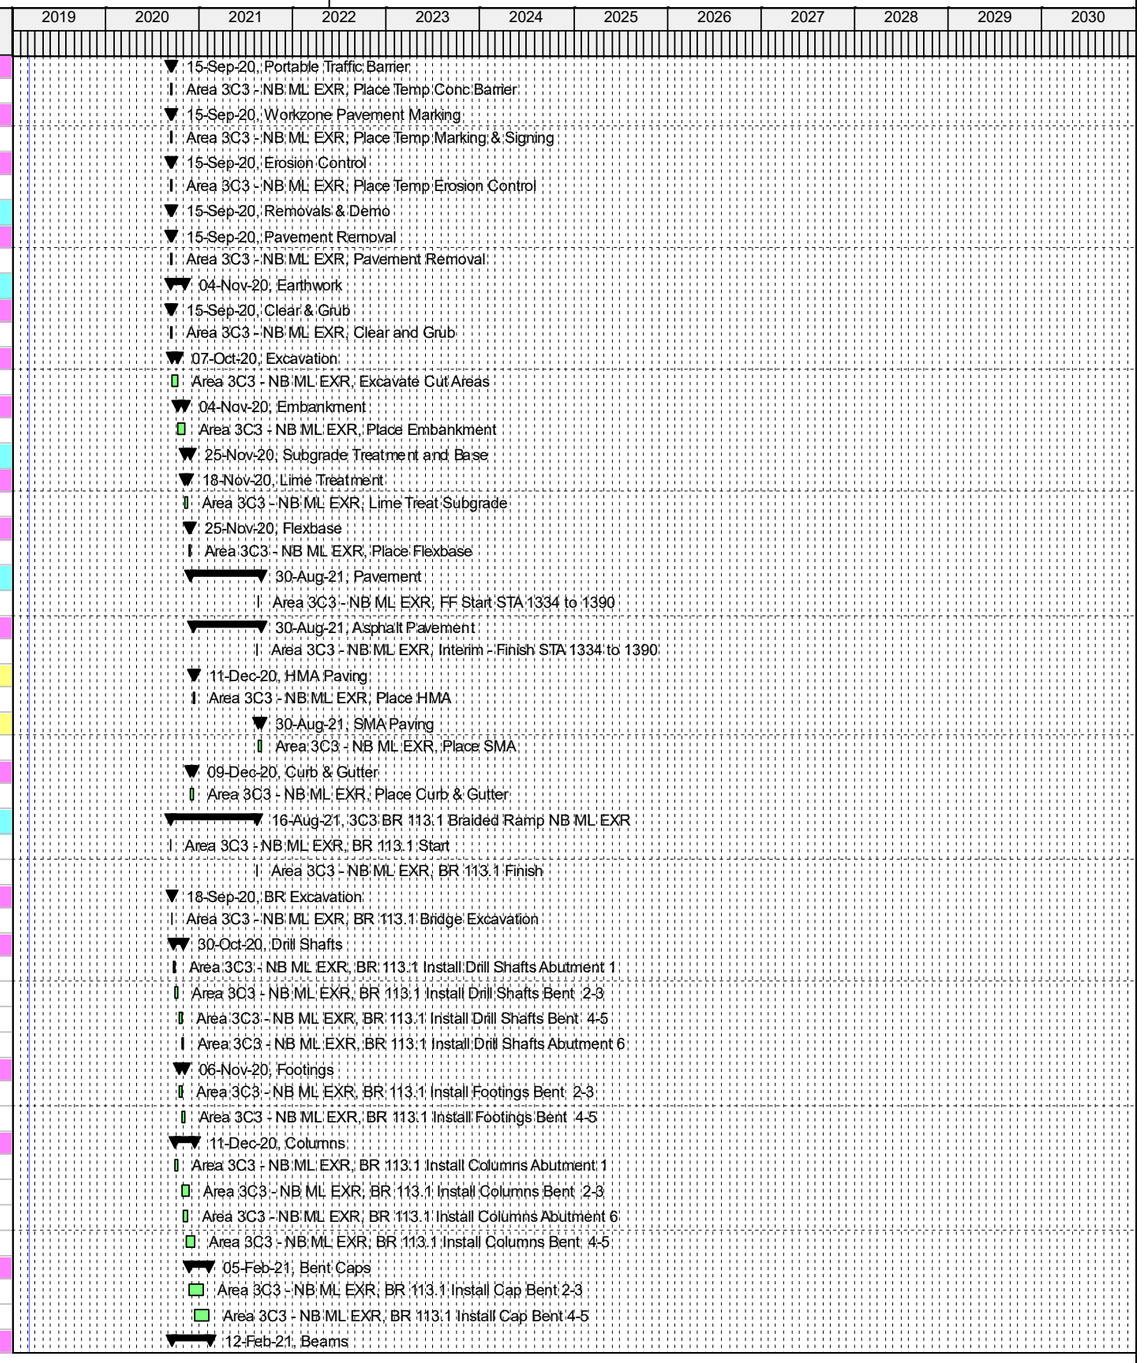

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Beam Procurement	20	550	14-Sep-20	09-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Forward Precast Beams Shopdrawings to TxDOT	1	550	12-Oct-20	12-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Precast Beam Fabrication & Delivery Leadtime	40	550	13-Oct-20	07-Dec-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Conc Beams	5	506	08-Feb-21	12-Feb-21
BR Place CTB Embankment			20	661	30-Nov-20	25-Dec-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Place Stabilized Backfill	20	661	30-Nov-20	25-Dec-20
Abutments			35	556	12-Oct-20	27-Nov-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Abutment 1	10	581	12-Oct-20	23-Oct-20
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Abutment 6	10	556	16-Nov-20	27-Nov-20
Approach Slab			10	506	02-Aug-21	13-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Apprch Slab Abutment 1	10	506	02-Aug-21	13-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Apprch Slab Abutment 6	10	506	02-Aug-21	13-Aug-21
Exspansion Joint			100	506	15-Feb-21	02-Jul-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Exp Joints	100	506	15-Feb-21	02-Jul-21
Deck			120	506	15-Feb-21	30-Jul-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Deck Slab	100	506	15-Feb-21	02-Jul-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Cure Deck Slab	20	506	05-Jul-21	30-Jul-21
Railings			10	506	02-Aug-21	13-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, BR 113.1 Install Conc Rail	10	506	02-Aug-21	13-Aug-21
Permanent Barriers			10	521	18-Aug-21	31-Aug-21
Concrete Barriers			10	521	18-Aug-21	31-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Place Conc Rail	10	521	18-Aug-21	31-Aug-21
Metal Beam Guardrails			10	521	18-Aug-21	31-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Install MBGF	10	521	18-Aug-21	31-Aug-21
Signals and Illumination			25	506	18-Aug-21	21-Sep-21
Roadway Illumination			25	506	18-Aug-21	21-Sep-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Illumination Pole Bases	5	506	18-Aug-21	24-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Illumination Poles/Fixtures	10	506	25-Aug-21	07-Sep-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Illumination Energize Fixtures	10	506	08-Sep-21	21-Sep-21
Signing and Marking			26	506	17-Aug-21	22-Sep-21
Overhead Sign Structures			10	521	18-Aug-21	31-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Overhead Signage	10	521	18-Aug-21	31-Aug-21
Small Signage			10	521	18-Aug-21	31-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Small Signage	10	521	18-Aug-21	31-Aug-21
Pavement Marking			26	506	17-Aug-21	22-Sep-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Permt Markings	2	530	17-Aug-21	18-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Finish STA 1334 to 1390	0	506	22-Sep-21	22-Sep-21
Landscaping			10	521	18-Aug-21	31-Aug-21
Seeding & Sodding			10	521	18-Aug-21	31-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Topsoil	10	521	18-Aug-21	31-Aug-21
	TX-3CD	Area 3C3 - NB ML EXR, Install Seeding/Sodding	10	521	18-Aug-21	31-Aug-21
ITS/TCS			20	673	26-Nov-20	23-Dec-20
Duct Bank System			20	673	26-Nov-20	23-Dec-20
	TX-3CD	Area 3C3 - NB ML EXR, ITS &TCS Civil Work Install Coduit	20	673	26-Nov-20	23-Dec-20
Northbound ML Sta 1280 to 1325 PH 1			158	618	09-Sep-20	19-Apr-21
C3(	TX-3CD	Area 3C3 - NB ML, Start STA 1280 to 1325	0	412	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			6	412	09-Sep-20	16-Sep-20
Barricades, Signs & Traffic Handling			1	412	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - NB ML, Move Traffic	1	412	16-Sep-20	16-Sep-20
Portable Traffic Barrier			5	412	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML, Place Temp Conc Barrier	5	412	09-Sep-20	15-Sep-20
Workzone Pavement Marking			5	412	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML, Place Temp Marking & Signing	5	412	09-Sep-20	15-Sep-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Erosion Control	5	412	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML, Place Temp Erosion Control	5	412	09-Sep-20	15-Sep-20
		Removals & Demo	5	412	09-Sep-20	15-Sep-20
		Pavement Removal	5	412	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML, Remove Pavement	5	412	09-Sep-20	15-Sep-20
		Earthwork	46	412	09-Sep-20	11-Nov-20
		Clear & Grub	5	412	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - NB ML, Clear and Grub	5	412	09-Sep-20	15-Sep-20
		Excavation	20	412	17-Sep-20	14-Oct-20
	TX-3CD	Area 3C3 - NB ML, Excavate Cut Areas	20	412	17-Sep-20	14-Oct-20
		Embankment	20	412	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C3 - NB ML, Place Embankment,	20	412	15-Oct-20	11-Nov-20
		Drainage	132	618	15-Oct-20	16-Apr-21
		Storm Sewer	20	452	15-Oct-20	11-Nov-20
	TX-3CD	Area 3C3 - NB ML, Install Small RCP	20	452	15-Oct-20	11-Nov-20
		Riprap	10	618	05-Apr-21	16-Apr-21
	TX-3CD	Area 3C3 - NB ML, Place RipRap	10	618	05-Apr-21	16-Apr-21
		Inlets	20	452	12-Nov-20	09-Dec-20
	TX-3CD	Area 3C3 - NB ML, Install MHs and Inlets	20	452	12-Nov-20	09-Dec-20
		Subgrade Treatment and Base	80	412	12-Nov-20	03-Mar-21
		Lime Treatment	60	412	12-Nov-20	03-Feb-21
	TX-3CD	Area 3C3 - NB ML, Lime Treat Subgrade	60	412	12-Nov-20	03-Feb-21
		Flexbase	20	412	04-Feb-21	03-Mar-21
	TX-3CD	Area 3C3 - NB ML, Place Flexbase	20	412	04-Feb-21	03-Mar-21
		Pavement	26	624	04-Mar-21	08-Apr-21
(	TX-3CD	Area 3C3 - NB ML, FF Start STA 1280 to 1325	0	618	02-Apr-21	02-Apr-21
		Asphalt Pavement	26	624	04-Mar-21	08-Apr-21
	TX-3CD	Area 3C3 - NB ML, Interim - Finish STA 1280 to 1325	0	412	01-Apr-21	01-Apr-21
		HMA Paving	10	422	04-Mar-21	17-Mar-21
	TX-3CD	Area 3C3 - NB ML, Place HMA	10	422	04-Mar-21	17-Mar-21
		SMA Paving	5	624	02-Apr-21	08-Apr-21
	TX-3CD	Area 3C3 - NB ML, Place SMA	5	624	02-Apr-21	08-Apr-21
		Signing and Marking	0	618	19-Apr-21	19-Apr-21
		Pavement Marking	0	618	19-Apr-21	19-Apr-21
	TX-3CD	Area 3C3 - NB ML, Finish STA 1280 to 1325	0	618	19-Apr-21	19-Apr-21
		ITS/TCS	20	412	04-Mar-21	31-Mar-21
		Duct Bank System	20	412	04-Mar-21	31-Mar-21
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Civil Work Install Coduit	20	412	04-Mar-21	31-Mar-21
		Northbound ML Sta 1280 to 1401 PH 2	273	371	10-Jun-21	28-Jun-22
C3(	TX-3CD	Area 3C3 - NB ML, Start STA 1280 to 1401	0	362	10-Jun-21	10-Jun-21
		Traffic Control and Temporary Work	11	362	10-Jun-21	24-Jun-21
		Barricades, Signs & Traffic Handling	1	362	24-Jun-21	24-Jun-21
	TX-3CD	Area 3C3 - NB ML, Move Traffic	1	362	24-Jun-21	24-Jun-21
		Portable Traffic Barrier	19-Feb-	362	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB ML, Place Temp Conc Barrier	10	362	10-Jun-21	23-Jun-21
		Workzone Pavement Marking	10	362	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB ML, Place Temp Marking & Signing	10	362	10-Jun-21	23-Jun-21
		Erosion Control	5	367	10-Jun-21	16-Jun-21
	TX-3CD	Area 3C3 - NB ML, Place Temp Erosion Control	5	367	10-Jun-21	16-Jun-21
		Removals & Demo	10	362	10-Jun-21	23-Jun-21
		Pavement Removal	10	362	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB ML, Remove Pavement	10	362	10-Jun-21	23-Jun-21
		Earthwork	76	362	10-Jun-21	23-Sep-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Clear & Grub	10	362	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - NB ML, Clear and Grub	10	362	10-Jun-21	23-Jun-21
		Excavation	35	362	25-Jun-21	12-Aug-21
	TX-3CD	Area 3C3 - NB ML, Excavate Cut Areas	35	362	25-Jun-21	12-Aug-21
		Embankment	30	362	13-Aug-21	23-Sep-21
	TX-3CD	Area 3C3 - NB ML, Place Embankment,	30	362	13-Aug-21	23-Sep-21
		Drainage	157	377	13-Aug-21	21-Mar-22
		Culverts	20	402	13-Aug-21	09-Sep-21
	TX-3CD	Area 3C3 - NB ML, CLV 10B Install Culvert	20	402	13-Aug-21	09-Sep-21
	TX-3CD	Area 3C3 - NB ML, CLV 11 Install Culvert	20	402	13-Aug-21	09-Sep-21
		Storm Sewer	20	402	10-Sep-21	07-Oct-21
	TX-3CD	Area 3C3 - NB ML, Install Small RCP	20	402	10-Sep-21	07-Oct-21
		Riprap	137	377	10-Sep-21	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Place Conc Headwall	10	477	10-Sep-21	23-Sep-21
	TX-3CD	Area 3C3 - NB ML, Place RipRap	10	377	08-Mar-22	21-Mar-22
		Inlets	20	402	08-Oct-21	04-Nov-21
	TX-3CD	Area 3C3 - NB ML, Install MHs and Inlets	20	402	08-Oct-21	04-Nov-21
		Subgrade Treatment and Base	95	362	24-Sep-21	03-Feb-22
		Lime Treatment	70	362	24-Sep-21	30-Dec-21
	TX-3CD	Area 3C3 - NB ML, Lime Treat Subgrade	70	362	24-Sep-21	30-Dec-21
		Flexbase	25	362	31-Dec-21	03-Feb-22
	TX-3CD	Area 3C3 - NB ML, Place Flexbase	25	362	31-Dec-21	03-Feb-22
		Pavement	26	383	04-Feb-22	11-Mar-22
(	TX-3CD	Area 3C3 - NB ML, FF Start STA 1280 to 1401	0	362	07-Mar-22	07-Mar-22
		Asphalt Pavement	26	383	04-Feb-22	11-Mar-22
	TX-3CD	Area 3C3 - NB ML, Interim - Finish STA 1280 to 1401	0	362	04-Mar-22	04-Mar-22
		HMA Paving	10	372	04-Feb-22	17-Feb-22
	TX-3CD	Area 3C3 - NB ML, Place HMA	10	372	04-Feb-22	17-Feb-22
		SMA Paving	5	383	07-Mar-22	11-Mar-22
	TX-3CD	Area 3C3 - NB ML, Place SMA	5	383	07-Mar-22	11-Mar-22
		Permanent Barriers	10	377	08-Mar-22	21-Mar-22
		Concrete Barriers	10	377	08-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Place Conc Rail	10	377	08-Mar-22	21-Mar-22
		Metal Beam Guardrails	10	377	08-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install MBGF	10	377	08-Mar-22	21-Mar-22
		Signals and Illumination	25	362	08-Mar-22	11-Apr-22
		Roadway Illumination	25	362	08-Mar-22	11-Apr-22
	TX-3CD	Area 3C3 - NB ML, Install Illumination Pole Bases	5	362	08-Mar-22	14-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install Illumination Poles/Fixtures	10	362	15-Mar-22	28-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install Illumination Energize Fixtures	10	362	29-Mar-22	11-Apr-22
		High Mast Illumination	15	372	08-Mar-22	28-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install High Mast Illumination Pole Bases	5	372	08-Mar-22	14-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install High Mast Illumination Poles/Fixtures	5	372	15-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install High Mast Illumination Energize Fixtures	5	372	22-Mar-22	28-Mar-22
		Signing and Marking	26	362	07-Mar-22	12-Apr-22
		Overhead Sign Structures	10	377	08-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install Overhead Signage	10	377	08-Mar-22	21-Mar-22
		Small Signage	10	377	08-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install Small Signage	10	377	08-Mar-22	21-Mar-22
		Pavement Marking	26	362	07-Mar-22	12-Apr-22
	TX-3CD	Area 3C3 - NB ML, Install Permt Markings	2	386	07-Mar-22	08-Mar-22
	TX-3CD	Area 3C3 - NB ML, Finish STA 1280 to 1401	0	362	12-Apr-22	12-Apr-22
		Landscaping	10	377	08-Mar-22	21-Mar-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Seeding & Sodding	10	377	08-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install Topsoil	10	377	08-Mar-22	21-Mar-22
	TX-3CD	Area 3C3 - NB ML, Install Seeding/Sodding	10	377	08-Mar-22	21-Mar-22
		ITS/TCS	102	371	04-Feb-22	28-Jun-22
		Duct Bank System	20	362	04-Feb-22	03-Mar-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Civil Work Install Coduit	20	362	04-Feb-22	03-Mar-22
		Equipment Foundations	20	371	07-Mar-22	01-Apr-22
	TX-3CD	Area 3C3 - NB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	20	371	07-Mar-22	01-Apr-22
		Equipment	40	371	07-Mar-22	02-May-22
	TX-3CD	Area 3C3 - NB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	371	07-Mar-22	07-Mar-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Fiber Install fiber	10	376	07-Mar-22	18-Mar-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Fiber Cut and splice	20	376	21-Mar-22	15-Apr-22
	TX-3CD	Area 3C3 - NB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	20	371	04-Apr-22	29-Apr-22
	TX-3CD	Area 3C3 - NB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	371	02-May-22	02-May-22
		Testing & Certification	51	371	18-Apr-22	28-Jun-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Fiber Local Site Test	5	376	18-Apr-22	22-Apr-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Fiber Fiber Complete	0	376	25-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - NB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	372	02-May-22	27-May-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Testing Start	0	371	03-May-22	03-May-22
	TX-3CD	Area 3C3 - NB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	371	03-May-22	30-May-22
	TX-3CD	Area 3C3 - NB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	20	371	31-May-22	27-Jun-22
	TX-3CD	Area 3C3 - NB ML, ITS &TCS Testing Complete	0	371	28-Jun-22	28-Jun-22
		Crossroad Heritage Trace Bridge Rehab Level 8 STA 1345	16	760	09-Sep-20	01-Oct-20
C3(	TX-3CD	Area 3C3 - CR BR RH, Start STA 1345	0	760	09-Sep-20	09-Sep-20
		Traffic Control and Temporary Work	6	760	09-Sep-20	16-Sep-20
		Barricades, Signs & Traffic Handling	1	760	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, Move Traffic	1	760	16-Sep-20	16-Sep-20
		Portable Traffic Barrier	5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, Place Temp Conc Barrier	5	760	09-Sep-20	15-Sep-20
		Workzone Pavement Marking	5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, Place Temp Marking & Signing	5	760	09-Sep-20	15-Sep-20
		Erosion Control	5	760	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, Place Temp Erosion Control	5	760	09-Sep-20	15-Sep-20
		BR 208 Heritage Trace	16	760	09-Sep-20	01-Oct-20
(	TX-3CD	Area 3C3 - CR BR RH, BR 208 Start STA 1345	2	763	09-Sep-20	10-Sep-20
(	TX-3CD	Area 3C3 - CR BR RH, BR 208 Finish STA 1345	0	760	01-Oct-20	01-Oct-20
		BR Demolition	5	760	17-Sep-20	23-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, BR 208 Concrete Removal	5	760	17-Sep-20	23-Sep-20
		Concret Repairs	5	760	24-Sep-20	30-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, BR 208Concrete Repairs	5	760	24-Sep-20	30-Sep-20
		Replace Exspansion Joint	10	764	11-Sep-20	24-Sep-20
	TX-3CD	Area 3C3 - CR BR RH, BR 208 Install Exp Joints	10	764	11-Sep-20	24-Sep-20
		Southbound ML Sta 1280 to 1401	288	346	24-Jun-21	02-Aug-22
C3(	TX-3CD	Area 3C3 - SB ML, Start STA 1280 to 1401	0	337	24-Jun-21	24-Jun-21
		Traffic Control and Temporary Work	11	337	24-Jun-21	08-Jul-21
(	TX-3CD	Area 3C3 - SB ML, Place Temp Marking & Signing	10	337	24-Jun-21	07-Jul-21
(	TX-3CD	Area 3C3 - SB ML, Place Temp Conc Barrier	10	337	24-Jun-21	07-Jul-21
		Barricades, Signs & Traffic Handling	1	337	08-Jul-21	08-Jul-21
	TX-3CD	Area 3C3 - SB ML, Move Traffic	1	337	08-Jul-21	08-Jul-21
		Erosion Control	5	342	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB ML, Place Temp Erosion Control	5	342	24-Jun-21	30-Jun-21
		Removals & Demo	10	337	24-Jun-21	07-Jul-21
		Pavement Removal	10	337	24-Jun-21	07-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB ML, Remove Pavement	10	337	24-Jun-21	07-Jul-21
Earthwork			76	337	24-Jun-21	07-Oct-21
Clear & Grub			10	337	24-Jun-21	07-Jul-21
	TX-3CD	Area 3C3 - SB ML, Clear and Grub	10	337	24-Jun-21	07-Jul-21
Excavation			35	337	09-Jul-21	26-Aug-21
	TX-3CD	Area 3C3 - SB ML, Excavate Cut Areas	35	337	09-Jul-21	26-Aug-21
Embankment			30	337	27-Aug-21	07-Oct-21
	TX-3CD	Area 3C3 - SB ML, Place Embankment,	30	337	27-Aug-21	07-Oct-21
Drainage			172	352	27-Aug-21	25-Apr-22
Culverts			20	392	27-Aug-21	23-Sep-21
	TX-3CD	Area 3C3 - SB ML, CLV 10B Install Culvert	20	392	27-Aug-21	23-Sep-21
	TX-3CD	Area 3C3 - SB ML, CLV 11 Install Culvert	20	392	27-Aug-21	23-Sep-21
Storm Sewer			20	392	24-Sep-21	21-Oct-21
	TX-3CD	Area 3C3 - SB ML, Install Small RCP	20	392	24-Sep-21	21-Oct-21
Riprap			152	352	24-Sep-21	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Place Conc Headwall	10	467	24-Sep-21	07-Oct-21
	TX-3CD	Area 3C3 - SB ML, Place RipRap	10	352	12-Apr-22	25-Apr-22
Inlets			20	392	22-Oct-21	18-Nov-21
	TX-3CD	Area 3C3 - SB ML, Install MHs and Inlets	20	392	22-Oct-21	18-Nov-21
Subgrade Treatment and Base			110	337	08-Oct-21	10-Mar-22
Lime Treatment			85	337	08-Oct-21	03-Feb-22
	TX-3CD	Area 3C3 - SB ML, Lime Treat Subgrade	85	337	08-Oct-21	03-Feb-22
Flexbase			25	337	04-Feb-22	10-Mar-22
	TX-3CD	Area 3C3 - SB ML, Place Flexbase	25	337	04-Feb-22	10-Mar-22
Pavement			28	356	11-Mar-22	19-Apr-22
(	TX-3CD	Area 3C3 - SB ML, FF Start STA 1280 to 1401	0	337	11-Apr-22	11-Apr-22
Asphalt Pavement			28	356	11-Mar-22	19-Apr-22
	TX-3CD	Area 3C3 - SB ML, Interim - Finish STA 1280 to 1401	0	337	08-Apr-22	08-Apr-22
HMA Paving			15	342	11-Mar-22	31-Mar-22
	TX-3CD	Area 3C3 - SB ML, Place HMA	15	342	11-Mar-22	31-Mar-22
SMA Paving			7	356	11-Apr-22	19-Apr-22
	TX-3CD	Area 3C3 - SB ML, Place SMA	7	356	11-Apr-22	19-Apr-22
Permanent Barriers			10	352	12-Apr-22	25-Apr-22
Concrete Barriers			10	352	12-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Place Conc Rail	10	352	12-Apr-22	25-Apr-22
Metal Beam Guardrails			10	352	12-Apr-22	25-Apr-22
	TX-3CD	19-Feb-20	10	352	12-Apr-22	25-Apr-22
Signals and Illumination			25	337	12-Apr-22	16-May-22
Roadway Illumination			25	337	12-Apr-22	16-May-22
	TX-3CD	Area 3C3 - SB ML, Install Illumination Pole Bases	5	337	12-Apr-22	18-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install Illumination Poles/Fixtures	10	337	19-Apr-22	02-May-22
	TX-3CD	Area 3C3 - SB ML, Install Illumination Energize Fixtures	10	337	03-May-22	16-May-22
High Mast Illumination			15	347	12-Apr-22	02-May-22
	TX-3CD	Area 3C3 - SB ML, Install High Mast Illumination Pole Bases	5	347	12-Apr-22	18-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install High Mast Illumination Poles/Fixtures	5	347	19-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install High Mast Illumination Energize Fixtures	5	347	26-Apr-22	02-May-22
Signing and Marking			26	337	11-Apr-22	17-May-22
Overhead Sign Structures			10	352	12-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install Overhead Signage	10	352	12-Apr-22	25-Apr-22
Small Signage			10	352	12-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install Small Signage	10	352	12-Apr-22	25-Apr-22
Pavement Marking			26	337	11-Apr-22	17-May-22
	TX-3CD	Area 3C3 - SB ML, Install Permt Markings	2	361	11-Apr-22	12-Apr-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB ML, Finish STA 1280 to 1401	0	337	17-May-22	17-May-22
Landscaping			10	352	12-Apr-22	25-Apr-22
Seeding & Sodding			10	352	12-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install Topsoil	10	352	12-Apr-22	25-Apr-22
	TX-3CD	Area 3C3 - SB ML, Install Seeding/Sodding	10	352	12-Apr-22	25-Apr-22
ITS/TCS			102	346	11-Mar-22	02-Aug-22
(	TX-3CD	Area 3C3 - SB ML, ITS &TCS Fiber Fiber Complete	0	351	30-May-22	30-May-22
Duct Bank System			20	337	11-Mar-22	07-Apr-22
	TX-3CD	Area 3C3 - SB ML, ITS &TCS Civil Work Install Coduit	20	337	11-Mar-22	07-Apr-22
Equipment Foundations			20	346	11-Apr-22	06-May-22
	TX-3CD	Area 3C3 - SB ML, Foundation Install DMS, CCTV, VD, TIDMS & TOLLING	20	346	11-Apr-22	06-May-22
Equipment			40	346	11-Apr-22	06-Jun-22
	TX-3CD	Area 3C3 - SB ML, DMS, CCTV, VD, TIDMS & TOLLING Equip Install Start	0	346	11-Apr-22	11-Apr-22
	TX-3CD	Area 3C3 - SB ML, ITS &TCS Fiber Install fiber	10	351	11-Apr-22	22-Apr-22
	TX-3CD	Area 3C3 - SB ML, ITS &TCS Fiber Cut and splice	20	351	25-Apr-22	20-May-22
	TX-3CD	Area 3C3 - SB ML, Mount DMS, CCTV, VD, TIDMS & TOLLING	20	346	09-May-22	03-Jun-22
	TX-3CD	Area 3C3 - SB ML, Equip Install DMS, CCTV, VD, TIDMS & TOLLING Complete	0	346	06-Jun-22	06-Jun-22
Testing & Certification			51	346	23-May-22	02-Aug-22
	TX-3CD	Area 3C3 - SB ML, ITS &TCS Fiber Local Site Test	5	351	23-May-22	27-May-22
	TX-3CD	Area 3C3 - SB ML, Local Site Network Test DMS, CCTV, VD, TIDMS & TOLLING	20	347	06-Jun-22	01-Jul-22
	TX-3CD	Area 3C3 - SB ML, ITS &TCS Testing Start	0	346	07-Jun-22	07-Jun-22
	TX-3CD	Area 3C3 - SB ML, Integration Test DMS, CCTV, VD, TIDMS & TOLLING	20	346	07-Jun-22	04-Jul-22
	TX-3CD	Area 3C3 - SB ML, Integrate & Test Central Network DMS, CCTV, VD, TIDMS & TOLLING	20	346	05-Jul-22	01-Aug-22
	TX-3CD	Area 3C3 - SB ML, ITS &TCS Testing Complete	0	346	02-Aug-22	02-Aug-22
Southbound Exit Ramp SBML to SBGP STA 1295 to 1310			148	628	09-Sep-20	05-Apr-21
C3(	TX-3CD	Area 3C3 - SB ML EXR, Start STA 1295 to 1310	0	628	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			6	628	09-Sep-20	16-Sep-20
Barricades, Signs & Traffic Handling			1	628	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - SB ML EXR, Move Traffic	1	628	16-Sep-20	16-Sep-20
Portable Traffic Barrier			5	628	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML EXR, Place Temp Conc Barrier	5	628	09-Sep-20	15-Sep-20
Workzone Pavement Marking			5	628	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML EXR, Place Temp Marking & Signing	5	628	09-Sep-20	15-Sep-20
Erosion Control			5	628	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML EXR, Place Temp Erosion Control	5	628	09-Sep-20	15-Sep-20
Removals & Demo			5	628	09-Sep-20	15-Sep-20
Pavement Removal			5	628	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML EXR, Remove Pavement	5	628	09-Sep-20	15-Sep-20
Earthwork			41	628	09-Sep-20	04-Nov-20
Clear & Grub			5	628	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML EXR, Clear and Grub	5	628	09-Sep-20	15-Sep-20
Excavation			15	628	17-Sep-20	07-Oct-20
	TX-3CD	Area 3C3 - SB ML EXR, Excavate Cut Areas	15	628	17-Sep-20	07-Oct-20
Embankment			20	628	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C3 - SB ML EXR, Place Embankment	20	628	08-Oct-20	04-Nov-20
Subgrade Treatment and Base			60	628	05-Nov-20	27-Jan-21
Lime Treatment			40	628	05-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB ML EXR, Lime Treat Subgrade	40	628	05-Nov-20	30-Dec-20
Flexbase			20	628	31-Dec-20	27-Jan-21
	TX-3CD	Area 3C3 - SB ML EXR, Place Flexbase	20	628	31-Dec-20	27-Jan-21
Pavement			26	649	28-Jan-21	04-Mar-21
(	TX-3CD	Area 3C3 - SB ML EXR, FF Start STA 1295 to 1310	0	628	26-Feb-21	26-Feb-21
Asphalt Pavement			16	649	11-Feb-21	04-Mar-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB ML EXR, Sec 1 Interim - Finish STA 1295 to 1310	0	628	25-Feb-21	25-Feb-21
HMA Paving			10	628	11-Feb-21	24-Feb-21
	TX-3CD	Area 3C3 - SB ML EXR, Place HMA	10	628	11-Feb-21	24-Feb-21
SMA Paving			5	649	26-Feb-21	04-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Place SMA	5	649	26-Feb-21	04-Mar-21
Curb & Gutter			10	628	28-Jan-21	10-Feb-21
	TX-3CD	Area 3C3 - SB ML EXR, Place Curb & Gutter	10	628	28-Jan-21	10-Feb-21
Permanent Barriers			10	643	01-Mar-21	12-Mar-21
Concrete Barriers			10	643	01-Mar-21	12-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Place Conc Rail	10	643	01-Mar-21	12-Mar-21
Metal Beam Guardrails			10	643	01-Mar-21	12-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install MBGF	10	643	01-Mar-21	12-Mar-21
Crash Attenuators			5	648	01-Mar-21	05-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Attenuator	5	648	01-Mar-21	05-Mar-21
Signals and Illumination			25	628	01-Mar-21	02-Apr-21
Roadway Illumination			25	628	01-Mar-21	02-Apr-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Illumination Pole Bases	5	628	01-Mar-21	05-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Illumination Poles/Fixtures	10	628	08-Mar-21	19-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Illumination Energize Fixtures	10	628	22-Mar-21	02-Apr-21
Signing and Marking			26	628	26-Feb-21	05-Apr-21
Overhead Sign Structures			10	643	01-Mar-21	12-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Overhead Signage	10	643	01-Mar-21	12-Mar-21
Small Signage			10	643	01-Mar-21	12-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Small Signage	10	643	01-Mar-21	12-Mar-21
Pavement Marking			26	628	26-Feb-21	05-Apr-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Permt Markings	2	652	26-Feb-21	01-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Finish STA 1295 to 1310	0	628	05-Apr-21	05-Apr-21
Landscaping			10	643	01-Mar-21	12-Mar-21
Seeding & Sodding			10	643	01-Mar-21	12-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Topsoil	10	643	01-Mar-21	12-Mar-21
	TX-3CD	Area 3C3 - SB ML EXR, Install Seeding/Sodding	10	643	01-Mar-21	12-Mar-21
ITS/TCS			20	628	28-Jan-21	24-Feb-21
Duct Bank System			20	628	28-Jan-21	24-Feb-21
	TX-3CD	Area 3C3 - SB ML EXR, ITS &TCS Civil Work Install Coduit	20	628	28-Jan-21	24-Feb-21
Southbound GP Sta 1325 to 1401 PH 1			206	337	09-Sep-20	24-Jun-21
C3(	TX-3CD	Area 3C3 - SB GP, PH 1 Start STA 1325 to 1401	0	337	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			11	337	09-Sep-20	23-Sep-20
(	TX-3CD	Area 3C3 - SB GP, PH 1 Place Temp Marking & Signing	10	337	09-Sep-20	22-Sep-20
(	TX-3CD	Area 3C3 - SB GP, PH 1 Place Temp Conc Barrier	10	337	09-Sep-20	22-Sep-20
Barricades, Signs & Traffic Handling			1	337	23-Sep-20	23-Sep-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Move Traffic	1	337	23-Sep-20	23-Sep-20
Erosion Control			5	342	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Place Temp Erosion Control	5	342	09-Sep-20	15-Sep-20
Removals & Demo			10	337	09-Sep-20	22-Sep-20
Pavement Removal			10	337	09-Sep-20	22-Sep-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Remove Pavement	10	337	09-Sep-20	22-Sep-20
Earthwork			81	337	09-Sep-20	30-Dec-20
Clear & Grub			5	342	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Clear and Grub	5	342	09-Sep-20	15-Sep-20
Excavation			40	337	24-Sep-20	18-Nov-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Excavate Cut Areas	40	337	24-Sep-20	18-Nov-20
Embankment			30	337	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Place Embankment,	30	337	19-Nov-20	30-Dec-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Drainage			60	392	19-Nov-20	10-Feb-21
Culverts			20	392	19-Nov-20	16-Dec-20
	TX-3CD	Area 3C3 - SB GP, CLV 11 PH 1 Install Culvert	20	392	19-Nov-20	16-Dec-20
	TX-3CD	Area 3C3 - SB GP, CLV 10B PH 1 Install Culvert	20	392	19-Nov-20	16-Dec-20
Storm Sewer			20	392	17-Dec-20	13-Jan-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Small RCP	20	392	17-Dec-20	13-Jan-21
Inlets			20	392	14-Jan-21	10-Feb-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install MHs and Inlets	20	392	14-Jan-21	10-Feb-21
Subgrade Treatment and Base			115	337	31-Dec-20	09-Jun-21
Lime Treatment			85	337	31-Dec-20	28-Apr-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Lime Treat Subgrade	85	337	31-Dec-20	28-Apr-21
Flexbase			30	337	29-Apr-21	09-Jun-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Place Flexbase	30	337	29-Apr-21	09-Jun-21
Pavement			10	337	10-Jun-21	24-Jun-21
Asphalt Pavement			10	337	10-Jun-21	24-Jun-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Interim - Finish STA 1325 to 1401	0	337	24-Jun-21	24-Jun-21
HMA Paving			10	337	10-Jun-21	23-Jun-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Place HMA	10	337	10-Jun-21	23-Jun-21
Retaining Walls			110	342	19-Nov-20	21-Apr-21
Wall RT-3C-N18A			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-N18A	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-N18A			10	422	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-N18A Coping Cap	10	422	17-Dec-20	30-Dec-20
Wall RT-3C-N20A			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-N20A	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-N20A			10	422	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-N20A Coping Cap	10	422	17-Dec-20	30-Dec-20
Wall RT-3C-S12A			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S12A	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-S12A			10	422	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S12A Coping Cap	10	422	17-Dec-20	30-Dec-20
Wall RT-3C-S15A			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S15A	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-S15A			10	422	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S15A Coping Cap	10	422	17-Dec-20	30-Dec-20
Wall RT-3C-S12			110	342	19-Nov-20	21-Apr-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S12	90	342	19-Nov-20	24-Mar-21
Wall Coping RT-3C-S12			20	342	25-Mar-21	21-Apr-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S12 Coping Cap	20	342	25-Mar-21	21-Apr-21
Wall RT-3C-S11			65	387	19-Nov-20	17-Feb-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S11	45	387	19-Nov-20	20-Jan-21
Wall Coping RT-3C-S11			20	387	21-Jan-21	17-Feb-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S11 Coping Cap	20	387	21-Jan-21	17-Feb-21
Wall RT-3C-S16			55	397	19-Nov-20	03-Feb-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S16	40	397	19-Nov-20	13-Jan-21
Wall Coping RT-3C-S16			15	397	14-Jan-21	03-Feb-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S16 Coping Cap	15	397	14-Jan-21	03-Feb-21
Wall RT-3C-S14			105	347	19-Nov-20	14-Apr-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S14	80	347	19-Nov-20	10-Mar-21
Wall Coping RT-3C-S14			25	347	11-Mar-21	14-Apr-21
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S14 Coping Cap	25	347	11-Mar-21	14-Apr-21
Wall RT-3C-S15			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S15	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-S15			10	422	17-Dec-20	30-Dec-20

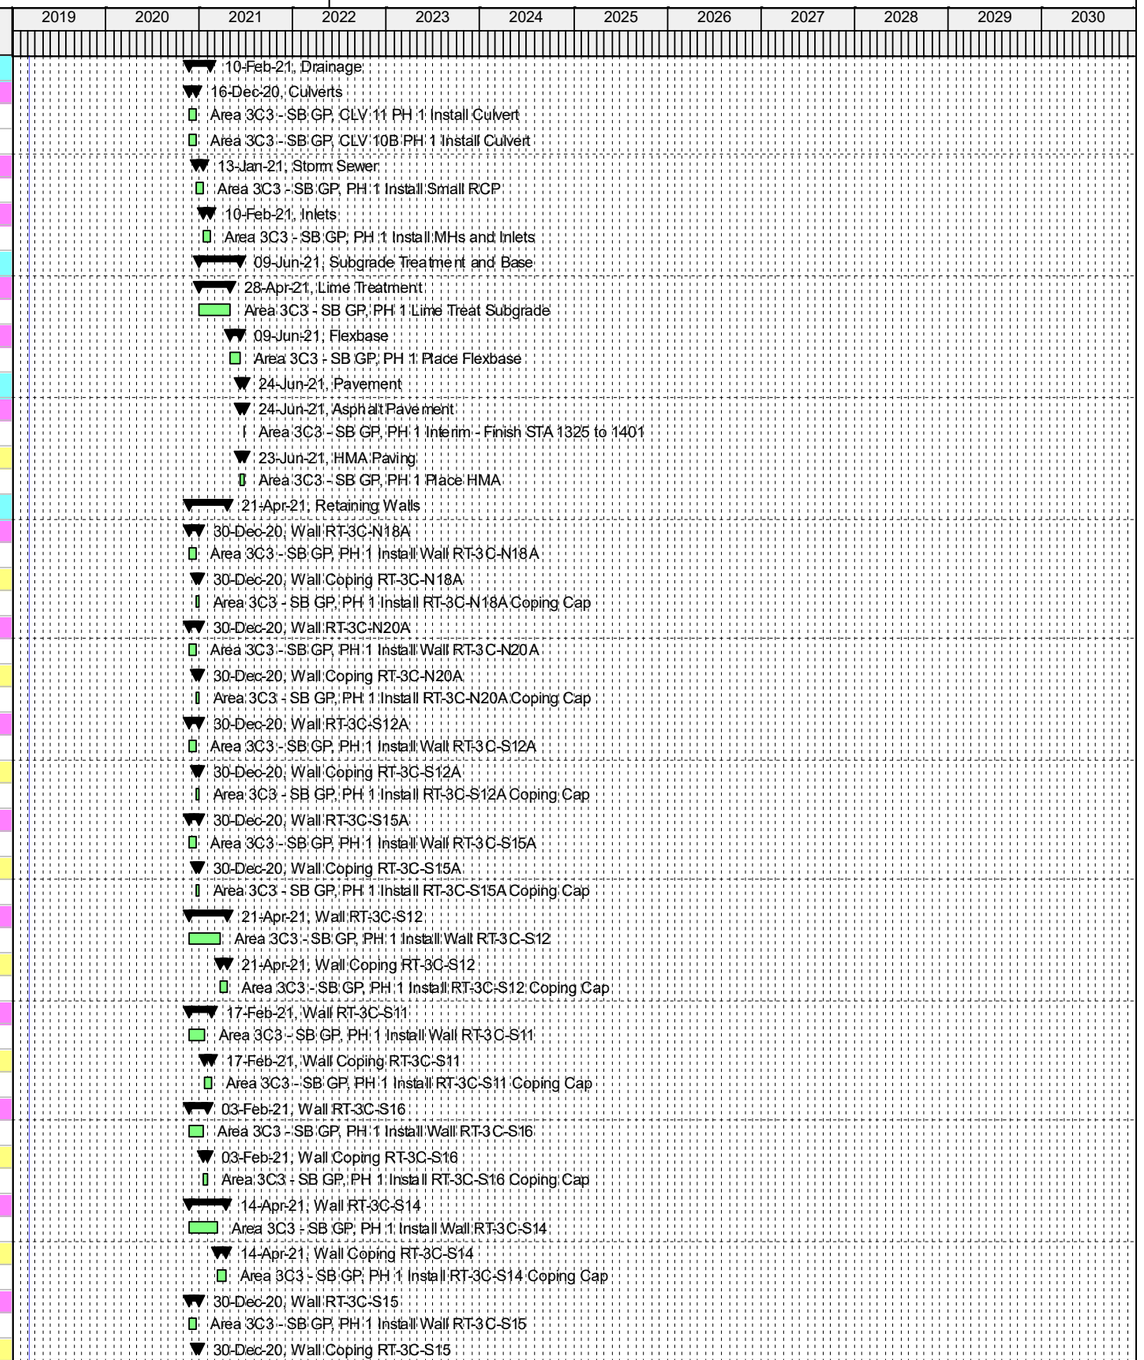

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S15 Coping Cap	10	422	17-Dec-20	30-Dec-20
Wall RT-3C-S13			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S13	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-S13			10	422	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S13 Coping Cap	10	422	17-Dec-20	30-Dec-20
Wall RT-3C-S17			30	422	19-Nov-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install Wall RT-3C-S17	20	422	19-Nov-20	16-Dec-20
Wall Coping RT-3C-S17			10	422	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP, PH 1 Install RT-3C-S17 Coping Cap	10	422	17-Dec-20	30-Dec-20
Southbound GP Sta 1280 to 1325 PH 2			168	402	24-Jun-21	15-Feb-22
C3(	TX-3CD	Area 3C3 - SB GP, PH 2 Start STA 1280 to 1325	0	402	24-Jun-21	24-Jun-21
Traffic Control and Temporary Work			6	402	24-Jun-21	01-Jul-21
Barricades, Signs & Traffic Handling			1	402	01-Jul-21	01-Jul-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Move Traffic	1	402	01-Jul-21	01-Jul-21
Erosion Control			5	402	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Place Temp Erosion Control	5	402	24-Jun-21	30-Jun-21
Removals & Demo			5	402	24-Jun-21	30-Jun-21
Pavement Removal			5	402	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Remove Pavement	5	402	24-Jun-21	30-Jun-21
Earthwork			41	402	24-Jun-21	19-Aug-21
Clear & Grub			5	402	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Clear and Grub	5	402	24-Jun-21	30-Jun-21
Excavation			15	402	02-Jul-21	22-Jul-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Excavate Cut Areas	15	402	02-Jul-21	22-Jul-21
Embankment			20	402	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Place Embankment,	20	402	23-Jul-21	19-Aug-21
Drainage			132	417	23-Jul-21	24-Jan-22
Culverts			20	442	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Medium CBC	20	442	23-Jul-21	19-Aug-21
Storm Sewer			20	442	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Small RCP	20	442	23-Jul-21	19-Aug-21
Riprap			10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Place RipRap	10	417	11-Jan-22	24-Jan-22
Inlets			20	442	20-Aug-21	16-Sep-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Install MHs and Inlets	20	442	20-Aug-21	16-Sep-21
Subgrade Treatment and Base			80	402	20-Aug-21	09-Dec-21
Lime Treatment			60	402	20-Aug-21	11-Nov-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Lime Treat Subgrade	60	402	20-Aug-21	11-Nov-21
Flexbase			20	402	12-Nov-21	09-Dec-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Place Flexbase	20	402	12-Nov-21	09-Dec-21
Pavement			31	418	10-Dec-21	21-Jan-22
(	TX-3CD	Area 3C3 - SB GP, PH 2 FF Start STA 1280 to 1325	0	402	10-Jan-22	10-Jan-22
Asphalt Pavement			31	418	10-Dec-21	21-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Sec 1 Interim - Finish STA 1280 to 1325	0	402	07-Jan-22	07-Jan-22
HMA Paving			5	417	10-Dec-21	16-Dec-21
	TX-3CD	Area 3C3 - SB GP, PH 2 Place HMA	5	417	10-Dec-21	16-Dec-21
SMA Paving			10	418	10-Jan-22	21-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Place SMA	10	418	10-Jan-22	21-Jan-22
Permanent Barriers			10	417	11-Jan-22	24-Jan-22
Concrete Barriers			10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Place Conc Rail	10	417	11-Jan-22	24-Jan-22
Metal Beam Guardrails			10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install MBGF	10	417	11-Jan-22	24-Jan-22

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Signals and Illumination			25	402	11-Jan-22	14-Feb-22
Roadway Illumination			25	402	11-Jan-22	14-Feb-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Illumination Pole Bases	5	402	11-Jan-22	17-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Illumination Poles/Fixtures	10	402	18-Jan-22	31-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Illumination Energize Fixtures	10	402	01-Feb-22	14-Feb-22
High Mast Illumination			15	412	11-Jan-22	31-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install High Mast Illumination Pole Bases	5	412	11-Jan-22	17-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install High Mast Illumination Poles/Fixtures	5	412	18-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install High Mast Illumination Energize Fixtures	5	412	25-Jan-22	31-Jan-22
Signing and Marking			26	402	10-Jan-22	15-Feb-22
Overhead Sign Structures			10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Overhead Signage	10	417	11-Jan-22	24-Jan-22
Small Signage			10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Small Signage	10	417	11-Jan-22	24-Jan-22
Pavement Marking			26	402	10-Jan-22	15-Feb-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Permt Markings	2	426	10-Jan-22	11-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Finish STA 1280 to 1325	0	402	15-Feb-22	15-Feb-22
Landscaping			10	417	11-Jan-22	24-Jan-22
Seeding & Sodding			10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Topsoil	10	417	11-Jan-22	24-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 Install Seeding/Sodding	10	417	11-Jan-22	24-Jan-22
ITS/TCS			20	402	10-Dec-21	06-Jan-22
Duct Bank System			20	402	10-Dec-21	06-Jan-22
	TX-3CD	Area 3C3 - SB GP, PH 2 ITS &TCS Civil Work Install Coduit	20	402	10-Dec-21	06-Jan-22
Southbound Exit Ramp SBGP to SBFR STA 1280 to 1293			128	648	09-Sep-20	08-Mar-21
C3(	TX-3CD	Area 3C3 - SB GP EXR, Start STA 1280 to 1293	0	648	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			6	648	09-Sep-20	16-Sep-20
Barricades, Signs & Traffic Handling			1	648	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - SB GP EXR, Move Traffic	1	648	16-Sep-20	16-Sep-20
Portable Traffic Barrier			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP EXR, Place Temp Conc Barrier	5	648	09-Sep-20	15-Sep-20
Workzone Pavement Marking			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP EXR, Place Temp Marking & Signing	5	648	09-Sep-20	15-Sep-20
Erosion Control			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP EXR, Place Temp Erosion Control	5	648	09-Sep-20	15-Sep-20
Removals & Demo			5	648	09-Sep-20	15-Sep-20
Pavement Removal			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP EXR, Remove Pavement	5	648	09-Sep-20	15-Sep-20
Earthwork			41	648	09-Sep-20	04-Nov-20
Clear & Grub			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP EXR, Clear and Grub	5	648	09-Sep-20	15-Sep-20
Excavation			15	648	17-Sep-20	07-Oct-20
	TX-3CD	Area 3C3 - SB GP EXR, Excavate Cut Areas	15	648	17-Sep-20	07-Oct-20
Embankment			20	648	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C3 - SB GP EXR, Place Embankment	20	648	08-Oct-20	04-Nov-20
Subgrade Treatment and Base			40	648	05-Nov-20	30-Dec-20
Lime Treatment			30	648	05-Nov-20	16-Dec-20
	TX-3CD	Area 3C3 - SB GP EXR, Lime Treat Subgrade	30	648	05-Nov-20	16-Dec-20
Flexbase			10	648	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB GP EXR, Place Flexbase	10	648	17-Dec-20	30-Dec-20
Pavement			23	672	31-Dec-20	01-Feb-21
(	TX-3CD	Area 3C3 - SB GP EXR, FF Start STA 1280 to 1293	0	648	29-Jan-21	29-Jan-21
Asphalt Pavement			13	672	14-Jan-21	01-Feb-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB GP EXR, Interim - Finish STA 1280 to 1293	0	648	28-Jan-21	28-Jan-21
	HMA Paving		5	653	14-Jan-21	20-Jan-21
	TX-3CD	Area 3C3 - SB GP EXR, Place HMA	5	653	14-Jan-21	20-Jan-21
	SMA Paving		2	672	29-Jan-21	01-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Place SMA	2	672	29-Jan-21	01-Feb-21
	Curb & Gutter		10	653	31-Dec-20	13-Jan-21
	TX-3CD	Area 3C3 - SB GP EXR, Place Curb & Gutter	10	653	31-Dec-20	13-Jan-21
	Permanent Barriers		10	663	01-Feb-21	12-Feb-21
	Concrete Barriers		10	663	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Place Conc Rail	10	663	01-Feb-21	12-Feb-21
	Metal Beam Guardrails		10	663	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install MBGF	10	663	01-Feb-21	12-Feb-21
	Crash Attenuators		5	668	01-Feb-21	05-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Attenuator	5	668	01-Feb-21	05-Feb-21
	Signals and Illumination		25	648	01-Feb-21	05-Mar-21
	Roadway Illumination		25	648	01-Feb-21	05-Mar-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Illumination Pole Bases	5	648	01-Feb-21	05-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Illumination Poles/Fixtures	10	648	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Illumination Energize Fixtures	10	648	22-Feb-21	05-Mar-21
	Signing and Marking		26	648	29-Jan-21	08-Mar-21
	Overhead Sign Structures		10	663	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Overhead Signage	10	663	01-Feb-21	12-Feb-21
	Small Signage		10	663	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Small Signage	10	663	01-Feb-21	12-Feb-21
	Pavement Marking		26	648	29-Jan-21	08-Mar-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Permt Markings	2	672	29-Jan-21	01-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Finish STA 1280 to 1293	0	648	08-Mar-21	08-Mar-21
	Landscaping		10	663	01-Feb-21	12-Feb-21
	Seeding & Sodding		10	663	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Seeding/Sodding	10	663	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP EXR, Install Topsoil	10	663	01-Feb-21	12-Feb-21
	ITS/TCS		20	648	31-Dec-20	27-Jan-21
	Duct Bank System		20	648	31-Dec-20	27-Jan-21
	TX-3CD	Area 3C3 - SB GP EXR, ITS &TCS Civil Work Install Coduit	20	648	31-Dec-20	27-Jan-21
	Southbound Entry Ramp SBFR to SBGP STA 1370 to 1334		133	643	09-Sep-20	15-Mar-21
C3(	TX-3CD	Area 3C3 - SB GP ENR, Start STA 1370 to 1334	0	643	09-Sep-20	09-Sep-20
	Traffic Control and Temporary Work		6	643	09-Sep-20	16-Sep-20
	Barricades, Signs & Traffic Handling		1	643	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - SB GP ENR, Move Traffic	1	643	16-Sep-20	16-Sep-20
	Portable Traffic Barrier		5	643	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP ENR, Place Temp Conc Barrier	5	643	09-Sep-20	15-Sep-20
	Workzone Pavement Marking		5	643	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP ENR, Place Temp Marking & Signing	5	643	09-Sep-20	15-Sep-20
	Erosion Control		5	643	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP ENR, Place Temp Erosion Control	5	643	09-Sep-20	15-Sep-20
	Removals & Demo		5	643	09-Sep-20	15-Sep-20
	Pavement Removal		5	643	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP ENR, Remove Pavement	5	643	09-Sep-20	15-Sep-20
	Earthwork		41	643	09-Sep-20	04-Nov-20
	Clear & Grub		5	643	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB GP ENR, Clear and Grub	5	643	09-Sep-20	15-Sep-20
	Excavation		15	643	17-Sep-20	07-Oct-20
	TX-3CD	Area 3C3 - SB GP ENR, Excavate Cut Areas	15	643	17-Sep-20	07-Oct-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
		Embankment	20	643	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C3 - SB GP ENR, Place Embankment	20	643	08-Oct-20	04-Nov-20
		Subgrade Treatment and Base	45	643	05-Nov-20	06-Jan-21
		Lime Treatment	30	643	05-Nov-20	16-Dec-20
	TX-3CD	Area 3C3 - SB GP ENR, Lime Treat Subgrade	30	643	05-Nov-20	16-Dec-20
		Flexbase	15	643	17-Dec-20	06-Jan-21
	TX-3CD	Area 3C3 - SB GP ENR, Place Flexbase	15	643	17-Dec-20	06-Jan-21
		Pavement	23	667	07-Jan-21	08-Feb-21
(	TX-3CD	Area 3C3 - SB GP ENR, FF Start STA 1370 to 1334	0	643	05-Feb-21	05-Feb-21
		Asphalt Pavement	13	667	21-Jan-21	08-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Sec 1 Interim - Finish STA 1370 to 1334	0	643	04-Feb-21	04-Feb-21
		HMA Paving	5	648	21-Jan-21	27-Jan-21
	TX-3CD	Area 3C3 - SB GP ENR, Place HMA	5	648	21-Jan-21	27-Jan-21
		SMA Paving	2	667	05-Feb-21	08-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Place SMA	2	667	05-Feb-21	08-Feb-21
		Curb & Gutter	10	648	07-Jan-21	20-Jan-21
	TX-3CD	Area 3C3 - SB GP ENR, Place Curb & Gutter	10	648	07-Jan-21	20-Jan-21
		Permanent Barriers	10	658	08-Feb-21	19-Feb-21
		Concrete Barriers	10	658	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Place Conc Rail	10	658	08-Feb-21	19-Feb-21
		Metal Beam Guardrails	10	658	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install MBGF	10	658	08-Feb-21	19-Feb-21
		Signals and Illumination	25	643	08-Feb-21	12-Mar-21
		Roadway Illumination	25	643	08-Feb-21	12-Mar-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Illumination Pole Bases	5	643	08-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Illumination Poles/Fixtures	10	643	15-Feb-21	26-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Illumination Energize Fixtures	10	643	01-Mar-21	12-Mar-21
		Signing and Marking	26	643	05-Feb-21	15-Mar-21
		Overhead Sign Structures	10	658	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Overhead Signage	10	658	08-Feb-21	19-Feb-21
		Small Signage	10	658	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Small Signage	10	658	08-Feb-21	19-Feb-21
		Pavement Marking	26	643	05-Feb-21	15-Mar-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Permt Markings	2	667	05-Feb-21	08-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Finish STA 1370 to 1334	0	643	15-Mar-21	15-Mar-21
		Landscaping	10	658	08-Feb-21	19-Feb-21
		Seeding & Sodding	10	658	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Topsoil	10	658	08-Feb-21	19-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, Install Seeding/Sodding	10	658	08-Feb-21	19-Feb-21
		ITS/TCS	20	643	07-Jan-21	03-Feb-21
		Duct Bank System	20	643	07-Jan-21	03-Feb-21
	TX-3CD	Area 3C3 - SB GP ENR, ITS &TCS Civil Work Install Coduit	20	643	07-Jan-21	03-Feb-21
		Southbound Entry Ramp SBFR to SBML STA 1330 to 1385	255	521	09-Sep-20	01-Sep-21
C3(	TX-3CD	Area 3C3 - SB ML ENR, Start STA 1330 to 1385	0	521	09-Sep-20	09-Sep-20
		Traffic Control and Temporary Work	6	648	09-Sep-20	16-Sep-20
		Barricades, Signs & Traffic Handling	1	648	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Move Traffic	1	648	16-Sep-20	16-Sep-20
		Portable Traffic Barrier	5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Temp Conc Barrier	5	648	09-Sep-20	15-Sep-20
		Workzone Pavement Marking	5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Temp Marking & Signing	5	648	09-Sep-20	15-Sep-20
		Erosion Control	5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Temp Erosion Control	5	648	09-Sep-20	15-Sep-20

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Removals & Demo			5	648	09-Sep-20	15-Sep-20
Pavement Removal			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Remove Pavement	5	648	09-Sep-20	15-Sep-20
Earthwork			41	648	09-Sep-20	04-Nov-20
Clear & Grub			5	648	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Clear and Grub	5	648	09-Sep-20	15-Sep-20
Excavation			15	648	17-Sep-20	07-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, Excavate Cut Areas	15	648	17-Sep-20	07-Oct-20
Embankment			20	648	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Embankment	20	648	08-Oct-20	04-Nov-20
Subgrade Treatment and Base			40	648	05-Nov-20	30-Dec-20
Lime Treatment			30	648	05-Nov-20	16-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, Lime Treat Subgrade	30	648	05-Nov-20	16-Dec-20
Flexbase			10	648	17-Dec-20	30-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Flexbase	10	648	17-Dec-20	30-Dec-20
Pavement			150	545	31-Dec-20	28-Jul-21
(	TX-3CD	Area 3C3 - SB ML ENR, FF Start STA 1330 to 1385	0	521	27-Jul-21	27-Jul-21
Asphalt Pavement			140	545	14-Jan-21	28-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, Interim - Finish STA 1330 to 1385	0	521	26-Jul-21	26-Jul-21
HMA Paving			5	653	14-Jan-21	20-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Place HMA	5	653	14-Jan-21	20-Jan-21
SMA Paving			2	545	27-Jul-21	28-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, Place SMA	2	545	27-Jul-21	28-Jul-21
Curb & Gutter			10	653	31-Dec-20	13-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Place Curb & Gutter	10	653	31-Dec-20	13-Jan-21
3C3 BR 113.2 Braided Ramp SB ML ENR			228	521	09-Sep-20	26-Jul-21
(	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Start	2	521	09-Sep-20	10-Sep-20
(	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Finish	0	521	26-Jul-21	26-Jul-21
BR Excavation			5	521	14-Sep-20	18-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Bridge Excavation	5	521	14-Sep-20	18-Sep-20
Drill Shafts			30	556	21-Sep-20	30-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Drill Shafts Abutment 1	5	521	21-Sep-20	25-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Drill Shafts Bent 2-3	10	521	28-Sep-20	09-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Drill Shafts Bent 4-5	10	521	12-Oct-20	23-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Drill Shafts Abutment 6	5	556	26-Oct-20	30-Oct-20
Footings			20	531	12-Oct-20	06-Nov-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Footings Bent 2-3	10	541	12-Oct-20	23-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Footings Bent 4-5	10	521	26-Oct-20	06-Nov-20
Columns			55	536	28-Sep-20	11-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Columns Abutment 1	10	581	28-Sep-20	09-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Columns Bent 2-3	20	541	26-Oct-20	20-Nov-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Columns Abutment 6	10	556	02-Nov-20	13-Nov-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Columns Bent 4-5	25	521	09-Nov-20	11-Dec-20
Bent Caps			40	521	23-Nov-20	15-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Cap Bent 2-3	20	541	23-Nov-20	18-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Cap Bent 4-5	25	521	14-Dec-20	15-Jan-21
Beams			95	521	14-Sep-20	22-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Beam Procurement	20	550	14-Sep-20	09-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Forward Precast Beams Shopdrawings to TxDOT	1	550	12-Oct-20	12-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Precast Beam Fabrication & Delivery Leadtime	40	550	13-Oct-20	07-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Conc Beams	5	521	18-Jan-21	22-Jan-21
BR Place CTB Embankment			20	661	30-Nov-20	25-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Place Stabilized Backfill	20	661	30-Nov-20	25-Dec-20

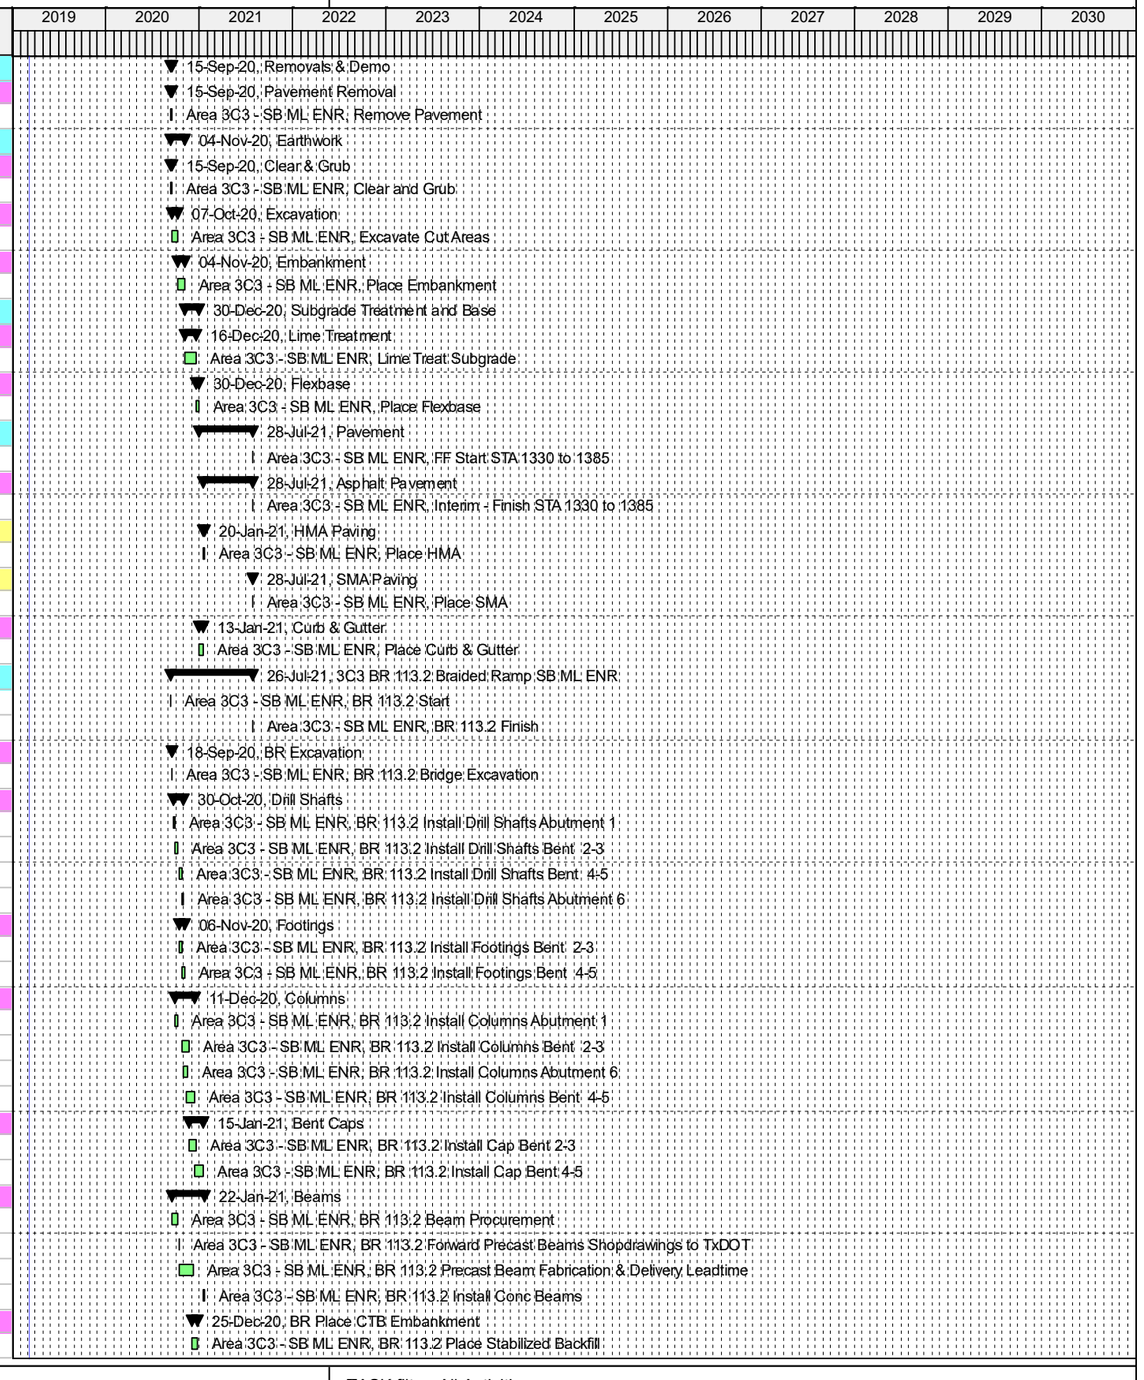

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Abutments			35	556	12-Oct-20	27-Nov-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Abutment 1	10	581	12-Oct-20	23-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Abutment 6	10	556	16-Nov-20	27-Nov-20
Approach Slab			10	521	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Apprch Slab Abutment 1	10	521	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Apprch Slab Abutment 6	10	521	12-Jul-21	23-Jul-21
Exspansion Joint			100	521	25-Jan-21	11-Jun-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Exp Joints	100	521	25-Jan-21	11-Jun-21
Deck			120	521	25-Jan-21	09-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Deck Slab	100	521	25-Jan-21	11-Jun-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Cure Deck Slab	20	521	14-Jun-21	09-Jul-21
Railings			10	521	12-Jul-21	23-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, BR 113.2 Install Conc Rail	10	521	12-Jul-21	23-Jul-21
Permanent Barriers			10	536	28-Jul-21	10-Aug-21
Concrete Barriers			10	536	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Place Conc Rail	10	536	28-Jul-21	10-Aug-21
Metal Beam Guardrails			10	536	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install MBGF	10	536	28-Jul-21	10-Aug-21
Crash Attenuators			5	541	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Attenuator	5	541	28-Jul-21	03-Aug-21
Signals and Illumination			25	521	28-Jul-21	31-Aug-21
Roadway Illumination			25	521	28-Jul-21	31-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Illumination Pole Bases	5	521	28-Jul-21	03-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Illumination Poles/Fixtures	10	521	04-Aug-21	17-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Illumination Energize Fixtures	10	521	18-Aug-21	31-Aug-21
Signing and Marking			26	521	27-Jul-21	01-Sep-21
Overhead Sign Structures			10	536	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Overhead Signage	10	536	28-Jul-21	10-Aug-21
Small Signage			10	536	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Small Signage	10	536	28-Jul-21	10-Aug-21
Pavement Marking			26	521	27-Jul-21	01-Sep-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Permt Markings	2	545	27-Jul-21	28-Jul-21
	TX-3CD	Area 3C3 - SB ML ENR, Finish STA 1330 to 1385	0	521	01-Sep-21	01-Sep-21
Landscaping			10	536	28-Jul-21	10-Aug-21
Seeding & Sodding			10	536	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Topsoil	10	536	28-Jul-21	10-Aug-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Seeding/Sodding	10	536	28-Jul-21	10-Aug-21
ITS/TCS			20	648	31-Dec-20	27-Jan-21
Duct Bank System			20	648	31-Dec-20	27-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, ITS &TCS Civil Work Install Coduit	20	648	31-Dec-20	27-Jan-21
Southbound Entry Ramp SBFR to SB ENR ML STA 1354 to 1360			123	653	09-Sep-20	01-Mar-21
C3(	TX-3CD	Area 3C3 - SB ML ENR, Start STA 1345 to 1360	0	653	09-Sep-20	09-Sep-20
Traffic Control and Temporary Work			6	653	09-Sep-20	16-Sep-20
Barricades, Signs & Traffic Handling			1	653	16-Sep-20	16-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Move Traffic	1	653	16-Sep-20	16-Sep-20
Portable Traffic Barrier			5	653	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Temp Conc Barrier	5	653	09-Sep-20	15-Sep-20
Workzone Pavement Marking			5	653	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Temp Marking & Signing	5	653	09-Sep-20	15-Sep-20
Erosion Control			5	653	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Temp Erosion Control	5	653	09-Sep-20	15-Sep-20
Removals & Demo			5	653	09-Sep-20	15-Sep-20
Pavement Removal			5	653	09-Sep-20	15-Sep-20

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB ML ENR, Remove Pavement	5	653	09-Sep-20	15-Sep-20
Earthwork			41	653	09-Sep-20	04-Nov-20
Clear & Grub			5	653	09-Sep-20	15-Sep-20
	TX-3CD	Area 3C3 - SB ML ENR, Clear and Grub	5	653	09-Sep-20	15-Sep-20
Excavation			15	653	17-Sep-20	07-Oct-20
	TX-3CD	Area 3C3 - SB ML ENR, Excavate Cut Areas	15	653	17-Sep-20	07-Oct-20
Embankment			20	653	08-Oct-20	04-Nov-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Embankment	20	653	08-Oct-20	04-Nov-20
Subgrade Treatment and Base			35	653	05-Nov-20	23-Dec-20
Lime Treatment			25	653	05-Nov-20	09-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, Lime Treat Subgrade	25	653	05-Nov-20	09-Dec-20
Flexbase			10	653	10-Dec-20	23-Dec-20
	TX-3CD	Area 3C3 - SB ML ENR, Place Flexbase	10	653	10-Dec-20	23-Dec-20
Pavement			31	669	24-Dec-20	04-Feb-21
(	TX-3CD	Area 3C3 - SB ML ENR, FF Start STA 1345 to 1360	0	653	22-Jan-21	22-Jan-21
Asphalt Pavement			21	669	07-Jan-21	04-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Interim - Finish STA 1345 to 1360	0	653	21-Jan-21	21-Jan-21
HMA Paving			5	658	07-Jan-21	13-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Place HMA	5	658	07-Jan-21	13-Jan-21
SMA Paving			10	669	22-Jan-21	04-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Place SMA	10	669	22-Jan-21	04-Feb-21
Curb & Gutter			10	658	24-Dec-20	06-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Place Curb & Gutter	10	658	24-Dec-20	06-Jan-21
Permanent Barriers			10	668	25-Jan-21	05-Feb-21
Concrete Barriers			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Place Conc Rail	10	668	25-Jan-21	05-Feb-21
Metal Beam Guardrails			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install MBGF	10	668	25-Jan-21	05-Feb-21
Crash Attenuators			5	673	25-Jan-21	29-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Attenuator	5	673	25-Jan-21	29-Jan-21
Signals and Illumination			25	653	25-Jan-21	26-Feb-21
Roadway Illumination			25	653	25-Jan-21	26-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Illumination Pole Bases	5	653	25-Jan-21	29-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Illumination Poles/Fixtures	10	653	01-Feb-21	12-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Illumination Energize Fixtures	10	653	15-Feb-21	26-Feb-21
Signing and Marking			26	653	22-Jan-21	01-Mar-21
Overhead Sign Structures			10	668	19-Feb-20	05-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Overhead Signage	10	668	25-Jan-21	05-Feb-21
Small Signage			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Small Signage	10	668	25-Jan-21	05-Feb-21
Pavement Marking			26	653	22-Jan-21	01-Mar-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Permt Markings	2	677	22-Jan-21	25-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, Finish STA 1345 to 1360	0	653	01-Mar-21	01-Mar-21
Landscaping			10	668	25-Jan-21	05-Feb-21
Seeding & Sodding			10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Seeding/Sodding	10	668	25-Jan-21	05-Feb-21
	TX-3CD	Area 3C3 - SB ML ENR, Install Topsoil	10	668	25-Jan-21	05-Feb-21
ITS/TCS			20	653	24-Dec-20	20-Jan-21
Duct Bank System			20	653	24-Dec-20	20-Jan-21
	TX-3CD	Area 3C3 - SB ML ENR, ITS &TCS Civil Work Install Coduit	20	653	24-Dec-20	20-Jan-21
Southbound Frontage Road Sta 1280 to 1401			158	412	24-Jun-21	01-Feb-22
C3(	TX-3CD	Area 3C3 - SB FR, Start STA 1280 to 1401	0	412	24-Jun-21	24-Jun-21
Traffic Control and Temporary Work			6	412	24-Jun-21	01-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Barricades, Signs & Traffic Handling			1	412	01-Jul-21	01-Jul-21
	TX-3CD	Area 3C3 - SB FR, Move Traffic	1	412	01-Jul-21	01-Jul-21
Portable Traffic Barrier			5	412	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB FR, Place Temp Conc Barrier	5	412	24-Jun-21	30-Jun-21
Workzone Pavement Marking			5	412	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB FR, Place Temp Marking & Signing	5	412	24-Jun-21	30-Jun-21
Erosion Control			5	412	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB FR, Place Temp Erosion Control	5	412	24-Jun-21	30-Jun-21
Removals & Demo			5	412	24-Jun-21	30-Jun-21
Pavement Removal			5	412	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB FR, Remove Pavement	5	412	24-Jun-21	30-Jun-21
Earthwork			61	412	24-Jun-21	16-Sep-21
Clear & Grub			5	412	24-Jun-21	30-Jun-21
	TX-3CD	Area 3C3 - SB FR, Clear and Grub	5	412	24-Jun-21	30-Jun-21
Excavation			15	412	02-Jul-21	22-Jul-21
	TX-3CD	Area 3C3 - SB FR, Excavate Cut Areas	15	412	02-Jul-21	22-Jul-21
Embankment			20	412	20-Aug-21	16-Sep-21
	TX-3CD	Area 3C3 - SB FR, Place Embankment	20	412	20-Aug-21	16-Sep-21
Drainage			121	428	23-Jul-21	07-Jan-22
Culverts			20	412	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C3 - SB FR, CLV 10A Install Culvert	20	412	23-Jul-21	19-Aug-21
	TX-3CD	Area 3C3 - SB FR, CLV 10B Install Culvert	20	412	23-Jul-21	19-Aug-21
Storm Sewer			20	412	20-Aug-21	16-Sep-21
	TX-3CD	Area 3C3 - NB ML, Install Small RCP	20	412	20-Aug-21	16-Sep-21
Riprap			10	428	27-Dec-21	07-Jan-22
	TX-3CD	Area 3C3 - NB ML, Place RipRap	10	428	27-Dec-21	07-Jan-22
Inlets			20	412	17-Sep-21	14-Oct-21
	TX-3CD	Area 3C3 - NB ML, Install MHs and Inlets	20	412	17-Sep-21	14-Oct-21
Headwall			10	492	20-Aug-21	02-Sep-21
	TX-3CD	Area 3C3 - NB ML, Place Conc Headwall	10	492	20-Aug-21	02-Sep-21
Subgrade Treatment and Base			40	412	17-Sep-21	11-Nov-21
Lime Treatment			20	412	17-Sep-21	14-Oct-21
	TX-3CD	Area 3C3 - SB FR, Lime Treat Subgrade	20	412	17-Sep-21	14-Oct-21
Flexbase			20	412	15-Oct-21	11-Nov-21
	TX-3CD	Area 3C3 - SB FR, Place Flexbase	20	412	15-Oct-21	11-Nov-21
Pavement			42	427	12-Nov-21	10-Jan-22
(	TX-3CD	Area 3C3 - SB FR, FF Start STA 1280 to 1401	0	412	27-Dec-21	27-Dec-21
Asphalt Pavement			16	433	10-Dec-21	31-Dec-21
	TX-3CD	Area 3C3 - SB FR, Interim - Finish STA 1280 to 1401	0	412	24-Dec-21	24-Dec-21
HMA Paving			10	412	10-Dec-21	23-Dec-21
	TX-3CD	Area 3C3 - SB FR, Place HMA	10	412	10-Dec-21	23-Dec-21
SMA Paving			5	433	27-Dec-21	31-Dec-21
	TX-3CD	Area 3C3 - SB FR, Place SMA	5	433	27-Dec-21	31-Dec-21
Curb & Gutter			20	412	12-Nov-21	09-Dec-21
	TX-3CD	Area 3C3 - SB FR, Place Curb & Gutter	20	412	12-Nov-21	09-Dec-21
Driveways			10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Place Driveways	10	427	28-Dec-21	10-Jan-22
Sidewalks & Median			10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Place Sidewalks/Pathways	10	427	28-Dec-21	10-Jan-22
Permanent Barriers			10	427	28-Dec-21	10-Jan-22
Concrete Barriers			10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Place Conc Rail	10	427	28-Dec-21	10-Jan-22
Metal Beam Guardrails			10	427	28-Dec-21	10-Jan-22

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
	TX-3CD	Area 3C3 - SB FR, Install MBGF	10	427	28-Dec-21	10-Jan-22
Signals and Illumination			26	412	27-Dec-21	31-Jan-22
Roadway Illumination			25	412	28-Dec-21	31-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Illumination Pole Bases	5	412	28-Dec-21	03-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Illumination Poles/Fixtures	10	412	04-Jan-22	17-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Illumination Energize Fixtures	10	412	18-Jan-22	31-Jan-22
High Mast Illumination			15	422	28-Dec-21	17-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install High Mast Illumination Pole Bases	5	422	28-Dec-21	03-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install High Mast Illumination Poles/Fixtures	5	422	04-Jan-22	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install High Mast Illumination Energize Fixtures	5	422	11-Jan-22	17-Jan-22
Traffic Signals			10	428	27-Dec-21	07-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Traffic Light Poles/Fixtures	10	428	27-Dec-21	07-Jan-22
Signing and Marking			26	412	27-Dec-21	01-Feb-22
Overhead Sign Structures			10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Overhead Signage	10	427	28-Dec-21	10-Jan-22
Small Signage			10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Small Signage	10	427	28-Dec-21	10-Jan-22
Pavement Marking			26	412	27-Dec-21	01-Feb-22
	TX-3CD	Area 3C3 - SB FR, Install Permt Markings	2	436	27-Dec-21	28-Dec-21
	TX-3CD	Area 3C3 - SB FR, Finish STA 1280 to 1401	0	412	01-Feb-22	01-Feb-22
Landscaping			10	427	28-Dec-21	10-Jan-22
Seeding & Sodding			10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Topsoil	10	427	28-Dec-21	10-Jan-22
	TX-3CD	Area 3C3 - SB FR, Install Seeding/Sodding	10	427	28-Dec-21	10-Jan-22
ITS/TCS			20	422	12-Nov-21	09-Dec-21
Duct Bank System			20	422	12-Nov-21	09-Dec-21
	TX-3CD	Area 3C3 - SB FR, ITS &TCS Civil Work Install Coduit	20	422	12-Nov-21	09-Dec-21
Interchange 820 Ramps			470	24	08-Oct-19	27-Jul-21
DC SB EXR SB IH35W to WB H820			470	24	08-Oct-19	27-Jul-21
C3A820S	TX-3CD	IH 820 - SB EXR, Start STA 1180 to 1220	20	91	07-Jan-20	03-Feb-20
C3A820S	TX-3CD	IH 820 - SB EXR, Interim - Finish STA 1180 to 1220	0	24	02-Jul-21	02-Jul-21
C3A820S	TX-3CD	IH 820 - SB EXR, FF Start STA 1180 to 1220	0	24	05-Jul-21	05-Jul-21
C3A820S	TX-3CD	IH 820 - SB EXR, Finish STA 1180 to 1220	0	24	27-Jul-21	27-Jul-21
Traffic Control and Temporary Work			6	246	04-Feb-20	11-Feb-20
Barricades, Signs & Traffic Handling			1	246	11-Feb-20	11-Feb-20
C3A	TX-3CD	IH 820 - SB EXR, Move Traffic	1	246	11-Feb-20	11-Feb-20
Portable Traffic Barrier			5	246	04-Feb-20	10-Feb-20
C3A	TX-3CD	IH 820 - SB EXR, Place Temp Conc Barrier	5	246	04-Feb-20	10-Feb-20
Workzone Pavement Marking			5	246	04-Feb-20	10-Feb-20
C3A	TX-3CD	IH 820 - SB EXR, Place Temp Marking & Signing	5	246	04-Feb-20	10-Feb-20
Erosion Control			5	246	04-Feb-20	10-Feb-20
C3A	TX-3CD	IH 820 - SB EXR, Place Temp Erosion Control	5	246	04-Feb-20	10-Feb-20
Removals & Demo			5	246	04-Feb-20	10-Feb-20
Pavement Removal			5	246	04-Feb-20	10-Feb-20
C3A	TX-3CD	IH 820 - Remove Pavement & Barriers	5	246	04-Feb-20	10-Feb-20
Earthwork			35	296	12-Feb-20	31-Mar-20
Excavation			15	246	12-Feb-20	03-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, Excavate Cut Areas	15	246	12-Feb-20	03-Mar-20
Embankment			20	296	04-Mar-20	31-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, Place Embankment	20	296	04-Mar-20	31-Mar-20
Subgrade Treatment and Base			85	246	01-Apr-20	28-Jul-20

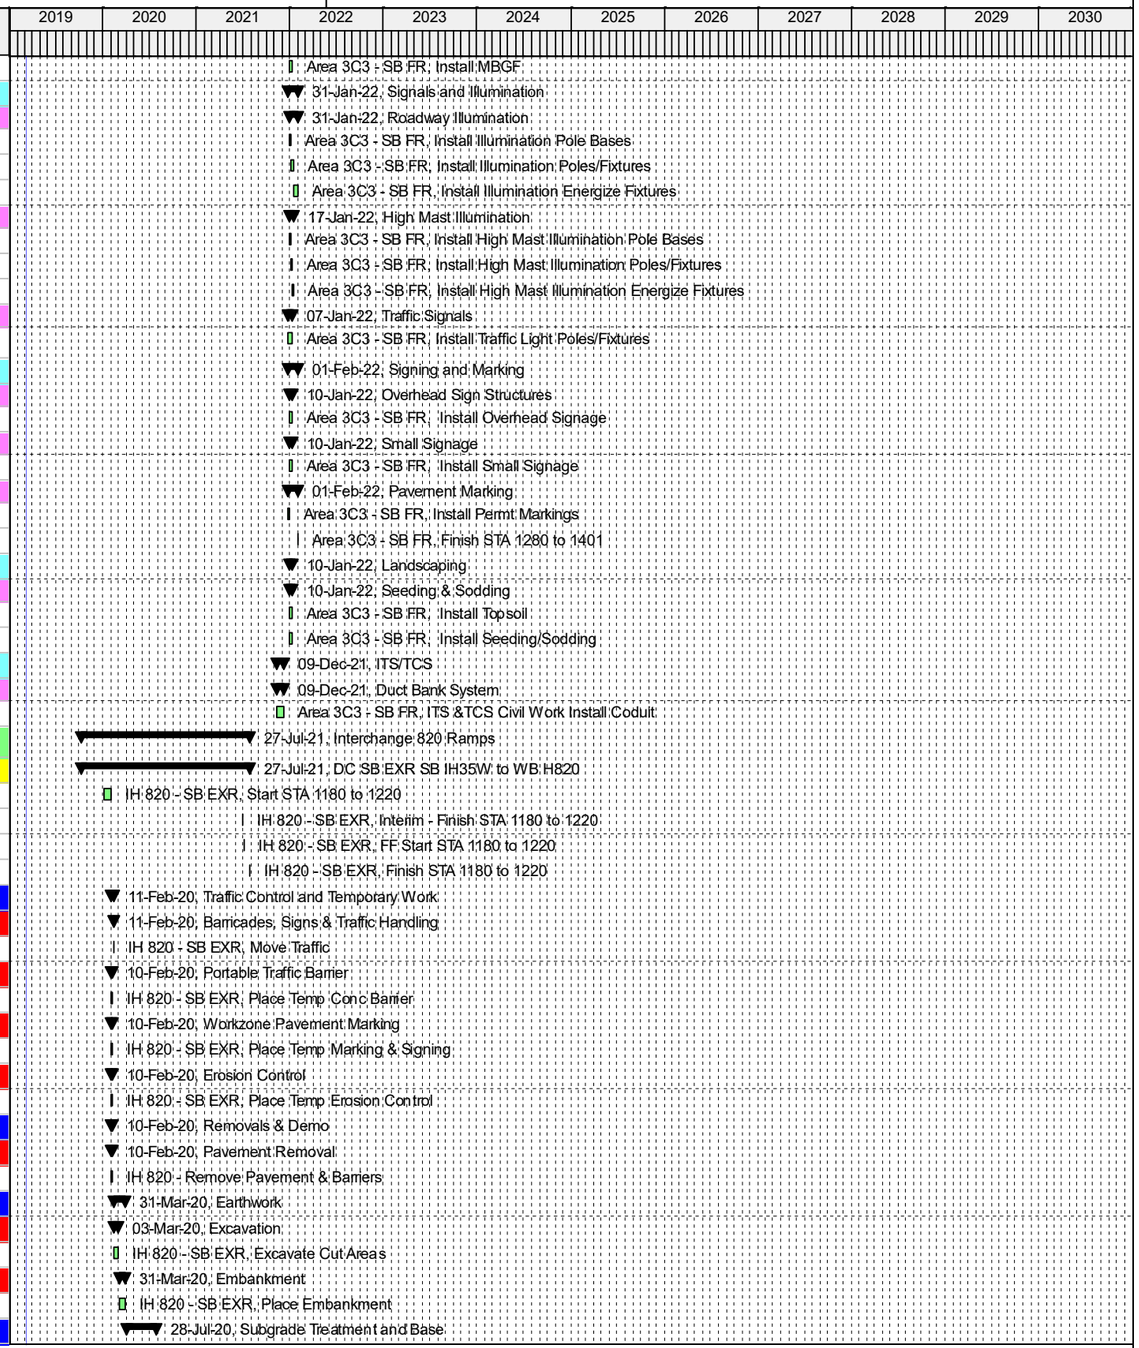

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Lime Treatment			20	296	01-Apr-20	28-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, Lime Treat Subgrade	20	296	01-Apr-20	28-Apr-20
Flexbase			15	246	08-Jul-20	28-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, Place Flexbase	15	246	08-Jul-20	28-Jul-20
Pavement			248	35	29-Jul-20	09-Jul-21
Asphalt Pavement			26	35	04-Jun-21	09-Jul-21
HMA Paving			5	39	04-Jun-21	10-Jun-21
C	TX-3CD	IH 820 - SB EXR, Place HMA	5	39	04-Jun-21	10-Jun-21
SMA Paving			5	35	05-Jul-21	09-Jul-21
C	TX-3CD	IH 820 - SB EXR, Place SMA	5	35	05-Jul-21	09-Jul-21
Curb & Gutter			10	251	29-Jul-20	11-Aug-20
C3A	TX-3CD	IH 820 - SB EXR, Place Curb & Gutter	10	251	29-Jul-20	11-Aug-20
Retaining Walls			90	246	04-Mar-20	07-Jul-20
Wall RTW A			90	246	04-Mar-20	07-Jul-20
C3C	TX-3CD	IH 820 - SB EXR, Install Leveling Pad RTW A	15	246	04-Mar-20	24-Mar-20
C3C	TX-3CD	IH 820 - SB EXR, Install Wall RTW A	60	246	25-Mar-20	16-Jun-20
Wall Coping RTW A			15	246	17-Jun-20	07-Jul-20
C	TX-3CD	IH 820 - SB EXR, Install Coping Cap RTW A	15	246	17-Jun-20	07-Jul-20
Wall RTW B			50	286	04-Mar-20	12-May-20
C3C	TX-3CD	IH 820 - SB EXR, Install Leveling Pad	5	286	04-Mar-20	10-Mar-20
C3C	TX-3CD	IH 820 - SB EXR, Install Wall RT-3C-N4	30	286	11-Mar-20	21-Apr-20
Wall Coping RTW B			15	286	22-Apr-20	12-May-20
C	TX-3CD	IH 820 - SB EXR, Install Coping Cap RT-3C-N4	15	286	22-Apr-20	12-May-20
Wall RTW C			90	246	04-Mar-20	07-Jul-20
C3C	TX-3CD	IH 820 - SB EXR, Install Leveling Pad	15	246	04-Mar-20	24-Mar-20
C3C	TX-3CD	IH 820 - SB EXR, Install Wall RT-3C-N7	60	246	25-Mar-20	16-Jun-20
Wall Coping RTW C			15	246	17-Jun-20	07-Jul-20
C	TX-3CD	IH 820 - SB EXR, Install Coping Cap RT-3C-N7	15	246	17-Jun-20	07-Jul-20
BR 13A DC SB EXR SB IH35W to WB H820			453	24	08-Oct-19	02-Jul-21
C3A82	TX-3CD	IH 820 - SB EXR, BR 13A Start	20	91	04-Feb-20	02-Mar-20
C3A82	TX-3CD	IH 820 - SB EXR, BR 13A Finish	0	24	02-Jul-21	02-Jul-21
BR Excavation			5	91	04-Mar-20	10-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Bridge Excavation	5	91	04-Mar-20	10-Mar-20
Drill Shafts			84	109	11-Mar-20	06-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Abutment 1	4	91	11-Mar-20	16-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 2	4	91	17-Mar-20	20-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 3	4	91	23-Mar-20	26-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 4	4	91	27-Mar-20	01-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 5	4	91	02-Apr-20	07-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 6	4	91	08-Apr-20	13-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 7	4	91	14-Apr-20	17-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 8	4	91	20-Apr-20	23-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 9	4	91	24-Apr-20	29-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 10	4	91	30-Apr-20	05-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 11	4	91	06-May-20	11-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 12	4	91	12-May-20	15-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 13	4	91	18-May-20	21-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 14	4	91	22-May-20	27-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 15	4	91	28-May-20	02-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 16	4	91	03-Jun-20	08-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 17	4	91	09-Jun-20	12-Jun-20

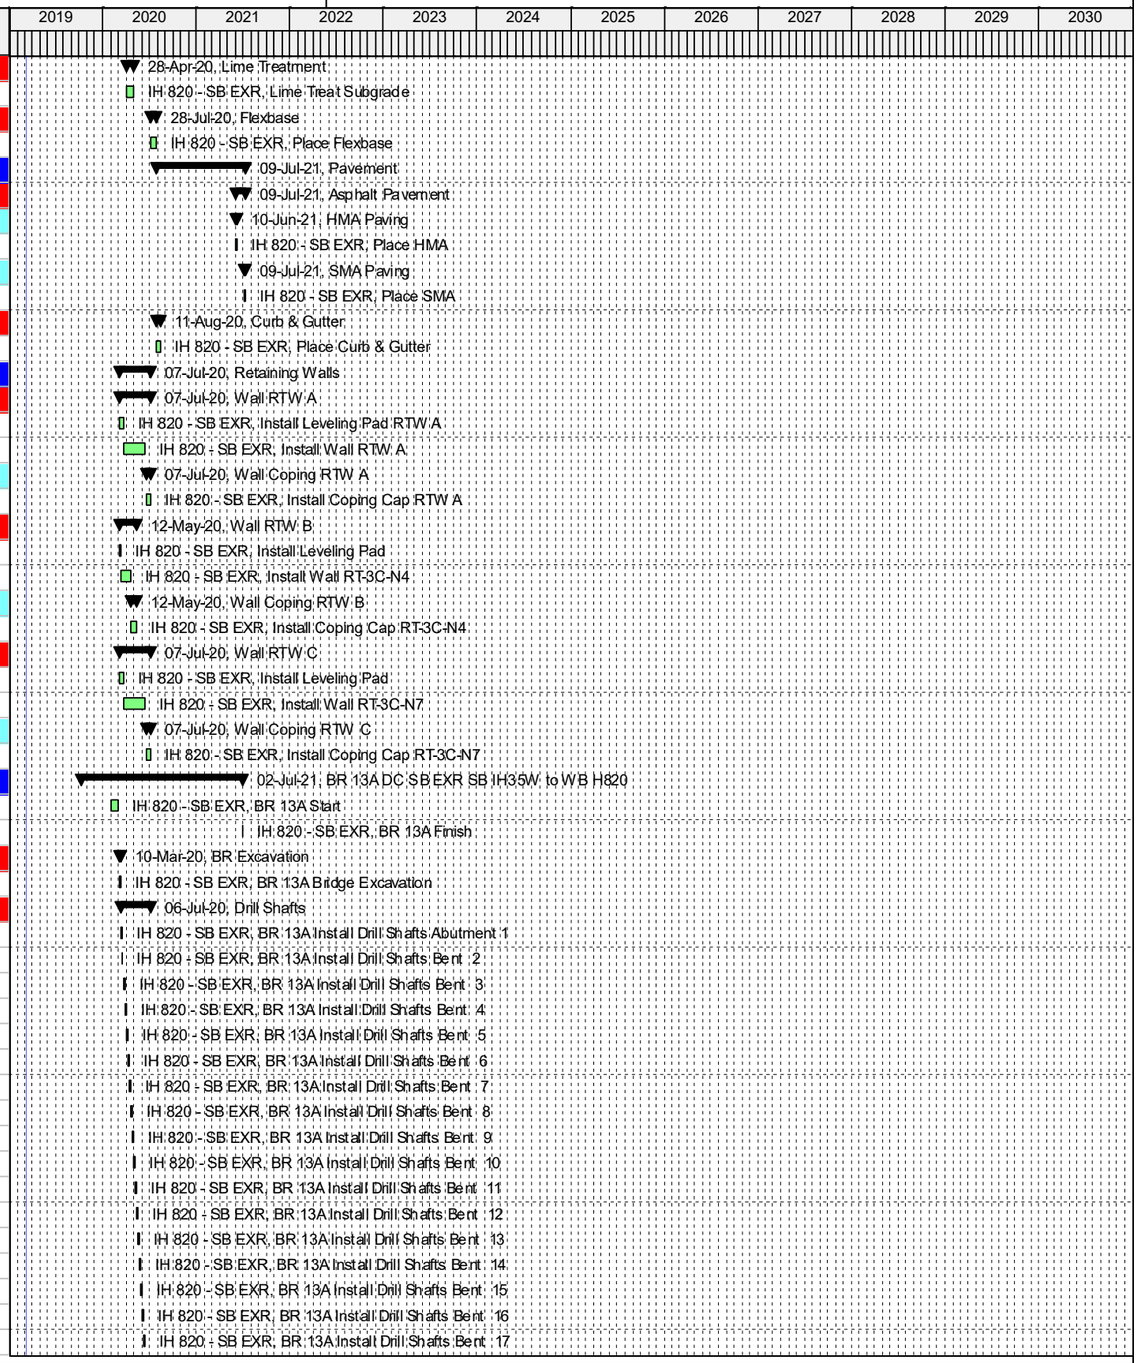

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 18	4	91	15-Jun-20	18-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 19	4	91	19-Jun-20	24-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Bent 20	4	91	25-Jun-20	30-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Drill Shafts Abutment 21	4	109	01-Jul-20	06-Jul-20
Footings			82	91	23-Mar-20	14-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 2	10	146	23-Mar-20	03-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 3	10	142	27-Mar-20	09-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 4	10	148	02-Apr-20	15-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 5	10	144	08-Apr-20	21-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 6	10	147	14-Apr-20	27-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 7	10	133	20-Apr-20	01-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 8	10	139	24-Apr-20	07-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 9	10	135	30-Apr-20	13-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 10	10	121	06-May-20	19-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 11	10	117	12-May-20	25-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 12	10	113	18-May-20	29-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 13	10	109	22-May-20	04-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 14	10	105	28-May-20	10-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 15	10	101	03-Jun-20	16-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 16	10	97	09-Jun-20	22-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 17	10	103	15-Jun-20	26-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 18	10	99	19-Jun-20	02-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 19	10	95	25-Jun-20	08-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Footings Bent 20	10	91	01-Jul-20	14-Jul-20
Columns			82	91	06-Apr-20	28-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 2	10	146	06-Apr-20	17-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 3	10	142	10-Apr-20	23-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 4	10	148	16-Apr-20	29-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 5	10	144	22-Apr-20	05-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 6	10	147	28-Apr-20	11-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 7	20	133	04-May-20	29-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 8	10	139	08-May-20	21-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 9	10	135	14-May-20	27-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 10	20	121	20-May-20	16-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 11	20	117	26-May-20	22-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 12	20	113	01-Jun-20	26-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 13	20	109	05-Jun-20	02-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 14	20	105	11-Jun-20	08-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 15	20	101	17-Jun-20	14-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 16	20	97	23-Jun-20	20-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 17	10	103	29-Jun-20	10-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 18	10	99	03-Jul-20	16-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 19	10	95	09-Jul-20	22-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Columns Bent 20	10	91	15-Jul-20	28-Jul-20
Bent Caps			84	91	20-Apr-20	13-Aug-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 2	12	146	20-Apr-20	05-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 3	12	142	24-Apr-20	11-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 4	12	148	30-Apr-20	15-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 5	12	144	06-May-20	21-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 6	12	147	12-May-20	27-May-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 8	12	139	22-May-20	08-Jun-20

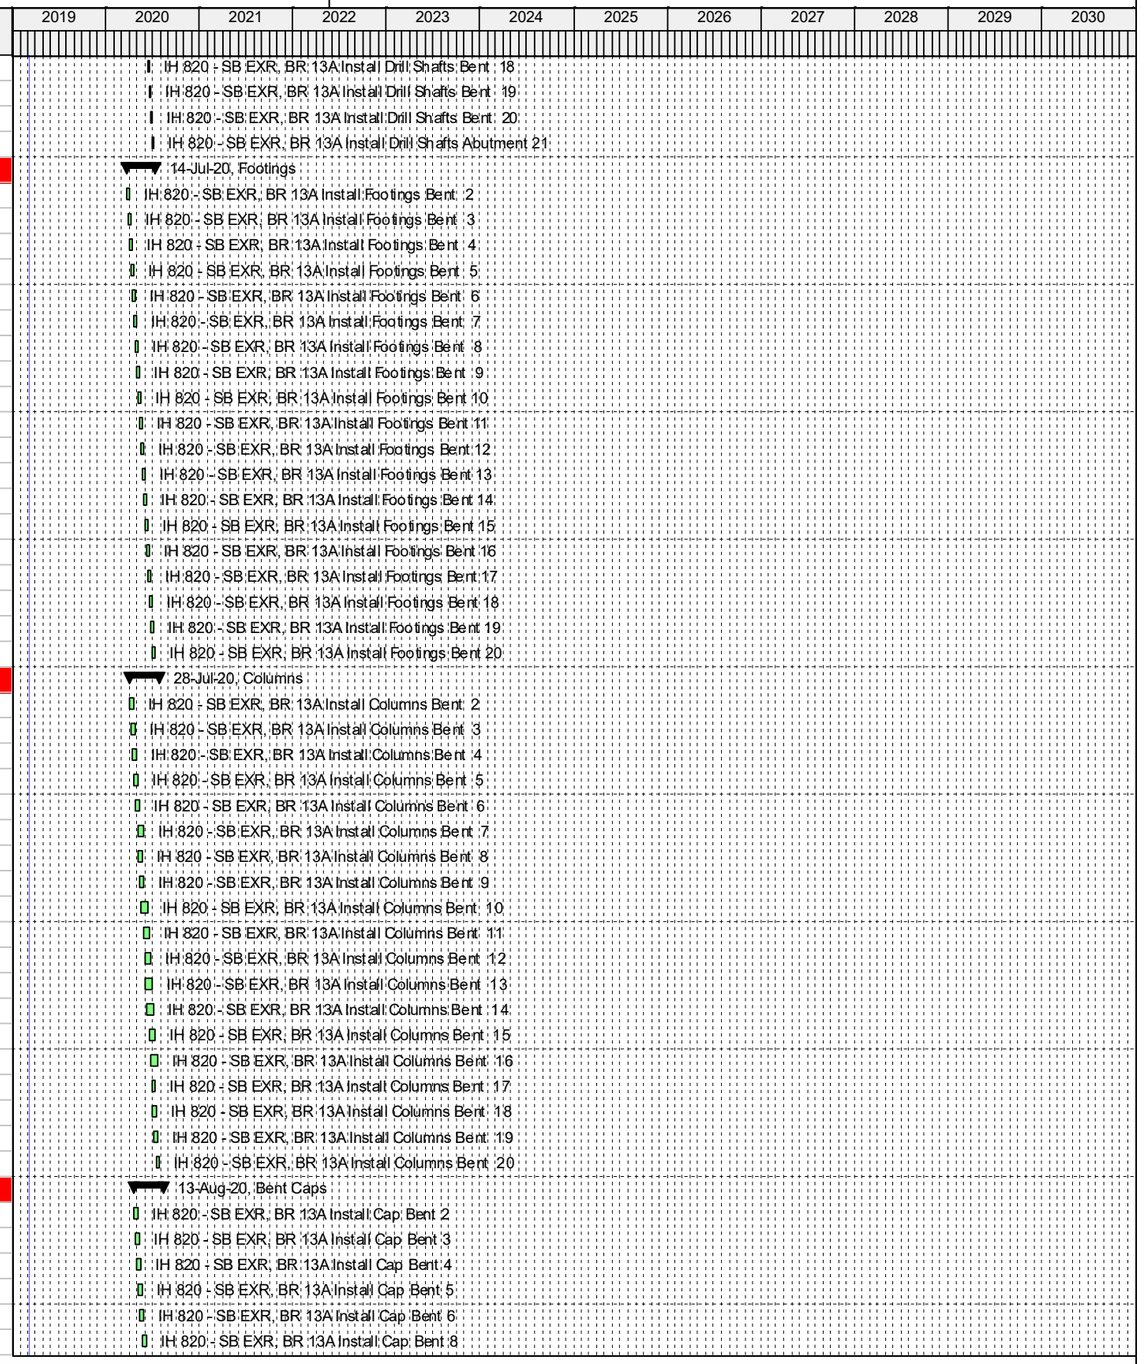

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 9	12	135	28-May-20	12-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 7	12	133	01-Jun-20	16-Jun-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 10	12	121	17-Jun-20	02-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 11	12	117	23-Jun-20	08-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 12	12	113	29-Jun-20	14-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 13	12	109	03-Jul-20	20-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 14	12	105	09-Jul-20	24-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 17	12	103	13-Jul-20	28-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 15	12	101	15-Jul-20	30-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 18	12	99	17-Jul-20	03-Aug-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 16	12	97	21-Jul-20	05-Aug-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 19	12	95	23-Jul-20	07-Aug-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Cap Bent 20	12	91	29-Jul-20	13-Aug-20
Beams			290	24	08-Oct-19	16-Nov-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Concrete Beam Procurement	60	176	08-Oct-19	30-Dec-19
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Steel Beam Procurement	45	24	08-Oct-19	09-Dec-19
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Forward Steel Beams Shopdrawings to TxDOT	1	24	10-Dec-19	10-Dec-19
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Steel Beam Fabrication & Delivery Leadtime	244	24	11-Dec-19	16-Nov-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Forward Precast Beams Shopdrawings to TxDOT	1	176	31-Dec-19	31-Dec-19
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Precast Beam Fabrication & Delivery Leadtime	60	176	01-Jan-20	24-Mar-20
BR Place CTB Embankment			20	317	31-Mar-20	27-Apr-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Place Stabilized Backfill	20	317	31-Mar-20	27-Apr-20
Abutments			90	109	17-Mar-20	20-Jul-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Abutment 1	10	172	17-Mar-20	30-Mar-20
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Abutment 21	10	109	07-Jul-20	20-Jul-20
Approach Slab			10	39	21-May-21	03-Jun-21
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Apprch Slab Abutment 1	10	39	21-May-21	03-Jun-21
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Apprch Slab Abutment 21	10	39	21-May-21	03-Jun-21
Exspansion Joint			133	24	17-Nov-20	20-May-21
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Exp Joints	133	24	17-Nov-20	20-May-21
Deck			288	24	11-May-20	17-Jun-21
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Cure Deck Slab	20	24	21-May-21	17-Jun-21
Unit 1			70	222	11-May-20	17-Aug-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 1-2) Install Beams	3	142	11-May-20	14-May-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 1-2) Deck Precast Panels	10	142	14-May-20	28-May-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 1-2) Deck PMD	10	222	01-Jun-20	15-Jun-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 1-2) Deck Overhangs	20	222	17-Jun-20	15-Jul-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 1-2) Deck Rebar	20	222	15-Jul-20	12-Aug-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 1-2) Pour Deck	3	222	12-Aug-20	17-Aug-20
Unit 2			74	210	21-May-20	02-Sep-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 3-5) Install Beams	3	144	21-May-20	26-May-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 3-5) Deck Precast Panels	10	142	28-May-20	11-Jun-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 3-5) Deck PMD	10	210	15-Jun-20	29-Jun-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 3-5) Deck Overhangs	20	210	01-Jul-20	29-Jul-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 3-5) Deck Rebar	20	210	31-Jul-20	28-Aug-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 3-5) Pour Deck	3	210	28-Aug-20	02-Sep-20
Unit 3			70	196	16-Jun-20	22-Sep-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 6-8) Install Beams	3	136	16-Jun-20	19-Jun-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 6-8) Deck Precast Panels	10	136	19-Jun-20	03-Jul-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 6-8) Deck PMD	10	196	07-Jul-20	21-Jul-20
C	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 6-8) Deck Overhangs	20	196	21-Jul-20	18-Aug-20

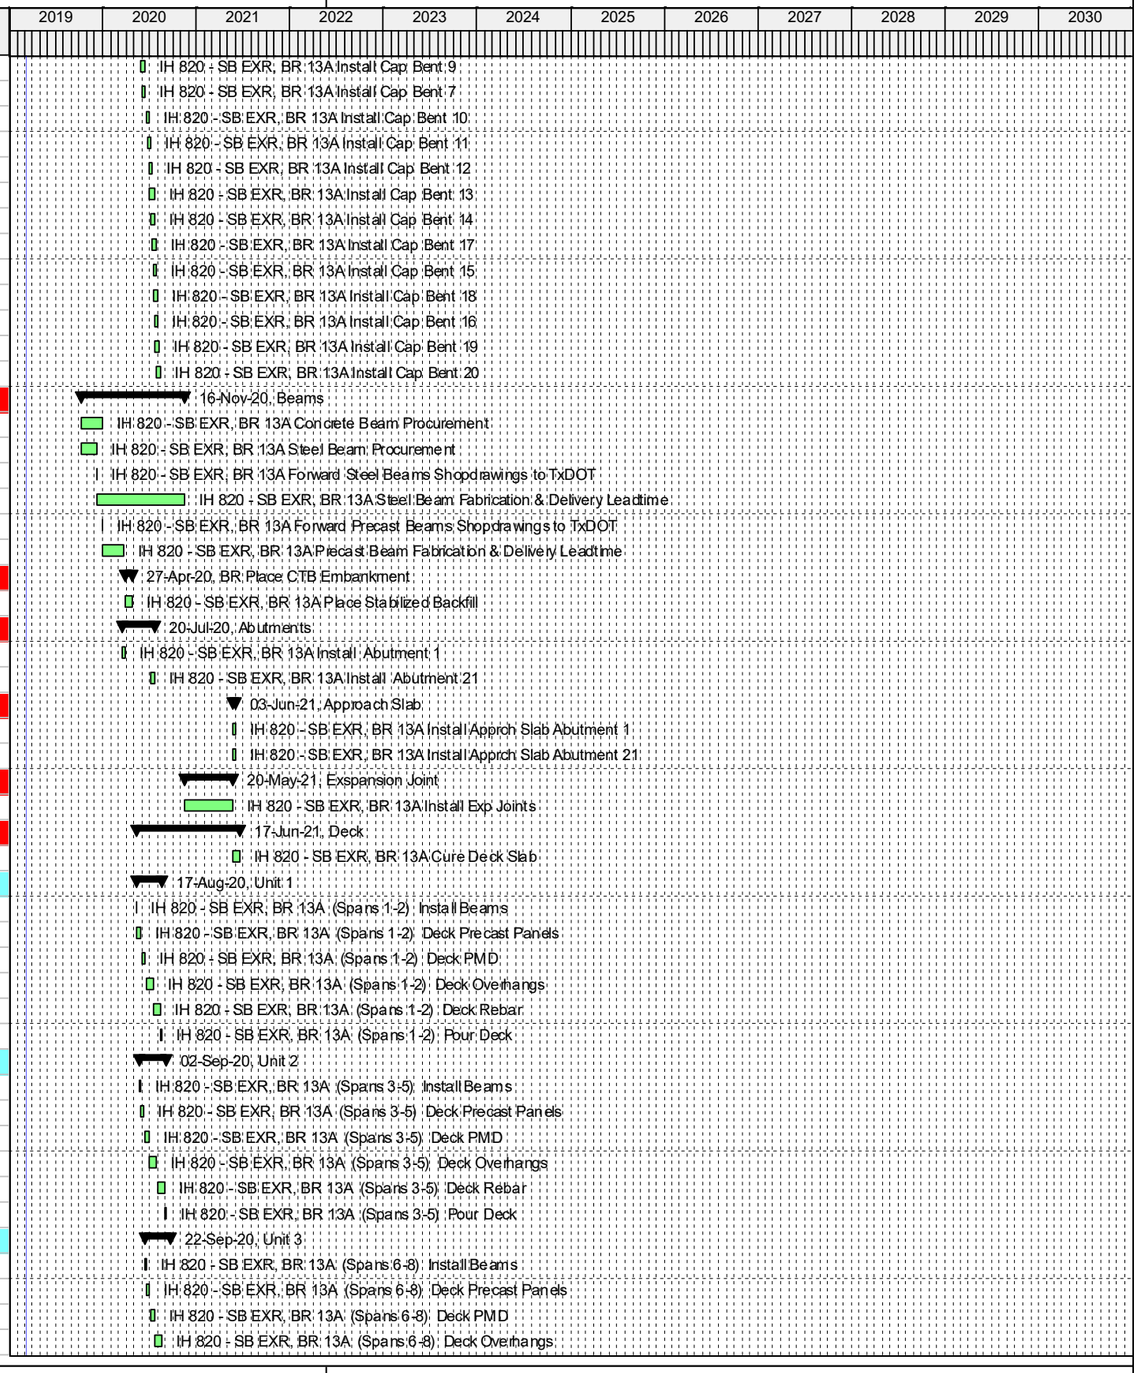

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 6-8) Deck Rebar	20	196	20-Aug-20	17-Sep-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 6-8) Pour Deck	3	196	17-Sep-20	22-Sep-20
Unit 4			70	177	08-Jul-20	14-Oct-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 9-11) Install Beams	3	130	08-Jul-20	13-Jul-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 9-11) Deck Precast Panels	10	130	13-Jul-20	27-Jul-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 9-11) Deck PMD	10	177	29-Jul-20	12-Aug-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 9-11) Deck Overhangs	20	177	14-Aug-20	11-Sep-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 9-11) Deck Rebar	20	177	11-Sep-20	09-Oct-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 9-11) Pour Deck	3	177	09-Oct-20	14-Oct-20
Unit 5			90	148	24-Jul-20	27-Nov-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 12-14) Install Beams	3	128	24-Jul-20	29-Jul-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 12-14) Deck Precast Panels	20	128	29-Jul-20	26-Aug-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 12-14) Deck PMD	20	148	28-Aug-20	25-Sep-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 12-14) Deck Overhangs	20	148	29-Sep-20	27-Oct-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 12-14) Deck Rebar	20	148	27-Oct-20	24-Nov-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 12-14) Pour Deck	3	148	24-Nov-20	27-Nov-20
Unit 6			90	67	16-Nov-20	22-Mar-21
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 15-17) Install Beams	3	67	16-Nov-20	19-Nov-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 15-17) Deck Precast Panels	20	67	19-Nov-20	17-Dec-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 15-17) Deck PMD	20	67	21-Dec-20	18-Jan-21
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 15-17) Deck Overhangs	20	67	20-Jan-21	17-Feb-21
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 15-17) Deck Rebar	20	67	17-Feb-21	17-Mar-21
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 15-17) Pour Deck	3	67	17-Mar-21	22-Mar-21
Unit 7			90	134	13-Aug-20	17-Dec-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 18-20) Ph1Stg1 Install Beams	3	134	13-Aug-20	18-Aug-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 18-20) Ph1Stg1 Deck Precast Panels	20	134	18-Aug-20	15-Sep-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 18-20) Ph1Stg1 Deck PMD	20	134	17-Sep-20	15-Oct-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 18-20) Ph1Stg1 Deck Overhangs	20	134	19-Oct-20	16-Nov-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 18-20) Ph1Stg1 Deck Rebar	20	134	16-Nov-20	14-Dec-20
(	TX-3CD	IH 820 - SB EXR, BR 13A (Spans 18-20) Ph1Stg1 Pour Deck	3	134	14-Dec-20	17-Dec-20
Railings			10	24	18-Jun-21	01-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, BR 13A Install Conc Rail	10	24	18-Jun-21	01-Jul-21
Permanent Barriers			10	29	06-Jul-21	19-Jul-21
Concrete Barriers			10	29	06-Jul-21	19-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Place Conc Rail	10	29	06-Jul-21	19-Jul-21
Metal Beam Guardrails			10	29	06-Jul-21	19-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install MBGF	10	29	06-Jul-21	19-Jul-21
Signals and Illumination			15	24	06-Jul-21	26-Jul-21
Roadway Illumination			15	24	06-Jul-21	26-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Illumination Pole Bases	5	24	06-Jul-21	12-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Illumination Poles/Fixtures	5	24	13-Jul-21	19-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Illumination Energize Fixtures	5	24	20-Jul-21	26-Jul-21
Signing and Marking			11	29	05-Jul-21	19-Jul-21
Overhead Sign Structures			10	29	06-Jul-21	19-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Overhead Signage	10	29	06-Jul-21	19-Jul-21
Small Signage			10	29	06-Jul-21	19-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Small Signage	10	29	06-Jul-21	19-Jul-21
Pavement Marking			2	38	05-Jul-21	06-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Permt Markings	2	38	05-Jul-21	06-Jul-21
Landscaping			10	29	06-Jul-21	19-Jul-21
Seeding & Sodding			10	29	06-Jul-21	19-Jul-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3A	TX-3CD	IH 820 - SB EXR, Install Topsoil	10	29	06-Jul-21	19-Jul-21
C3A	TX-3CD	IH 820 - SB EXR, Install Seeding/Sodding	10	29	06-Jul-21	19-Jul-21
ITS/TCS			20	246	29-Jul-20	25-Aug-20
Duct Bank System			20	246	29-Jul-20	25-Aug-20
C3A	TX-3CD	IH 820 - SB EXR, ITS &TCS Civil Work Install Coduit	20	246	29-Jul-20	25-Aug-20
DC NB ENR EBH820 to NB IH35W			470	24	08-Oct-19	27-Jul-21
C3A820N	TX-3CD	IH 820 - NB ENR, Start STA 1180 to 1220	0	109	07-Jan-20	07-Jan-20
C3A820N	TX-3CD	IH 820 - NB ENR, Interim - Finish STA 1180 to 1220	0	24	05-Jul-21	05-Jul-21
C3A820N	TX-3CD	IH 820 - NB ENR, FF Start STA 1180 to 1220	0	24	06-Jul-21	06-Jul-21
C3A820N	TX-3CD	IH 820 - NB ENR, Finish STA 1180 to 1220	0	24	27-Jul-21	27-Jul-21
Traffic Control and Temporary Work			6	222	07-Jan-20	14-Jan-20
Barricades, Signs & Traffic Handling			1	222	14-Jan-20	14-Jan-20
C3A	TX-3CD	IH 820 - NB ENR, Move Traffic	1	222	14-Jan-20	14-Jan-20
Portable Traffic Barrier			5	222	07-Jan-20	13-Jan-20
C3A	TX-3CD	IH 820 - NB ENR, Place Temp Conc Barrier	5	222	07-Jan-20	13-Jan-20
Workzone Pavement Marking			5	222	07-Jan-20	13-Jan-20
C3A	TX-3CD	IH 820 - NB ENR, Place Temp Marking & Signing	5	222	07-Jan-20	13-Jan-20
Erosion Control			5	222	07-Jan-20	13-Jan-20
C3A	TX-3CD	IH 820 - NB ENR, Place Temp Erosion Control	5	222	07-Jan-20	13-Jan-20
Removals & Demo			5	222	07-Jan-20	13-Jan-20
Pavement Removal			5	222	07-Jan-20	13-Jan-20
C3A	TX-3CD	IH 820 IH 820 - Remove Pavement & Barriers	5	222	07-Jan-20	13-Jan-20
Bridge Removal			5	222	07-Jan-20	13-Jan-20
C3A	TX-3CD	IH 820 IH 820 - Demo Bridge	5	222	07-Jan-20	13-Jan-20
Earthwork			35	317	15-Jan-20	03-Mar-20
Excavation			15	222	15-Jan-20	04-Feb-20
C3A	TX-3CD	IH 820 - NB ENR, Excavate Cut Areas	15	222	15-Jan-20	04-Feb-20
Embankment			20	317	05-Feb-20	03-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, Place Embankment	20	317	05-Feb-20	03-Mar-20
Subgrade Treatment and Base			130	222	04-Mar-20	01-Sep-20
Lime Treatment			20	317	04-Mar-20	31-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, Lime Treat Subgrade	20	317	04-Mar-20	31-Mar-20
Flexbase			15	222	12-Aug-20	01-Sep-20
C3A	TX-3CD	IH 820 - NB ENR, Place Flexbase	15	222	12-Aug-20	01-Sep-20
Pavement			224	34	02-Sep-20	12-Jul-21
Asphalt Pavement			16	34	21-Jun-21	12-Jul-21
HMA Paving			10	24	21-Jun-21	02-Jul-21
(	TX-3CD	IH 820 - NB ENR, Place HMA	10	24	21-Jun-21	02-Jul-21
SMA Paving			5	34	06-Jul-21	12-Jul-21
(	TX-3CD	IH 820 - NB ENR, Place SMA	5	34	06-Jul-21	12-Jul-21
Curb & Gutter			10	222	02-Sep-20	15-Sep-20
C3A	TX-3CD	IH 820 - NB ENR, Place Curb & Gutter	10	222	02-Sep-20	15-Sep-20
Retaining Walls			135	222	05-Feb-20	11-Aug-20
Wall RTW A			135	222	05-Feb-20	11-Aug-20
C3(	TX-3CD	IH 820 - NB ENR, Install Leveling Pad RTW A	60	222	05-Feb-20	28-Apr-20
C3(	TX-3CD	IH 820 - NB ENR, Install Wall RTW A	60	222	29-Apr-20	21-Jul-20
Wall Coping RTW A			15	222	22-Jul-20	11-Aug-20
(	TX-3CD	IH 820 - NB ENR, Install Coping Cap RTW A	15	222	22-Jul-20	11-Aug-20
Wall RTW B			135	222	05-Feb-20	11-Aug-20
C3(	TX-3CD	IH 820 - NB ENR, Install Leveling Pad RTW AB	60	222	05-Feb-20	28-Apr-20
C3(	TX-3CD	IH 820 - NB ENR, Install Wall RTW AB	60	222	29-Apr-20	21-Jul-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
Wall Coping RTW B			15	222	22-Jul-20	11-Aug-20
(	TX-3CD	IH 820 - NB ENR, Install Coping Cap RTW AB	15	222	22-Jul-20	11-Aug-20
Wall RTW C			135	222	05-Feb-20	11-Aug-20
C3(	TX-3CD	IH 820 - NB ENR, Install Leveling Pad RTW C	60	222	05-Feb-20	28-Apr-20
C3(	TX-3CD	IH 820 - NB ENR, Install Wall RTW C	60	222	29-Apr-20	21-Jul-20
Wall Coping RTW C			15	222	22-Jul-20	11-Aug-20
(	TX-3CD	IH 820 - NB ENR, Install Coping Cap RTW C	15	222	22-Jul-20	11-Aug-20
BR 22 DC NB ENR EBH820 to NB IH35W			449	29	08-Oct-19	28-Jun-21
C3A82	TX-3CD	IH 820 - NB ENR, BR 22 Start	20	109	07-Jan-20	03-Feb-20
C3A82	TX-3CD	IH 820 - NB ENR, BR 22 Finish	0	29	28-Jun-21	28-Jun-21
BR Excavation			5	109	05-Feb-20	11-Feb-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Bridge Excavation	5	109	05-Feb-20	11-Feb-20
Drill Shafts			84	125	12-Feb-20	08-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Abutment 1	4	109	12-Feb-20	17-Feb-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 2	4	109	18-Feb-20	21-Feb-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 3	4	109	24-Feb-20	27-Feb-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 4	4	109	28-Feb-20	04-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 5	4	109	05-Mar-20	10-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 6	4	109	11-Mar-20	16-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 7	4	109	17-Mar-20	20-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 8	4	109	23-Mar-20	26-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 9	4	109	27-Mar-20	01-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 10	4	109	02-Apr-20	07-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 11	4	109	08-Apr-20	13-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 12	4	109	14-Apr-20	17-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 13	4	109	20-Apr-20	23-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 14	4	109	24-Apr-20	29-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 15	4	109	30-Apr-20	05-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 16	4	109	06-May-20	11-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 17	4	109	12-May-20	15-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 18	4	109	18-May-20	21-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 19	4	109	22-May-20	27-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Bent 20	4	109	28-May-20	02-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Drill Shafts Abutment 21	4	125	03-Jun-20	08-Jun-20
Footings			82	109	24-Feb-20	16-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 2	10	164	24-Feb-20	06-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 3	10	160	28-Feb-20	12-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 4	10	166	05-Mar-20	18-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 5	10	162	11-Mar-20	24-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 6	10	165	17-Mar-20	30-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 7	10	151	23-Mar-20	03-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 8	10	157	27-Mar-20	09-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 9	10	153	02-Apr-20	15-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 10	10	139	08-Apr-20	21-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 11	10	135	14-Apr-20	27-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 12	10	131	20-Apr-20	01-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 13	10	127	24-Apr-20	07-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 14	10	123	30-Apr-20	13-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 15	10	119	06-May-20	19-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 16	10	115	12-May-20	25-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 17	10	121	18-May-20	29-May-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 18	10	117	22-May-20	04-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 19	10	113	28-May-20	10-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Footings Bent 20	10	109	03-Jun-20	16-Jun-20
Columns			82	109	09-Mar-20	30-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 2	10	164	09-Mar-20	20-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 3	10	160	13-Mar-20	26-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 4	10	166	19-Mar-20	01-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 5	10	162	25-Mar-20	07-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 6	10	165	31-Mar-20	13-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 7	20	151	06-Apr-20	01-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 8	10	157	10-Apr-20	23-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 9	10	153	16-Apr-20	29-Apr-20
C3A	TX-3CD	19-Feb-20	20	139	22-Apr-20	19-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 11	20	135	28-Apr-20	25-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 12	20	131	04-May-20	29-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 13	20	127	08-May-20	04-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 14	20	123	14-May-20	10-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 15	20	119	20-May-20	16-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 16	20	115	26-May-20	22-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 17	10	121	01-Jun-20	12-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 18	10	117	05-Jun-20	18-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 19	10	113	11-Jun-20	24-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Columns Bent 20	10	109	17-Jun-20	30-Jun-20
Bent Caps			82	109	23-Mar-20	14-Jul-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 2	10	164	23-Mar-20	03-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 3	10	160	27-Mar-20	09-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 4	10	166	02-Apr-20	15-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 5	10	162	08-Apr-20	21-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 6	10	165	14-Apr-20	27-Apr-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 8	10	157	24-Apr-20	07-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 9	10	153	30-Apr-20	13-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 7	10	151	04-May-20	15-May-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 10	10	139	20-May-20	02-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 11	10	135	26-May-20	08-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 12	10	131	01-Jun-20	12-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 13	10	127	05-Jun-20	18-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 14	10	123	11-Jun-20	24-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 17	10	121	15-Jun-20	26-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 15	10	119	17-Jun-20	30-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 18	10	117	19-Jun-20	02-Jul-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 16	10	115	23-Jun-20	06-Jul-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 19	10	113	25-Jun-20	08-Jul-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Cap Bent 20	10	109	01-Jul-20	14-Jul-20
Beams			286	24	08-Oct-19	10-Nov-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Concrete Beam Procurement	20	232	08-Oct-19	04-Nov-19
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Steel Beam Procurement	40	24	08-Oct-19	02-Dec-19
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Forward Precast Beams Shopdrawings to TxDOT	1	232	05-Nov-19	05-Nov-19
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Precast Beam Fabrication & Delivery Leadtime	40	232	06-Nov-19	31-Dec-19
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Forward Steel Beams Shopdrawings to TxDOT	1	24	03-Dec-19	03-Dec-19
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Steel Beam Fabrication & Delivery Leadtime	245	24	04-Dec-19	10-Nov-20
BR Place CTB Embankment			20	338	03-Mar-20	30-Mar-20

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Place Stabilized Backfill	20	338	03-Mar-20	30-Mar-20
Abutments			90	125	18-Feb-20	22-Jun-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Abutment 1	10	188	18-Feb-20	02-Mar-20
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Abutment 21	10	125	09-Jun-20	22-Jun-20
Approach Slab			5	24	14-Jun-21	18-Jun-21
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Apprch Slab Abutment 1	5	24	14-Jun-21	18-Jun-21
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Apprch Slab Abutment 21	5	24	14-Jun-21	18-Jun-21
Exspansion Joint			133	24	11-Nov-20	14-May-21
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Install Exp Joints	133	24	11-Nov-20	14-May-21
Deck			306	24	09-Apr-20	11-Jun-21
C3A	TX-3CD	IH 820 - NB ENR, BR 22 Cure Deck Slab	20	24	17-May-21	11-Jun-21
Unit 1			70	240	09-Apr-20	16-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 1-2) Install Beams	3	160	09-Apr-20	14-Apr-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 1-2) Deck Precast Panels	10	160	14-Apr-20	28-Apr-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 1-2) Deck PMD	10	240	30-Apr-20	14-May-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 1-2) Deck Overhangs	20	240	18-May-20	15-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 1-2) Deck Rebar	20	240	15-Jun-20	13-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 1-2) Pour Deck	3	240	13-Jul-20	16-Jul-20
Unit 2			74	228	21-Apr-20	03-Aug-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 3-5) Install Beams	3	162	21-Apr-20	24-Apr-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 3-5) Deck Precast Panels	10	160	28-Apr-20	12-May-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 3-5) Deck PMD	10	228	14-May-20	28-May-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 3-5) Deck Overhangs	20	228	01-Jun-20	29-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 3-5) Deck Rebar	20	228	01-Jul-20	29-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 3-5) Pour Deck	3	228	29-Jul-20	03-Aug-20
Unit 3			70	214	15-May-20	21-Aug-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 6-8) Install Beams	3	154	15-May-20	20-May-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 6-8) Deck Precast Panels	10	154	20-May-20	03-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 6-8) Deck PMD	10	214	05-Jun-20	19-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 6-8) Deck Overhangs	20	214	19-Jun-20	17-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 6-8) Deck Rebar	20	214	21-Jul-20	18-Aug-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 6-8) Pour Deck	3	214	18-Aug-20	21-Aug-20
Unit 4			70	195	08-Jun-20	14-Sep-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 9-11) Install Beams	3	148	08-Jun-20	11-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 9-11) Deck Precast Panels	10	148	11-Jun-20	25-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 9-11) Deck PMD	10	195	29-Jun-20	13-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 9-11) Deck Overhangs	20	195	15-Jul-20	12-Aug-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 9-11) Deck Rebar	20	195	12-Aug-20	09-Sep-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 9-11) Pour Deck	3	195	09-Sep-20	14-Sep-20
Unit 5			90	166	24-Jun-20	28-Oct-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 12-14) Install Beams	3	146	24-Jun-20	29-Jun-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 12-14) Deck Precast Panels	20	146	29-Jun-20	27-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 12-14) Deck PMD	20	166	29-Jul-20	26-Aug-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 12-14) Deck Overhangs	20	166	28-Aug-20	25-Sep-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 12-14) Deck Rebar	20	166	25-Sep-20	23-Oct-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 12-14) Pour Deck	3	166	23-Oct-20	28-Oct-20
Unit 6			90	67	10-Nov-20	16-Mar-21
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 15-17) Install Beams	3	67	10-Nov-20	13-Nov-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 15-17) Deck Precast Panels	20	67	13-Nov-20	11-Dec-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 15-17) Deck PMD	20	67	15-Dec-20	12-Jan-21
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 15-17) Deck Overhangs	20	67	14-Jan-21	11-Feb-21

© Oracle Corporation

Activity ID	WBS	Activity Name	Original Duration	Total Float	Start	Finish
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 15-17) Deck Rebar	20	67	11-Feb-21	11-Mar-21
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 15-17) Pour Deck	3	67	11-Mar-21	16-Mar-21
Unit 7			90	152	14-Jul-20	17-Nov-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 18-20) Ph1Stg1 Install Beams	3	152	14-Jul-20	17-Jul-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 18-20) Ph1Stg1 Deck Precast Panels	20	152	17-Jul-20	14-Aug-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 18-20) Ph1Stg1 Deck PMD	20	152	18-Aug-20	15-Sep-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 18-20) Ph1Stg1 Deck Overhangs	20	152	17-Sep-20	15-Oct-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 18-20) Ph1Stg1 Deck Rebar	20	152	15-Oct-20	12-Nov-20
(	TX-3CD	IH 820 - NB ENR, BR 22 (Spans 18-20) Ph1Stg1 Pour Deck	3	152	12-Nov-20	17-Nov-20
Railings			10	29	14-Jun-21	25-Jun-21
C3A	TX-3CD	IH 820 - NB ENR, BR 122 Install Conc Rail	10	29	14-Jun-21	25-Jun-21
Permanent Barriers			10	28	07-Jul-21	20-Jul-21
Concrete Barriers			10	28	07-Jul-21	20-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Place Conc Rail	10	28	07-Jul-21	20-Jul-21
Metal Beam Guardrails			10	28	07-Jul-21	20-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install MBGF	10	28	07-Jul-21	20-Jul-21
Signals and Illumination			14	24	07-Jul-21	26-Jul-21
Roadway Illumination			14	24	07-Jul-21	26-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Illumination Pole Bases	5	24	07-Jul-21	13-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Illumination Poles/Fixtures	2	24	14-Jul-21	15-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Illumination Energize Fixtures	7	24	16-Jul-21	26-Jul-21
Signing and Marking			11	28	06-Jul-21	20-Jul-21
Overhead Sign Structures			10	28	07-Jul-21	20-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Overhead Signage	10	28	07-Jul-21	20-Jul-21
Small Signage			10	28	07-Jul-21	20-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Small Signage	10	28	07-Jul-21	20-Jul-21
Pavement Marking			2	37	06-Jul-21	07-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Permt Markings	2	37	06-Jul-21	07-Jul-21
Landscaping			10	28	07-Jul-21	20-Jul-21
Seeding & Sodding			10	28	07-Jul-21	20-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Topsoil	10	28	07-Jul-21	20-Jul-21
C3A	TX-3CD	IH 820 - NB ENR, Install Seeding/Sodding	10	28	07-Jul-21	20-Jul-21
ITS/TCS			20	222	02-Sep-20	29-Sep-20
Duct Bank System			20	222	02-Sep-20	29-Sep-20
C3A	TX-3CD	IH 820 - NB ENR, ITS &TCS Civil Work Install Coduit	20	222	02-Sep-20	29-Sep-20

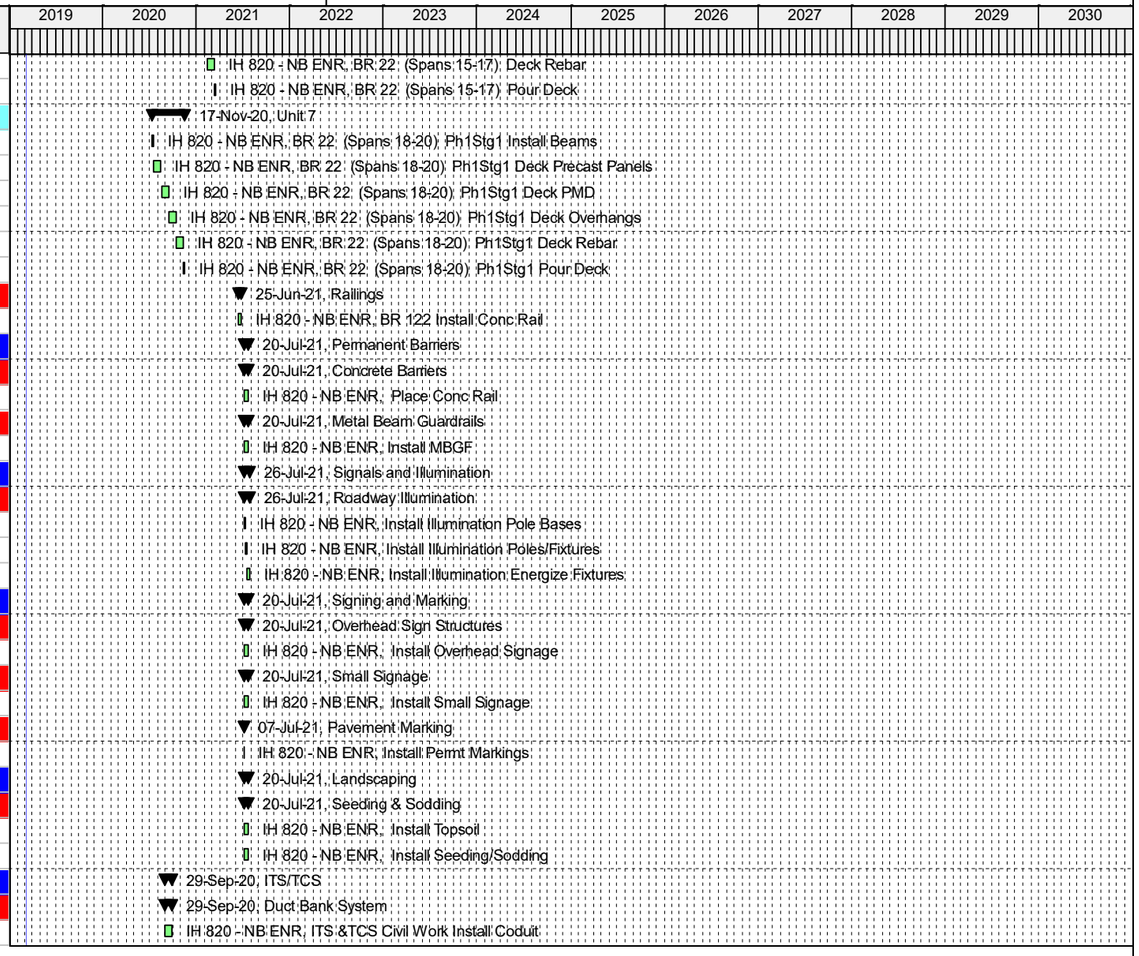

Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: All Activities

© Oracle Corporation
